

*Storm Water Pollution Prevention Plan (SWPPP)*  
**Alpine Regional Field Office**  
**1010 Tavern Road**  
**Alpine, CA 91901**



**October 28, 2010, Revision 1**



**Prepared for:**  
**SDG&E**  
8326 Century Park Court  
San Diego, CA 92123

**Prepared by:**  
**Bureau Veritas**  
11590 West Bernardo Court, Suite 100  
San Diego, CA 92127  
858.451.6100  
[www.us.bureauveritas.com](http://www.us.bureauveritas.com)

# STORM WATER POLLUTION PREVENTION PLAN (SWPPP)

FOR

**SUNRISE POWERLINK  
ALPINE REGIONAL FIELD OFFICE  
LEVEL 2  
1010 TAVERN ROAD  
ALPINE, CA 91901**

**San Diego Gas and Electric (SDG&E)  
Contract Number: 5660016733**

This SWPPP has been prepared for **Traditional Projects** in accordance/compliance with the **State Water Resources Control Board** (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002 Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities.

WDID # 9 37C357448



A  Sempra Energy utility<sup>SM</sup>

Prepared for:  
SDG&E

8315 Century Park Court, CP21G  
San Diego, CA 92123  
(858) 650-4064

Prepared by:

Bureau Veritas North America, Inc.  
11590 W. Bernardo Court, Suite 100  
San Diego, CA 92127

**September 1, 2011**

**This Document Must Be Returned to  
AMETHYST CRUSPERO (858) 650-4064 at Job Completion**

## **EMERGENCY CONTACT INFORMATION**

Use the following contact numbers if there is an injury or other non-storm water related emergency occurs during the course of the project:

SDG&E projects –

Life threatening:	911
Non-life threatening:	(619) 725-5100 (Trouble Dispatch)

See Appendix XIII for the contact information for the Legally Responsible Person (LRP), Qualified SWPPP Developer (QSD), Qualified SWPPP Practitioner (QSP) and other parties responsible for the SWPPP implementation.

## TABLE OF CONTENTS

---

<b>EMERGENCY CONTACT INFORMATION</b> .....	<b>i</b>
<b>1.0 SWPPP CERTIFICATION</b> .....	<b>1</b>
<b>2.0 GENERAL INFORMATION</b> .....	<b>2</b>
2.1 Background .....	2
2.2 Permit Registration Documents (PRDs).....	2
2.3 SWPPP Amendments.....	2
2.4 Availability of the SWPPP.....	3
2.5 Anticipated Non-Compliance Reporting .....	3
If there are any anticipated non-compliance incidents for the Alpine Regional Field Office project, a blank form (located in Appendix I) should be completed. Records of completed forms are retained in Appendix XVII....	3
2.6 Certifications .....	3
2.7 Soil Contamination.....	3
2.8 Responsible Parties .....	4
<b>3.0 PROJECT INFORMATION</b> .....	<b>5</b>
3.1 OVERVIEW .....	5
3.2 PROJECT CHARACTERISTICS .....	5
3.2.1 Project Location .....	5
3.2.2 Project Description .....	5
3.2.3 Soil Disturbance and Total Area Estimate .....	6
3.2.4 Site Imperviousness .....	6
3.3 RECEIVING WATERS .....	6
3.4 WETLANDS .....	8
3.5 CONSTRUCTION, BMP IMPLEMENTATION AND MAINTENANCE SCHEDULES .....	8
3.6 SITE MAPS AND DIAGRAMS .....	9
<b>4.0 RISK LEVEL 2 REQUIREMENTS</b> .....	<b>10</b>
4.1 RISK DETERMINATION.....	10
4.2 GOOD SITE MANAGEMENT “HOUSEKEEPING” .....	10
A. Good Site Management (“Housekeeping”) Measures for Construction Materials	12
C. Good Site Management (“Housekeeping”) Measures for Vehicle Storage and Maintenance.....	15
E. Good Housekeeping for Assessment of Potential Pollutant Sources.....	17
F. Good Housekeeping for Control of Air Deposition .....	17
G. “Good Housekeeping” Documentation.....	18
4.3 NON-STORM WATER MANAGEMENT .....	18
4.4 EROSION CONTROL MEASURES.....	19
4.5 SEDIMENT CONTROL MEASURES.....	20
4.6 RUN-ON AND RUN-OFF CONTROLS .....	22
4.7 INSPECTION, MAINTENANCE AND REPAIR .....	23
4.8 RAIN EVENT ACTION PLAN (REAP).....	24
<b>5.0 CONSTRUCTION SITE MONITORING PROGRAM (CSMP)</b> .....	<b>25</b>
<b>6.0 RECORDKEEPING</b> .....	<b>26</b>
6.1 ANNUAL REPORTS.....	26
<b>7.0 TRAINING</b> .....	<b>28</b>
<b>8.0 EMERGENCY RESPONSE PLAN</b> .....	<b>29</b>

---

## APPENDICES

---

### APPENDIX I – BLANK FORMS

Notice of Intent  
Permit Registration Documents (PRDs) Were Filed Record  
Annual Reporting Form  
Notice of Termination (NOT)  
Post Construction Best Management Practice (BMP) Type, Description, Location,  
and Inspection & Maintenance Requirements (if required)  
SWPPP Amendment Log  
Certification Form  
Notification of Anticipated Non-Compliance Form  
SWPPP Training and Qualifications Forms  
Visual Observation (Inspection) Form for Non-Storm Water Discharge  
Visual Observation Form for Qualifying Rain Event  
Inspection Form  
Rain Event Action plan (REAP) Form  
Qualified SWPPP Practitioner (QSP) Implementation Checklist  
Sampling Event Worksheet  
Numeric Effluent Limitation (NEL) Violation Report  
Numeric Action Level (NAL) Exceedance Report  
Leaks and Spills Documentation  
Secondary Containment and Spill Kit Inventory  
Inventory of Potential Pollutant Sources Planned to be Used or Stored at the  
Project Site  
List of Responsible Parties (Contact Information Form)  
BMP Selection Worksheet

### APPENDIX II – COPY OF CONSTRUCTION GENERAL PERMIT

Storm Water Regional Control Board (SWRCB) Order No. 2009 - 0009 – Division  
of Water Quality (DWQ), National Pollutant Discharge Elimination System  
(NPDES) General Permit No. CAS000002, Waste Discharge Requirements  
(WDRs) for Discharges of Storm Water Runoff Associated with Construction and  
Land Disturbance Activities

### APPENDIX III – SITE MAP (Retain in this appendix the current and all historic Site Maps)

#### Site map includes the following information:

- Project's surrounding area (vicinity)
- Site layout
- Construction site boundaries
- Drainage areas
- Discharge locations
- Sampling locations
- Areas of soil disturbance (temporary or permanent)
- Active areas of soil disturbance (cut or fill)
- Locations of all BMPs (original & revised)

- Active Treatment System (ATS) location (if applicable)
- Locations of sensitive habitats, watercourses, or other features which are not to be disturbed
- Locations of all post-construction BMPs
- Locations of storage areas for waste, vehicles, service, loading/ unloading of materials, access (entrance/exits) points to construction site, fueling, and water storage, water transfer for dust control and compaction practices

#### **APPENDIX IV – CALCULATIONS/ANALYSES**

Risk Determination Analysis  
Run-off Coefficient Calculations  
Run-on Calculations  
Particle Size Analysis Results – N/A  
Alternative Risk Analysis  
Receiving Water Information, Including Applicable Water Quality Standards  
Sediment Basin Sizing SWPPP Information Request Form – N/A  
Post-Construction Water Balance Calculator – N/A  
(see PRDs in Appendix XII) – N/A

#### **APPENDIX V – CONSTRUCTION MATERIALS**

Inventory of Potential Pollutant Sources Planned to be Used or Stored at the Project Site  
List of Potential Pollutant Sources

#### **APPENDIX VI – CONSTRUCTION BMP MANUAL**

SDG&E Water Quality Construction Best Management Practices Manual  
Other BMPs Cited in the SWPPP

#### **APPENDIX VII – BMP INFORMATION**

QSP Implementation Checklist  
BMP Selection Worksheet  
BMP Site Map  
BMP Site Information List – N/A  
Final Landscaping and Site Stabilization BMPs  
Post-Construction Water Balance Calculator – N/A

#### **APPENDIX VIII – REAPS**

#### **APPENDIX IX – SITE INSPECTION RECORDS**

## **APPENDIX X – CONSTRUCTION SITE MONITORING PROGRAM (CSMP)**

1. Overview
2. Visual Monitoring (Inspection) Requirements
  - 2.1 Exemptions for Visual Observation and Observation and Sample Collection
3. Water Quality Sampling and Analysis
4. Storm Water Discharge Water Quality Sampling Locations
5. Storm Water Sample Collection and Handling Instructions
6. Analytical and Monitoring Methods
7. NAL Exceedance Reports (Required for Risk Level 2 and 3 Projects) – N/A
8. NEL Violation Report (Required for Risk Level 3 Projects) – N/A
9. Compliance Storm Event Exemption
10. Watershed Monitoring Option  
(Required for Risk Level 2 and 3 Projects) – N/A
11. Particle Size Analysis for Project Risk Justification

## **APPENDIX XI – CSMP ATTACHMENTS**

- A. Blank Forms
  - Visual Observation (Inspection) Form for Qualifying Rain Event \*
  - Visual Observation (Inspection) Form for Non-Storm Water Discharge \*
  - Sampling Event Worksheet \*
- B. Observation (Inspection) Forms
  - Visual Observation (Inspection) Form for Qualifying Rain Event\*
  - Visual Observation (Inspection) Form for Non-Storm Water Discharge\*
- C. Reports
  - Internal NAL Non-Compliance Documentation (Numeric Action Level Report located in Appendix XVII of the SWPPP)
  - Internal NEL Non-Compliance Documentation (Numeric Effluent Limitation Report located in Appendix XVII of the SWPPP)
- D. Sampling and Analysis Results
  - Sampling Event Worksheet\*
  - Field Meter Information
  - Calibration Records
  - Contact Information for Analytical Laboratory
  - Analytical Laboratory Results
- E. RWQCB Correspondence: Additional Parameters for Storm Water Sampling
  - a. Sample Forms
  - b. Sample Chain of Custody Forms
- F. Watershed Monitoring Option

## **APPENDIX XII –Permit Registration Documents (PRDS)**

PRDs, including:

- PRDs Were Filed Record \*
- Notice of Intent (NOI)
- Risk Assessment
- Site Map (original)
- SWPPP (electronic version, as submitted)
- Risk Assessment - N/A
- Post-Construction Water Balance Calculation - N/A
- ATS Design Documentation & Certification - N/A
- Approved Signatory Delegation (original), if applicable
- Annual Fee (copy of check)
- Signed Certification Statement

NOT, including:

- Application
- Receipt of Approval
- Waste Discharge Identification Number Letter

## **APPENDIX XIII – RESPONSIBLE PARTIES**

List of Responsible Parties (LRPs) (Contact Information Form) \*, including

- LRP/Approved Signatory
- Qualified SWPPP Developer (QSD)
- QSP
- Sampling Personnel
- Inspection Personnel
- Other SWPPP Implementation Personnel
- Non-Storm Water Management
- Project Contractors & Sub-Contractors List

## **APPENDIX XIV – INSPECTION CHECKLISTS**

Spill/ Leak History Record

## **APPENDIX XV – TRAINING DOCUMENTATION**

SWPPP Training, including\*:

- Spill Response
- QSD
- QSP
- Personnel directed by QSP
- SWPPP Training and Qualifications Log

## **APPENDIX XVI – AMENDMENT LOG**

Amendments Log\*

**APPENDIX XVII – REPORTS**

Annual Report \*  
NEL Violation Report \*  
NAL Exceedance Report \*  
Anticipated Non-Compliance Reporting \*  
Storm Water Reports  
Bioassessment Study Reports – N/A

**APPENDIX XVIII – SECONDARY CONTAINMENT AND SPILL KIT INVENTORY**

Secondary Containment and Spill Kit Inventory \*

**APPENDIX XIX – OTHER SWPPP EXHIBITS**

**APPENDIX XX – ACTIVE TREATMENT SYSTEM (ATS)**

ATS Plan

**APPENDIX XXI – BIOASSESSMENT – N/A**

Study Plan  
RWQCB approval for payment in lieu of field study  
Other documentation

**APPENDIX XXII – Glossary/Acronyms**

\* - Indicates that a blank form is available in Appendix I

**1.0 SWPPP CERTIFICATION**

This SWPPP has been prepared for a Traditional Project in accordance/compliance with the State Water Resources Control Board (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002 Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities.

**Alpine Regional Field Office**  
1010 Tavern Road  
Alpine, California 91901

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is true, accurate, and complete.

I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

Signed:

ROBERT C. JACKSON

Name of LRP \*

General Manager & Director-Construction & Engineering - Sunrise Powerlink

Title

San Diego Gas & Electric

Company

(858) 654-6451

Telephone Number



Signature

JULY 9, 2010

Date

\*or approved signatory. The delegation of authority, for the Approved Signatory is included in Appendix XII.

I, Sharon L. Humphreys, P.E., am a Qualified Storm Water Pollution Prevention Plan (SWPPP) Developer and certify that I have completed this SWPPP for the **Alpine Regional Field Office** project and/or the amendments contained herein, in compliance with the **State Water Resources Control Board** (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002 Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities.

Signature: *Sharon L. Humphreys*

Print Name: Sharon L. Humphreys

Date: 10/19/2010

Affix Certificate Number and/or Seal here:

Certificate Number C60946

Seal:



I, Sharon L. Humphreys, P.E., certify that I am a Qualified Storm Water Pollution Prevention Plan (SWPPP) Developer. I have completed one or more of the following qualifying conditions (check all that apply):

- A California registered professional civil engineer;
- A California registered professional geologist or engineering geologist;
- A California registered landscape architect;
- A professional hydrologist registered through the American Institute of Hydrology;
- A Certified Professional in Erosion and Sediment Control (CPESC) TM registered through Enviro Cert International, Inc.;
- A Certified Professional in Storm Water Quality (CPSWQ) TM registered through Enviro Cert International, Inc.; or
- A professional in erosion and sediment control registered through the National Institute for Certification in Engineering Technologies (NICET).

Signature: *Sharon L. Humphreys*

Print Name: Sharon L. Humphreys, P.E.

Date: 10/19/2010

Affix Certificate Number and/or Seal here:

Certificate Number C60946

Seal:



## **2.0 GENERAL INFORMATION**

### **2.1 Background**

This SWPPP was prepared for the Alpine Regional Field Office as a part of the overall Sunrise Powerlink Project (SPL), a linear construction project.

This Storm Water Pollution Prevention Plan (SWPPP) has been prepared in accordance with the State Water Resources Control Board (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002, Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities (Construction General Permit) (herein after referred to as the CGP). The CGP will be effective on July 1, 2010. This SWPPP has also been prepared to comply with the current permit, SWRCB Order No. 99-08-DWQ, which will be effective until July 1, 2010.

This SWPPP has been amended to comply with Order No. 2009-0009-DWQ [as amended by Order No. 2010-0014-DWQ] Section II.4.b Risk Determination requirements.

A copy of the CGP has been included in Appendix II of this SWPPP.

The goal of this SWPPP is to protect overall water quality during construction activities. Construction activities could potentially effect water quality by the storage and handling of various construction related materials as well as by causing soil erosion or the accumulation of sedimentation. With the implementation of the Best Management Practices (BMPs) and/or treatment outlined in this plan, the potential for the transport of contaminants or sediment to receiving waters will be minimized.

The SWPPP must be evaluated on an ongoing basis to document the changes and progression of construction activities throughout the life of the project.

The Project has identified the need for approximately 23 temporary construction support sites consisting of main construction yards, staging yards, fly yards, laydown yards and contractor yards. The Alpine site has been selected as the regional headquarters office complex supporting the construction of Links 4 and 5 of the Project.

### **2.2 Permit Registration Documents (PRDs)**

The Project Registration Documents (PRDs) and the State Water Resources Control Board's (SWRCB) confirmation of permit coverage (and associated Waste Discharge Identification Number) are contained in Appendix XII. Copies of PRD updates and annual fee checks are also contained in Appendix XII.

### **2.3 SWPPP Amendments**

The Qualified SWPPP Developer (QSD) must prepare and certify each SWPPP amendment.

Blank SWPPP Amendment forms and Certification log is located in Appendix I. These forms completed SWPPP Amendment forms are located in Appendix XVI.

## **2.4 Availability of the SWPPP**

The SWPPP shall be available at the construction site during working hours while construction is occurring and shall be made available upon request by State or Municipal inspectors. When the original SWPPP is retained by a crewmember in a construction vehicle and is not currently at the construction site, current copies of the BMPs and exhibits will be left with the field crew and the original SWPPP shall be made available via a request by radio or telephone. Once construction activities are complete, until stabilization is achieved, the SWPPP shall be made available by the LRP.

## **2.5 Anticipated Non-Compliance Reporting**

If there are any anticipated non-compliance incidents for the Alpine Regional Field Office project, a blank form (located in Appendix I) should be completed. Records of completed forms are retained in Appendix XVII.

A completed Notification of Anticipated Non-Compliance Form must be submitted in advance of a planned change in construction activity that may result in non-compliance with the CGP to the Regional Water Board and local storm water management agency (see contact information in Appendix XIII).

## **2.6 Certifications**

Certification requirements are described in Attachment A, Section E.9 and E.10 of the CGP as provided in Appendix II of this SWPPP on pages 10 and 11 of Attachment A.

## **2.7 Soil Contamination**

If soil contamination is found or suspected, and a responsible party is not identified, or the responsible party fails to promptly take the appropriate action, the LRP shall have those soils sampled and tested to ensure proper handling and public safety measures are implemented. Sampling and testing records shall be retained in Appendix XI. Blank forms for sampling and testing records are provided at the front of Appendix XI. The LRP shall notify the appropriate local, state, and federal agency(ies) when contaminated soil is found at a construction site, and will notify the appropriate Regional Water Board.

LRP's shall ensure that trench spoils or any other soils disturbed during construction activities that are contaminated are not discharged with storm water or non-storm water discharges into any storm drain or water body except pursuant to a project specific NPDES permit.

## **2.8 Responsible Parties**

Implementation of the SWPPP involves a number of responsible parties including, but not limited to, the Legally Responsible Party (LRP), Approved Signatory, Qualified SWPPP Developer (QSD) and Qualified SWPPP Practitioner (QSP). Additionally, other persons may be specifically responsible for conducting inspections, sampling, and BMP installation under the direction of the QSP. These responsible parties are identified in Appendix XIII.

### 3.0 PROJECT INFORMATION

---

#### 3.1 OVERVIEW

San Diego Gas & Electric is dedicated to providing for the energy needs of its customers through the transmission and distribution of electric services. The need to upgrade existing facilities and to construct new facilities in support of new development is the primary impetus for SDG&E construction projects.

This Storm Water Pollution Prevention Plan (SWPPP) covers the Alpine Regional Field Office, a traditional construction project ("Project").

The goal of this SWPPP is to protect overall water quality during construction activities. Construction activities could potentially affect water quality by the storage and handling of various construction-related materials as well as by causing soil erosion or the accumulation of sedimentation. With the implementation of the Best Management Practices (BMPs) outlined in this plan, the potential for the transport of contaminants or sediment to receiving waters will be minimized.

#### 3.2 PROJECT CHARACTERISTICS

##### 3.2.1 Project Location

<b>The Alpine Regional Field Office project is located at:</b>	
<b>ADDRESS</b>	<b>1010 Tavern Road</b>
<b>CITY, STATE, ZIP CODE</b>	<b>Alpine, CA 91901</b>
<b>THOMAS GUIDE LOCATION</b>	<b>2008/ Pg. 1233/ J5/ San Diego County</b>
<b>LATITUDE / LONGITUDE</b>	<b>32° 50' 28"N, 116° 47' 03"W</b>

The project location is shown on the project Vicinity Map included in Appendix III.

##### 3.2.2 Project Description

This SWPPP has been prepared for **this** in accordance/compliance with the **State Water Resources Control Board** (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002 Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities (CGP). The CGP identifies the following distinct phases of construction activities (listed below).

- Grading and Land Development Phase,
- Streets and Utilities Phase,
- Vertical Construction Phase,
- Final Landscaping and Site Stabilization and

- Inactive Construction Phase (i.e., 14 or more days of inactivity).

This Project is a part of a common plan of development or sale. This project is a part of the SPL. The project proposes to construct a new 120 mile electric transmission line between the existing Imperial Valley and Sycamore Canyon Substations.

### 3.2.3 Soil Disturbance and Total Area Estimate

The initial estimated soil disturbance area for this Project is 10.5 acres. Changes to the initial estimate will be documented in the copies of the revised Notice of Intent documents submitted to the SWRCB (see Appendix XII).

### 3.2.4 Site Imperviousness

Approximately 0% of the pre-project site is impervious. Approximately 7% of the post-project site is impervious. Runoff coefficient calculations and run-on flow calculations are located in Appendix IV.

## 3.3 RECEIVING WATERS

This section identifies the receiving waters into which the project discharges and the conditions and specific requirements for this project.

- **Receiving Water Name(s):** Chocolate Canyon
- **Hydrologic Number(s)/Name(s):** 907.33/Alpine Hydrologic Sub Area
- **Surface Water Quality Objectives** applicable to this project's receiving waters are contained in Appendix IV.
- **Specific information** for the **receiving waterbodies** and listed above (Check all that apply):

- Listed on SWRCB's 303(d) list for sedimentation, siltation or turbidity.

- A Total Maximum Daily Load (TMDL) has been adopted that addresses this impairment.

Name of Waterbody / Impairment:

---

---

---

---

- A TMDL has not yet been adopted for this impairment.

- Listed on SWRCB's 303(d) list for pollutants other than sedimentation, siltation or turbidity.

- A TMDL has been adopted that addresses this impairment.

Name of Waterbody / Impairment:

---

---

---

---

- A TMDL has not yet been adopted for this impairment.

- The 303(d) and/or TMDL requirements identified above are incorporated into the SWPPP site map/plans and other appropriate sections of the SWPPP.

- o **Specific information** for the **watersheds** down-gradient from the receiving water body (Check all that apply):

- No surface waters are listed on the SWRCB's 303(d) list for sedimentation, siltation or turbidity.

- A surface water body is listed on SWRCB's 303(d) list for sedimentation, siltation or turbidity.

Name of Waterbody / Impairment:

---

---

---

---

- A TMDL has been adopted that addresses this impairment. .

Name of Waterbody / Impairment:

---

---

---

---

- A TMDL has not yet been adopted for this impairment.

- No surface waters are listed on the SWRCB's 303(d) list for pollutants other than sedimentation, siltation or turbidity.

- A surface water body is listed on SWRCB's 303(d) list for pollutants other than sedimentation, siltation or turbidity.
- A TMDL has been adopted that addresses this impairment.

Name of Waterbody / Impairment:

San Diego River (Lower)/Fecal Coliform

Pacific Ocean Shoreline/Indicator Bacteria

- A TMDL has not yet been adopted for this impairment.

Name of Waterbody / Impairment:

El Capitan Lake/color, Manganese, pH

San Diego River (Lower)/ Fecal Coliform

Pacific Ocean Shoreline/Indicator Bacteria

### 3.4 WETLANDS

Projects that will cross or will conduct work within or immediately adjacent to waters of the US or state-only waters may require additional permits for these activities. Check all the boxes below that apply:

- The project will cross or involve construction activities in a US Army Corps of Engineer's jurisdictional water body (e.g., wetland or waters of the United States).
  - Applicable federal & state permits have or will be obtained.
- The project will cross or involve construction activities in a state-only jurisdictional water body (e.g., wetland or waters of the state, but not of the US).
  - Applicable state permits have or will be obtained.

### 3.5 CONSTRUCTION, BMP IMPLEMENTATION AND MAINTENANCE SCHEDULES

Estimated Date Construction will begin: *June 30, 2010*

Estimated Completion Date: *June 1, 2013*

Actual Start Date *TBD*

Applicable BMPs identified in this SWPPP are to be installed concurrently with the initiation of work and as work progresses at each location and will be routinely inspected and maintained.

### **3.6 SITE MAPS AND DIAGRAMS**

The Site Map is included in Appendix III.

The Site Map is also included with the Permit Registration Documents (PRD's) in Appendix XII.

The Site Map shows:

- Project's surrounding area (vicinity);
- Site layout;
- Construction site boundaries;
- Locations of sensitive habitats, watercourses, or other features which are not to be disturbed;
- Areas of soil disturbance (temporary or permanent);
- Active areas of soil disturbance (cut or fill);
- Drainage areas;
- Discharge locations;
- Locations of all BMPs;
- ATS location (if applicable);
- Locations of storage areas for waste, vehicles, service, loading/unloading of materials, access (entrance/exits) points to construction site, fueling, and water storage, water transfer for dust control and compaction practices;
- Sampling location; and
- Locations of all post-construction BMPs.

Storm Water Pollution Prevention Plan	SDG&E
Alpine Regional Field Office	September 1, 2011

## 4.0 RISK LEVEL 2 REQUIREMENTS

### 4.1 RISK DETERMINATION

Construction for this project will begin under the existing permit 99-08DWQ. On July 1, 2010 the 99-08 DWQ permit expires and is replaced by the 2009-0009-DWQ Permit. This project was grandfathered into the assignment of Risk Level 1. At the request of the Regional Water Quality Control Board (RWQCB), the project site has since been reassessed to determine the risk level as stipulated by the CGP. A risk assessment has been performed and the Alpine Regional Field Office has been assigned a Risk Level 2. See Appendix IV for the risk assessment.

#### A. Effluent Standards

Risk Level 2 dischargers shall comply with the narrative effluent standards listed below:

- a. Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
- b. Dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.

#### B. Numeric

Risk Level 2 dischargers are subject to a pH NAL of 6.5 – 8.5, and turbidity NAL of 250 NTU.

### 4.2 GOOD SITE MANAGEMENT “HOUSEKEEPING”

The following sections describe specific measures to be implemented based on the risk level for this project. Tables have been provided for each measure described in the CGP Attachment C, D, or E that is applicable to the project’s risk level. In this case, as the project is a Risk Level 2, Attachment D is applicable.

The first column of the table beginning on page 12 provides a measure identification number that corresponds to the applicable measure in the next column. The measures listed in the second column are required for Risk Level 2 projects.

The third column of the table describes whether this measure is applicable for the project.

The fourth column provides one or more BMP options that correspond to each required measure. These BMP Options(s) are references to the SDG&E Water Quality Construction Best Management Practices Manual (or “BMP Manual”).

The fifth column of the table identifies the location within the SWPPP that contains the information applicable to the fourth column. The information in the fourth column is either a BMP Option or an inventory form.

Locations of the applicable measures and BMP Options are identified on the Site Map located in Appendix III. The initial layout of the BMPs has been identified by the QSD as part of the preparation of the SWPPP. As site conditions change, it will be the responsibility of the QSD to make all revisions necessary.

The QSD prepared the tables on the following pages as part of this SWPPP. It is the responsibility of the QSP to review these tables during the course of the project and to update the SWPPP as applicable. In addition, a QSP Implementation Checklist has been provided in Appendix VII to document the updates as applicable.

This section addresses good site management (i.e., "housekeeping") practices, including practices for:

- A. Construction Materials;
- B. Waste Management;
- C. Vehicle Storage and Maintenance;
- D. Landscape Materials;
- E. Assessment of Potential Pollutant Sources;
- F. Air Deposition; and
- G. Good Housekeeping Documentation

Tables have been provided for each good housekeeping measure described in the above sections, with the exception of Sections E and G. Sections E and G describe specific actions that must be taken to comply with the permit.

Each of the following measures is an element of Good Site Management "Housekeeping" as described in the CGP.

A. Good Site Management ("Housekeeping") Measures for **Construction Materials** at a minimum, shall consist of the following:

Construction Materials Measure ID No.	Construction Materials Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
CM-a	Conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced.	X		QSP must conduct an inventory	Appendix V <sup>1</sup>
CM-b	Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).	X		<input checked="" type="checkbox"/> BMP 1-08	Appendix VI
CM-c	Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).	X		<input checked="" type="checkbox"/> BMP 2-01 <input type="checkbox"/> BMP 2-02 <input checked="" type="checkbox"/> BMP 2-03 <input checked="" type="checkbox"/> BMP 2-04 <input type="checkbox"/> BMP 2-05 <input type="checkbox"/> BMP 2-06	Appendix VI
CM-d	Minimize exposure of construction materials with precipitation. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (ie. Poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).	X		<input checked="" type="checkbox"/> BMP 2-01 <input type="checkbox"/> BMP 2-02 <input checked="" type="checkbox"/> BMP 2-03 <input checked="" type="checkbox"/> BMP 2-04 <input type="checkbox"/> BMP 2-05 <input type="checkbox"/> BMP 2-06 <input checked="" type="checkbox"/> BMP 2-07 <input type="checkbox"/> BMP 2-08	Appendix VI
CM-e	Implement BMPs to prevent the off-site tracking of loose construction and landscape materials.	X		<input checked="" type="checkbox"/> BMP 1-07	Appendix VI

<sup>1</sup> QSP to review List of Potential Pollutant Sources in Appendix V and complete an Inventory of Potential Pollutant Sources planned to be used or stored at the project site in Appendix V as well.


B. Good Site Management (“Housekeeping”) Measures for **Waste Management** at a minimum, shall consist of the following:

Waste Management Measure ID No.	Waste Management Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
WM-a	Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.	<b>X</b>		<input checked="" type="checkbox"/> BMP 3-02 <input type="checkbox"/> BMP 3-03 <input type="checkbox"/> BMP 3-04 <input checked="" type="checkbox"/> BMP 3-05 <input type="checkbox"/> BMP 3-06 <input checked="" type="checkbox"/> BMP 3-07 <input type="checkbox"/> BMP 3-08 <input type="checkbox"/> BMP 3-09	Appendix VI
WM-b	Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-07	
WM-c	Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-07	Appendix VI
WM-d	Cover waste disposal containers at the end of every business day and during a rain event.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-01 <input type="checkbox"/> BMP 2-02 <input checked="" type="checkbox"/> BMP 2-03 <input checked="" type="checkbox"/> BMP 2-04 <input type="checkbox"/> BMP 2-05 <input type="checkbox"/> BMP 2-06 <input checked="" type="checkbox"/> BMP 2-07 <input type="checkbox"/> BMP 2-08	Appendix VI
WM-e	Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-01 <input type="checkbox"/> BMP 2-02 <input checked="" type="checkbox"/> BMP 2-03 <input checked="" type="checkbox"/> BMP 2-04 <input type="checkbox"/> BMP 2-05 <input type="checkbox"/> BMP 2-06 <input checked="" type="checkbox"/> BMP 2-07 <input type="checkbox"/> BMP 2-08	Appendix VI

B. Good Site Management ("Housekeeping") Measures for **Waste Management** at a minimum, shall consist of the following:

Waste Management Measure ID No.	Waste Management Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
WM-f	Contain and securely protect stockpiled waste material from wind and rain at all times unless actively being used.	<b>X</b>		<input checked="" type="checkbox"/> BMP 1-08	Appendix VI
WM-g	Implement procedures that effectively address hazardous and non-hazardous spills.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-03	Appendix VI
WM-h	Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require that: <ul style="list-style-type: none"> <li>• Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly; and</li> <li>• Appropriate spill response personnel are assigned and trained.</li> </ul>	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-03	-Appendix VI. -For spill response personnel, see Appendix XIII. -For relevant training see Appendix XV.
WM-i	Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.	<b>X</b>		<input checked="" type="checkbox"/> BMP 2-04	Appendix VI




D. Good Site Management (“Housekeeping”) Measures for **Landscape Materials** at a minimum, shall consist of the following:

Landscape Materials Measure ID No.	Landscape Materials Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
LM-a	Contain stockpiled materials such as mulches and topsoil when they are not actively being used.	<b>X</b>		<input checked="" type="checkbox"/> BMP 1-08 <input checked="" type="checkbox"/> BMP 4-07 <input type="checkbox"/> BMP 4-02	Appendix VI
LM-b	Contain fertilizers and other landscape materials when they are not actively being used.	<b>X</b>		<input checked="" type="checkbox"/> BMP 1-08 <input checked="" type="checkbox"/> BMP 2-01 <input checked="" type="checkbox"/> BMP 2-02	Appendix VI
LM-c	Discontinue the application of any erodible landscape material within 2 days before a forecasted rain event <sup>2</sup> or during periods of precipitation.	<b>X</b>		<input checked="" type="checkbox"/> BMP 3-07 <input checked="" type="checkbox"/> BMP 2-02	Appendix VI
LM-d	Apply erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.	<b>X</b>		<input checked="" type="checkbox"/> BMP 3-07 <input checked="" type="checkbox"/> BMP 2-02	Appendix VI
LM-e	Stack erodible landscape material on pallets and covering or storing such materials when not being used or applied.	<b>X</b>		<input checked="" type="checkbox"/> BMP 3-07 <input checked="" type="checkbox"/> BMP 2-01 <input checked="" type="checkbox"/> BMP 2-02	Appendix VI

<sup>2</sup> Excerpt from CGP – 50% or greater chance of producing precipitation.


### E. Good Housekeeping for Assessment of Potential Pollutant Sources

Pollutant sources will be dynamic over the life of the construction project due to the various phases of construction.

An assessment of construction materials that may be used and activities that will be performed during this project that may have the potential to contribute pollutants, other than sediment, to storm water runoff for the project is located in Appendix V. The QSP must review the list throughout the life of the project and update it accordingly. Appropriate revisions to the SWPPP based on any changes to the list shall be made by the QSD.

This potential pollutant list shall identify all non-visible pollutants which are known, or should be known, to occur on the construction site. At a minimum, Risk Level 2 dischargers shall do the following:

- a. Consider the quantity, physical characteristics, (eg. Liquid, powder, solid), and locations of each potential pollutants source handled, produced, stored, recycled, or disposed of at the site.
- b. Consider the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water.
- c. Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas.
- d. Ensure retention of sampling, visual observations, and inspection records.
- e. Ensure effectiveness of existing BMPs to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges.

In addition, a history of leaks or spills is maintained in Appendix XIV.

### F. Good Housekeeping for Control of Air Deposition

This project shall implement good housekeeping measures on the construction site related to Air Deposition:

Air Deposition Measure ID No.	Air Deposition Measures	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
AD-a	Control the air deposition of site materials and from site operations. Such particulates can include, but are not limited to, sediment, nutrients, trash, metals, bacteria, oil and grease and organics.	<b>X</b>		<input checked="" type="checkbox"/> BMP 4-08	Appendix VI

--



Implement the following measures to control all Non-Storm Water Discharges during construction:

Non-Storm Water Management Measure ID No.	Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
NSWM-a	Implement measures to control all non-storm water discharges during construction.	<b>X</b>		<input type="checkbox"/> BMP 3-03 <input checked="" type="checkbox"/> BMP 3-02 <input checked="" type="checkbox"/> BMP 1-07	Appendix VI
NSWM-b	Wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.		<b>X</b>	<input type="checkbox"/> BMP 3-03	Appendix VI
NSWM-c	Clean streets in such a manner as to prevent non-storm water discharges from reaching surface water or MS4 drainage systems.	<b>X</b>		<input checked="" type="checkbox"/> BMP 3-02 <input checked="" type="checkbox"/> BMP 1-07	Appendix VI

Vehicles will not be washed onsite, however, wash stations will be on site for weed control to wash tires, undercarriages and tools.

#### 4.4 EROSION CONTROL MEASURES

Erosion is the detachment of soil from existing landscapes by water or wind. Erosion is a natural process that can be accelerated by construction activities such as grading or trenching. For example, when a site is cleared or grubbed, protective vegetation is removed and the disturbed soil is directly exposed to wind and water. Erosion controls protect the surface and prevent the soil particles from being detached by rainfall or wind. BMPs for erosion control include soil stabilization.

Erosion Control measures, at a minimum, shall consist of the following:

Erosion Control Measure ID No.	Measures	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
ECM-a	Implement effective wind erosion control.	<b>X</b>		<input checked="" type="checkbox"/> BMP 4-08	Appendix VI
ECM-b	Provide effective soil cover for inactive <sup>3</sup> areas and all finished slopes, open space, utility backfill, and completed lots.	<b>X</b>		<input checked="" type="checkbox"/> BMP 4-02 <input type="checkbox"/> BMP 4-03 <input checked="" type="checkbox"/> BMP 4-04 <input type="checkbox"/> BMP 4-05 <input checked="" type="checkbox"/> BMP 4-06 <input type="checkbox"/> BMP 4-07	Appendix VI

ECM-c	Limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the LRP shall consider the use of plastic materials resistant to solar degradation.		<b>X</b>	<input type="checkbox"/> BMP 4-07	Appendix VI
-------	--	--	----------	-----------------------------------	-------------

<sup>3</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

<u>The project will not use plastic materials in erosion control measures.</u>

#### 4.5 SEDIMENT CONTROL MEASURES

Sediment Control measures, at a minimum, shall consist of the following:

Sediment Measure ID No.	Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
SC-a	Establish and maintain effective perimeter controls and stabilize all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.	<b>X</b>		<input checked="" type="checkbox"/> BMP 1-01 <input checked="" type="checkbox"/> BMP 1-02 <input checked="" type="checkbox"/> BMP 1-03 <input checked="" type="checkbox"/> BMP 1-04 <input type="checkbox"/> BMP 1-05 <input checked="" type="checkbox"/> BMP 1-06 <input checked="" type="checkbox"/> BMP 1-07 <input checked="" type="checkbox"/> BMP 1-08	Appendix VI
SC-b	On sites where sediment basins are to be used, at a minimum, design sediment basins according to the method provided in CASQA's Construction BMP Guidance Handbook	<b>X</b>		N/A	Appendix VI
SC-c	Implement appropriate erosion control BMPs (runoff control and soil stabilization) in conjunction with sediment control BMPs for areas under active <sup>4</sup> construction.	<b>X</b>		<input checked="" type="checkbox"/> BMP 4-02 <input type="checkbox"/> BMP 4-03 <input checked="" type="checkbox"/> BMP 4-04 <input type="checkbox"/> BMP 4-05 <input checked="" type="checkbox"/> BMP 4-06 <input type="checkbox"/> BMP 4-07	Appendix VI

SC-d	Apply linear sediment controls along the toe of the slope, face of the slope, and at the grade breaks of exposed slopes to comply with sheet flow lengths <sup>5</sup> in accordance with Table 1 (See Table 1 on the following page).	X		<input checked="" type="checkbox"/> BMP 1-02 <input checked="" type="checkbox"/> BMP 1-03	Appendix VI
SC-e	Ensure that construction activity traffic to and from the project is limited to entrances and exits that employ effective controls to prevent offsite tracking of sediment.	X		<input checked="" type="checkbox"/> BMP 1-07	Appendix VI
SC-f	Ensure that all storm drain inlets and perimeter controls, runoff control BMPs, and pollutant controls at entrances and exits (e.g. tire washoff locations) are maintained and protected from activities that reduce their effectiveness.	X		<input checked="" type="checkbox"/> BMP 1-06	Appendix VI

<sup>4</sup> Active areas of construction are areas undergoing land surface disturbance. This includes construction activity during the preliminary stage, mass grading stage, streets and utilities stage, and the vertical construction stage.

<sup>5</sup> Sheet flow length is the length that shallow, low velocity flow travels across a site.

Sediment Measure ID No.	Measure	Applicable to Project?		BMP Option (check applicable option(s))	Location in SWPPP
		Yes	No		
SC-g	Inspect on a daily basis all immediate access roads daily. At a minimum daily (when necessary) and prior to any rain event, the LRP shall remove any sediment or other construction activity-related materials that are deposited on the roads (by vacuuming or sweeping).	X		<input checked="" type="checkbox"/> BMP 1-07	Appendix VI
SC-h	The Regional Water Quality Control Board (RWQCB) may require LRP's to implement additional site-specific sediment control requirements if the implementation of the other requirements in this section is not adequately protecting the receiving waters.	X		N/A	Appendix VI

**Table 1 - Critical Slope/Sheet Flow Length Combinations (refer to ID No. SC-d)**

Slope Percentage	Sheet flow length not to exceed
0-25%	20 feet
25-50%	15 feet
Over 50%	10 feet



#### **4.7 INSPECTION, MAINTENANCE AND REPAIR**

Inspections shall be conducted by the QSP or a trained individual directed by a QSP.

For each inspection required, Risk Level 2 projects shall complete a Site Inspection Form, located in Appendix IX. Prior to conducting a site inspection, obtain weather information at the following website: <http://www.srh.noaa.gov/forecast> and attach the information to the Inspection Form.

Risk Level 2 projects shall perform weekly inspections and observations and at least once each 24-hour period during extended storm events, to identify and record BMPs that need maintenance to operate effectively, that have failed, or that could fail to operate as intended.

Upon identifying failures or other shortcomings, as directed by the QSP, the project shall begin implementing repairs or design changes to BMPs within 72 hours of identification and complete the changes as soon as possible.

##### **Project Specific Inspection Requirements:**

The inspection forms shall remain onsite with the SWPPP and at a minimum shall include:

- a. Inspection date and date the inspection report was written.
- b. Weather information (rain gauge), including presence or absence of precipitation, estimate of beginning of qualifying storm event, duration of event, time elapsed since last storm, and approximate amount of rainfall in inches.
- c. Site information, including stage of construction, activities completed, and approximate area of the site exposed.
- d. A description of any BMPs evaluated and any deficiencies noted.
- e. If the construction site is safely accessible during inclement weather, list the observations of all BMPs: erosion controls, sediment controls, chemical and waste controls, and non-storm water controls. Otherwise, list the results of visual inspections at all relevant outfalls, discharge points, downstream locations and any projected maintenance activities.
- f. Report the presence of noticeable odors or of any visible sheen on the surface of any discharges.
- g. Any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates.
- h. Photographs taken during the inspection, if any. These photos should be representative of actual site conditions, and be time stamped (dated).
- i. Inspector's name, title, and signature.

Blank Inspection Forms are located in Appendix I. Completed Site Inspection Forms are retained in Appendix IX.

#### **4.8 RAIN EVENT ACTION PLAN (REAP)**

The QSP will develop a Rain Event Action Plan 48 hours prior to any likely precipitation event. A likely precipitation event is any weather pattern that is forecast to have a 50% or greater probability of producing precipitation in the project area. The QSP will obtain a copy of precipitation forecast information from the National Weather Service Forecast Office at <http://www.srh.noaa.gov/forecast>.

The QSP will develop a REAP for all phases of construction.

At a minimum the REAP will include:

- a. Site Address
- b. Calculated Risk Level
- c. Site Storm Water Manager including name, company, and 24-hour emergency phone number
- d. Erosion and Sediment Control Provider including name, company, and 24-hour emergency phone number
- e. Storm Water Sampling Agent including name, company, and 24-hour emergency phone number
- f. Activities associated with each construction phase
- g. Trades active on the construction site during each construction phase
- h. Trade contractor information
- i. Suggested actions for each project phase.

The QSP will develop additional REAPs for project sites where construction activities are indefinitely halted or postponed (Inactive Construction). At a minimum, Inactive Construction REAP will include:

- a. Site Address
- b. Calculated Risk Level
- c. Site Storm Water Manager including name, company, and 24-hour emergency phone number
- d. Erosion and Sediment Control Provider including name, company, and 24-hour emergency phone number
- e. Storm Water Sampling Agent including name, company, and 24-hour emergency phone number
- f. Trades active on the construction site during each construction phase
- g. Trade contractor information
- h. Suggested actions for each project phase.

The QSP will begin implementation and make the REAP available onsite no later than 24 hours prior to the likely precipitation event.

The QSP will maintain onsite paper copies of each REAP in compliance with the record retention requirements of the Special Provisions in the General Permit.

Completed REAPs will be kept in Appendix VIII of this SWPPP.

## **5.0 CONSTRUCTION SITE MONITORING PROGRAM (CSMP)**

The Construction Site Monitoring Program (CSMP) for this project is located in Appendix X of this SWPPP.

## **6.0 RECORDKEEPING**

The LRP shall electronically submit all storm event sampling results to the State Water Board no later than 5 days (for field samples only) after the conclusion of the storm event. For electronic submittal instructions, refer to Section IV, page 24 of the CGP.

Records of all storm water monitoring information and copies of all reports (including Annual Reports) shall be retained for a period of at least three years. If, after three years the RWQCB has not required the records to be retained for a longer period, these records shall be managed in accordance with the company's record retention policy. All records shall be retained on-site while construction is ongoing. These records include:

- The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation;
- The individual(s) who performed the facility inspections, sampling, visual observation (inspections), and or measurements; for laboratory analysis, all sampling, sample preservation, and analyses must be conducted according to test procedures under 40 CFR Part 136. Field discharge samples shall be collected and analyzed according to the specifications of the manufacturer of the sampling devices employed;
- The date and approximate time of analyses;
- The individual(s) who performed the analyses;
- A summary of all analytical results from the last three years, the method detection limits and reporting units, and the analytical techniques or methods used, and the chain of custody forms;
- Rain gauge readings from visual observations (inspections);
- Quality assurance/quality control records and results;
- Non-storm water discharge inspections and visual observation (inspections) and storm water discharge visual observation records (see Section I, page 4 of the CGP);
- Visual observation and sample collection exception records (see Section I, page 4 of the CGP), including the corrective actions taken in response to the observations;
- The records of any corrective actions and follow-up activities that resulted from analytical results, visual observation (inspections), or inspections; and
- All field and/or analytical data.

All of these records can be found in Appendix XI in this SWPPP.

### **6.1 ANNUAL REPORTS**

The Annual Report must be certified by the LRP. A blank certification form is located in Appendix I. Include the signed certification form with the Annual Report submittal. Records of Annual Reports are maintained in Appendix XVII of this SWPPP.

The LRP shall prepare and electronically submit an Annual Report no later than September 1 of each year.

Refer to the CGP Section XVI, page number 40, for all pertinent submittal requirements.

## 7.0 TRAINING

The QSP shall ensure that all persons responsible for implementing requirements of the CGP are appropriately trained in accordance with the requirements described in Section VII of the CGP, page 33.

The QSP shall provide documentation of all training for persons responsible for implementing the requirements of the CGP in the Annual Reports.

Storm water pollution prevention training should be provided regularly by the QSP. Topics can include, but are not limited to:

- spill prevention and response;
- inspections;
- annual reporting;
- locations and functions of sediment/erosion control devices;
- good housekeeping;
- sampling;
- fines and penalties; and
- material management practices.

Blank Training Logs can be found in Appendix I. Attendance records should be kept for each training session in Appendix XV. Training relevant for the QSD, QSP and individuals directed by the QSP are also located in Appendix XV.

## 8.0 EMERGENCY RESPONSE PLAN

### EMERGENCY RESPONSE PLAN

1. BUSINESS NAME: San Diego Gas & Electric – Alpine Regional Field Office
2. BUSINESS SITE ADDRESS: 1010 Tavern Road, Alpine, CA 91901
3. BUSINESS TELEPHONE: (858) 603-6241 24-Hour: (619) 725-5100

4. BRIEF DESCRIPTION OF PRODUCT MANUFACTURED AND/OR SERVICE PROVIDED:

The electric utility construction office site includes: two temporary trailers, two modular buildings, parking lot, and a back-up generator.

5. EVACUATION PROCEDURES: Notify employees to evacuate by shouting or fire alarm. Employees will exit through the nearest exterior door and/or through the driveway entrance and meet at the storage yard located across Tavern Road. Emergency Coordinators will be available at the storage yard to assist Emergency Responders.

6. NOTIFICATION PROCEDURES:

In the event of a release or threatened release of a hazardous material the following agencies are to be notified:

PHONE NUMBERS:

A. Local Emergency Response Agencies 911  
Hazardous Materials Management Division (619) 338-2222 (911 after working hours)

B. State Office of Emergency Services (800) 852-7550 or (916) 427-4341

NAME OF PERSON(S) RESPONSIBLE FOR COMPLETING NOTIFICATIONS:

DESCRIBE NOTIFICATION PROCEDURES: Notify agencies and call SDG&E Trouble Department as needed.

7. EMERGENCY PROCEDURES: Main Concerns: Fire of Chemical Spill.


FIRE – Evacuate if Necessary. Employees will notify local fire department. If safe, employees will shut off power and attempt to control fire using fire extinguisher.

SMALL CHEMICAL SPILL - Spilled material will be identified, contained and cleaned up with appropriate materials by trained personnel.

LARGE CHEMICAL SPILLS - Employee will notify Emergency Coordinator. If safe, spill will be identified, contained and prevented from entering storm drains and sewer. Spilled material will be cleaned up by trained personnel such as SDG&E's Hazmat Team or appropriate clean up contractors.

NOTE: Disposal of hazardous waste generated from spill cleanup will be managed in compliance with Local, State and Federal regulations.

## Driving Directions to Nearest Hospital

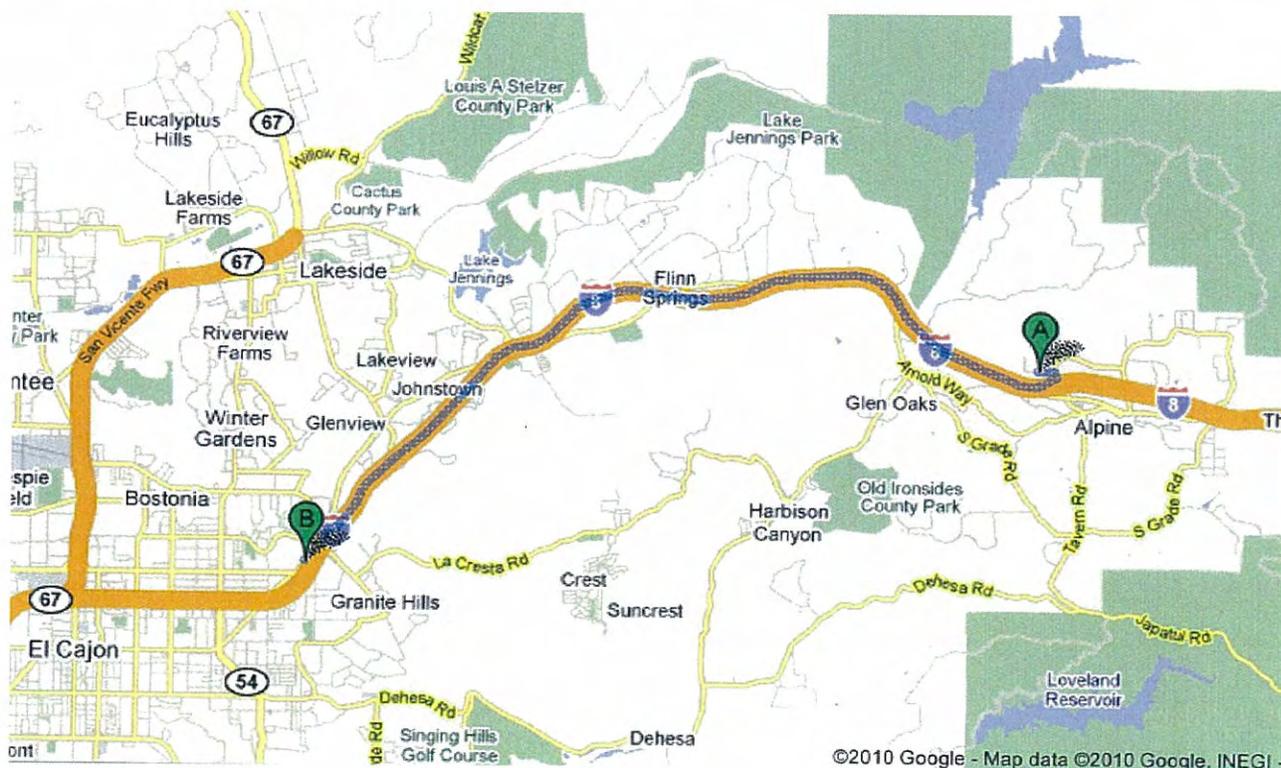

### Directions to 1625 E Main St #100, El Cajon, CA 92021 10.2 mi – about 12 mins

1010 Tavern Rd, Alpine, CA 91901

- |    |   |                            |
|----|---|----------------------------|
| 1. | Head <b>east</b> on <b>Tavern Rd</b> toward <b>Victoria Park Terrace</b><br>About 1 min             | go 0.2 mi<br>total 0.2 mi  |
|    | 2. Turn <b>right</b> to merge onto <b>I-8 W</b><br>About 9 mins                                     | go 9.4 mi<br>total 9.7 mi  |
|    | 3. Take the <b>Greenfield Dr</b> exit   | go 0.3 mi<br>total 10.0 mi |
|    | 4. Turn <b>right</b> at <b>Greenfield Dr/I-8 BUS E</b>  | go 213 ft<br>total 10.0 mi |
|    | 5. Take the 1st <b>left</b> onto <b>E Main St</b><br>Destination will be on the left<br>About 1 min | go 0.2 mi<br>total 10.2 mi |

1625 E Main St #100, El Cajon, CA 92021

# **Appendix I**

## **Blank Forms**



State Water Resources Control Board

# NOTICE OF INTENT

TO COMPLY WITH THE TERMS OF THE  
GENERAL PERMIT TO DISCHARGE STORM WATER  
ASSOCIATED WITH CONSTRUCTION ACTIVITY (WQ ORDER No. 99-08-DWQ)



## I. NOI STATUS (SEE INSTRUCTIONS)

MARK ONLY ONE ITEM	1. <input type="checkbox"/> New Construction	2. <input type="checkbox"/> Change of Information for WDID#	<input type="text"/>
--------------------	--	---	----------------------

## II. PROPERTY OWNER

Name		Contact Person		
Mailing Address		Title		
City	State	Zip	Phone	
Owner Type (check one) 1. <input type="checkbox"/> Private Individual    2. <input type="checkbox"/> Business    3. <input type="checkbox"/> Municipal    4. <input type="checkbox"/> State    5. <input type="checkbox"/> Federal    6. <input type="checkbox"/> Other				

## III. DEVELOPER/CONTRACTOR INFORMATION

Developer/Contractor		Contact Person		
Mailing Address		Title		
City	State	Zip	Phone	

## IV. CONSTRUCTION PROJECT INFORMATION

Site/Project Name		Site Contact Person		
Physical Address/Location		Latitude _____°	Longitude _____°	County
City (or nearest City)		Zip	Site Phone Number	Emergency Phone Number
A. Total size of construction site area: _____ Acres	C. Percent of site imperviousness (including rooftops): Before Construction: _____% After Construction: _____%		D. Tract Number(s): _____, _____	
B. Total area to be disturbed: _____ Acres (% of total _____)			E. Mile Post Marker: _____	
F. Is the construction site part of a larger common plan of development or sale? <input type="checkbox"/> YES <input type="checkbox"/> NO		G. Name of plan or development:		
H. Construction commencement date: ____/____/____		J. Projected construction dates: Complete grading: ____/____/____    Complete project: ____/____/____		
I. % of site to be mass graded: _____				
K. Type of Construction (Check all that apply): 1. <input type="checkbox"/> Residential    2. <input type="checkbox"/> Commercial    3. <input type="checkbox"/> Industrial    4. <input type="checkbox"/> Reconstruction    5. <input type="checkbox"/> Transportation 6. <input type="checkbox"/> Utility    Description: _____    7. <input type="checkbox"/> Other (Please List): _____				

## V. BILLING INFORMATION

SEND BILL TO: <input type="checkbox"/> OWNER (as in II. above)	Name	Contact Person	
<input type="checkbox"/> DEVELOPER (as in III. above)	Mailing Address	Phone/Fax	
<input type="checkbox"/> OTHER (enter information at right)	City	State	Zip

**VI. REGULATORY STATUS**

A. Has a local agency approved a required erosion/sediment control plan?.....  YES  NO  
Does the erosion/sediment control plan address construction activities such as infrastructure and structures?.....  YES  NO  
Name of local agency: \_\_\_\_\_ Phone: \_\_\_\_\_

B. Is this project or any part thereof, subject to conditions imposed under a CWA Section 404 permit of 401 Water Quality Certification?.....  YES  No  
If yes, provide details: \_\_\_\_\_

**VII. RECEIVING WATER INFORMATION**

A. Does the storm water runoff from the construction site discharge to (Check all that apply):  
1.  Indirectly to waters of the U.S.  
2.  Storm drain system - Enter owner's name: \_\_\_\_\_  
3.  Directly to waters of U.S. (e.g. , river, lake, creek, stream, bay, ocean, etc.)

B. Name of receiving water: (river, lake, creek, stream, bay, ocean): \_\_\_\_\_

**VIII. IMPLEMENTATION OF NPDES PERMIT REQUIREMENTS**

A. STORM WATER POLLUTION PREVENTION PLAN (SWPPP) (check one)  
 A SWPPP has been prepared for this facility and is available for review: Date Prepared: \_\_\_\_/\_\_\_\_/\_\_\_\_ Date Amended: \_\_\_\_/\_\_\_\_/\_\_\_\_  
 A SWPPP will be prepared and ready for review by (enter date): \_\_\_\_/\_\_\_\_/\_\_\_\_  
 A tentative schedule has been included in the SWPPP for activities such as grading, street construction, home construction, etc.

B. MONITORING PROGRAM  
 A monitoring and maintenance schedule has been developed that includes inspection of the construction BMPs before anticipated storm events and after actual storm events and is available for review.  
If checked above: A qualified person has been assigned responsibility for pre-storm and post-storm BMP inspections to identify effectiveness and necessary repairs or design changes.....  YES  NO  
Name: \_\_\_\_\_ Phone: \_\_\_\_\_

C. PERMIT COMPLIANCE RESPONSIBILITY  
A qualified person has been assigned responsibility to ensure full compliance with the Permit, and to implement all elements of the Storm Water Pollution Prevention Plan including:  
1. Preparing an annual compliance evaluation.....  YES  NO  
Name: \_\_\_\_\_ Phone: \_\_\_\_\_  
2. Eliminating all unauthorized discharges.....  YES  NO

**IX. VICINITY MAP AND FEE (must show site location in relation to nearest named streets, intersections, etc.)**

Have you included a vicinity map with this submittal? .....  YES  NO  
Have you included payment of the annual fee with this submittal?.....  YES  NO

**X. CERTIFICATIONS**

"I certify under penalty of law that this document and all attachments were prepared under my direction and supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine or imprisonment. In addition, I certify that I have read the entire General Permit, including all attachments, and agree to comply with and be bound by all of the provisions, requirements, and prohibitions of the permit, including the development and implementation of a Storm Water Pollution Prevention Plan and a Monitoring Program Plan will be complied with."

Printed Name: \_\_\_\_\_  
Signature: \_\_\_\_\_ Date: \_\_\_\_\_  
Title: \_\_\_\_\_

**ORIGINAL - MAKE COPIES**

---

**PRDs Filed  
(Store Completed Forms in Appendix XII)**

PRDs were filed:

---

---

---

---

---

Copy of Submittal:

The following documents, except the Annual Fee which was mailed, were submitted electronically to the SWRCB:

- Notice of Intent (NOI) – Enclosed
- Risk Assessment – Enclosed
- Site Map – Enclosed
- Storm Water Pollution Prevention Plan – Enclosed
- Annual Fee – Enclosed
- Signed Certification Statement – Enclosed

---

## **ANNUAL REPORTING FORM (Store Completed Forms in Appendix XVII)**

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

- Electronically submit no later than September 1 of each year
- Keep a copy in Appendix XVII of the SWPPP. Retain an electronic or paper copy for a minimum of three years after the date that the Annual Report is filed; after three years, retain in accordance with the company's record retention policy.

This Annual Reporting Form is for the period of \_\_\_\_\_ to \_\_\_\_\_ and includes the following documents:

Training Information:  
(See Appendix XV)

1. Documentation of all training for individuals responsible for all activities associated with compliance with this Construction General Permit (CGP);
2. Documentation of all training for individuals responsible for BMP installation, inspection, maintenance, and repair; and
3. Documentation of all training for individuals responsible for overseeing, revising, and amending the SWPPP.

Storm Water Monitoring Information:  
(See Appendix XI)

1. A summary and evaluation of all sampling and analysis results, including original laboratory reports;
2. The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as "less than the method detection limit");
3. A summary of all corrective actions taken during the compliance year;
4. Identification of any compliance activities or corrective actions that were not implemented;
5. A summary of all violations of the Construction General Permit (CGP);
6. The names of individual(s) who performed the facility inspections, sampling, visual observation (inspections), and/or measurements;
7. The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation (rain gauge); and
8. The visual observation and sample collection exception records and reports specified in Attachments C, D, and E of the CGP.

Refer to Section XVI of the CGP for additional information specific to the Annual Reporting Requirements.



**Linda S. Adams**  
Secretary for  
Environmental Protection

# State Water Resources Control Board

## Division of Water Quality

1001 I Street • Sacramento, California 95814 • (916) 341-5537  
Mailing Address: P.O. Box 1977 • Sacramento, California • 95812-1977  
FAX (916) 341-5543 • Internet Address: <http://www.waterboards.ca.gov/stormwtr/index.html>



**Arnold Schwarzenegger**  
Governor

To: Storm Water Permit Holder

**RE: NOTICE OF TERMINATION OF COVERAGE UNDER THE GENERAL  
CONSTRUCTION STORM WATER PERMIT (GENERAL PERMIT)**

In order for us to terminate your coverage under the General Permit, please complete and submit the enclosed Notice of Termination (NOT) your local Regional Water Quality Control Board (RWQCB). Refer to the last page of the NOT packet for RWQCB locations.

Submittal of a NOT does not guarantee termination and outstanding invoices are still valid. If your NOT is denied, you will be required to continue complying with the requirements of the General Permit and all outstanding invoice(s) are due. You will be notified of your NOT status by the RWQCB or State Water Resources Control Board. Approval of your Notice of Termination does not relieve you from paying any applicable outstanding invoices.

Should you have any questions regarding this matter, please contact your local RWQCB at the number listed on the back page of the NOT package, or the Storm Water Unit at (916) 341-5537.

Sincerely,

Storm Water Unit  
Division of Water Quality

Enclosure

SEND TO YOUR LOCAL RWQCB FOR APPROVAL

State of California  
State Water Resources Control Board

**NOTICE OF TERMINATION**

OF COVERAGE UNDER THE NPDES GENERAL PERMIT NO. CAS000002  
FOR DISCHARGES OF STORM WATER  
ASSOCIATED WITH CONSTRUCTION ACTIVITY

Submission of this Notice of Termination constitutes notice that the owner (and his/her agent) of the site identified on this form is no longer authorized to discharge storm water associated with construction activity by NPDES General Permit No. CAS000002.

**I. WDID NO.**

**II. OWNER**

COMPANY NAME \_\_\_\_\_ CONTACT PERSON \_\_\_\_\_  
STREET ADDRESS \_\_\_\_\_ TITLE \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_ PHONE \_\_\_\_\_

**III. CONSTRUCTION SITE INFORMATION**

A. DEVELOPER NAME \_\_\_\_\_ CONTACT PERSON \_\_\_\_\_  
STREET ADDRESS \_\_\_\_\_ TITLE \_\_\_\_\_  
CITY \_\_\_\_\_ CA \_\_\_\_\_ ZIP \_\_\_\_\_ PHONE \_\_\_\_\_

B. SITE ADDRESS \_\_\_\_\_ COUNTY \_\_\_\_\_  
CITY \_\_\_\_\_ CA \_\_\_\_\_ ZIP \_\_\_\_\_ PHONE \_\_\_\_\_

**IV. BASIS OF TERMINATION**

\_\_\_\_\_ 1. The construction project is complete and the following conditions have been met.

- All elements of the Storm Water Pollution Prevention Plan have been completed.
- Construction materials and waste have been disposed of properly.
- The site is in compliance with all local storm water management requirements.
- A post-construction storm water operation and management plan is in place.

Date of project completion \_\_\_\_/\_\_\_\_/\_\_\_\_

\_\_\_\_\_ 2. Construction activities have been suspended, either temporarily \_\_\_\_\_ or indefinitely \_\_\_\_\_ and the following conditions have been met.

- All elements of the Storm Water Pollution Prevention Plan have been completed.
- Construction materials and waste have been disposed of properly.
- All denuded areas and other areas of potential erosion are stabilized.
- An operation and maintenance plan for erosion and sediment control is in place.
- The site is in compliance with all local storm water management requirements.

**SEND TO YOUR LOCAL RWQCB FOR APPROVAL**

Date of suspension \_\_\_\_/\_\_\_\_/\_\_\_\_ Expected start up date \_\_\_\_/\_\_\_\_/\_\_\_\_

\_\_\_\_ 3. Site can not discharge storm water to waters of the United States (check one).

\_\_\_\_ All storm water is retained on site.

\_\_\_\_ All storm water is discharged to evaporation or percolation ponds offsite.

\_\_\_\_ 4. Discharge of storm water from the site is now subject to another NPDES general permit or an individual NPDES permit.

NPDES Permit No. \_\_\_\_\_ Date coverage began \_\_\_\_/\_\_\_\_/\_\_\_\_

\_\_\_\_ 5. There is a new owner of the identified site. Date of owner transfer \_\_\_\_/\_\_\_\_/\_\_\_\_

Was the new owner notified of the General Permit requirements? YES \_\_\_\_ NO \_\_\_\_

**NEW OWNER INFORMATION**

COMPANY NAME \_\_\_\_\_ CONTACT PERSON \_\_\_\_\_

STREET ADDRESS \_\_\_\_\_ TITLE \_\_\_\_\_

CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_ PHONE \_\_\_\_\_

**V. EXPLANATION OF BASIS OF TERMINATION (Attach site photographs - see instructions).**

**VI. CERTIFICATION:**

I certify under penalty of law that all storm water discharges associated with construction activity from the identified site that are authorized by NPDES General Permit No. CAS000002 have been eliminated or that I am no longer the owner of the site. I understand that by submitting this Notice of Termination, I am no longer authorized to discharge storm water associated with construction activity under the general permit, and that discharging pollutants in storm water associated with construction activity to waters of the United States is unlawful under the Clean Water Act where the discharge is not authorized by a NPDES permit. I also understand that the submittal of this Notice of Termination does not release an owner from liability for any violations of the general permit or the Clean Water Act.

PRINTED NAME \_\_\_\_\_ TITLE \_\_\_\_\_

SIGNATURE: \_\_\_\_\_ DATE \_\_\_\_/\_\_\_\_/\_\_\_\_

**REGIONAL WATER BOARD USE ONLY**

This Notice of Termination has been reviewed, and I recommend termination of coverage under the subject NPDES general permit.

Printed Name \_\_\_\_\_ Region No. \_\_\_\_\_

Signature \_\_\_\_\_ Date \_\_\_\_/\_\_\_\_/\_\_\_\_

NOT effective date:  
Date: \_\_\_\_/\_\_\_\_/\_\_\_\_

**INSTRUCTIONS FOR COMPLETING  
NOTICE OF TERMINATION  
FOR CONSTRUCTION ACTIVITY**

Who May File

Dischargers who are presently covered under NPDES General Permit No. CAS000002 for discharge of storm water associated with construction activity may submit a Notice of Termination when they meet one of the following criteria.

1. The construction project has been completed and the following conditions have been met: all elements of the Stormwater Pollution Prevention Plan have been completed; construction materials and equipment maintenance waste have been disposed of properly; the site is in compliance with all local storm water management requirements including erosion/sediment control requirements and the appropriate use permits have been obtained; and a post-construction storm water operation and management plan is in place.
2. Construction activities have been suspended, either temporarily or indefinitely and the following conditions have been: all elements of the Stormwater Pollution Prevention Plan have been completed; construction materials and equipment maintenance waste have been disposed of properly; all denuded areas and other areas of potential erosion are stabilized; an operation and maintenance plan for erosion and sediment control is in place; and the site is in compliance with all local storm water management requirements including erosion/sediment control requirements.  
The date construction activities were suspended, and the expected date construction activities will start up again should be provided.
3. Construction site can not discharge storm water to waters of the United States. Please indicate if all storm water is retained on site or if storm water is collected offsite.
4. Discharge of construction storm water from the site is now subject to another NPDES general permit or an individual NPDES permit. The general permit or individual permit NPDES number and date coverage began should be provided.
5. There is a new owner of the identified site. If ownership or operation of the facility has been transferred then the previous owner must submit a Notice of Termination and the new owner must submit a Notice of Intent for coverage under the general permit. The date of transfer and information on the new owner should be provided. Note that the previous owner may be liable for discharge from the site until the new owner files a Notice of Intent for coverage under the general permit.

Where to File

Submit the Notice of Termination to the Executive Officer of the Regional Water Quality Control Board responsible for the area in which the facility is located. See attached. Submittal of a NOT does not guarantee termination and outstanding invoices are still valid. If the Executive Officer, or his designated staff, agrees with the basis of termination, the Notice of Termination will be transmitted to the State Water Board for processing at which time it will be determined if any outstanding invoices are still valid. Approval of your Notice of Termination does not relieve you from paying any applicable outstanding invoices. If the Executive Officer, or his designated staff, does not agree with the basis of termination, the Notice of Termination will be returned. The Regional Water Board may also inspect your site prior to accepting the basis of termination.

## **LINE-BY-LINE INSTRUCTIONS**

All necessary information must be provided on the form. Type or print in the appropriate areas only. Submit additional information, if necessary, on a separate sheet of paper.

### **SECTION I--WDID NO.**

The WDID No. is a number assigned to each discharger covered under the General Permit. If you do not know your WDID No., please call the State Water Board or Regional Water Board and request it prior to submittal of the Notice of Termination.

### **SECTION II--OWNER**

Enter the owner of the construction site's official or legal name (This should correspond with the name on the Notice of Intent submitted for the site), address of the owner, contact person, and contact person's title and telephone number.

### **SECTION III--CONSTRUCTION SITE INFORMATION**

In Part A, enter the name of the developer (or general contractor), address, contact person, and contact person's title and telephone number. The contact person should be the construction site manager completely familiar with the construction site and charged with compliance and oversight of the general permit. This information should correspond with information on the Notice of Intent submitted for the site.

In Part B, enter the address, county, and telephone number (if any) of the construction site. Construction sites that do not have a street address must attach a legal description of the site.

### **SECTION IV--BASIS OF TERMINATION**

Check the category which best defines the basis of your termination request. See the discussion of the criteria in the Who May File section of these instructions. Provide dates and other information requested. Use the space under Explanation of Basis of Termination heading.

### **SECTION V--EXPLANATION OF BASIS OF TERMINATION**

Please explain the basis or reasons why you believe your construction site is not required to comply with the General Permit. To support your explanation, provide a site map and photograph of your site.

### **SECTION VI--CERTIFICATION**

This section must be completed by the owner of the site.

The Notice of Termination must be signed by:

For a Corporation: a responsible corporate officer

For a Partnership or Sole Proprietorship: a general partner or the proprietor, respectively.

For a Municipality, State, or other Non-Federal Public Agency: either a principal executive officer or ranking elected official.

For a Federal Agency: either the chief or senior executive officer of the agency.





**ORIGINAL - MAKE COPIES**

---

**CERTIFICATION FORM  
(Store Completed Forms in Appendix XII)**

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

This certification is for (check appropriate box):

The QSD will complete this box and, once signed by the approved signatory, insert the signed certification form in the appropriate Appendix.

- Amendment to SWPPP (Appendix XVI)
- PRDs (Appendix XII)
- NOT (Appendix XII)
- Annual Report (Appendix XVII)
- Other \_\_\_\_\_

*Any person signing documents under Section IV.1 of the CGP shall make the following certification:*

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

\_\_\_\_\_  
Name of LRP \*

\_\_\_\_\_  
Title

\_\_\_\_\_  
Company

\_\_\_\_\_  
Telephone Number

\_\_\_\_\_  
Signature

\_\_\_\_\_  
Date

\*or approved signatory.

**ORIGINAL - MAKE COPIES**

**NOTIFICATION OF ANTICIPATED NON-COMPLIANCE  
(Store Completed Forms in Appendix XVII)**

This form will be used to report instances of anticipated non-compliance. The LRP must provide advanced notice to the local Regional Water Quality Control Board and local Storm Water Management Agency (see Appendix XIII for the relevant contact information).

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

in accordance/compliance with the **State Water Resources Control Board** (SWRCB) Order No. 2009-0009-DWQ, National Pollutant Discharge Elimination System (NPDES) General Permit No. CAS000002 Waste Discharge Requirements for Discharges of Storm Water Runoff Associated with Construction and Land Disturbance Activities, the following discharge is anticipated:

Nature of planned change in construction activity that may result in non-compliance with CGP requirements:

Date, time, and location of anticipated discharge:

\_\_\_\_\_  
Name of LRP \*

\_\_\_\_\_  
Title

\_\_\_\_\_  
Company

\_\_\_\_\_  
Telephone Number

\_\_\_\_\_  
Signature

\_\_\_\_\_  
Date

*\*or approved signatory.*

**ORIGINAL - MAKE COPIES**

**SWPPP Training and Qualifications Log  
(Store Completed Form in Appendix XV)**

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

Training Location: \_\_\_\_\_

Trainer(s): \_\_\_\_\_ **Date:** \_\_\_\_\_

**TRAINING TOPICS COVERED**

- Review and Discussion of SWPPP
- General BMPs for Site and Materials Management
- BMPs for Erosion and Sediment Control
- Spill or Release Response
- Proper Selection of BMPs
- Proper BMP Implementation/Maintenance Techniques
- Review and Discussion of SWPPP Inspection Requirements
- Review and Discussion of Sampling Requirements
- Sampling and Monitoring
- Record Keeping
- Other: \_\_\_\_\_

NAME	AREA OF RESPONSIBILITY	COMPANY NAME	PHONE NUMBER



---

**Qualified SWPPP Developer (QSD) Qualifications**

The Qualified SWPPP Developer (QSD) holds the following registration(s) and/or certification(s):

(Check all that apply and include a copy of the registration(s) and/or certification(s)):

- A California registered professional civil engineer;
- A California registered professional geologist or engineering geologist;
- A California registered landscape architect;
- A professional hydrologist registered through the American Institute of Hydrology;
- A Certified Professional in Erosion and Sediment Control (SPESC)<sup>TM</sup> registered through Enviro Cert, International, Inc.;
- A Certified Professional in Storm Water Quality (CPSWQ)<sup>TM</sup> registered through Enviro Cert, International, Inc.; or
- A professional in erosion and sediment control registered through the National Institute for Certification in Engineering Technologies (NICET).

**-- AND --**

The QSD attended formal State Water Board sponsored or approved QSD training course on the following date \*:

Date: \_\_\_\_\_

Name of Course: \_\_\_\_\_

Presented by: \_\_\_\_\_

A copy of the certification of attendance is attached.

\* A requirement as of September 2, 2011

---

**Qualified SWPPP Practitioner (QSP) Qualifications**

The Qualified SWPPP Practitioner (QSP)\* holds the following registration(s) and/or certification(s):

Check all that apply and include a copy of the registration(s) and/or certification(s):

- Qualified SWPPP Developer (QSD)
- A certified erosion, sediment and storm water inspector registered through Enviro Cert, International, Inc.; or
- A certified inspector of sediment and erosion control registered through Certified Inspector of Sediment and Erosion Control, Inc.

\* A requirement as of September 2, 2011, the QSP shall be either a QSD or have one of the above certifications:

**-- AND --**

The QSP attended formal State Water Board sponsored or approved QSP training course on the following date \*\*:

Date: \_\_\_\_\_

Name of Course: \_\_\_\_\_

Presented by: \_\_\_\_\_

A copy of the certification of attendance is attached.

\*\* A requirement as of September 2, 2011

**ORIGINAL - MAKE COPIES**

**Visual Observation (Inspection) Form for Non-Storm Water Discharges**

**(Store the Completed Form in Appendix XI.B)**

Inspect each drainage area for the presence of (or indications of prior) unauthorized and authorize non-storm water discharges and their sources

Project Name \_\_\_\_\_

WDID Number: \_\_\_\_\_

Date and Time of Inspection \_\_\_\_\_

Current Weather Conditions \_\_\_\_\_

Name of Inspector \_\_\_\_\_

Inspector's Company/Title \_\_\_\_\_

QSP's Signature \_\_\_\_\_

Visual observation serves as the quarterly inspection for the following quarter (check which is applicable):

- January – March
- April - June
- July – September
- October – December

A visual observation (inspection) must document the presence or evidence of any non-storm water discharge (authorized or unauthorized).

Were any of these discharges observed at the time of the inspection

- YES
- NO

If yes, describe the discharge, their source and response taken to eliminate unauthorized non-sw discharges and to reduce or prevent pollutants from contacting non-sw discharges

\_\_\_\_\_

\_\_\_\_\_

\_\_\_\_\_

\_\_\_\_\_

\_\_\_\_\_

<b>Non-Storm Pollutant Water Characteristics</b>	
<b>Characteristic</b>	<b>Observation (Circle one)</b>
Discolorations	Clear    Brown    Gray    Yellow    Red    Other_____
Turbidity	Clear    Cloudy    Opaque
Floating or Suspended Materials?	None    Vegetation    Mulch Trash    Foam    Other_____
Sheen	None    Slight    Heavy
Any observed pollutants?	None    Sewage    Other_____
Possible sources?	

Were samples collected?

YES\*     NO    Reason: \_\_\_\_\_

If yes, refer to Appendix X for sampling information.



Are BMPs properly implemented in accordance with the SWPPP/REAP?  Yes\*  No  
 If yes, describe implemented corrective actions below


Do any storm water storage and containment areas have leaks?  Yes\*  No  
 If yes, describe below


Are BMPs were adequately designed, implemented, and effective?  Yes\*  No


Inspect all discharge locations. If any of the characteristics are observed, describe the conditions and discharge location(s) below.

Storm Water Characteristics	
Characteristic	Observation (Circle applicable response)
Discolorations	None    Brown    Gray    Yellow    Red    Other_____
Turbidity	Cloudy    Opaque
Floating or Suspended Materials?	None    Vegetation    Mulch    Trash    Foam    Other_____
Sheen	None    Slight    Heavy
Any observed pollutants? Possible sources?	None    Sewage    Other_____

Description of observations and location:

Is there a need for any additional BMPs? If so, describe below and inform the QSD that the SWPPP needs to be revised.



BMP No.	BMP Options (Additional BMPs shall be implemented as necessary to protect water quality as determined by field conditions)	Selected BMPs
BMP-1-02	Silt Fence	<input type="checkbox"/>
BMP-1-03	Fiber Rolls	<input type="checkbox"/>
BMP-1-04	Gravel Bag Berm	<input type="checkbox"/>
BMP-1-05	Sand Bag Barrier	<input type="checkbox"/>
BMP-1-06	Storm Drain Inlet Protection	<input type="checkbox"/>
BMP-1-07	Tracking Controls	<input type="checkbox"/>
BMP-1-08	Stockpile Management	<input type="checkbox"/>
BMP-2-01	Material Delivery and Storage	<input type="checkbox"/>
BMP-2-02	Material Use	<input type="checkbox"/>
BMP-2-03	Spill Control	<input type="checkbox"/>
BMP-2-04	Solid Waste Management	<input type="checkbox"/>
BMP-2-05	Hazardous Materials/Waste Management	<input type="checkbox"/>
BMP-2-06	Contaminated Soil Management	<input type="checkbox"/>
BMP-2-07	Sanitary/Septic Waste Management	<input type="checkbox"/>
BMP-2-08	Liquid Waste Management	<input type="checkbox"/>
BMP-3-01	Dewatering Operations	<input type="checkbox"/>
BMP-3-02	Paving Operations	<input type="checkbox"/>
BMP-3-03	Vehicle and Equipment Washing	<input type="checkbox"/>
BMP-3-04	Vehicle and Equipment Fueling	<input type="checkbox"/>
BMP-3-05	Concrete/Coring/Saw Cutting and Drilling Waste Management	<input type="checkbox"/>
BMP-3-06	Dewatering Utility Substructures and Vaults	<input type="checkbox"/>
BMP-3-07	Vegetation Management including Mechanical and Chemical Weed Control	<input type="checkbox"/>
BMP-3-08	Over-Water Protection	<input type="checkbox"/>
BMP-3-09	Removal of Utility Location/Mark-Out Paint	<input type="checkbox"/>
BMP-4-01	Preservation of Existing Vegetation	<input type="checkbox"/>
BMP-4-02	Temporary Soil Stabilization	<input type="checkbox"/>
BMP-4-03	Hydraulic Mulch	<input type="checkbox"/>
BMP-4-04	Hydroseeding	<input type="checkbox"/>
BMP-4-05	Soil Binders	<input type="checkbox"/>
BMP-4-06	Straw Mulch	<input type="checkbox"/>
BMP-4-07	Geotextiles, Plastic Covers and Erosion Control Blankets/Mats	<input type="checkbox"/>
BMP-4-08	Dust (Wind Erosion) Control	<input type="checkbox"/>
CASQA EC-10	Velocity Dissipation Devices	<input type="checkbox"/>
CASQA EC-12	Streambank Stabilization	<input type="checkbox"/>
CASQA NS-4	Temporary Stream Crossing	<input type="checkbox"/>
CASQA NS-5	Clear Water Diversion	<input type="checkbox"/>

Site Information		
Current stage of construction (check which applies)	<input type="checkbox"/> Grading and Land Development Phase <input type="checkbox"/> Streets and Utilities Phase <input type="checkbox"/> Inactive Construction	<input type="checkbox"/> Final Landscaping and Site Stabilization <input type="checkbox"/> Vertical Construction Phase
Activities completed:		
Approximate area of the site exposed (in acres):		

Review and update (as applicable) the QSP Implementation Checklist in Appendix VIII. Based on a review of this checklist and an evaluation of BMPs on-site complete the following:

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Construction Materials</u>		
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)?	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
*If yes, describe the deficiency:		
Describe any BMP Corrective Actions..		
Date	BMP Corrective Action Taken	
Date		
Date		
Date		

**ORIGINAL - MAKE COPIES**

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Waste Management</u> :	
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)?	<input type="checkbox"/> Yes* <input type="checkbox"/> No
*If yes, describe below:	
Describe any BMP Corrective Actions.	
Date	BMP Corrective Action Taken
Date	
Date	
Date	

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Vehicle Storage and Maintenance</u> :	
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)?	<input type="checkbox"/> Yes* <input type="checkbox"/> No
*If yes, describe below:	
Describe any BMP Corrective Actions.	
Date	BMP Corrective Action Taken
Date	
Date	
Date	

**ORIGINAL - MAKE COPIES**

Inspected the site for good site management (i.e., "housekeeping") measures implemented for Landscape Materials:

Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
---	-------------------------------	-----------------------------

Date	BMP Corrective Action Taken
Date	
Date	
Date	

Inspected the site for good site management (i.e., "housekeeping") measures implemented for Air Deposition:

Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
---	-------------------------------	-----------------------------

Date	BMP Corrective Action Taken
Date	
Date	
Date	

**ORIGINAL - MAKE COPIES**

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Non-Storm Water Discharges</u> :		
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
Date	BMP Corrective Action Taken	
Date		
Date		
Date		

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Erosion Control</u> :		
	<input type="checkbox"/> Yes	<input type="checkbox"/> No
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
Date	BMP Corrective Action Taken	
Date		
Date		
Date		

**ORIGINAL - MAKE COPIES**

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Sediment Control</u> : <input type="checkbox"/> Yes <input type="checkbox"/> No		
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
Describe any BMP Corrective Actions.. €  €  €  €		

Inspected the site for good site management (i.e., "housekeeping") measures implemented for <u>Run-on and Runoff Controls</u> : <input type="checkbox"/> Yes <input type="checkbox"/> No		
Were any BMP deficiencies observed (i.e., BMPs requiring maintenance and repair)? *If yes, describe below:	<input type="checkbox"/> Yes*	<input type="checkbox"/> No
Describe any BMP Corrective Actions. €  €  €  €		

---

List any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates:

Report the presence of noticeable odors/visible sheen on the surface of any discharges immediately to \_\_\_\_\_ at \_\_\_\_\_ and document observations below:

Were photographs taken during the inspection?  Yes  No  
If yes, attach to this site inspection.

## QSP IMPLEMENTATION CHECKLIST (Store Completed Forms in Appendix VII)

The QSP completes this checklist prior to each phase of construction.

Phase of construction: \_\_\_\_\_

### A. Good Site Management ("Housekeeping") Measures for Construction Materials:

Construction Materials Measures ID No.	Construction Materials Measures	BMP Option		Alternative BMP Option *Describe why BMP was not implemented	
		Implemented?			
		Y	N*		
CM-b	Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).	BMP-2-01 BMP-2-02 BMP-2-03 BMP-2-04 BMP-2-05 BMP-2-06			
CM-c	Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).	BMP-2-01 BMP-2-02 BMP-2-03 BMP-2-04 BMP-2-05 BMP-2-06 BMP-2-07 BMP-2-08			
CM-d	Minimize exposure of construction materials with precipitation.	BMP 1-07			

<sup>1</sup> QSP to review List of Potential Pollutant Sources in Appendix V and complete an Inventory of Potential Pollutant Sources planned to be used or stored at the project site in Appendix V as well.

### B. Good Site Management ("Housekeeping") Measures for Waste Management:

Construction Materials Measures ID No.	Construction Materials Measures	BMP Option		Alternative BMP Option *Describe why BMP was not implemented	
		Implemented?			
		Y	N*		
WM-a	Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.	BMP 3-02 BMP 3-03 BMP 3-04 BMP 3-05 BMP 3-06 BMP 3-07 BMP 3-08 BMP 3-09			
WM-b	Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.	BMP 2-07			
WM-c	Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.	BMP 2-07			

**QSP IMPLEMENTATION CHECKLIST**

**B. Good Site Management ("Housekeeping") Measures for Waste Management:**

		BMP Option			Alternative BMP Option
WM-d	Cover waste disposal containers at the end of every business day and during a rain event.	BMP 2-01 BMP 2-02 BMP 2-03 BMP 2-04 BMP 2-05 BMP 2-06 BMP 2-07 BMP 2-08			
WM-e	Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.	BMP 2-01 BMP 2-02 BMP 2-03 BMP 2-04 BMP 2-05 BMP 2-06 BMP 2-07 BMP 2-08			
WM-f	Contain and securely protect stockpiled waste material from wind and rain at all times unless actively being used.	BMP 1-08			
WM-g	Implement procedures that effectively address hazardous and non-hazardous spills.	BMP 2-03			
WM-h	Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require that: <ul style="list-style-type: none"> <li>• Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly; and</li> <li>• Appropriate spill response personnel are assigned and trained.</li> </ul>	BMP 2-03			
WM-i	Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.	BMP 2-04			

**C. Good Site Management ("Housekeeping") Measures for Vehicle Storage and Maintenance:**

Construction Materials Measures		BMP Option			Alternative BMP Option
		Implemented?		*Describe why BMP was not implemented	
		Y	N*		
VSM-a	Prevent oil, grease, or fuel to leak in to the ground, storm drains or surface waters.	BMP 3-03 BMP 3-04 BMP 3-05			
VSM-b	Place all equipment or vehicles, which are to be fueled, maintained and stored in a designated area fitted with appropriate BMPs.	BMP 2-03 BMP 2-02 BMP 3-03 BMP 3-04			

**QSP IMPLEMENTATION CHECKLIST**

**C. Good Site Management ("Housekeeping") Measures for Vehicle Storage and Maintenance:**

		BMP Option			Alternative BMP Option
		BMP 2-03	Implemented?		
Y	N*				
VSM-c	Clean leaks immediately and disposing of leaked materials properly.				

**D. Good Site Management ("Housekeeping") Measures for Landscape Materials:**

Landscape Materials Measures		BMP Option			Alternative BMP Option *Describe why BMP was not implemented
			Implemented?		
			Y	N*	
LM-a	Contain stockpiled materials such as mulches and topsoil when they are not actively being used.	BMP 1-08 BMP 4-07 BMP 4-02			
LM-b	Contain fertilizers and other landscape materials when they are not actively being used.	BMP 1-08 BMP 2-01 BMP 2-02			
LM-c	Discontinuing the application of any erodible landscape material within 2 days before a forecasted rain event <sup>2</sup> or during periods of precipitation.	BMP 3-07 BMP 2-02			
LM-d	Apply erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.	BMP 3-07 BMP 2-02			
LM-e	Stacking erodible landscape material on pallets and covering or storing such materials when not being used or applied.	BMP 3-07 BMP 2-01 BMP 2-02			

<sup>2</sup> Excerpt from CGP – 50% or greater chance of producing precipitation.

**F. Good Site Management ("Housekeeping") Measures for Air Deposition:**

Air Deposition		BMP Option			Alternative BMP Option *Describe why BMP was not implemented
			Implemented?		
			Y	N*	
AD-a	Control the air deposition of site materials and from site operations. Such particulates can include, but are not limited to, sediment, nutrients, trash, metals, bacteria, oil and grease and organics.	BMP 4-08			

### QSP IMPLEMENTATION CHECKLIST

Non-Storm Water Management:		BMP Option		Alternative BMP Option
		Implemented?		*Describe why BMP was not implemented
		Y	N*	
NSWM-a	Implement measures to control all non-storm water discharges during construction.	BMP 3-03 BMP 3-02 BMP 1-07		
NSWM-b	Wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.	BMP 3-03		
NSWM-c	Clean streets in such a manner as to prevent non-storm water discharges from reaching surface water or MS4 drainage systems.	BMP 3-02 BMP 1-07		

<sup>2</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

Erosion Control		BMP Option		Alternative BMP Option
		Implemented?		*Describe why BMP was not implemented
		Y	N*	
ECM-a	Effective wind erosion control	BMP 4-08		
ECM-b	Provide effective soil cover for inactive <sup>3</sup> areas and all finished slopes, open space, utility backfill, and completed lots.	BMP 4-02 BMP 4-03 BMP 4-04 BMP 4-05 BMP 4-06 BMP 4-07		
ECM-c	Limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the discharger shall consider the use of plastic materials resistant to solar degradation.	BMP 4-07		

<sup>3</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

## QSP IMPLEMENTATION CHECKLIST

Sediment Control: SC-c, SC-d, SC-e, SC-f, SC-g, SC-h are not applicable to Risk Level 1 projects. If the project is a Risk Level 1, delete SC-c, SC-d, SC-e, SC-f, SC-g, SC-h in the table below. SC-h also does not apply to Risk Level 2 projects; delete this BMP if the project is Risk Level 2.

Sediment Control		BMP Option			Alternative BMP Option
		Implemented?		*Describe why BMP was not implemented	
		Y	N*		
SC-a	Establish and maintain effective perimeter controls and stabilize all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.	BMP 1-01 BMP 1-02 BMP 1-03 BMP 1-04 BMP 1-05 BMP 1-06 BMP 1-07 BMP 1-08			
SC-b	On sites where sediment basins are to be used, at a minimum, design sediment basins according to the method provided in CASQA's Construction BMP Guidance Handbook	N/A			
SC-c	Implement appropriate erosion control BMPs (runoff control and soil stabilization) in conjunction with sediment control BMPs for areas under active <sup>4</sup> construction.	BMP 4-02 BMP 4-03 BMP 4-04 BMP 4-05 BMP 4-06 BMP 4-07			
SC-d	Apply linear sediment controls along the toe of the slope, face of the slope, and at the grade breaks of exposed slopes to comply with sheet flow lengths <sup>5</sup> in accordance with Table 1.	BMP 1-02 BMP 1-03			

<sup>4</sup> Active areas of construction are areas undergoing land surface disturbance. This includes construction activity during the preliminary stage, mass grading stage, streets and utilities stage, and the vertical construction stage.

<sup>5</sup> Sheet flow length is the length that shallow, low velocity flow travels across a site.

SC-e	Ensure that construction activity traffic to and from the project is limited to entrances and exits that employ effective controls to prevent offsite tracking of sediment.	BMP 1-07			
SC-f	Ensure that all storm drain inlets and perimeter controls, runoff control BMPs, and pollutant controls at entrances and exits (e.g. tire washoff locations) are maintained and protected from activities that reduce their effectiveness.	BMP 1-06			

**QSP IMPLEMENTATION CHECKLIST**

		BMP Option			Alternative BMP Option
SC-g	Inspect on a daily basis all immediate access roads daily. At a minimum daily (when necessary) and prior to any rain event, the discharger shall remove any sediment or other construction activity-related materials that are deposited on the roads (by vacuuming or sweeping).	BMP 1-07			
SC-h	The Regional Water Board may require Risk Level 3 dischargers to implement additional site-specific sediment control requirements if the implementation of the other requirements in this section are not adequately protecting the receiving waters.	N/A			

Excerpt from the CGP Attachment D:  
 Excerpt from the CGP Attachment E:

**Table 1 - Critical Slope/Sheet Flow Length Combinations**

Slope Percentage	Sheet flow length not to exceed
0-25%	20 feet
25-50%	15 feet
Over 50%	10 feet

Run-on and Run-off Controls		Applicable to Project?		Alternative BMP Option
		Y	N*	*Describe why BMP was not implemented
RRC-a	Effectively manage all run-on, all runoff within the site and all runoff that discharges off the site.			
RRC-b	Run-on from off-site shall be directed away from all disturbed areas or shall collectively be in compliance with the effluent limitation in the CGP.			

**SAMPLING EVENT WORKSHEET  
(Store Completed Forms in Appendix XI.D)**

Name of Inspector: \_\_\_\_\_

Storm Event Date(s): \_\_\_\_\_

Rain Gauge Readings: \_\_\_\_\_ Risk Level: \_\_\_\_\_

Samples collected:

Qualifying Rain Event

Samples not collected:

Non-Target Storm Event – Event was not preceded by 72 hours of dry weather

Non-Target Storm Event – Event occurred outside of daylight hours

False Alert – Predicted storm event never started or did not produce runoff

Compliance Storm Event Exception

Dangerous Conditions

Outside Business Hours

Storm Start Time:		Storm End Time:	
-------------------	--	-----------------	--

Runoff Start Time:		Total Precipitation:	
--------------------	--	----------------------	--

Check All That Apply (complete form for each sampling location per day):

Dischargers shall ensure that the grab samples collected of stored or contained storm water are from discharges subsequent to a qualifying rain event (producing precipitation of ½ inch or more with a 48 hour or greater period between rain events)

Discharge run-off location

Run-on location

ATS discharge location

Non-visible pollutant location

3 samples per day:

Sample 1

Sample 2

Sample 3

Effluent Sampled for:

pH

Turbidity

Any additional parameters for which monitoring is required by the Regional Water Board:

---

---

---

---

Who collected the sample? Name, company, phone number? Rain gauge readings?

Name:

---

Company:

---

Phone Number

---

Who collected the sample? Name, company, phone number? Rain gauge readings?

Name:

---

Company:

---

Phone Number

---

Who collected the sample? Name, company, phone number? Rain gauge readings?

Name:

---

Company:

---

Phone Number

---

Who collected the sample? Name, company, phone number? Rain gauge readings?

Name:

---

Company:

---

Phone Number

---

**ORIGINAL - MAKE COPIES**

For Monitoring Location:

		Sampler Name	Time Sample Taken	Results	Daily Average	Was there an NAL Exceedance (Y <sup>1</sup> / N <sup>2</sup> )	Was there an NEL Violation (Y/N) <sup>3</sup>
pH	1 <sup>st</sup> Sample						
	2 <sup>nd</sup> Sample						
	3 <sup>rd</sup> Sample						
Turbidity	1 <sup>st</sup> Sample						
	2 <sup>nd</sup> Sample						
	3 <sup>rd</sup> Sample						
SSC							

<sup>1</sup> Refer to Appendix X.7 for required action.  
<sup>2</sup> No further action required.  
<sup>3</sup> Refer to Appendix X.8 for required action.

**ORIGINAL - MAKE COPIES**

**Numeric Effluent Limitation (NEL) Violation Report  
(Store Completed Form in Appendix XVII)**

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

Risk Level \_\_\_\_\_

**Attach the following documents to this NEL Violation Report:**

- Description of the current onsite BMPs and the proposed corrective actions taken to manage the NEL exceedance.
- A copy of the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (from Appendix X)
- A copy of the completed Visual Observation (Inspection) form for the sampling event (from Appendix X.B)

Date and Time of Sampling Event \_\_\_\_\_

Weather Conditions \_\_\_\_\_

Name of NEL Preparer \_\_\_\_\_

NEL Preparer's Company/Title \_\_\_\_\_

Sample Identification Number	Location	Parameter pH/Turbidity	Reporting Units	Result

Daily Average Value: \_\_\_\_\_ NEL Limitation: \_\_\_\_\_

**ORIGINAL - MAKE COPIES**

Describe the current BMPs associated with the effluent sample that exceeded the NEL:

---

---

---

---

---

---

---

---

Describe the proposed corrective actions taken to manage the effluent associated with the NEL exceedance:

---

---

---

---

---

---

---

---

Any person signing documents under Section IV.I of the CGP shall make the following certification:

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

\_\_\_\_\_  
Name of LRP \*

\_\_\_\_\_  
Title

\_\_\_\_\_  
Company

\_\_\_\_\_  
Telephone Number

\_\_\_\_\_  
Signature

\_\_\_\_\_  
Date

\*or approved signatory.

**ORIGINAL - MAKE COPIES**

**Numeric Action Level (NAL) Exceedance Report  
(Store Completed Forms in Appendix XVII)**

Project Name \_\_\_\_\_

WDID Number \_\_\_\_\_

Risk Level \_\_\_\_\_

**Attach the following documents to this NAL Exceedance Report:**

- The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (Appendix X)
- The completed Visual Observation (Inspection) form and the sampling event worksheet ( Appendix XI)

Date and Time of Sampling Event \_\_\_\_\_

Weather Conditions \_\_\_\_\_

Name of NAL Preparer \_\_\_\_\_

NAL Preparer's Company/Title \_\_\_\_\_

Sample Identification Number	Location	Parameter pH/Turbidity	Reporting Units	Result

Daily Average Value: \_\_\_\_\_ NAL Limitation: \_\_\_\_\_

Describe the current BMPs associated with the effluent sample that exceeded the NAL

\_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Were any corrective actions taken? If yes, describe below:

\_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

**ORIGINAL - MAKE COPIES**

# LEAKS AND SPILLS DOCUMENTATION (Completed Form Stored in Appendix XIV)

Immediately report any leaks or spills to the LRP

Name \_\_\_\_\_

Phone Number \_\_\_\_\_

Date & Time of incident or  
time of discovery of spill: \_\_\_\_\_

Material Spilled:  Liquid  Solid  Gas

What is it used for? \_\_\_\_\_

Known dangerous quantities? \_\_\_\_\_

MSDS available  YES \*  NO

If yes, consult the MSDS sheet for appropriate handling, storage and disposal practices

Chemical or Trade Name \_\_\_\_\_

Estimate Amount  \_\_\_\_\_ *Gallons if liquid*  
 \_\_\_\_\_ *Pounds if solid or gas*  
 \_\_\_\_\_ *Leaked or Spilled*

Potential dangers (as appropriate)  Fire  Explosion  Toxic Fumes & Fluids  Threat to life or property

Other (describe): \_\_\_\_\_

Cause and source of incident (e.g., human error, corrosion):  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

## Secondary Containment and Spill Kit Inventory (Store Completed Form in Appendix XVIII)

To be completed by the QSP

- Equipment and materials for cleanup of spills shall be available on site and spills and leaks shall be cleaned up **immediately** and the materials used to clean up the spills shall be disposed of properly; and
- Ensure appropriate spill response personnel are assigned and trained.
- Ensure the containment of washout areas that may contain additional pollutants so that there is no discharge into the underlying soil and/or surrounding areas.

The following spill control equipment can be found on-site:

Quantity <sup>1</sup>	Description <sup>2</sup>	Location <sup>3</sup>	Absorbent Capacity (Gallons) <sup>4</sup>

1 – Number of spill kits or product  
2 - Contents of spill kit or product

3 – Storage location of spill kit or product  
4 – Absorbent capacity of the spill kit or product

Note: Spill response kits come from a variety of suppliers. Kit contents and absorbent capacity may vary from supplier’s description.

The following secondary containment equipment can be found on-site:

Description of Material Stored in Secondary Containment <sup>5</sup>	Location <sup>6</sup>	Type of Containment/Enclosure <sup>7</sup>	Volume	
			Maximum Storage/Containment <sup>8</sup>	Spill Potential <sup>9</sup>

5- For example, paint, oil, lubricant, solvent, etc.

6- Location of secondary containment

7- Description of the secondary containment enclosure. For example, poly-pack, poly-pallet, cabinet, visqueen-lined sump.

8- Capacity of the secondary device (usually identified on the device or can be obtained from the manufacturer)

9- Quantity of material (in gallons) stored in the secondary containment

**Inventory of Potential Pollutant Sources Planned to be Used or Stored at the Project Site  
(Store Completed Forms in Appendix V)**

The QSP shall conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced at the site.

A list of possible products that are typically found at construction sites are listed in Appendix V.

Typical Materials Handled, Produced, Stored, Recycled, or Disposed of at the Site	Quantity (e.g., gal, lbs, oz)	Physical Characteristics (e.g., liquid, powder, solid)	Location of Each Material	Proximity to Storm Drain Inlet/Receiving Waters

Based on the table above, describe the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water (i.e., proximity to storm drain inlets or receiving waters).

---

---

---

---

---

---

---

---

Describe BMPs implemented to address these pollutant sources:

---

---

---

---

---

---

---

---

Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas

---

---

---

---

---

---

---

---

Based on the inventory and evaluation above, describe the anticipated pollutants for the project below and include these analytes in the CSMP in Appendix X of the SWPPP.

## Appendix XIII List of Responsible Parties

PROJECT: Alpine Regional Field Office      WDID NUMBER: 9 37C357448

LEGALLY RESPONSIBLE PART (LRP)     THE LRP's APPROVED SIGNATORY

AREA OF RESPONSIBILITY: Construction and Engineering Sunrise Powerlink Project

NAME Robert C. Jackson      TITLE: General Manager & Director

COMPANY NAME: SDG&E

ADDRESS 8315 Century Park Court

CITY San Diego      STATE CA      ZIP 92123

TELEPHONE 858-654-6451

EMERGENCY TELEPHONE 619-778-6029

FAX 858-637-3731

E-MAIL RCJackson@semprautilities.com

### QUALIFIED SWPPP DEVELOPER (QSD): RESPONSIBLE FOR PREPARING THE SWPPP:

NAME Sharon Humphreys, PE      TITLE: Senior Project Manager

COMPANY NAME: Bureau Veritas

ADDRESS 11590 West Bernardo Drive, Suite 100

CITY San Diego      STATE CA      ZIP 92127

TELEPHONE 858-207-5091

EMERGENCY TELEPHONE 858-776-9402

FAX 858-451-2846

E-MAIL Sharon.humphreys@us.bureauveritas.com

### ADDITIONAL QSD:

AREA OF RESPONSIBILITY: Preparation of the SWPPP

NAME Tracy Beach, PE      TITLE: Civil Engineer

COMPANY NAME: Bureau Veritas

ADDRESS 11590 West Bernardo Drive, Suite 100

CITY San Diego      STATE CA      ZIP 92127

TELEPHONE 858-207-5091

EMERGENCY TELEPHONE 858-663-1887

FAX 858-451-2846

E-MAIL Tracy.beach@us.bureauveritas.com

**START DATE**

**END DATE**

**QUALIFIED SWPPP PRACTITIONER (QSP):**

**AREA OF RESPONSIBILITY:**

**NAME**

**TITLE:**

**COMPANY NAME:**

**ADDRESS**

**CITY**

**STATE**

**ZIP**

**TELEPHONE**

**EMERGENCY TELEPHONE**

**FAX**

**E-MAIL**

**START DATE**

**END DATE**

**ADDITIONAL QSP:**

**AREA OF RESPONSIBILITY:**

**NAME**

**TITLE:**

**COMPANY NAME:**

**ADDRESS**

**CITY**

**STATE**

**ZIP**

**TELEPHONE**

**EMERGENCY TELEPHONE**

**FAX**

**E-MAIL**

**START DATE**

**END DATE**

**SPILL RESPONSE PERSONNEL**

**NAME**

**TITLE:**

**ADDRESS**

**CITY**

**STATE**

**ZIP**

**TELEPHONE**

**EMERGENCY TELEPHONE**

**FAX**

**E-MAIL**

**START DATE**

**END DATE**

**SPILL RESPONSE PERSONNEL**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

**SPILL RESPONSE PERSONNEL**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

**SPILL RESPONSE PERSONNEL**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

**STORM WATER SAMPLING AGENT:**

**CONTACT PERSON** \_\_\_\_\_ **TITLE:** \_\_\_\_\_  
**ADDRESS** \_\_\_\_\_  
**CITY** \_\_\_\_\_ **STATE** \_\_\_\_\_ **ZIP** \_\_\_\_\_  
**TELEPHONE** \_\_\_\_\_  
**EMERGENCY TELEPHONE** \_\_\_\_\_  
**FAX** \_\_\_\_\_  
**E-MAIL** \_\_\_\_\_  
**START DATE** \_\_\_\_\_ **END DATE** \_\_\_\_\_

**STORM WATER SAMPLING AGENT:**

**CONTACT PERSON** \_\_\_\_\_ **TITLE:** \_\_\_\_\_  
**ADDRESS** \_\_\_\_\_  
**CITY** \_\_\_\_\_ **STATE** \_\_\_\_\_ **ZIP** \_\_\_\_\_  
**TELEPHONE** \_\_\_\_\_  
**EMERGENCY TELEPHONE** \_\_\_\_\_  
**FAX** \_\_\_\_\_  
**E-MAIL** \_\_\_\_\_  
**START DATE** \_\_\_\_\_ **END DATE** \_\_\_\_\_

**STORM WATER SAMPLING AGENT:**

**CONTACT PERSON** \_\_\_\_\_ **TITLE:** \_\_\_\_\_  
**ADDRESS** \_\_\_\_\_  
**CITY** \_\_\_\_\_ **STATE** \_\_\_\_\_ **ZIP** \_\_\_\_\_  
**TELEPHONE** \_\_\_\_\_  
**EMERGENCY TELEPHONE** \_\_\_\_\_  
**FAX** \_\_\_\_\_  
**E-MAIL** \_\_\_\_\_  
**START DATE** \_\_\_\_\_ **END DATE** \_\_\_\_\_

<b>STORM WATER SAMPLING AGENT:</b>			
<b>CONTACT PERSON</b>	_____	<b>TITLE:</b>	_____
<b>ADDRESS</b>	_____		
<b>CITY</b>	_____	<b>STATE</b>	_____ <b>ZIP</b> _____
<b>TELEPHONE</b>	_____		
<b>EMERGENCY TELEPHONE</b>	_____		
<b>FAX</b>	_____		
<b>E-MAIL</b>	_____		
<b>START DATE</b>	_____	<b>END DATE</b>	_____

<b>REGIONAL BOARD CONTACT INFORMATION</b>	<b>RQWQB NAME:</b>	_____
<b>CONTACT PERSON</b>	_____	<b>TITLE:</b> _____
<b>ADDRESS</b>	_____	
<b>CITY</b>	_____	<b>STATE</b> _____ <b>ZIP</b> _____
<b>TELEPHONE</b>	_____	
<b>EMERGENCY TELEPHONE</b>	_____	
<b>FAX</b>	_____	
<b>E-MAIL</b>	_____	

<b>LOCAL STORM WATER MANAGEMENT AGENCY</b>	<b>AGENCY NAME:</b>	_____
<b>CONTACT PERSON</b>	_____	<b>TITLE:</b> _____
<b>ADDRESS</b>	_____	
<b>CITY</b>	_____	<b>STATE</b> _____ <b>ZIP</b> _____
<b>TELEPHONE</b>	_____	
<b>EMERGENCY TELEPHONE</b>	_____	
<b>FAX</b>	_____	
<b>E-MAIL</b>	_____	

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

COMPANY NAME \_\_\_\_\_  
CONTACT PERSON \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_  
ADDRESS \_\_\_\_\_  
CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_  
TELEPHONE \_\_\_\_\_  
EMERGENCY TELEPHONE \_\_\_\_\_  
FAX \_\_\_\_\_  
E-MAIL \_\_\_\_\_  
START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
NAME	_____	TITLE:	_____
ADDRESS	_____		
CITY	_____	STATE	_____ ZIP _____
TELEPHONE	_____		
EMERGENCY TELEPHONE	_____		
FAX	_____		
E-MAIL	_____		
START DATE	_____	END DATE	_____

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
NAME	_____	TITLE:	_____
ADDRESS	_____		
CITY	_____	STATE	_____ ZIP _____
TELEPHONE	_____		
EMERGENCY TELEPHONE	_____		
FAX	_____		
E-MAIL	_____		
START DATE	_____	END DATE	_____

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
NAME	_____	TITLE:	_____
ADDRESS	_____		
CITY	_____	STATE	_____ ZIP _____
TELEPHONE	_____		
EMERGENCY TELEPHONE	_____		
FAX	_____		
E-MAIL	_____		
START DATE	_____	END DATE	_____

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_

ADDRESS \_\_\_\_\_

CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_

TELEPHONE \_\_\_\_\_

EMERGENCY TELEPHONE \_\_\_\_\_

FAX \_\_\_\_\_

E-MAIL \_\_\_\_\_

START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_

ADDRESS \_\_\_\_\_

CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_

TELEPHONE \_\_\_\_\_

EMERGENCY TELEPHONE \_\_\_\_\_

FAX \_\_\_\_\_

E-MAIL \_\_\_\_\_

START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

CONTRACTOR    SUBCONTRACTOR    INDIVIDUAL DIRECTED BY QSP    OTHER

**PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:**

NAME \_\_\_\_\_ TITLE: \_\_\_\_\_

ADDRESS \_\_\_\_\_

CITY \_\_\_\_\_ STATE \_\_\_\_\_ ZIP \_\_\_\_\_

TELEPHONE \_\_\_\_\_

EMERGENCY TELEPHONE \_\_\_\_\_

FAX \_\_\_\_\_

E-MAIL \_\_\_\_\_

START DATE \_\_\_\_\_ END DATE \_\_\_\_\_

**BMP SELECTION WORKSHEET**  
**(Store Completed Forms in Appendix VII)**

BMP No.	BMP Options (Additional BMPs shall be implemented as necessary to protect water quality as determined by field conditions)	Selected BMPs	Option 1	Option 2
<b>Section 1 Sediment Controls</b>				
BMP-1-02	Silt Fence	<input type="checkbox"/>	*_*_*	-SF-
BMP-1-03	Fiber Rolls	<input type="checkbox"/>	- - -	-FR-
BMP-1-04	Gravel Bag Berm	<input type="checkbox"/>	o o o	~GBB~
BMP-1-05	Sand Bag Barrier	<input type="checkbox"/>	• • •	-SBB-
BMP-1-06	Storm Drain Inlet Protection	<input type="checkbox"/>	□	-SDIP-
BMP-1-07	Tracking Controls	<input type="checkbox"/>	■	-TC-
BMP-1-08	Stockpile Management	<input type="checkbox"/>	◇	-SM-
Other – User Defined	BMP Description	<input type="checkbox"/>		
The following rows have been provided to add additional BMPs that may be required during the course of the project. QSD to provide this information as applicable.				
Other – User Defined	BMP Description:	<input type="checkbox"/>		
<b>Section 2 Waste Management and Material Controls</b>				
BMP-2-01	Material Delivery and Storage	<input type="checkbox"/>	» » » »	-MDS-
BMP-2-02	Material Use	<input type="checkbox"/>	☀	-MV-
BMP-2-03	Spill Control	<input type="checkbox"/>	⬡	-SC-
BMP-2-04	Solid Waste Management	<input type="checkbox"/>	o-o-o	-SWM-
BMP-2-05	Hazardous Materials/Waste Management	<input type="checkbox"/>	▴	-HM/WM-
BMP-2-06	Contaminated Soil Management	<input type="checkbox"/>	⊙	-CSM-

**BMP SELECTION WORKSHEET  
(Store Completed Forms in Appendix VII)**

BMP No.	BMP Options (Additional BMPs shall be implemented as necessary to protect water quality as determined by field conditions)	Selected BMPs	Option 1	Option 2
BMP-2-07	Sanitary/Septic Waste Management	<input type="checkbox"/>	▲	-S/SWM-
BMP-2-08	Liquid Waste Management	<input type="checkbox"/>	△	-LWM-
The following rows have been provided to add additional BMPs that may be required during the course of the project. QSD to provide this information as applicable.				
Other – User Defined	BMP Description:	<input type="checkbox"/>		
<b>Section 3 Non-Storm Water Discharge Controls</b>				
BMP-3-01	Dewatering Operations	<input type="checkbox"/>	☆	-DW-
BMP-3-02	Paving Operations	<input type="checkbox"/>	●-●-●	-PO-
BMP-3-03	Vehicle and Equipment Washing	<input type="checkbox"/>	⬠	-VEW-
BMP-3-04	Vehicle and Equipment Fueling	<input type="checkbox"/>	⬡	-VEF-
BMP-3-05	Concrete/Coring/Saw Cutting and Drilling Waste Management	<input type="checkbox"/>	⊗	-CWM-
BMP-3-06	Dewatering Utility Substructures and Vaults	<input type="checkbox"/>	▶	-DUS&V-
BMP-3-07	Vegetation Management including Mechanical and Chemical Weed Control	<input type="checkbox"/>	↔	-VM-
BMP-3-08	Over-Water Protection	<input type="checkbox"/>	⬢	-OWP-
BMP-3-09	Removal of Utility Location/Mark-Out Paint	<input type="checkbox"/>	⊕	-UL-
The following rows have been provided to add additional BMPs that may be required during the course of the project. QSD to provide this information as applicable.				
Other – User Defined	BMP Description:	<input type="checkbox"/>		

**BMP SELECTION WORKSHEET  
(Store Completed Forms in Appendix VII)**

BMP No.	BMP Options (Additional BMPs shall be implemented as necessary to protect water quality as determined by field conditions)	Selected BMPs	Option 1	Option 2
<b>Section 4 Erosion Control and Soil Stabilization</b>				
BMP-4-01	Preservation of Existing Vegetation	<input type="checkbox"/>	▼	-PEV-
BMP-4-02	Temporary Soil Stabilization	<input type="checkbox"/>	■-■-■	-TSS-
BMP-4-03	Hydraulic Mulch	<input type="checkbox"/>	≈≈≈	-M-
BMP-4-04	Hydroseeding	<input type="checkbox"/>	>>>>	-BP-
BMP-4-05	Soil Binders	<input type="checkbox"/>	┌┌┌┌	-SOS-
BMP-4-06	Straw Mulch	<input type="checkbox"/>	««««	-S-
BMP-4-07	Geotextiles, Plastic Covers and Erosion Control Blankets/Mats	<input type="checkbox"/>	□□□□	-ECB-
BMP-4-08	Dust (Wind Erosion) Control	<input type="checkbox"/>	....	-WE-
The following rows have been provided to add additional BMPs that may be required during the course of the project. QSD to provide this information as applicable.				
Other – User Defined	BMP Description:	<input type="checkbox"/>		

**ORIGINAL - MAKE COPIES**

**BMP SELECTION WORKSHEET  
(Store Completed Forms in Appendix VII)**

BMP No.	BMP Options (Additional BMPs shall be implemented as necessary to protect water quality as determined by field conditions)	Selected BMPs	Option 1	Option 2
<b>Section 5 Streambed Discharges and Crossings</b>				
CASQA EC-10	Velocity Dissipation Devices	<input type="checkbox"/>	≡≡≡≡	-VDD-
CASQA EC-12	Streambank Stabilization	<input type="checkbox"/>	~~~~	-SBS-
CASQA NS-4	Temporary Stream Crossing	<input type="checkbox"/>	<<<<	-TSC-
CASQA NS-5	Clear Water Diversion	<input type="checkbox"/>	+++++	-CWD-
The following rows have been provided to add additional BMPs that may be required during the course of the project. QSD to provide this information as applicable.				
Other – User Defined	BMP Description:	<input type="checkbox"/>		

# **Appendix II**

## **Construction General Permit**



Linda S. Adams  
Secretary for  
Environmental Protection

# State Water Resources Control Board



Arnold Schwarzeneg  
Governor

**Division of Water Quality**  
1001 I Street • Sacramento, California 95814 • (916) 341-5455  
Mailing Address: P.O. Box 100 • Sacramento, California • 95812-0100  
Fax (916) 341-5463 • <http://www.waterboards.ca.gov>

NATIONAL POLLUTANT DISCHARGE ELIMINATION SYSTEM (NPDES)  
GENERAL PERMIT FOR  
STORM WATER DISCHARGES  
ASSOCIATED WITH CONSTRUCTION AND LAND DISTURBANCE  
ACTIVITIES

ORDER NO. 2009-0009-DWQ  
NPDES NO. **CAS000002**

This Order was adopted by the State Water Resources Control Board on:	<b>September 2, 2009</b>
This Order shall become effective on:	<b>July 1, 2010</b>
This Order shall expire on:	<b>September 2, 2014</b>

IT IS HEREBY ORDERED, that this Order supersedes [Order No. 99-08-DWQ](#) except for enforcement purposes. The Discharger shall comply with the requirements in this Order to meet the provisions contained in Division 7 of the California Water Code (commencing with section 13000) and regulations adopted thereunder, and the provisions of the federal Clean Water Act and regulations and guidelines adopted thereunder.

I, Jeanine Townsend, Clerk to the Board, do hereby certify that this Order with all attachments is a full, true, and correct copy of an Order adopted by the State Water Resources Control Board, on September 2, 2009.

AYE: Vice Chair Frances Spivy-Weber  
Board Member Arthur G. Baggett, Jr.  
Board Member Tam M. Doduc

NAY: Chairman Charles R. Hoppin

ABSENT: None

ABSTAIN: None

\_\_\_\_\_  
Jeanine Townsend  
Clerk to the Board

List of Documents included in this single file saved in pdf format on September 22, 2009:

- Fact Sheet
- Order
- Attachment A – Linear Underground/Overhead Requirements
- Attachment A.1 – LUP Project Type Determination
- Attachment A.2 – LUP Permit Registration Documents
- Attachment B – Permit Registration Documents
- Attachment C – Risk Level 1 Requirements
- Attachment D – Risk Level 2 Requirements
- Attachment E – Risk Level 3 Requirements
- Attachment F – Active Treatment System Requirements
- Appendix 1 – Risk Determination Worksheet and Sediment-related 303d List
- Appendix 2 – Post-Construction Water Balance
- Appendix 2.1 – Post-Construction Water Balance Calculator
- Appendix 3 - Bioassessment Monitoring Guidelines
- Appendix 4 – Adopted/Implemented Sediment and Non-sediment TMDLs
- Appendix 5 – Glossary
- Appendix 6 - Acronym List
- Appendix 7 – State and Regional Water Board Contacts



**Linda S. Adams**  
Secretary for  
Environmental Protection

# State Water Resources Control Board

Division of Water Quality  
1001 I Street • Sacramento, California 95814 • (916) 341-5455  
Mailing Address: P.O. Box 100 • Sacramento, California • 95812-0100  
Fax (916) 341-5463 • <http://www.waterboards.ca.gov>



**Arnold Schwarzenegger**  
Governor

## CONSTRUCTION GENERAL PERMIT FACT SHEET TABLE OF CONTENTS

<b>I.</b>	<b>BACKGROUND .....</b>	<b>1</b>
<b>A.</b>	<b>History .....</b>	<b>1</b>
<b>B.</b>	<b>Legal Challenges and Court Decisions.....</b>	<b>1</b>
<b>C.</b>	<b>Blue Ribbon Panel of Experts and Feasibility of Numeric Effluent Limitations .....</b>	<b>3</b>
<b>D.</b>	<b>Summary of Panel Findings on Construction Activities .....</b>	<b>4</b>
<b>E.</b>	<b>How the Panel’s Findings are Used in this General Permit .....</b>	<b>5</b>
<b>F.</b>	<b>Summary of Significant Changes in This General Permit .....</b>	<b>5</b>
<b>II.</b>	<b>RATIONALE .....</b>	<b>7</b>
<b>A.</b>	<b>General Permit Approach.....</b>	<b>7</b>
<b>B.</b>	<b>Construction Activities Covered.....</b>	<b>7</b>
<b>C.</b>	<b>Construction Activities Not Covered .....</b>	<b>9</b>
<b>D.</b>	<b>Obtaining and Terminating Permit Coverage .....</b>	<b>11</b>
<b>E.</b>	<b>Discharge Prohibitions .....</b>	<b>12</b>
<b>F.</b>	<b>Effluent Standards for All Types of Discharges.....</b>	<b>13</b>
<b>G.</b>	<b>Receiving Water Limitations .....</b>	<b>20</b>
<b>H.</b>	<b>Training Qualifications and Requirements .....</b>	<b>21</b>
<b>I.</b>	<b>Sampling, Monitoring, Reporting and Record Keeping.....</b>	<b>21</b>
<b>J.</b>	<b>Risk Determination.....</b>	<b>28</b>
<b>K.</b>	<b>ATS Requirements.....</b>	<b>36</b>
<b>L.</b>	<b>Post-Construction Requirements .....</b>	<b>37</b>
<b>M.</b>	<b>Storm Water Pollution Prevention Plans .....</b>	<b>45</b>
<b>N.</b>	<b>Regional Water Board Authorities.....</b>	<b>47</b>

## LIST OF TABLES

Table 1 - Regional Water Board Basin Plans, Water Quality Objectives for Turbidity .....	16
Table 2 - Results of Ecoregion Analysis .....	16
Table 3 – ACL Sampling Data taken by Regional Water Board Staff.....	17
Table 4 - Required Monitoring Elements for Risk Levels.....	21
Table 5 - Storm Water Effluent Monitoring Requirements by Risk Level .....	23
Table 6 - Receiving Water Monitoring Requirements .....	26
Table 7 - Combined Risk Level Matrix .....	30
Table 8 -National Oceanic and Atmospheric Administration (NOAA) Definition of Probability of Precipitation (PoP) .....	32
Table 9 - Qualified SWPPP Developer/ Qualified SWPPP Practitioner Certification Criteria.....	46

## LIST OF FIGURES

Figure 1 -Statewide Map of K * LS.....	29
Figure 2 - Suite of Storm Events .....	38
Figure 3 - Northern CA (2009) Counties / Cities With SUSMP-Plus Coverage.....	39
Figure 4 - Southern CA (2009) Counties / Cities With SUSMP-Plus Coverage .....	40
Figure 5 - Schematic of the Lane Relationship .....	42
Figure 6 - Channel Changes Associated with Urbanization .....	43

## I. BACKGROUND

### A. History

In 1972, the Federal Water Pollution Control Act (also referred to as the Clean Water Act [CWA]) was amended to provide that the discharge of pollutants to waters of the United States from any point source is unlawful unless the discharge is in compliance with a National Pollutant Discharge Elimination System (NPDES) permit. The 1987 amendments to the CWA added Section 402(p), which establishes a framework for regulating municipal and industrial storm water discharges under the NPDES Program. On November 16, 1990, the U.S. Environmental Protection Agency (USEPA) published final regulations that established storm water permit application requirements for specified categories of industries. The regulations provide that discharges of storm water to waters of the United States from construction projects that encompass five or more acres of soil disturbance are effectively prohibited unless the discharge is in compliance with an NPDES Permit. Regulations (Phase II Rule) that became final on December 8, 1999 lowered the permitting threshold from five acres to one acre.

While federal regulations allow two permitting options for storm water discharges (Individual Permits and General Permits), the State Water Board has elected to adopt only one statewide General Permit at this time that will apply to most storm water discharges associated with construction activity.

On August 19, 1999, the State Water Board reissued the General Construction Storm Water Permit (Water Quality Order 99-08-DWQ). On December 8, 1999 the State Water Board amended Order 99-08-DWQ to apply to sites as small as one acre.

The General Permit accompanying this fact sheet regulates storm water runoff from construction sites. Regulating many storm water discharges under one permit will greatly reduce the administrative burden associated with permitting individual storm water discharges. To obtain coverage under this General Permit, dischargers shall electronically file the Permit Registration Documents (PRDs), which includes a Notice of Intent (NOI), Storm Water Pollution Prevention Plan (SWPPP), and other compliance related documents required by this General Permit and mail the appropriate permit fee to the State Water Board. It is expected that as the storm water program develops, the Regional Water Quality Control Boards (Regional Water Boards) may issue General Permits or Individual Permits containing more specific permit provisions. When this occurs, this General Permit will no longer regulate those dischargers.

## B. Legal Challenges and Court Decisions

### 1. Early Court Decisions

Shortly after the passage of the CWA, the USEPA promulgated regulations exempting most storm water discharges from the NPDES permit requirements. (See 40 C.F.R. § 125.4 (1975); see also *Natural Resources Defense Council v. Costle* (D.C. Cir. 1977) 568 F.2d 1369, 1372 (*Costle*); *Defenders of Wildlife v. Browner* (9th Cir. 1999) 191 F.3d 1159, 1163 (*Defenders of Wildlife*)). When environmental groups challenged this exemption in federal court, the District of Columbia Court of Appeals invalidated the regulation, holding that the USEPA “does not have authority to exempt categories of point sources from the permit requirements of [CWA] § 402.” (*Costle*, 568 F.2d at 1377.) The *Costle* court rejected the USEPA's argument that effluent-based storm sewer regulation was administratively infeasible because of the variable nature of storm water pollution and the number of affected storm sewers throughout the country. (*Id.* at 1377-82.) Although the court acknowledged the practical problems relating to storm sewer regulation, the court found the USEPA had the flexibility under the CWA to design regulations that would overcome these problems. (*Id.* at 1379-83.) In particular, the court pointed to general permits and permits based on requiring best management practices (BMPs).

During the next 15 years, the USEPA made numerous attempts to reconcile the statutory requirement of point source regulation with the practical problem of regulating possibly millions of diverse point source discharges of storm water. (See *Defenders of Wildlife*, 191 F.3d at 1163; see also Gallagher, Clean Water Act in Environmental Law Handbook (Sullivan, edit., 2003) p. 300 (Environmental Law Handbook); Eisen, *Toward a Sustainable Urbanism: Lessons from Federal Regulation of Urban Storm Water Runoff* (1995) 48 Wash. U.J. Urb. & Contemp. L.1, 40-41 [Regulation of Urban Storm Water Runoff].)

In 1987, Congress amended the CWA to require NPDES permits for storm water discharges. (See CWA § 402(p), 33 U.S.C. § 1342(p); *Defenders of Wildlife*, 191 F.3d at 1163; *Natural Resources Defense Council v. USEPA* (9th Cir. 1992) 966 F.2d 1292, 1296.) In these amendments, enacted as part of the Water Quality Act of 1987, Congress distinguished between industrial and municipal storm water discharges. With respect to industrial storm water discharges, Congress provided that NPDES permits "shall meet all applicable provisions of this section and section 1311 [requiring the USEPA to establish effluent limitations under specific timetables]." (CWA § 402(p)(3)(A), 33 U.S.C. § 1342(p)(3)(A); see also *Defenders of Wildlife*, 191 F.3d at 1163-64.)

In 1990, USEPA adopted regulations specifying what activities were considered "industrial" and thus required discharges of storm water associated with those activities to obtain coverage under NPDES permits. (55 Fed. Reg. 47,990 (1990); 40 C.F.R. § 122.26(b)(14).) Construction activities, deemed a subset of the industrial activities category, must also be regulated by an NPDES permit. (40 C.F.R. § 122.26(b)(14)(x)). In 1999, USEPA issued regulations for "Phase II" of storm water regulation, which required most small construction sites (1-5 acres) to be regulated under the NPDES program. (64 Fed. Reg. 68,722; 40 C.F.R. § 122.26(b)(15)(i).)

## 2. Court Decisions on Public Participation

Two recent federal court opinions have vacated USEPA rules that denied meaningful public review of NPDES permit conditions. On January 14, 2003, the Ninth Circuit Court of Appeals held that certain aspects of USEPA's Phase II regulations governing MS4s were invalid primarily because the general permit did not contain express requirements for public participation. (*Environmental Defense Center v. USEPA* (9th Cir. 2003) 344 F.3d 832.) Specifically, the court determined that applications for general permit coverage (including the Notice of Intent (NOI) and Storm Water Management Program (SWMP)) must be made available to the public, the applications must be reviewed and determined to meet the applicable standard by the permitting authority before coverage commences, and there must be a process to accommodate public hearings. (*Id.* at 852-54.) Similarly, on February 28, 2005, the Second Circuit Court of Appeals held that the USEPA's confined animal feeding operation (CAFO) rule violated the CWA because it allowed dischargers to write their own nutrient management plans without public review. (*Waterkeeper Alliance v. USEPA* (2d Cir. 2005) 399 F.3d 486.) Although neither decision involved the issuance of construction storm water permits, the State Water Board's Office of Chief Counsel has recommended that the new General Permit address the courts' rulings where feasible<sup>1</sup>.

---

<sup>1</sup> In *Texas Independent Producers and Royalty Owners Assn. v. USEPA* (7th Cir. 2005) 410 F.3d 964, the Seventh Circuit Court of Appeals held that the USEPA's construction general permit was not required to provide the public with the opportunity for a public hearing on the Notice of Intent or Storm Water Pollution Prevention Plan. The Seventh Circuit briefly discussed why it agreed with the Ninth Circuit's dissent in *Environmental Defense Center*, but generally did not discuss the substantive holdings in *Environmental Defense Center* and *Waterkeeper Alliance*, because neither court addressed the initial question of whether the plaintiffs had standing to challenge the permits at issue. However, notwithstanding the Seventh Circuit's decision, it is not binding or controlling on the State Water Board because California is located within the Ninth Circuit.

The CWA and the USEPA's regulations provide states with the discretion to formulate permit terms, including specifying best management practices (BMPs), to achieve strict compliance with federal technology-based and water quality-based standards. (*Natural Resources Defense Council v. USEPA* (9th Cir. 1992) 966 F.2d 1292, 1308.) Accordingly, this General Permit has developed specific BMPs as well as numeric action levels (NALs) and numeric effluent limitations (NELs) in order to achieve these minimum federal standards. In addition, the General Permit requires a SWPPP and REAP (another dynamic, site-specific plan) to be developed but has removed all language requiring the discharger to implement these plans – instead, the discharger is required to comply with specific requirements. By requiring the dischargers to implement these specific BMPs, NALs, and NELs, this General Permit ensures that the dischargers do not “write their own permits.” As a result this General Permit does not require each discharger's SWPPP and REAP to be reviewed and approved by the Regional Water Boards.

This General Permit also requires dischargers to electronically file all permit-related compliance documents. These documents include, but are not limited to, NOIs, SWPPPs, annual reports, Notice of Terminations (NOTs), and numeric action level (NAL) exceedance reports. Electronically submitted compliance information is immediately available to the public, as well as the Regional Water Quality Control Board (Regional Water Board) offices, via the Internet. In addition, this General Permit enables public review and hearings on permit applications when appropriate. Under this General Permit, the public clearly has a meaningful opportunity to participate in the permitting process.

### **C. Blue Ribbon Panel of Experts and Feasibility of Numeric Effluent Limitations**

In 2005 and 2006, the State Water Board convened an expert panel (panel) to address the feasibility of numeric effluent limitations (NELs) in California's storm water permits. Specifically, the panel was asked to address:

“Is it technically feasible to establish numeric effluent limitations, or some other quantifiable limit, for inclusion in storm water permits? How would such limitations or criteria be established, and what information and data would be required?”

“The answers should address industrial general permits, construction general permits, and area-wide municipal permits. The answers should also address both technology-based limitations or criteria and water quality-based limitations or criteria. In evaluating establishment of any objective criteria, the panel should address all of the following:

The ability of the State Water Board to establish appropriate objective limitations or criteria;

How compliance determinations would be made;

The ability of dischargers and inspectors to monitor for compliance; and

The technical and financial ability of dischargers to comply with the limitations or criteria.”

Through a series of public participation processes (State Water Board meetings, State Water Board workshops, and the solicitation of written comments), a number of water quality, public process and overall program effectiveness problems were identified. Some of these problems are addressed through this General Permit.

## D. Summary of Panel Findings on Construction Activities

The panel's final report can be downloaded and viewed through links at [www.waterboards.ca.gov](http://www.waterboards.ca.gov) or by clicking [here](#)<sup>2</sup>.

The panel made the following observations:

"Limited field studies indicate that traditional erosion and sediment controls are highly variable in performance, resulting in highly variable turbidity levels in the site discharge."

"Site-to-site variability in runoff turbidity from undeveloped sites can also be quite large in many areas of California, particularly in more arid regions with less natural vegetative cover and steep slopes."

"Active treatment technologies involving the use of polymers with relatively large storage systems now exist that can provide much more consistent and very low discharge turbidity. However, these technologies have as yet only been applied to larger construction sites, generally five acres or greater. Furthermore, toxicity has been observed at some locations, although at the vast majority of sites, toxicity has not occurred. There is also the potential for an accidental large release of such chemicals with their use."

"To date most of the construction permits have focused on TSS and turbidity, but have not addressed other, potentially significant pollutants such as phosphorus and an assortment of chemicals used at construction sites."

"Currently, there is no required training or certification program for contractors, preparers of soil erosion and sediment control Storm Water Pollution Prevention Plans, or field inspectors."

"The quality of storm water discharges from construction sites that effectively employ BMPs likely varies due to site conditions such as climate, soil, and topography."

"The States of Oregon and Washington have recently adopted similar concepts to the Action Levels described earlier."

In addition, the panel made the following conclusions:

"It is the consensus of the Panel that active treatment technologies make Numeric Limits technically feasible for pollutants commonly associated with storm water discharges from construction sites (e.g. TSS and turbidity) for larger construction sites. Technical practicalities and cost-effectiveness may make these technologies less feasible for smaller sites, including small drainages within a larger site, as these technologies have seen limited use at small construction sites. If chemical addition is not permitted, then Numeric Limits are not likely feasible."

"The Board should consider Numeric Limits or Action Levels for other pollutants of relevance to construction sites, but in particular pH. It is of particular concern where fresh concrete or wash water from cement mixers/equipment is exposed to storm water."

"The Board should consider the phased implementation of Numeric Limits and Action Levels, commensurate with the capacity of the dischargers and support industry to respond."

---

<sup>2</sup> [http://www.waterboards.ca.gov/stormwtr/docs/numeric/swpanel\\_final\\_report.pdf](http://www.waterboards.ca.gov/stormwtr/docs/numeric/swpanel_final_report.pdf)

## E. How the Panel's Findings are Used in this General Permit

The State Water Board carefully considered the findings of the panel and related public comments. The State Water Board also reviewed and considered the comments regarding statewide storm water policy and the reissuance of the Industrial General Permit. From the input received the State Water Board identified some permit and program performance gaps that are addressed in this General Permit. The Summary of Significant Changes (below) in this General Permit are a direct result of this process.

## F. Summary of Significant Changes in This General Permit

The State Water Board has significant changes to Order 99-08-DWQ. This General Permit differs from Order 99-08-DWQ in the following significant ways:

**Rainfall Erosivity Waiver:** this General Permit includes the option allowing a small construction site (>1 and <5 acres) to self-certify if the rainfall erosivity value (R value) for their site's given location and time frame compute to be less than or equal to 5.

**Technology-Based Numeric Action Levels:** this General Permit includes NALs for pH and turbidity.

**Technology-Based Numeric Effluent Limitations:** this General Permit contains daily average NELs for pH during any construction phase where there is a high risk of pH discharge and daily average NELs turbidity for all discharges in Risk Level 3. The daily average NEL for turbidity is set at 500 NTU to represent the minimum technology that sites need to employ (to meet the traditional Best Available Technology Economically Achievable (BAT)/ Best Conventional Pollutant Control Technology (BCT) standard) and the traditional, numeric receiving water limitations for turbidity.

**Risk-Based Permitting Approach:** this General Permit establishes three levels of risk possible for a construction site. Risk is calculated in two parts: 1) Project Sediment Risk, and 2) Receiving Water Risk.

**Minimum Requirements Specified:** this General Permit imposes more minimum BMPs and requirements that were previously only required as elements of the SWPPP or were suggested by guidance.

**Project Site Soil Characteristics Monitoring and Reporting:** this General Permit provides the option for dischargers to monitor and report the soil characteristics at their project location. The primary purpose of this requirement is to provide better risk determination and eventually better program evaluation.

**Effluent Monitoring and Reporting:** this General Permit requires effluent monitoring and reporting for pH and turbidity in storm water discharges. The purpose of this monitoring is to determine compliance with the NELs and evaluate whether NALs included in this General Permit are exceeded.

**Receiving Water Monitoring and Reporting:** this General Permit requires some Risk Level 3 dischargers to monitor receiving waters and conduct bioassessments.

**Post-Construction Storm Water Performance Standards:** this General Permit specifies runoff reduction requirements for all sites not covered by a Phase I or Phase II MS4 NPDES permit, to avoid, minimize and/or mitigate post-construction storm water runoff impacts.

**Rain Event Action Plan:** this General Permit requires certain sites to develop and implement a Rain Event Action Plan (REAP) that must be designed to protect all exposed portions of the site within 48 hours prior to any likely precipitation event.

**Annual Reporting:** this General Permit requires all projects that are enrolled for more than one continuous three-month period to submit information and annually certify that their site is in compliance

with these requirements. The primary purpose of this requirement is to provide information needed for overall program evaluation and public information.

**Certification/Training Requirements for Key Project Personnel:** this General Permit requires that key personnel (e.g., SWPPP preparers, inspectors, etc.) have specific training or certifications to ensure their level of knowledge and skills are adequate to ensure their ability to design and evaluate project specifications that will comply with General Permit requirements.

**Linear Underground/Overhead Projects:** this General Permit includes requirements for all Linear Underground/Overhead Projects (LUPs).

## II. RATIONALE

### A. General Permit Approach

A general permit for construction activities is an appropriate permitting approach for the following reasons:

1. A general permit is an efficient method to establish the essential regulatory requirements for a broad range of construction activities under differing site conditions;
2. A general permit is the most efficient method to handle the large number of construction storm water permit applications;
3. The application process for coverage under a general permit is far less onerous than that for individual permit and hence more cost effective;
4. A general permit is consistent with USEPA's four-tier permitting strategy, the purpose of which is to use the flexibility provided by the CWA in designing a workable and efficient permitting system; and
5. A general permit is designed to provide coverage for a group of related facilities or operations of a specific industry type or group of industries. It is appropriate when the discharge characteristics are sufficiently similar, and a standard set of permit requirements can effectively provide environmental protection and comply with water quality standards for discharges. In most cases, the general permit will provide sufficient and appropriate management requirements to protect the quality of receiving waters from discharges of storm water from construction sites.

There may be instances where a general permit is not appropriate for a specific construction project. A Regional Water Board may require any discharger otherwise covered under the General Permit to apply for and obtain an Individual Permit or apply for coverage under a more specific General Permit. The Regional Water Board must determine that this General Permit does not provide adequate assurance that water quality will be protected, or that there is a site-specific reason why an individual permit should be required.

### B. Construction Activities Covered

#### 1. Construction activity subject to this General Permit:

Any construction or demolition activity, including, but not limited to, clearing, grading, grubbing, or excavation, or any other activity that results in a land disturbance of equal to or greater than one acre.

Construction activity that results in land surface disturbances of less than one acre if the construction activity is part of a larger common plan of development or sale of one or more acres of disturbed land surface.

Construction activity related to residential, commercial, or industrial development on lands currently used for agriculture including, but not limited to, the construction of buildings related to agriculture that are considered industrial pursuant to USEPA regulations, such as dairy barns or food processing facilities.

Construction activity associated with LUPs including, but not limited to, those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment and associated ancillary facilities) and include, but are not limited to, underground utility mark-out, potholing, concrete

and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/tower pad and cable/wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/or pavement repair or replacement, and stockpile/borrow locations.

Discharges of sediment from construction activities associated with oil and gas exploration, production, processing, or treatment operations or transmission facilities.<sup>3</sup>

Storm water discharges from dredge spoil placement that occur outside of U.S. Army Corps of Engineers jurisdiction<sup>4</sup> (upland sites) and that disturb one or more acres of land surface from construction activity are covered by this General Permit. Construction projects that intend to disturb one or more acres of land within the jurisdictional boundaries of a CWA § 404 permit should contact the appropriate Regional Water Board to determine whether this permit applies to the project.

## 2. Linear Underground/Overhead Projects (LUPs) subject to this General Permit:

Underground/overhead facilities typically constructed as LUPs include, but are not limited to, any conveyance, pipe, or pipeline for the transportation of any gaseous, liquid (including water, wastewater for domestic municipal services), liquescent, or slurry substance; any cable line or wire for the transmission of electrical energy; any cable line or wire for communications (e.g., telephone, telegraph, radio or television messages); and associated ancillary facilities. Construction activities associated with LUPs include, but are not limited to, those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment and associated ancillary facilities) and include, but are not limited to, underground utility mark-out, potholing, concrete and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/tower pad and cable/wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/or pavement repair or replacement, and stockpile/borrow locations.

Water Quality Order 2003-0007-DWQ regulated construction activities associated with small LUPs that resulted in land disturbances greater than one acre, but less than five acres. These projects were considered non-traditional construction projects. Attachment A of this Order now regulates all construction activities from LUPs resulting in land disturbances greater than one acre.

## 3. Common Plan of Development or Sale

USEPA regulations include the term "common plan of development or sale" to ensure that acreage within a common project does not artificially escape the permit requirements because construction activities are phased, split among smaller parcels, or completed by different owners/developers. In the absence of an exact definition of "common plan of development or sale," the State Water Board is required to exercise its regulatory discretion in providing a common sense interpretation of the term as it applies to construction projects and permit coverage. An overbroad interpretation of the term would render meaningless the clear "one acre" federal permitting threshold and would potentially trigger permitting of

---

<sup>3</sup> Pursuant to the Ninth Circuit Court of Appeals' decision in *NRDC v. EPA* (9th Cir. 2008) 526 F.3d 591, and subsequent denial of the USEPA's petition for reconsideration in November 2008, oil and gas construction activities discharging storm water contaminated only with sediment are no longer exempt from the NPDES program.

<sup>4</sup> A construction site that includes a dredge and/or fill discharge to any water of the United States (e.g., wetland, channel, pond, or marine water) requires a CWA Section 404 permit from the U.S. Army Corps of Engineers and a CWA Section 401 Water Quality Certification from the Regional Water Board or State Water Board.

almost any construction activity that occurs within an area that had previously received area-wide utility or road improvements.

Construction projects generally receive grading and/or building permits (Local Permits) from local authorities prior to initiating construction activity. These Local Permits spell out the scope of the project, the parcels involved, the type of construction approved, etc. Referring to the Local Permit helps define "common plan of development or sale." In cases such as tract home development, a Local Permit will include all phases of the construction project including rough grading, utility and road installation, and vertical construction. All construction activities approved in the Local Permit are part of the common plan and must remain under the General Permit until construction is completed. For custom home construction, Local Permits typically only approve vertical construction as the rough grading, utilities, and road improvements were already independently completed under the a previous Local Permit. In the case of a custom home site, the homeowner must submit plans and obtain a distinct and separate Local Permit from the local authority in order to proceed. It is not the intent of the State Water Board to require permitting for an individual homeowner building a custom home on a private lot of less than one acre if it is subject to a separate Local Permit. Similarly, the installation of a swimming pool, deck, or landscaping that disturbs less than one acre that was not part of any previous Local Permit are not required to be permitted.

The following are several examples of construction activity of less than one acre that would require permit coverage:

- a. A landowner receives a building permit(s) to build tract homes on a 100-acre site split into 200 one-third acre parcels, (the remaining acreage consists of streets and parkways) which are sold to individual homeowners as they are completed. The landowner completes and sells all the parcels except for two. Although the remaining two parcels combined are less than one acre, the landowner must continue permit coverage for the two parcels.
- b. One of the parcels discussed above is sold to another owner who intends to complete the construction as already approved in the Local Permit. The new landowner must file Permit Registration Documents (PRDs) to complete the construction even if the new landowner is required to obtain a separate Local Permit.
- c. Landowner in (1) above purchases 50 additional one half-acre parcels adjacent to the original 200-acre project. The landowner seeks a Local Permit (or amendment to existing Local permit) to build on 20 parcels while leaving the remaining 30 parcels for future development. The landowner must amend PRDs to include the 20 parcels 14 days prior to commencement of construction activity on those parcels.

## **C. Construction Activities Not Covered**

### **1. Traditional Construction Projects Not Covered**

This General Permit does not apply to the following construction activity:

- a. Routine maintenance to maintain original line and grade, hydraulic capacity, or original purpose of the facility.
- b. Disturbances to land surfaces solely related to agricultural operations such as disking, harrowing, terracing and leveling, and soil preparation.

- c. Discharges of storm water from areas on tribal lands; construction on tribal lands is regulated by a federal permit.
- d. Discharges of storm water within the Lake Tahoe Hydrologic Unit. The Lahontan Regional Water Board has adopted its own permit to regulate storm water discharges from construction activity in the Lake Tahoe Hydrologic Unit (Regional Water Board 6SLT). Owners of construction projects in this watershed must apply for the Lahontan Regional Water Board permit rather than the statewide Construction General Permit. Construction projects within the Lahontan region must also comply with the Lahontan Region Project Guideline for Erosion Control (R6T-2005-0007 Section), which can be found at [http://www.waterboards.ca.gov/lahontan/Adopted\\_Orders/2005/r6t\\_2005\\_0007.pdf](http://www.waterboards.ca.gov/lahontan/Adopted_Orders/2005/r6t_2005_0007.pdf)
- e. Construction activity that disturbs less than one acre of land surface, unless part of a larger common plan of development or the sale of one or more acres of disturbed land surface.
- f. Construction activity covered by an individual NPDES Permit for storm water discharges.
- g. Landfill construction activity that is subject to the Industrial General Permit.
- h. Construction activity that discharges to Combined Sewer Systems.
- i. Conveyances that discharge storm water runoff combined with municipal sewage.
- j. Discharges of storm water identified in CWA § 402(l)(2), 33 U.S.C. § 1342(l)(2).

## 2. Linear Projects Not Covered

- a. LUP construction activity does not include linear routine maintenance projects. Routine maintenance projects are projects associated with operations and maintenance activities that are conducted on existing lines and facilities and within existing right-of-way, easements, franchise agreements, or other legally binding agreements of the discharger. Routine maintenance projects include, but are not limited to projects that are conducted to:
  - i. Maintain the original purpose of the facility or hydraulic capacity.
  - ii. Update existing lines<sup>5</sup> and facilities to comply with applicable codes, standards, and regulations regardless if such projects result in increased capacity.
  - iii. Repairing leaks.

Routine maintenance does not include construction of new<sup>6</sup> lines or facilities resulting from compliance with applicable codes, standards, and regulations.

Routine maintenance projects do not include those areas of maintenance projects that are outside of an existing right-of-way, franchise, easements, or agreements. When a project must secure new areas,

---

<sup>5</sup>Update existing lines includes replacing existing lines with new materials or pipes.

<sup>6</sup>New lines are those that are not associated with existing facilities and are not part of a project to update or replace existing lines.

those areas may be subject to this General Permit based on the area of disturbed land outside the original right-of-way, easement, or agreement.

- b. LUP construction activity does not include field activities associated with the planning and design of a project (e.g., activities associated with route selection).
- c. Tie-ins conducted immediately adjacent to “energized” or “pressurized” facilities by the discharger are not considered construction activities where all other LUP construction activities associated with the tie-in are covered by an NOI and SWPPP of a third party or municipal agency.

### 3. EPA’s Small Construction Rainfall Erosivity Waiver

EPA’s Storm Water Phase II Final Rule provides the option for a Small Construction Rainfall Erosivity Waiver. This waiver applies to small construction sites between 1 and 5 acres, and allows permitting authorities to waive those sites that do not have adverse water quality impacts.

Dischargers eligible for this waiver are exempt from Construction General Permit Coverage. In order to obtain the waiver, the discharger must certify to the State Water Board that small construction activity will occur only when the rainfall erosivity factor is less than 5 (“R” in the Revised Universal Soil Loss Equation). The period of construction activity begins at initial earth disturbance and ends with final stabilization. Where vegetation will be used for final stabilization, the date of installation of a practice that provides interim non-vegetative stabilization can be used for the end of the construction period. The operator must agree (as a condition waiver eligibility) to periodically inspect and properly maintain the area until the criteria for final stabilization as defined in the General Permit have been met. If use of this interim stabilization eligibility condition was relied on to qualify for the waiver, signature on the waiver with a certification statement constitutes acceptance of and commitment to complete the final stabilization process. The discharger must submit a waiver certification to the State Board prior to commencing construction activities.

USEPA funded a cooperative agreement with Texas A&M University to develop an online rainfall erosivity calculator. Dischargers can access the calculator from EPA’s website at: [www.epa.gov/npdes/stormwater/cgp](http://www.epa.gov/npdes/stormwater/cgp). Use of the calculator allows the discharger to determine potential eligibility for the rainfall erosivity waiver. It may also be useful in determining the time periods during which construction activity could be waived from permit coverage.

## D. Obtaining and Terminating Permit Coverage

The Legally Responsible Person (LRP) must obtain coverage under this General Permit, except in two limited circumstances. First, where the construction of pipelines, utility lines, fiber-optic cables, or other linear underground/overhead projects will occur across several properties, the utility company, municipality, or other public or private company or agency that owns or operates the linear underground/overhead project is responsible for obtaining coverage under the General Permit. Second, where there is a lease of a mineral estate (oil, gas, geothermal, aggregate, precious metals, and/or industrial metals), the lessee is responsible for obtaining coverage under the General Permit. To obtain coverage, the LRP or other entity described above must file Permit Registration Documents (PRDs) prior to the commencement of construction activity. Failure to obtain coverage under this General Permit for storm water discharges to waters of the United States is a violation of the CWA and the California Water Code.

To obtain coverage under this General Permit, LRPs must electronically file the PRDs, which include a Notice of Intent (NOI), Storm Water Pollution Prevention Plan (SWPPP), and other documents required by this General Permit, and mail the appropriate permit fee to the State Water Board. It is expected that as the storm water program develops, the Regional Water Boards may issue General Permits or

Individual Permits that contain more specific permit provisions. When this occurs, this General Permit will no longer regulate those dischargers that obtain coverage under Individual Permits.

Any information provided to the Regional Water Board shall comply with the Homeland Security Act and any other federal law that concerns security in the United States; any information that does not comply should not be submitted.

The application requirements of the General Permit establish a mechanism to clearly identify the responsible parties, locations, and scope of operations of dischargers covered by the General Permit and to document the discharger's knowledge of the General Permit's requirements.

This General Permit provides a grandfathering exception to existing dischargers subject to Water Quality Order No. 99-08-DWQ. Construction projects covered under Water Quality Order No. 99-08-DWQ shall obtain permit coverage at Risk Level 1. LUP projects covered under Water Quality Order No. 2003-0007-DWQ shall obtain permit coverage at LUP Type 1. The Regional Water Boards have the authority to require Risk Determination to be performed on projects currently covered under Water Quality Order No. 99-08-DWQ and 2003-0007-DWQ where they deem necessary.

LRPs must file a Notice of Termination (NOT) with the Regional Water Board when construction is complete and final stabilization has been reached or ownership has been transferred. The discharger must certify that all State and local requirements have been met in accordance with this General Permit. In order for construction to be found complete, the discharger must install post-construction storm water management measures and establish a long-term maintenance plan. This requirement is intended to ensure that the post-construction conditions at the project site do not cause or contribute to direct or indirect water quality impacts (i.e., pollution and/or hydromodification) upstream and downstream. Specifically, the discharger must demonstrate compliance with the post-construction standards set forth in this General Permit (Section XIII). The discharger is responsible for all compliance issues including all annual fees until the NOT has been filed and approved by the local Regional Water Board.

## **E. Discharge Prohibitions**

This General Permit authorizes the discharge of storm water to surface waters from construction activities that result in the disturbance of one or more acres of land, provided that the discharger satisfies all permit conditions set forth in the Order. This General Permit prohibits the discharge of pollutants other than storm water and non-storm water discharges authorized by this General Permit or another NPDES permit. This General Permit also prohibits all discharges which contain a hazardous substance in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges. In addition, this General Permit incorporates discharge prohibitions contained in water quality control plans, as implemented by the nine Regional Water Boards. Discharges to Areas of Special Biological Significance (ASBS) are prohibited unless covered by an exception that the State Water Board has approved.

Non-storm water discharges include a wide variety of sources, including improper dumping, spills, or leakage from storage tanks or transfer areas. Non-storm water discharges may contribute significant pollutant loads to receiving waters. Measures to control spills, leakage, and dumping, and to prevent illicit connections during construction must be addressed through structural as well as non-structural BMPs. The State Water Board recognizes, however, that certain non-storm water discharges may be necessary for the completion of construction projects. Authorized non-storm water discharges may include those from de-chlorinated potable water sources such as: fire hydrant flushing, irrigation of vegetative erosion control measures, pipe flushing and testing, water to control dust, uncontaminated ground water dewatering, and other discharges not subject to a separate general NPDES permit adopted by a region. Therefore this General Permit authorizes such discharges provided they meet the following conditions.

These authorized non-storm water discharges must:

1. be infeasible to eliminate;
2. comply with BMPs as described in the SWPPP;
3. filter or treat, using appropriate technology, all dewatering discharges from sedimentation basins;
4. meet the NELs and NALs for pH and turbidity; and
5. not cause or contribute to a violation of water quality standards.

Additionally, authorized non-storm water discharges must not be used to clean up failed or inadequate construction or post-construction BMPs designed to keep materials onsite. Authorized non-storm water dewatering discharges may require a permit because some Regional Water Boards have adopted General Permits for dewatering discharges.

This General Permit prohibits the discharge of storm water that causes or threatens to cause pollution, contamination, or nuisance.

## F. Effluent Standards for All Types of Discharges

### 1. Technology-Based Effluent Limitations

Permits for storm water discharges associated with construction activity must meet all applicable provisions of Sections 301 and 402 of the CWA. These provisions require controls of pollutant discharges that utilize best available technology economically achievable (BAT) for toxic pollutants and non conventional pollutants and best conventional pollutant control technology (BCT) for conventional pollutants. Additionally, these provisions require controls of pollutant discharges to reduce pollutants and any more stringent controls necessary to meet water quality standards. The USEPA has already established such limitations, known as effluent limitation guidelines (ELGs), for some industrial categories. This is not the case with construction discharges. In instances where there are no ELGs the permit writer is to use best professional judgment (BPJ) to establish requirements that the discharger must meet using BAT/BCT technology. This General Permit contains both narrative effluent limitations and new numeric effluent limitations for pH and turbidity, set using the best professional judgment (BPJ) equivalent to BAT and BCT (respectively).

BAT/BCT technologies not only include passive systems such as conventional runoff and sediment control, but also treatment systems such as coagulation/flocculation using sand filtration, when appropriate. Such technologies allow for effective treatment of soil particles less 0.02 mm (medium silt) in diameter. The discharger must install structural controls, as necessary, such as erosion and sediment controls that meet BAT and BCT to achieve compliance with water quality standards. The narrative effluent limitations constitute compliance with the requirements of the CWA.

The numeric effluent limitations for pH and turbidity are based upon BPJ, which authorizes the State Water Board to issue a permit containing "such conditions as the Administrator determines are necessary to carry out the provisions of this Chapter" (CWA § 402(a)(1), 33 U.S.C. § 1342(a)(1).) Because the USEPA has not yet issued an effluent limit guideline for storm water, the State Water Board must use BPJ to consider the appropriate technology for the category or class of point sources, based upon all available information and any unique factors relating to the sources. In addition, the permitting authority must consider a number of factors including the cost of achieving effluent reductions in relation to the effluent reduction benefits, the age of the equipment and facilities, the processes employed and any required process changes, engineering aspects of the control technologies, non-water quality environmental impacts (including energy requirements), and other such other factors as the State Water Board deems appropriate (CWA 304(b)(1)(B)).

Because the permit is an NPDES permit, there is no legal requirement to address the factors set forth in Water Code sections 13241 and 13263, unless the permit is more stringent than what federal law requires. (See *City of Burbank v. State Water Resources Control Bd.* (2005) 35 Cal.4th 613, 618, 627.) None of the requirements in this permit are more stringent than the minimum federal requirements, which include technology-based requirements achieving BAT/BCT and strict compliance with water quality standards. The inclusion of numeric effluent limitations (NELs) in the permit do not cause the permit to be more stringent than current federal law. NELs and best management practices are simply two different methods of achieving the same federal requirement: strict compliance with state water quality standards. Federal law authorizes both narrative and numeric effluent limitations to meet state water quality standards. The use of NELs to achieve compliance with water quality standards is not a more stringent requirement than the use of BMPs. (State Water Board Order No. WQ 2006-0012 (*Boeing*).) Accordingly, the State Water Board does not need to take into account the factors in Water Code sections 13241 and 13263.

The State Water Board has concluded that the establishment of BAT/BCT will not create or aggravate other environmental problems through increases in air pollution, solid waste generation, or energy consumption. While there may be a slight increase in non-water quality impacts due to the implementation of additional monitoring or the construction of additional BMPs, these impacts will be negligible in comparison with the construction activities taking place on site and would be justified by the water quality benefits associated with compliance.

Considerations related to the processes employed and the changes necessitated by the adoption of the BAT/BCT effluent limits have been assessed throughout the stakeholder process (e.g., the Blue Ribbon Panel and the March 2007 preliminary draft) and are discussed in detail in Section I.C of this Fact Sheet. The following sections set forth the engineering aspects of the control technologies and the rationale for the determination of the numeric effluents for pH and turbidity.

In consideration of the costs for the establishment of BAT and BCT limits for pH and turbidity, existing requirements for the control of storm water pollution from construction sites have been established by USEPA and the previous Construction General Permit (State Water Board Order No. 99-08-DWQ) issued by the State Water Board. The General Permit establishes one, consistent set of performance standards for all levels and types of discharges (i.e., risk, linear utility, and ATS). The only difference is that for each level or type of discharge there may be more or less specific effluent limitations (e.g., the addition of numeric effluent limitations for turbidity applies to level/type 3 discharges). And the numeric effluent limitations themselves represent a minimum technology standard. In other words, the additional numeric effluent limitations, compared to the existing permit's narrative effluent limitations, do not increase compliance requirements; rather, they simply represent a point where one can quantitatively measure compliance with the lower end of the range of required technologies. Therefore, the compliance costs associated with the BAT/BCT numeric effluent limitations in this permit only differ by the costs required to measure compliance with the NELs when compared to the baseline compliance costs to comply with the limitations already established through EPA regulations and the existing Construction General Permit.

The State Water Board estimates these measurement costs to be approximately \$1000 per construction site for the duration of the project. This represents the estimated cost of purchasing (or renting) monitoring equipment, in this case a turbidimeter (~\$600) and a pH meter (~\$400). In some cases the costs may be higher or lower. Costs could be lower if the discharger chooses to design and implement the project in a manner where effluent monitoring is likely to be avoided (e.g., no exposure during wet weather seasons, no discharge due to containment, etc.). Costs could be more if the project is subject to many effluent monitoring events or if the discharger exceeds NALs and/or NELs, resulting in additional monitoring requirements.

#### i. pH NEL

Given the potential contaminants, the minimum standard method for control of pH in runoff requires the use of preventive measures such as avoiding concrete pours during rainy weather, covering concrete and directing flow away from fresh concrete if a pour occurs during rain, covering scrap drywall and stucco

materials when stored outside and potentially exposed to rain, and other housekeeping measures. If necessary, pH-impaired storm water from construction sites can be treated in a filter or settling pond or basin, with additional natural or chemical treatment required to meet pH limits set forth in this permit. The basin or pond acts as a collection point and holds storm water for a sufficient period for the contaminants to be settled out, either naturally or artificially, and allows any additional treatment to take place. The State Water Board considers these techniques to be equivalent to BCT. In determining the pH concentration limit for discharges, the State Water Board used BPJ to set these limitations.

The chosen limits were established by calculating three standard deviations above and below the mean pH of runoff from highway construction sites<sup>7</sup> in California. Proper implementation of BMPs should result in discharges that are within the range of 6.0 to 9.0 pH Units.

## ii. *Turbidity NEL*

The Turbidity NEL of 500 NTU is a technology-based numeric effluent limitation and was developed using three different analyses aimed at finding the appropriate threshold to set the technology-based limit to ensure environmental protection, effluent quality and cost-effectiveness. The analyses fell into three, main types: (1) an ecoregion-specific dataset developed by Simon et. al. (2004)<sup>8</sup>; (2) Statewide Regional Water Quality Control Board enforcement data; and (3) published, peer-reviewed studies and reports on in-situ performance of best management practices in terms of erosion and sediment control on active construction sites.

A 1:3 relationship between turbidity (expressed as NTU) and suspended sediment concentration (expressed as mg/L) is assumed based on a review of suspended sediment and turbidity data from three gages used in the USGS National Water Quality Assessment Program:

USGS 11074000 SANTA ANA R BL PRADO DAM CA  
 USGS 11447650 SACRAMENTO R A FREEPORT CA  
 USGS 11303500 SAN JOAQUIN R NR VERNALIS CA

The turbidity NEL represents a feasible and cost effective performance standard that is demonstrated to be achievable. Although data has been collected to demonstrate that lower effluent levels may be achievable at some sites, staff cannot conclude at this time that a lower NEL is achievable within all the ecoregions of the state. The NEL represents staff determination that the NEL is the most practicable based on available data. The turbidity NEL represents a bridge between the narrative effluent limitations and receiving water limitations. The NEL limit may be considered an interim performance standard as additional data becomes available for evaluation during the next permit cycle. To support this NEL, State Water Board staff analyzed construction site discharge information (monitoring data, estimates) and receiving water monitoring information.

Since the turbidity NEL represents an appropriate threshold level expected at a site, compliance with this value does not necessarily represent compliance with either the narrative effluent limitations (as enforced through the BAT/BCT standard) or the receiving water limitations. In the San Diego region, some inland surface waters have a receiving water objective for turbidity equal to 20 NTU. Obviously a discharge up to, but not exceeding, the turbidity NEL of 500 NTU may still cause or contribute to the exceedance of the 20 NTU standard. Most of the waters of the State are protected by turbidity objectives based on background conditions.

---

<sup>7</sup> Caltrans Construction Sites Runoff Characterization Study, 2002. Available at: <http://www.dot.ca.gov/hq/env/stormwater/pdf/CTSW-RT-02-055.pdf>.

<sup>8</sup> Simon, A., W.D. Dickerson, and A. Heins. 2004. Suspended-sediment transport rates at the 1.5-year recurrence interval for ecoregions of the United States: transport conditions at the bankfull and effective discharge. *Geomorphology* 58: pp. 243-262.

**Table 1 - Regional Water Board Basin Plans, Water Quality Objectives for Turbidity**

REGIONAL WATER BOARD	WQ Objective	Background/Natural Turbidity	Maximum Increase
1 Based	on background	All levels	20%
2 Based	on background	> 50 NTU	10%
3 Based	on background	0-50 JTU 50-100 JTU > 100 JTU	20% 10 NTU 10%
4 Based	on background	0-50 NTU > 50 NTU	20% 10%
5 Based	on background	0-5 NTU 5-50 NTU 50-100 NTU >100 NTU	1 NTU 20% 10 NTU 10%
6 Based	on background	All levels	10%
7 Based	on background	N/A N/A	
8 Based	on background	0-50 NTU 50-100 NTU >100 NTU	20% 10 NTU 10%
9 Inland	Surface Waters, 20 NTU  All others, based on background	  0-50 NTU 50-100 NTU >100 NTU	  20% 10 NTU 10%

Table 2 shows the suspended sediment concentrations at the 1.5 year flow recurrence interval for the 12 ecoregions in California from Simon et. al (2004).

**Table 2 - Results of Ecoregion Analysis**

Ecoregion	Percent of California Land Area	Median Suspended Sediment Concentration (mg/L)
1 9.1		874
4 0.2		120
5 8.8		35.6
6 20.7		1530
7 7.7		122
8 3.0		47.4
9 9.4		284
13 5.2		143
14 21.7		5150
78 8.1		581
80 2.4		199
81 3.7		503
Area-weighted average		1633

If a 1:3 relationship between turbidity and suspended sediment is assumed, the median turbidity is 544 NTU.

The following table is composed of turbidity readings measured in NTUs from administrative civil liberty (ACL) actions for construction sites from 2003 - 2009. This data was derived from the complete listing of construction-related ACLs for the six year period. All ACLs were reviewed and those that included turbidimeter readings at the point of storm water discharge were selected for this dataset.

**Table 3 – ACL Sampling Data taken by Regional Water Board Staff**

WDID# Regi	on	Discharger	Turbidity (NTU)
5S34C331884	5S Brad	shaw Interceptor Section 6B	1800
5S05C325110	5S Bridal	wood Subdivision	1670
5S48C336297	5S Cheye	rne at Browns Valley	1629
5R32C314271	5R Gri	zzly Ranch Construction	1400
6A090406008	6T	El Dorado County Department of Transportation, Angora Creek	97.4
5S03C346861	5S	TML Development, LLC	1600
6A31C325917	6T	Northstar Village	See Subdata Set

**Subdata Set - Turbidity for point of storm water runoff discharge at Northstar Village**

Date Turbi	dity (NTU)	Location
10/5/2006	900	Middle Martis Creek
11/2/2006	190	Middle Martis Creek
01/04/2007	36	West Fork, West Martis Creek
02/08/2007	180	Middle Martis Creek
02/09/2007	130	Middle Martis Creek
02/09/2007	290	Middle Martis Creek
02/09/2007	100	West Fork, West Martis Creek
02/10/2007	28	Middle Martis Creek
02/10/2007	23	Middle Martis Creek
02/10/2007	32	Middle Martis Creek
02/10/2007	12	Middle Martis Creek
02/10/2007	60	West Fork, West Martis Creek
02/10/2007	34	West Fork, West Martis Creek

A 95% confidence interval for mean turbidity in an ACL order was constructed. The data set used was a small sample size, so the 500 NTU (the value derived as the NEL for this General Permit) needed to be verified as a possible population mean. In this case, the population refers to a hypothetical population of turbidity measurements of which our sample of 20 represents. A t-distribution was assumed due to the small sample size:



chosen due to its relative infrequent occurrence and the fact that the runoff volume associated with it is not as large as a 10-year, 24-hour storm event. The discharger shall determine this value using Western Regional Climate Center Precipitation Frequency Maps<sup>9</sup> for 5-year 24-hour storm events in Northern and Southern California (note that these are expressed in tenths of inches – divide by 10 to get inches).

#### **b. TMDLs and Waste Load Allocations**

Dischargers located within the watershed of a CWA § 303(d) impaired water body, for which a TMDL for sediment has been adopted by the Regional Water Board or USEPA, must comply with the approved TMDL if it identifies “construction activity” or land disturbance as a source of sediment. If it does, the TMDL should include a specific waste load allocation for this activity/source. The discharger, in this case, may be required by a separate Regional Water Board order to implement additional BMPs, conduct additional monitoring activities, and/or comply with an applicable waste load allocation and implementation schedule. If a specific waste load allocation has been established that would apply to a specific discharge, the Regional Water Board may adopt an order requiring specific implementation actions necessary to meet that allocation. In the instance where an approved TMDL has specified a general waste load allocation to construction storm water discharges, but no specific requirements for construction sites have been identified in the TMDL, dischargers must consult with the state TMDL authority<sup>10</sup> to confirm that adherence to a SWPPP that meets the requirements of the General Permit will be consistent with the approved TMDL.

### **2. Determining Compliance with Effluent Standards**

#### **a. Technology-Based Numeric Action Levels (NALs)**

This General Permit contains technology-based NALs for pH and turbidity, and requirements for effluent monitoring at all Risk level 2 & 3, and LUP Type 2 & 3 sites. Numeric action levels are essentially numeric benchmark values for certain parameters that, if exceeded in effluent sampling, trigger the discharger to take actions. Exceedance of an NAL does not itself constitute a violation of the General Permit. If the discharger fails to take the corrective action required by the General Permit, though, that may constitute a violation.

The primary purpose of NALs is to assist dischargers in evaluating the effectiveness of their on-site measures. Construction sites need to employ many different systems that must work together to achieve compliance with the permit's requirements. The NALs chosen should indicate whether the systems are working as intended.

Another purpose of NALs is to provide information regarding construction activities and water quality impacts. This data will provide the State and Regional Water Boards and the rest of the storm water community with more information about levels and types of pollutants present in runoff and how effective the dischargers BMPs are at reducing pollutants in effluent. The State Water Board also hopes to learn more about the linkage between effluent and receiving water quality. In addition, these requirements will provide information on the mechanics needed to establish compliance monitoring programs at construction sites in future permit deliberations.

#### **i. pH**

---

<sup>9</sup> <http://www.wrcc.dri.edu/pcpnfreq/nca5y24.gif> & <http://www.wrcc.dri.edu/pcpnfreq/sca5y24.gif> .

<sup>10</sup> <http://www.waterboards.ca.gov/tmdl/tmdl.html>.

The chosen limits were established by calculating one standard deviation above and below the mean pH of runoff from highway construction sites<sup>11</sup> in California. Proper implementation of BMPs should result in discharges that are within the range of 6.5 to 8.5 pH Units.

The Caltrans study included 33 highway construction sites throughout California over a period of four years, which included 120 storm events. All of these sites had BMPs in place that would be generally implemented at all types of construction sites in California.

## ii. *Turbidity*

BPJ was used to develop an NAL that can be used as a learning tool to help dischargers improve their site controls, and to provide meaningful information on the effectiveness of storm water controls. A statewide turbidity NAL has been set at 250 NTU.

## G. Receiving Water Limitations

Construction-related activities that cause or contribute to an exceedance of water quality standards must be addressed. The dynamic nature of construction activity gives the discharger the ability to quickly identify and monitor the source of the exceedances. This is because when storm water mobilizes sediment, it provides visual cues as to where corrective actions should take place and how effective they are once implemented.

This General Permit requires that storm water discharges and authorized non-storm water discharges must not contain pollutants that cause or contribute to an exceedance of any applicable water quality objective or water quality standards. The monitoring requirements in this General Permit for sampling and analysis procedures will help determine whether BMPs installed and maintained are preventing pollutants in discharges from the construction site that may cause or contribute to an exceedance of water quality standards.

Water quality standards consist of designated beneficial uses of surface waters and the adoption of ambient criteria necessary to protect those uses. When adopted by the State Water Board or a Regional Water Board, the ambient criteria are termed "water quality objectives." If storm water runoff from construction sites contains pollutants, there is a risk that those pollutants could enter surface waters and cause or contribute to an exceedance of water quality standards. For that reason, dischargers should be aware of the applicable water quality standards in their receiving waters. (The best method to ensure compliance with receiving water limitations is to implement BMPs that prevent pollutants from contact with storm water or from leaving the construction site in runoff.)

In California, water quality standards are published in the Basin Plans adopted by each Regional Water Board, the California Toxics Rule (CTR), the National Toxics Rule (NTR), and the Ocean Plan.

Dischargers can determine the applicable water quality standards by contacting Regional Water Board staff or by consulting one of the following sources. The actual Basin Plans that contain the water quality standards can be viewed at the website of the appropriate Regional Water Board. (<http://www.waterboards.ca.gov/regions.html>), the State Water Board site for statewide plans (<http://www.waterboards.ca.gov/plnspols/index.html>), or the USEPA regulations for the NTR and CTR (40 C.F.R. §§ 131.36-38). Basin Plans and statewide plans are also available by mail from the appropriate Regional Water Board or the State Water Board. The USEPA regulations are available at <http://www.epa.gov/>. Additional information concerning water quality standards can be accessed through [http://www.waterboards.ca.gov/stormwtr/gen\\_const.html](http://www.waterboards.ca.gov/stormwtr/gen_const.html).

---

<sup>11</sup> Caltrans Construction Sites Runoff Characterization Study, 2002. Available at: <http://www.dot.ca.gov/hq/env/stormwater/pdf/CTSW-RT-02-055.pdf>.

## H. Training Qualifications and Requirements

The Blue Ribbon Panel (BRP) made the following observation about the lack of industry-specific training requirements:

“Currently, there is no required training or certification program for contractors, preparers of soil erosion and sediment control Storm Water Pollution Prevention Plans, or field inspectors.”

Order 99-08-DWQ required that all dischargers train their employees on how to comply with the permit, but it did not specify a curriculum or certification program. This has resulted in inconsistent implementation by all affected parties - the dischargers, the local governments where the construction activity occurs, and the regulators required to enforce 99-08-DWQ. This General Permit requires Qualified SWPPP Developers and practitioners to obtain appropriate training, and makes this curriculum mandatory two years after adoption, to allow time for course completion. The State and Regional Water Board are working with many stakeholders to develop the curriculum and mechanisms needed to develop and deliver the courses.

To ensure that the preparation, implementation, and oversight of the SWPPP is sufficient for effective pollution prevention, the Qualified SWPPP Developer and Qualified SWPPP Practitioners responsible for creating, revising, overseeing, and implementing the SWPPP must attend a State Water Board-sponsored or approved Qualified SWPPP Developer and Qualified SWPPP Practitioner training course.

## I. Sampling, Monitoring, Reporting and Record Keeping

### I. Traditional Construction Monitoring Requirements

This General Permit requires visual monitoring at all sites, and effluent water quality at all Risk Level 2 & 3 sites. It requires receiving water monitoring at some Risk Level 3 sites. All sites are required to submit annual reports, which contain various types of information, depending on the site characteristics and events. A summary of the monitoring and reporting requirements is found in Table 4.

**Table 4 - Required Monitoring Elements for Risk Levels**

	Visual	Non-visible Pollutant	Effluent	Receiving Water
Risk Level 1			where applicable	not required
Risk Level 2	three types required	As needed for all Risk Levels (see below)	pH, turbidity	not required
Risk Level 3	for all Risk Levels: non-storm water, pre-rain and post-rain		(if NEL exceeded) pH, turbidity and SSC	(if NEL exceeded) pH, turbidity and SSC. Bioassessment for sites 30 acres or larger.

#### a. Visual

All dischargers are required to conduct quarterly, non-storm water visual inspections. For these inspections, the discharger must visually observe each drainage area for the presence of (or indications of prior) unauthorized and authorized non-storm water discharges and their sources. For storm-related inspections, dischargers must visually observe storm water discharges at all discharge locations within two business days after a qualifying event. For this requirement, a qualifying rain event is one producing precipitation of ½ inch or more of discharge. Dischargers must conduct a post-storm event inspection to

(1) identify whether BMPs were adequately designed, implemented, and effective, and (2) identify any additional BMPs necessary and revise the SWPPP accordingly. Dischargers must maintain on-site records of all visual observations, personnel performing the observations, observation dates, weather conditions, locations observed, and corrective actions taken in response to the observations.

#### **b. Non-Visible Pollutant Monitoring**

This General Permit requires that all dischargers develop a sampling and analysis strategy for monitoring pollutants that are not visually detectable in storm water. Monitoring for non-visible pollutants must be required at any construction site when the exposure of construction materials occurs and where a discharge can cause or contribute to an exceedance of a water quality objective.

Of significant concern for construction discharges are the pollutants found in materials used in large quantities at construction sites throughout California and exposed throughout the rainy season, such as cement, flyash, and other recycled materials or by-products of combustion. The water quality standards that apply to these materials will depend on their composition. Some of the more common storm water pollutants from construction activity are not CTR pollutants. Examples of non-visible pollutants include glyphosate (herbicides), diazinon and chlorpyrifos (pesticides), nutrients (fertilizers), and molybdenum (lubricants). The use of diazinon and chlorpyrifos is a common practice among landscaping professionals and may trigger sampling and analysis requirements if these materials come into contact with storm water. High pH values from cement and gypsum, high pH and SSC from wash waters, and chemical/fecal contamination from portable toilets, also are not CTR pollutants. Although some of these constituents do have numeric water quality objectives in individual Basin Plans, many do not and are subject only to narrative water quality standards (i.e. not causing toxicity). Dischargers are encouraged to discuss these issues with Regional Water Board staff and other storm water quality professionals.

The most effective way to avoid the sampling and analysis requirements, and to ensure permit compliance, is to avoid the exposure of construction materials to precipitation and storm water runoff. Materials that are not exposed do not have the potential to enter storm water runoff, and therefore receiving waters sampling is not required. Preventing contact between storm water and construction materials is one of the most important BMPs at any construction site.

Preventing or eliminating the exposure of pollutants at construction sites is not always possible. Some materials, such as soil amendments, are designed to be used in a manner that will result in exposure to storm water. In these cases, it is important to make sure that these materials are applied according to the manufacturer's instructions and at a time when they are unlikely to be washed away. Other construction materials can be exposed when storage, waste disposal or the application of the material is done in a manner not protective of water quality. For these situations, sampling is required unless there is capture and containment of all storm water that has been exposed. In cases where construction materials may be exposed to storm water, but the storm water is contained and is not allowed to run off the site, sampling will only be required when inspections show that the containment failed or is breached, resulting in potential exposure or discharge to receiving waters.

The discharger must develop a list of potential pollutants based on a review of potential sources, which will include construction materials soil amendments, soil treatments, and historic contamination at the site. The discharger must review existing environmental and real estate documentation to determine the potential for pollutants that could be present on the construction site as a result of past land use activities.

Good sources of information on previously existing pollution and past land uses include:

- i. Environmental Assessments;
- ii. Initial Studies;
- iii. Phase 1 Assessments prepared for property transfers; and

- iv. Environmental Impact Reports or Environmental Impact Statements prepared under the requirements of the National Environmental Policy Act or the California Environmental Quality Act.

In some instances, the results of soil chemical analyses may be available and can provide additional information on potential contamination.

The potential pollutant list must include all non-visible pollutants that are known or should be known to occur on the construction site including, but not limited to, materials that:

- i. are being used in construction activities;
- ii. are stored on the construction site;
- iii. were spilled during construction operations and not cleaned up;
- iv. were stored (or used) in a manner that created the potential for a release of the materials during past land use activities;
- v. were spilled during previous land use activities and not cleaned up; or
- vi. were applied to the soil as part of past land use activities.

**c. Effluent Monitoring**

Federal regulations<sup>12</sup> require effluent monitoring for discharges subject to NALs and NELs. Subsequently, all Risk Level 2 and 3 dischargers must perform sampling and analysis of effluent discharges to characterize discharges associated with construction activity from the entire area disturbed by the project. Dischargers must collect samples of stored or contained storm water that is discharged subsequent to a storm event producing precipitation of ½ inch or more at the time of discharge.

**Table 5 - Storm Water Effluent Monitoring Requirements by Risk Level**

	Frequency	Effluent Monitoring (Section E, below)
Risk Level 1	when applicable	non-visible pollutant parameters (if applicable)
Risk Level 2	Minimum of 3 samples per day during qualifying rain event characterizing discharges associated with construction activity from the entire project disturbed area.	pH, turbidity, and non-visible pollutant parameters (if applicable)
Risk Level 3	Minimum of 3 samples per day during qualifying rain event characterizing discharges associated with construction activity from the entire project disturbed area.	If NEL exceeded: pH, turbidity and suspended sediment concentration (SSC)., Plus non-visible pollutant parameters if applicable

Risk Level 1 dischargers must analyze samples for:

---

<sup>12</sup> 40 C.F.R. § 122.44.

- i. any parameters indicating the presence of pollutants identified in the pollutant source assessment required in Attachment C contained in the General Permit.

Risk Level 2 dischargers must analyze samples for:

- i. pH and turbidity;
- ii. any parameters indicating the presence of pollutants identified in the pollutant source assessment required in Attachment D contained in the General Permit, and
- iii. any additional parameters for which monitoring is required by the Regional Water Board.

Risk Level 3 dischargers must analyze samples for:

- i. pH, turbidity and SSC;
- ii. any parameters indicating the presence of pollutants identified in the pollutant source assessment required in Attachment E contained in the General Permit, and
- iii. any additional parameters for which monitoring is required by the Regional Water Board.

## **2. Linear Monitoring and Sampling Requirements**

Attachment A, establishes minimum monitoring and reporting requirements for all LUPs. It establishes different monitoring requirements depending on project complexity and risk to water quality. The monitoring requirements for Type 1 LUPs are less than Type 2 & 3 projects because Type 1 projects have a lower potential to impact water quality.

A discharger shall prepare a monitoring program prior to the start of construction and immediately implement the program at the start of construction for LUPs. The monitoring program must be implemented at the appropriate level to protect water quality at all times throughout the life of the project.

### **a. Type 1 LUP Monitoring Requirements**

A discharger must conduct daily visual inspections of Type 1 LUPs during working hours while construction activities are occurring. Inspections are to be conducted by qualified personnel and can be conducted in conjunction with other daily activities. Inspections will be conducted to ensure the BMPs are adequate, maintained, and in place at the end of the construction day. The discharger will revise the SWPPP, as appropriate, based on the results of the daily inspections. Inspections can be discontinued in non-active construction areas where soil disturbing activities have been completed and final stabilization has been achieved (e.g., trench has been paved, substructures have been installed, and successful final vegetative cover or other stabilization criteria have been met).

A discharger shall implement the monitoring program for inspecting Type 1 LUPs. This program requires temporary and permanent stabilization BMPs after active construction is completed. Inspection activities will continue until adequate permanent stabilization has been established and will continue in areas where re-vegetation is chosen until minimum vegetative coverage has been established. Photographs shall be taken during site inspections and submitted to the State Water Board.

### **b. Type 2 & 3 LUP Monitoring Requirements**

A discharger must conduct daily visual inspections of Type 2 & 3 LUPs during working hours while construction activities are occurring. Inspections are to be conducted by qualified personnel and can be in conjunction with other daily activities.

All dischargers of Type 2 & 3 LUPs are required to conduct inspections by qualified personnel of the construction site during normal working hours prior to all anticipated storm events and after actual storm events. During extended storm events, the discharger shall conduct inspections during normal working hours for each 24-hour period. Inspections can be discontinued in non-active construction areas where soil disturbing activities have been completed and final stabilization has been achieved (e.g., trench has been paved, substructures installed, and successful vegetative cover or other stabilization criteria have been met).

The goals of these inspections are (1) to identify areas contributing to a storm water discharge; (2) to evaluate whether measures to reduce pollutant loadings identified in the SWPPP are adequate and properly installed and functioning in accordance with the terms of the General Permit; and (3) to determine whether additional control practices or corrective maintenance activities are needed. Equipment, materials, and workers must be available for rapid response to failures and emergencies. All corrective maintenance to BMPs shall be performed as soon as possible, depending upon worker safety.

All dischargers shall develop and implement a monitoring program for inspecting Type 2 & 3 LUPs that require temporary and permanent stabilization BMPs after active construction is completed. Inspections will be conducted to ensure the BMPs are adequate and maintained. Inspection activities will continue until adequate permanent stabilization has been established and will continue in areas where revegetation is chosen until minimum vegetative coverage has been established.

A log of inspections conducted before, during, and after the storm events must be maintained in the SWPPP. The log will provide the date and time of the inspection and who conducted the inspection. Photographs must be taken during site inspections and submitted to the State Water Board.

### **c. Sampling Requirements for all LUP Project Types**

LUPs are also subject to sampling and analysis requirements for visible pollutants (i.e., sedimentation/siltation, turbidity) and for non-visible pollutants.

Sampling for visible pollutants is required for Type 2 & 3 LUPs.

Non-visible pollutant monitoring is required for pollutants associated with construction sites and activities that (1) are not visually detectable in storm water discharges, and (2) are known or should be known to occur on the construction site, and (3) could cause or contribute to an exceedance of water quality objectives in the receiving waters. Sample collection for non-visible pollutants must only be required (1) during a storm event when pollutants associated with construction activities may be discharged with storm water runoff due to a spill, or in the event there was a breach, malfunction, failure, and/or leak of any BMP, and (2) when the discharger has failed to adequately clean the area of material and pollutants. Failure to implement appropriate BMPs will trigger the same sampling requirements as those required for a breach, malfunction and/or leak, or when the discharger has failed to implement appropriate BMPs prior to the next storm event.

Additional monitoring parameters may be required by the Regional Water Boards.

It is not anticipated that many LUPs will be required to collect samples for pollutants not visually detected in runoff due to the nature and character of the construction site and activities as previously described in this fact sheet. Most LUPs are constructed in urban areas with public access (e.g., existing roadways, road shoulders, parking areas, etc.). This raises a concern regarding the potential contribution of pollutants from vehicle use and/or from normal activities of the public (e.g., vehicle washing, landscape fertilization, pest spraying, etc.) in runoff from the project site. Since the dischargers are not the land

owners of the project area and are not able to control the presence of these pollutants in the storm water that runs through their projects, it is not the intent of this General Permit to require dischargers to sample for these pollutants. This General Permit does not require the discharger to sample for these types of pollutants except where the discharger has brought materials onsite that contain these pollutants and when a condition (e.g., breach, failure, etc.) described above occurs.

**3. Receiving Water Monitoring**

In order to ensure that receiving water limitations are met, discharges subject to numeric effluent limitations (i.e., Risk Level 3, LUP Type 3, and ATS with direct discharges into receiving waters) must also monitor the downstream receiving water(s) for turbidity, SSC, and pH (if applicable) when an NEL is exceeded.

**a. Bioassessment Monitoring**

This General Permit requires a bioassessment of receiving waters for dischargers of Risk Level 3 or LUP Type 3 construction projects equal to or larger than 30 acres with direct discharges into receiving waters. Benthic macroinvertebrate samples will be taken upstream and downstream of the site's discharge point in the receiving water. Bioassessments measure the quality of the stream by analyzing the aquatic life present. Higher levels of appropriate aquatic species tend to indicate a healthy stream; whereas low levels of organisms can indicate stream degradation. Active construction sites have the potential to discharge large amounts of sediment and pollutants into receiving waters. Requiring a bioassessment for large project sites, with the most potential to impact water quality, provides a snapshot of the health of the receiving water prior to initiation of construction activities. This snapshot can be used in comparison to the health of the receiving water after construction has commenced.

Each ecoregion (biologically and geographically related area) in the State has a specific yearly peak time where stream biota is in a stable and abundant state. This time of year is called an Index Period. The bioassessment requirements in this General Permit, requires benthic macroinvertebrate sampling within a sites index period. The State Water Board has developed a map designating index periods for the ecoregions in the State (see State Water Board Website).

This General Permit requires the bioassessment methods to be in accordance with the Surface Water Ambient Monitoring Program (SWAMP) in order to provide data consistency within the state as well as generate useable biological stream data.

**Table 6 - Receiving Water Monitoring Requirements**

	Receiving Water Monitoring Parameters
Risk Level 1 /LUP Type 1	not required
Risk Level 2 / LUP Type 2	not required
Risk Level 3 / LUP Type 3	If NEL exceeded: pH (if applicable), turbidity, and SSC. Bioassessment for sites 30 acres or larger.

**4. Reporting Requirements**

**a. NEL Violation Report**

All Risk Level 3 and LUP Type 3 dischargers must electronically submit all storm event sampling results to the State and Regional Water Boards, via SMARTS, no later than 5 days after the conclusion of the storm event. The purpose of the electronic filing of the NEL Violation Report is to 1) inform stakeholder agencies and organizations and the general public, and 2) notify the State and Regional Water Boards of

the exceedance so that they can determine whether any follow-up (e.g., inspection, enforcement, etc.) is necessary to bring the site into compliance.

In the event that an applicable NEL has been exceeded during a storm event equal to or larger than the Compliance Storm Event, Risk level 3/LUP Type 3 dischargers shall report the on-site rain gauge reading and nearby governmental rain gauge readings for verification. Specifically, the NEL Exceedance Report is required to contain:

- the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit are to be reported as "less than the method detection limit or <MDL");
- the date, place, and time of sampling;
- any visual observation (inspections);
- any measurements, including precipitation; and
- a description of the current BMPs associated with the effluent sample that exceeded the NEL and any proposed corrective actions taken.

#### **b. NAL Exceedance Report**

All Risk Level 3 and LUP Type 3 dischargers must electronically submit all storm event sampling results to the State and Regional Water Boards, via the electronic data system, no later than 5 days after the conclusion of the storm event. In the event that any effluent sample exceeds an applicable NAL, all Risk Level 2 and LUP Type 2 dischargers must electronically submit all storm event sampling results to the State and Regional Water Boards no later than 10 days after the conclusion of the storm event. The Regional Water Boards have the authority to require the submittal of an NAL Exceedance Report.

Specifically, the NAL Exceedance Report is required to contain:

- the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit are to be reported as "less than the method detection limit or <MDL");
- the date, place, and time of sampling;
- any visual observation (inspections);
- any measurements, including precipitation; and
- a description of the current BMPs associated with the effluent sample that exceeded the NAL and any proposed corrective actions taken.

#### **c. Annual Report**

All dischargers must prepare and electronically submit an annual report no later than September 1 of each year using the Storm water Multi-Application Reporting and Tracking System (SMARTS). The Annual Report must include a summary and evaluation of all sampling and analysis results, original laboratory reports, chain of custody forms, a summary of all corrective actions taken during the compliance year, and identification of any compliance activities or corrective actions that were not implemented.

## 5. Record Keeping

According to 40 C.F.R. Parts 122.21(p) and 122.41(j), the discharger is required to retain paper or electronic copies of all records required by this General Permit for a period of at least three years from the date generated or the date submitted to the State Water Board or Regional Water Boards. A discharger must retain records for a period beyond three years as directed by Regional Water Board.

## J. Risk Determination

### 1. Traditional Projects

#### a. Overall Risk Determination

There are two major requirements related to site planning and risk determination in this General Permit. The project's overall risk is broken up into two elements – (1) project sediment risk (the relative amount of sediment that can be discharged, given the project and location details) and (2) receiving water risk (the risk sediment discharges pose to the receiving waters).

#### Project Sediment Risk:

Project Sediment Risk is determined by multiplying the R, K, and LS factors from the Revised Universal Soil Loss Equation (RUSLE) to obtain an estimate of project-related bare ground soil loss expressed in tons/acre. The RUSLE equation is as follows:

$$A = (R)(K)(LS)(C)(P)$$

Where: A = the rate of sheet and rill erosion

R = rainfall-runoff erosivity factor

K = soil erodibility factor


LS = length-slope factor

C = cover factor (erosion controls)

P = management operations and support practices (sediment controls)

The C and P factors are given values of 1.0 to simulate bare ground conditions.

There is a map option and a manual calculation option for determining soil loss. For the map option, the R factor for the project is calculated using the online calculator at <http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm>. The product of K and LS are shown on Figure 1. To determine soil loss in tons per acre, the discharger multiplies the R factor times the value for K times LS from the map.

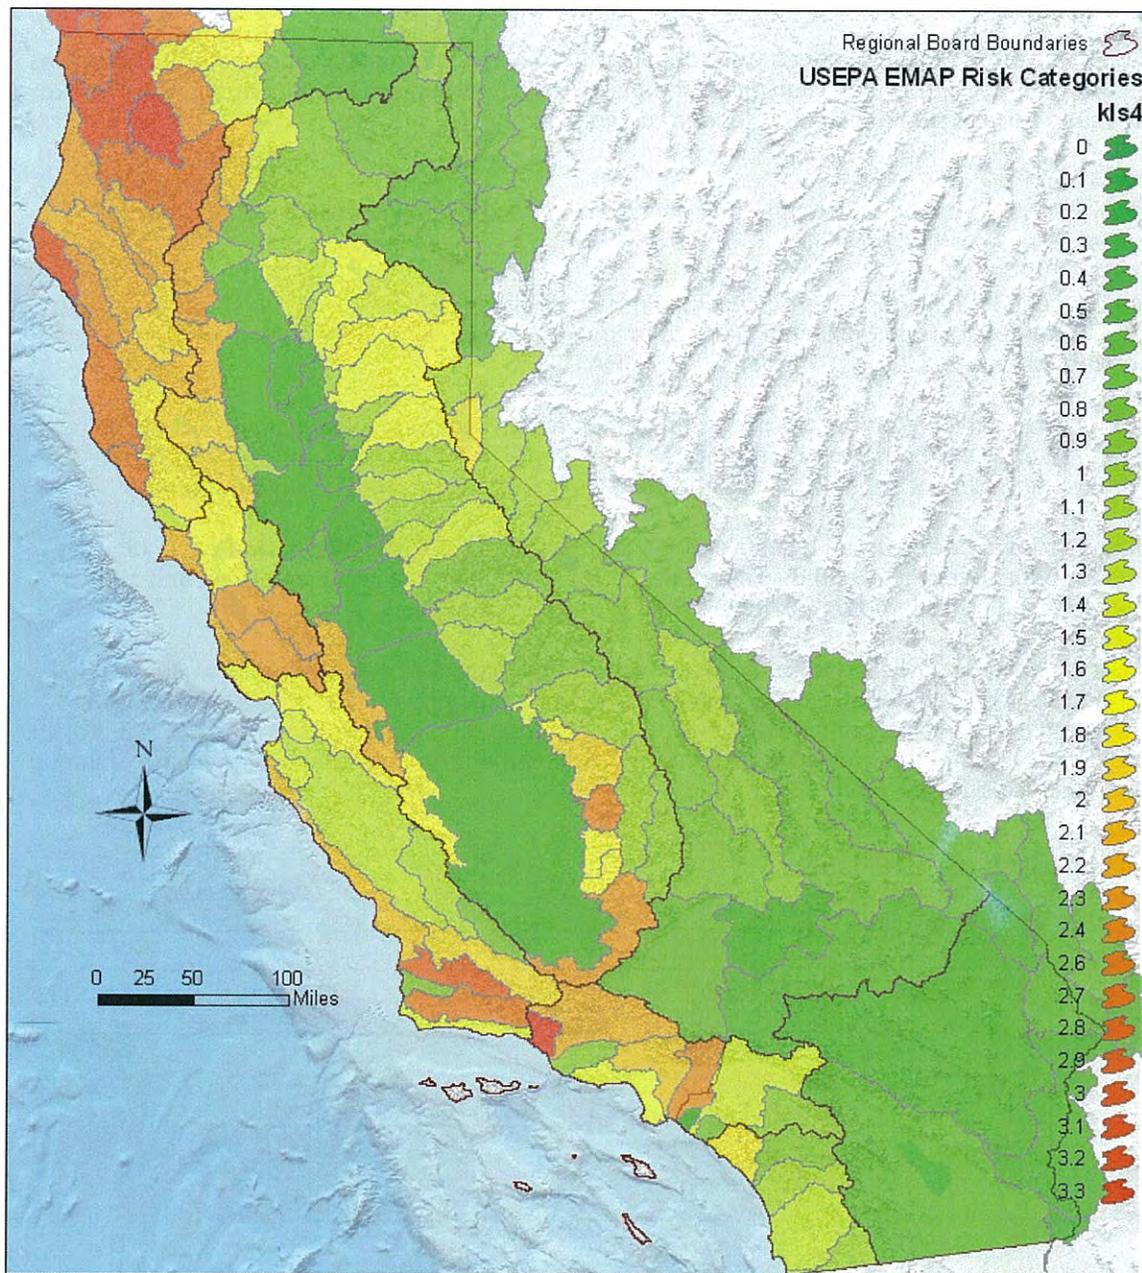

State Water Resources Control Board, January 15, 2008

Figure 1 -Statewide Map of K \* LS

For the manual calculation option, the R factor for the project is calculated using the online calculator at <http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm>. The K and LS factors are determined using Appendix 1.

Soil loss of less than 15 tons/acre is considered **low** sediment risk.  
 Soil loss between 15 and 75 tons/acre is **medium** sediment risk.  
 Soil loss over 75 tons/acre is considered **high** sediment risk.

The soil loss values and risk categories were obtained from mean and standard deviation RKLS values from the USEPA EMAP program. High risk is the mean RKLS value plus two standard deviations. Low risk is the mean RKLS value minus two standard deviations.

**Receiving Water Risk:**

Receiving water risk is based on whether a project drains to a sediment-sensitive waterbody. A sediment-sensitive waterbody is either

- on the most recent 303d list for waterbodies impaired for sediment;
- has a USEPA-approved Total Maximum Daily Load implementation plan for sediment; **or**
- has the beneficial uses of COLD, SPAWN, and MIGRATORY.

A project that meets at least one of the three criteria has a high receiving water risk. A list of sediment-sensitive waterbodies will be posted on the State Water Board’s website. It is anticipated that an interactive map of sediment sensitive water bodies in California will be available in the future.

The Risk Levels have been altered by eliminating the possibility of a Risk Level 4, and expanding the constraints for Risk Levels 1, 2, and 3. Therefore, projects with high receiving water risk and high sediment risk will be considered a Risk Level 3 risk to water quality.

In response to public comments, the Risk Level requirements have also been changed such that Risk Level 1 projects will be subject to minimum BMP and visual monitoring requirements, Risk Level 2 projects will be subject to NALs and some additional monitoring requirements, and Risk Level 3 projects will be subject to NELs, and more rigorous monitoring requirements such as receiving water monitoring and in some cases bioassessment.

**Table 7 - Combined Risk Level Matrix**

Combined Risk Level Matrix			
Receiving Water Risk		Sediment Risk	
		Low Medium	High
	Low	Level 1	Level 2
High	Level 2		Level 3

**b. Effluent Standards**

All dischargers are subject to the narrative effluent limitations specified in the General Permit. The narrative effluent limitations require storm water discharges associated with construction activity to meet all applicable provisions of Sections 301 and 402 of the CWA. These provisions require controls of pollutant discharges that utilize BAT and BCT to reduce pollutants and any more stringent controls necessary to meet water quality standards.

Risk Level 2, and 3 dischargers are subject to numeric effluent standards comparable to the project’s risk to water quality. Risk Level 2 dischargers that pose a medium risk to water quality are subject to technology-based NALs for pH and turbidity. Risk Level 3 dischargers that pose a high risk to water quality are subject to technology-based NALs and technology-based NELs for pH and turbidity.

### **c. Good Housekeeping**

Proper handling and managing of construction materials can help minimize threats to water quality. The discharger must consider good housekeeping measures for: construction materials, waste management, vehicle storage & maintenance, landscape materials, and potential pollutant sources. Examples include; conducting an inventory of products used, implementing proper storage & containment, and properly cleaning all leaks from equipment and vehicles.

### **d. Non-Storm Water Management**

Non-storm water discharges directly connected to receiving waters or the storm drain system have the potential to negatively impact water quality. The discharger must implement measures to control all non-storm water discharges during construction, and from dewatering activities associated with construction. Examples include; properly washing vehicles in contained areas, cleaning streets, and minimizing irrigation runoff.

### **e. Erosion Control**

The best way to minimize the risk of creating erosion and sedimentation problems during construction is to disturb as little of the land surface as possible by fitting the development to the terrain. When development is tailored to the natural contours of the land, little grading is necessary and, consequently, erosion potential is lower.<sup>14</sup> Other effective erosion control measures include: preserving existing vegetation where feasible, limiting disturbance, and stabilizing and re-vegetating disturbed areas as soon as possible after grading or construction activities. Particular attention must be paid to large, mass-graded sites where the potential for soil exposure to the erosive effects of rainfall and wind is great and where there is potential for significant sediment discharge from the site to surface waters. Until permanent vegetation is established, soil cover is the most cost-effective and expeditious method to protect soil particles from detachment and transport by rainfall. Temporary soil stabilization can be the single most important factor in reducing erosion at construction sites. The discharger is required to consider measures such as: covering disturbed areas with mulch, temporary seeding, soil stabilizers, binders, fiber rolls or blankets, temporary vegetation, and permanent seeding. These erosion control measures are only examples of what should be considered and should not preclude new or innovative approaches currently available or being developed. Erosion control BMPs should be the primary means of preventing storm water contamination, and sediment control techniques should be used to capture any soil that becomes eroded.<sup>13</sup>

Risk Level 3 dischargers pose a higher risk to water quality and are therefore additionally required to ensure that post-construction soil loss is equivalent to or less than the pre-construction levels.

### **f. Sediment Control**

Sediment control BMPs should be the secondary means of preventing storm water contamination. When erosion control techniques are ineffective, sediment control techniques should be used to capture any soil that becomes eroded. The discharger is required to consider perimeter control measures such as: installing silt fences or placing straw wattles below slopes. These sediment control measures are only examples of what should be considered and should not preclude new or innovative approaches currently available or being developed.

Because Risk Level 2 and 3 dischargers pose a higher risk to water quality, additional requirements for the application of sediment controls are imposed on these projects. This General Permit also authorizes the Regional Water Boards to require Risk Level 3 dischargers to implement additional site-specific

---

<sup>13</sup> U.S. Environmental Protection Agency. 2007. Developing Your Storm Water Pollution Prevention Plan: A Guide for Construction Sites.

sediment control requirements if the implementation of other erosion or sediment controls are not adequately protecting the receiving waters.

**g. Run-on and Runoff Control**

Inappropriate management of run-on and runoff can result in excessive physical impacts to receiving waters from sediment and increased flows. The discharger is required to manage all run-on and runoff from a project site. Examples include: installing berms and other temporary run-on and runoff diversions.

Risk Level 1 dischargers with lower risks to impact water quality are not subject to the run-on and runoff control requirements unless an evaluation deems them necessary or visual inspections show that such controls are required.

**h. Inspection, Maintenance and Repair**

All measures must be periodically inspected, maintained and repaired to ensure that receiving water quality is protected. Frequent inspections coupled with thorough documentation and timely repair is necessary to ensure that all measures are functioning as intended.

**i. Rain Event Action Plan (REAP)**

A Rain Event Action Plan (REAP) is a written document, specific for each rain event. A REAP should be designed that when implemented it protects all exposed portions of the site within 48 hours of any likely precipitation event forecast of 50% or greater probability.

This General Permit requires Risk Level 2 and 3 dischargers to develop and implement a REAP designed to protect all exposed portions of their sites within 48 hours prior to any likely precipitation event. The REAP requirement is designed to ensure that the discharger has adequate materials, staff, and time to implement erosion and sediment control measures that are intended to reduce the amount of sediment and other pollutants generated from the active site. A REAP must be developed when there is likely a forecast of 50% or greater probability of precipitation in the project area. (The National Oceanic and Atmospheric Administration (NOAA) defines a chance of precipitation as a probability of precipitation of 30% to 50% chance of producing precipitation in the project area.<sup>14</sup> NOAA defines the probability of precipitation (PoP) as the likelihood of occurrence (expressed as a percent) of a measurable amount (0.01 inch or more) of liquid precipitation (or the water equivalent of frozen precipitation) during a specified period of time at any given point in the forecast area.) Forecasts are normally issued for 12-hour time periods. Descriptive terms for uncertainty and aerial coverage are used as follows:

**Table 8 -National Oceanic and Atmospheric Administration (NOAA) Definition of Probability of Precipitation (PoP)**

PoP	Expressions of Uncertainty	Aerial Coverage
0%	none used	none used
10%	none used	isolated
20%	slight chance	isolated
30-50%	chance	scattered

<sup>14</sup> <http://www.crh.noaa.gov/lot/severe/wxterms.php>.

60-70%	likely	numerous
80-100%	none used	none used

The discharger must obtain the precipitation forecast information from the National Weather Service Forecast Office (<http://www.srh.noaa.gov/>).

## 2. Linear Projects

### a. Linear Risk Determination

LUPs vary in complexity and water quality concerns based on the type of project. This General Permit has varying application requirements based on the project's risk to water quality. Factors that lead to the characterization of the project include location, sediment risk, and receiving water risk.

Based on the location and complexity of a project area or project section area, LUPs are separated into project types. As described below, LUPs have been categorized into three project types.

#### i. Type 1 LUPs

Type 1 LUPs are those construction projects where:

- (1) 70 percent or more of the construction activity occurs on a paved surface and where areas disturbed during construction will be returned to preconstruction conditions or equivalent protection established at the end of the construction activities for the day, or
- (2) greater than 30 percent of construction activities occur within the non-paved shoulders or land immediately adjacent to paved surfaces, or where construction occurs on unpaved improved roads, including their shoulders or land immediately adjacent to them where:

Areas disturbed during construction will be returned to pre-construction conditions or equivalent protection established at the end of the construction activities for the day to minimize the potential for erosion and sediment deposition, and

Areas where established vegetation was disturbed during construction will be stabilized and re-vegetated by the end of project. When required, adequate temporary stabilization Best Management Practices (BMPs) will be installed and maintained until vegetation is established to meet minimum cover requirements established in this General Permit for final stabilization.

Type 1 LUPs typically do not have a high potential to impact storm water quality because (1) these construction activities are not typically conducted during a rain event, (2) these projects are normally constructed over a short period of time<sup>15</sup>, minimizing the duration that pollutants could potentially be exposed to rainfall; and (3) disturbed soils such as those from trench excavation are required to be hauled away, backfilled into the trench, and/or covered (e.g., metal plates, pavement, plastic covers over spoil piles) at the end of the construction day.

---

<sup>15</sup> Short period of time refers to a project duration of weeks to months, but typically less than one year in duration.

Type 1 LUPs are determined during the risk assessment found in Attachment A.1 to be 1) low sediment risk and low receiving water risk; 2) low sediment risk and medium receiving water risk; and 3) medium sediment risk and low receiving water risk.

This General Permit requires the discharger to ensure a SWPPP is developed for these construction activities that is specific to project type, location and characteristics.

**ii. Type 2 LUPs:**

Type 2 projects are determined to have a combination of High, Medium, and Low project sediment risk along with High, Medium, and Low receiving water risk. Like Type 1 projects, Type 2 projects are typically constructed over a short period of time. However, these projects have a higher potential to impact water quality because they:

- (1) typically occur outside the more urban/developed areas;
- (2) have larger areas of soil disturbance that are not closed or restored at the end of the day;
- (3) may have onsite stockpiles of soil, spoil and other materials;
- (4) cross or occur in close proximity to a wide variety of sensitive resources that may include, but are not limited to, steep topography and/or water bodies; and
- (5) have larger areas of disturbed soils that may be exposed for a longer time interval before final stabilization, cleanup and/or reclamation occurs.

This General Permit requires the discharger to develop and implement a SWPPP for these construction activities that are specific for project type, location and characteristics.

**iii. Type 3 LUPs:**

Type 3 projects are determined to have a combination of High and Medium project sediment risk along with High and Medium receiving water risk. Similar to Type 2 projects, Type 3 projects have a higher potential to impact water quality because they:

- (1) typically occur outside of the more urban/developed areas;
- (2) have larger areas of soil disturbance that are not closed or restored at the end of the day;
- (3) may have onsite stockpiles of soil, spoil and other materials;
- (4) cross or occur in close proximity to a wide variety of sensitive resources that may include, but are not limited to, steep topography and/or water bodies; and
- (5) have larger areas of disturbed soils that may be exposed for a longer time interval before final stabilization, cleanup and/or reclamation occurs.

This General Permit requires the discharger to develop and implement a SWPPP for these construction activities that are specific for project type, location, and characteristics.

**b. Linear Effluent Standards**

All LUPs are subject to the narrative effluent limitations specified in the General Permit.

Type 2 and 3 LUPs are subject to NELs comparable to the project type's risk to water quality. Type 2 projects that pose an intermediate risk to water quality are subject to technology-based NALs for pH and turbidity. Type 3 projects posing a high risk to water quality are subject to technology-based NALs and NELs for pH and turbidity.

**c. Linear Good Housekeeping**

Improper use and handling of construction materials could potentially cause a threat to water quality. In order to ensure proper site management of these construction materials, all LUP dischargers must comply with a minimum set of Good Housekeeping measures specified in Attachment A of this General Permit.

**d. Linear Non-Storm Water Management**

In order to ensure control of all non-storm water discharges during construction, all LUP dischargers must comply with the Non-Storm Water Management measures specified in Attachment A of this General Permit.

**e. Linear Erosion Control**

This General Permit requires all LUP dischargers to implement effective wind erosion control measures, and soil cover for inactive areas. Type 3 LUPs posing a higher risk to water quality are additionally required to ensure the post-construction soil loss is equivalent to or less than the pre-construction levels.

**f. Linear Sediment Control**

In order to ensure control and containment of all sediment discharges, all LUP dischargers must comply with the general Sediment Control measures specified in Attachment A or this General Permit. Additional requirements for sediment controls are imposed on Type 2 & 3 LUPs due to their higher risk to water quality.

**g. Linear Run-on and Runoff Control**

Discharges originating outside of a project's perimeter and flowing onto the property can adversely affect the quantity and quality of discharges originating from a project site. In order to ensure proper management of run-on and runoff, all LUPs must comply with the run-on and runoff control measures specified in Attachment A of this General Permit. Due to the lower risk of impacting water quality, Type 1 LUPs are not required to implement run-on and runoff controls unless deemed necessary by the discharger.

**h. Linear Inspection, Maintenance and Repair**

Proper inspection, maintenance, and repair activities are important to ensure the effectiveness of on-site measures to control water quality. In order to ensure that inspection, maintenance, and repair activities are adequately performed, the all LUP dischargers are required to comply with the Inspection, Maintenance, and Repair requirements specified in Attachment A of this General Permit.

## K. ATS<sup>16</sup> Requirements

There are instances on construction sites where traditional erosion and sediment controls do not effectively control accelerated erosion. Under such circumstances, or under circumstances where storm water discharges leaving the site may cause or contribute to an exceedance of a water quality standard, the use of an Active Treatment System (ATS) may be necessary. Additionally, it may be appropriate to use an ATS when site constraints inhibit the ability to construct a correctly sized sediment basin, when clay and/or highly erosive soils are present, or when the site has very steep or long slope lengths.<sup>17</sup>

Although treatment systems have been in use in some form since the mid-1990s, the ATS industry in California is relatively young, and detailed regulatory standards have not yet been developed. Many developers are using these systems to treat storm water discharges from their construction sites. The new ATS requirements set forth in this General Permit are based on those in place for small wastewater treatment systems, ATS regulations from the Central Valley Regional Water Quality Control Board (September 2005 memorandum "2005/2006 Rainy Season – Monitoring Requirements for Storm Water Treatment Systems that Utilize Chemical Additives to Enhance Sedimentation"), the Construction Storm Water Program at the State of Washington's Department of Ecology, as well as recent advances in technology and knowledge of coagulant performance and aquatic safety.

The effective design of an ATS requires a detailed survey and analysis of site conditions. With proper planning, ATS performance can provide exceptional water quality discharge and prevent significant impacts to surface water quality, even under extreme environmental conditions.

These systems can be very effective in reducing the sediment in storm water runoff, but the systems that use additives/polymers to enhance sedimentation also pose a potential risk to water quality (e.g., operational failure, equipment failure, additive/polymer release, etc.). The State Water Board is concerned about the potential acute and chronic impacts that the polymers and other chemical additives may have on fish and aquatic organisms if released in sufficient quantities or concentrations. In addition to anecdotal evidence of polymer releases causing aquatic toxicity in California, the literature supports this concern.<sup>18</sup> For example, cationic polymers have been shown to bind with the negatively charged gills of fish, resulting in mechanical suffocation.<sup>19</sup> Due to the potential toxicity impacts, which may be caused by the release of additives/polymers into receiving waters, this General Permit establishes residual polymer monitoring and toxicity testing requirements have been established in this General Permit for discharges from construction sites that utilize an ATS in order to protect receiving water quality and beneficial uses.

The primary treatment process in an ATS is coagulation/flocculation. ATS's operate on the principle that the added coagulant is bound to suspended sediment, forming floc, which is gravitationally settled in tanks or a basin, or removed by sand filters. A typical installation utilizes an injection pump upstream from the clarifier tank, basin, or sand filters, which is electronically metered to both flow rate and suspended solids level of the influent, assuring a constant dose. The coagulant mixes and reacts with the influent, forming a dense floc. The floc may be removed by gravitational setting in a clarifier tank or basin, or by filtration. Water from the clarifier tank, basin, or sand filters may be routed through cartridge(s) and/or bag filters for final polishing. Vendor-specific systems use various methods of dose control, sediment/floc removal, filtration, etc., that are detailed in project-specific documentation. The

<sup>16</sup> An ATS is a treatment system that employs chemical coagulation, chemical flocculation, or electrocoagulation in order to reduce turbidity caused by fine suspended sediment.

<sup>17</sup> Pitt, R., S. Clark, and D. Lake. 2006. Construction Site Erosion and Sediment Controls: Planning, Design, and Performance. DEStech Publications. Lancaster, PA. 370pp.

<sup>18</sup> Romøen, K., B. Thu, and Ø. Evensen. 2002. Immersion delivery of plasmid DNA II. A study of the potentials of a chitosan based delivery system in rainbow trout (*Oncorhynchus mykiss*) fry. *Journal of Controlled Release* 85: 215-225.

<sup>19</sup> Bullock, G., V. Blazer, S. Tsukuda, and S. Summerfelt. 2000. Toxicity of acidified chitosan for cultured rainbow trout (*Oncorhynchus mykiss*). *Aquaculture* 185:273-280.

particular coagulant/flocculant to be used for a given project is determined based on the water chemistry of the site because the coagulants are specific in their reactions with various types of sediments. Appropriate selection of dosage must be carefully matched to the characteristics of each site.

ATS's are operated in two differing modes, either Batch or Flow-Through. Batch treatment can be defined as Pump-Treat-Hold-Test-Release. In Batch treatment, water is held in a basin or tank, and is not discharged until treatment is complete. Batch treatment involves holding or recirculating the treated water in a holding basin or tank(s) until treatment is complete or the basin or storage tank(s) is full. In Flow-Through treatment, water is pumped into the ATS directly from the runoff collection system or storm water holding pond, where it is treated and filtered as it flows through the system, and is then directly discharged. "Flow-Through Treatment" is also referred to as "Continuous Treatment."

### 1. Effluent Standards

This General Permit establishes NELs for discharges from construction sites that utilize an ATS. These systems lend themselves to NELs for turbidity and pH because of their known reliable treatment. Advanced systems have been in use in some form since the mid-1990s. An ATS is considered reliable, can consistently produce a discharge of less than 10 NTU, and has been used successfully at many sites in several states since 1995 to reduce turbidity to very low levels.<sup>20</sup>

This General Permit contains "compliance storm event" exceptions from the technology-based NELs for ATS discharges. The rationale is that technology-based requirements are developed assuming a certain design storm. In the case of ATS the industry-standard design storm is 10-year, 24-hour (as stated in Attachment F of this General Permit), so the compliance storm event has been established as the 10-year 24-hour event as well to provide consistency.

### 2. Training

Operator training is critical to the safe and efficient operation and maintenance of the ATS, and to ensure that all State Water Board monitoring and sampling requirements are met. The General Permit requires that all ATS operators have training specific to using ATS's liquid coagulants.

## L. Post-Construction Requirements

Under past practices, new and redevelopment construction activities have resulted in modified natural watershed and stream processes. This is caused by altering the terrain, modifying the vegetation and soil characteristics, introducing impervious surfaces such as pavement and buildings, increasing drainage density through pipes and channels, and altering the condition of stream channels through straightening, deepening, and armoring. These changes result in a drainage system where sediment transport capacity is increased and sediment supply is decreased. A receiving channel's response is dependent on dominant channel materials and its stage of adjustment.


Construction activity can lead to impairment of beneficial uses in two main ways. First, during the actual construction process, storm water discharges can negatively affect the chemical, biological, and physical properties of downstream receiving waters. Due to the disturbance of the landscape, the most likely pollutant is sediment, however pH and other non-visible pollutants are also of great concern. Second, after most construction activities are completed at a construction site, the finished project may result in significant modification of the site's response to precipitation. New development and redevelopment

---

<sup>20</sup> Currier, B., G. Minton, R. Pitt, L. Roesner, K. Schiff, M. Stenstrom, E. Strassler, and E. Strecker. 2006. The Feasibility of Numeric Effluent Limits Applicable to Discharges of Storm Water Associated with Municipal, Industrial and Construction Activities.

projects have almost always resulted in permanent post-construction water quality impacts because more precipitation ends up as runoff and less precipitation is intercepted, evapotranspired, and infiltrated.

General Permit 99-08-DWQ required the SWPPP to include a description of all post-construction BMPs on a site and a maintenance schedule. An effective storm water management strategy must address the full suite of storm events (water quality, channel protection, overbank flood protection, extreme flood protection) (Figure 2).

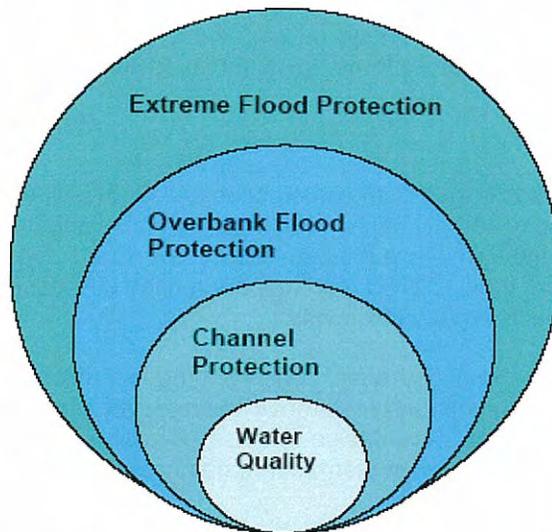

**Figure 2 - Suite of Storm Events**

The post-construction storm water performance standards in this General Permit specifically address water quality and channel protection events. Overbank flood protection and extreme flood protection events are traditionally dealt with in local drainage and flood protection ordinances. However, measures in this General Permit to address water quality and channel protection also reduce overbank and extreme flooding impacts. This General Permit aims to match post-construction runoff to pre-construction runoff for the 85<sup>th</sup> percentile storm event, which not only reduces the risk of impact to the receiving water's channel morphology but also provides some protection of water quality.

This General Permit clarifies that its runoff reduction requirements only apply to projects that lie outside of jurisdictions covered by a Standard Urban Storm water Management Plan (SUSMP) (or other more protective) post-construction requirements in either Phase I or Phase II permits.

Figures 3 and 4, below, show the General Permit enrollees (to Order 99-08-DWQ, as of March 10, 2008) overlaid upon a map with SUSMP (or more protective) areas in blue and purple. Areas without blue or purple indicate where the General Permit's runoff reduction requirements would actually apply.

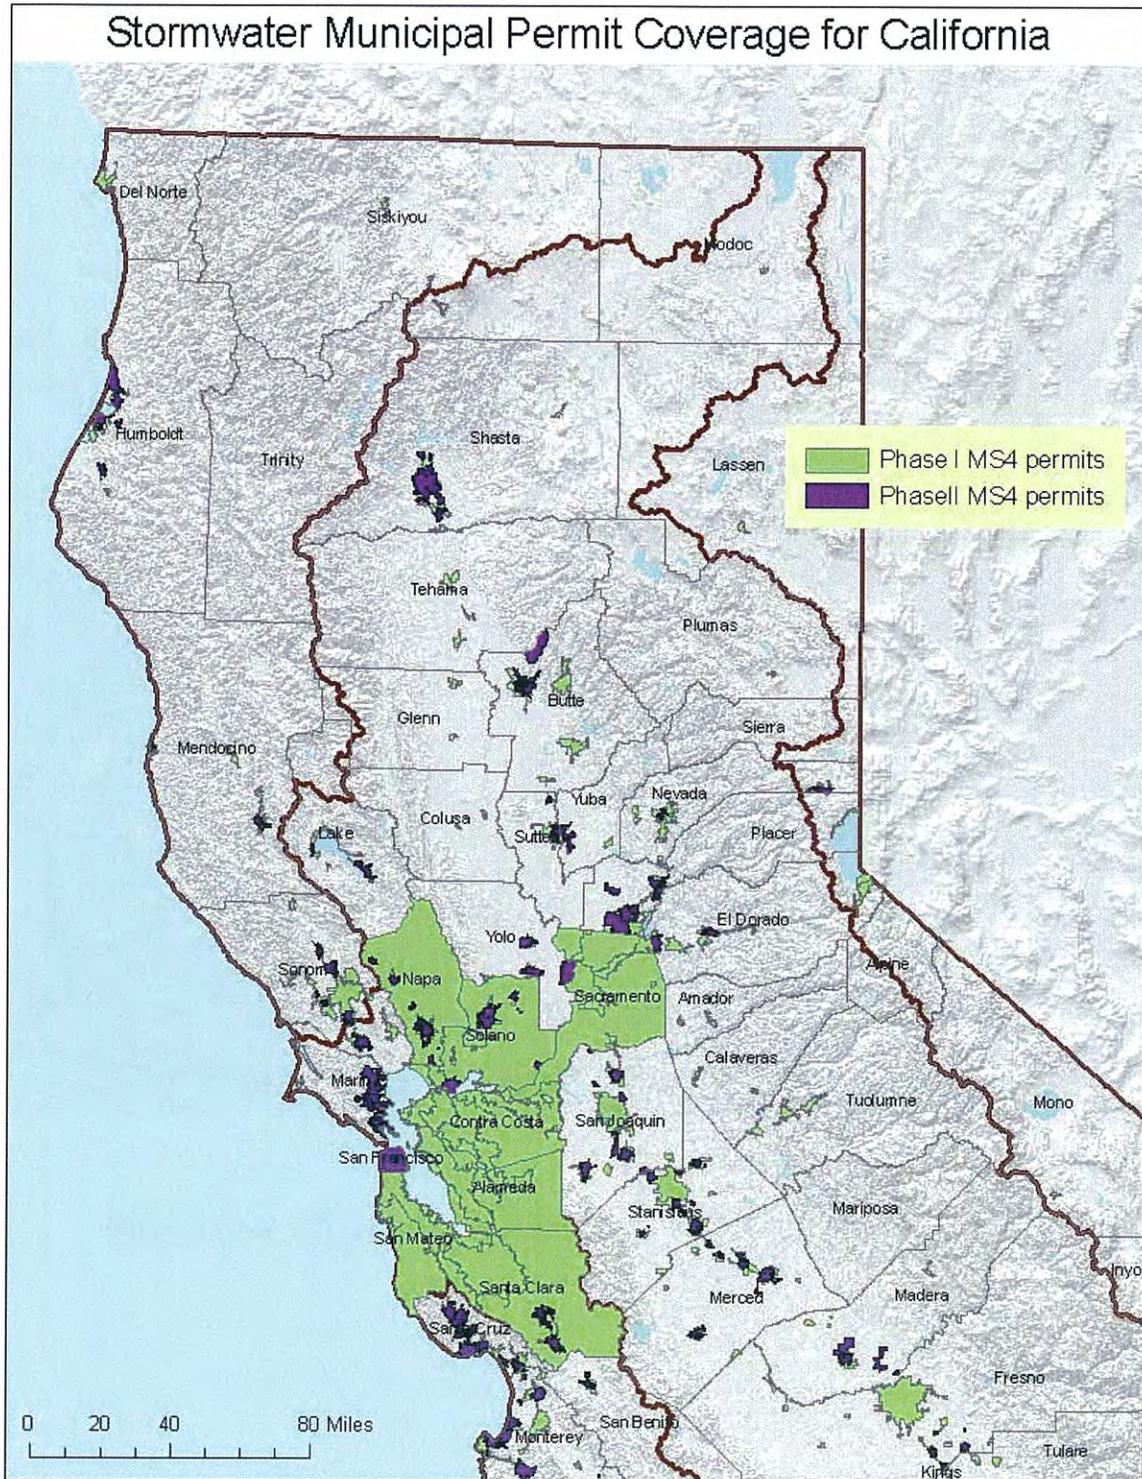


Figure 3 - Northern CA (2009) Counties / Cities With SUSMP-Plus Coverage



Figure 4 - Southern CA (2009) Counties / Cities With SUSMP-Plus Coverage

**Water Quality:**

This General Permit requires dischargers to replicate the pre-project runoff water balance (defined as the amount of rainfall that ends up as runoff) for the smallest storms up to the 85<sup>th</sup> percentile storm event, or the smallest storm event that generates runoff, whichever is larger. Contemporary storm water management generally routes these flows directly to the drainage system, increasing pollutant loads and potentially causing adverse effects on receiving waters. These smaller water quality events happen much more frequently than larger events and generate much higher pollutant loads on an annual basis. There are other adverse hydrological impacts that result from not designing according to the site's pre-construction water balance. In Maryland, Klein<sup>21</sup> noted that baseflow decreases as the extent of urbanization increases. Ferguson and Suckling<sup>22</sup> noted a similar relation in watersheds in Georgia. On Long Island, Spinello and Simmons<sup>23</sup> noted substantial decreases in base flow in intensely urbanized watersheds.

The permit emphasizes runoff reduction through on-site storm water reuse, interception, evapotranspiration and infiltration through non-structural controls and conservation design measures (e.g., downspout disconnection, soil quality preservation/enhancement, interceptor trees). Employing these measures close to the source of runoff generation is the easiest and most cost-effective way to comply with the pre-construction water balance standard. Using low-tech runoff reduction techniques close to the source is consistent with a number of recommendations in the literature.<sup>24</sup> In many cases, BMPs implemented close to the source of runoff generation cost less than end-of the pipe measures.<sup>25</sup> Dischargers are given the option of using Appendix 2 to calculate the required runoff volume or a watershed process-based, continuous simulation model such as the EPA's Storm Water Management Model (SWMM) or Hydrologic Simulation Program Fortran (HSPF). Such methods used by the discharger will be reviewed by the Regional Water Board upon NOT application.

**Channel Protection:**

In order to address channel protection, a basic understanding of fluvial geomorphic concepts is necessary. A dominant paradigm in fluvial geomorphology holds that streams adjust their channel dimensions (width and depth) in response to long-term changes in sediment supply and bankfull discharge (1.5 to 2 year recurrence interval). The bankfull stage corresponds to the discharge at which channel maintenance is the most effective, that is, the discharge at which the moving sediment, forming or removing bars, forming or changing bends and meanders, and generally doing work that results in the average morphologic characteristics of channels.<sup>26</sup> Lane (1955 as cited in Rosgen 1996<sup>27</sup>) showed the generalized relationship between sediment load, sediment size, stream discharge and stream slope in Figure 5. A change in any one of these variables sets up a series of mutual adjustments in the companion variables with a resulting direct change in the physical characteristics of the stream channel.

---

<sup>21</sup> Klein 1979 as cited in Delaware Department of Natural Resources (DDNR). 2004. Green Technology: The Delaware Urban Runoff Management Approach. Dover, DE. 117 pp.

<sup>22</sup> Ferguson and Suckling 1990 as cited Delaware Department of Natural Resources (DDNR). 2004. Green Technology: The Delaware Urban Runoff Management Approach. Dover, DE. 117 pp.

<sup>23</sup> Center for Watershed Protection (CWP). 2000. The Practice of Watershed Protection: Techniques for protecting our nation's streams, lakes, rivers, and estuaries. Ellicott City, MD. 741 pp.

<sup>24</sup> Bay Area Storm Water Management Agencies Association (BASMAA). 1997. Start at the Source: Residential Site Planning and Design Guidance Manual for Storm Water Quality Protection. Palo Alto, CA;


McCuen, R.H. 2003 Smart Growth: hydrologic perspective. Journal of Professional Issues in Engineering Education and Practice. Vol (129), pp.151-154;

Moglen, G.E. and S. Kim. 2007. Impervious imperviousness-are threshold based policies a good idea? Journal of the American Planning Association, Vol 73 No. 2. pp 161-171.

<sup>25</sup> Delaware Department of natural Resources (DDNR). 2004. Green technology: The Delaware urban Runoff Management Approach. Dover, DE. 117 pp.

<sup>26</sup> Dunne, T and L.B. Leopold. 1978. Water in Environmental Planning. San Francisco W.H. Freeman and Company

<sup>27</sup> Rosgen, D.L. 1996. Applied River Morphology. Pagosa Springs. Wildland Hydrology

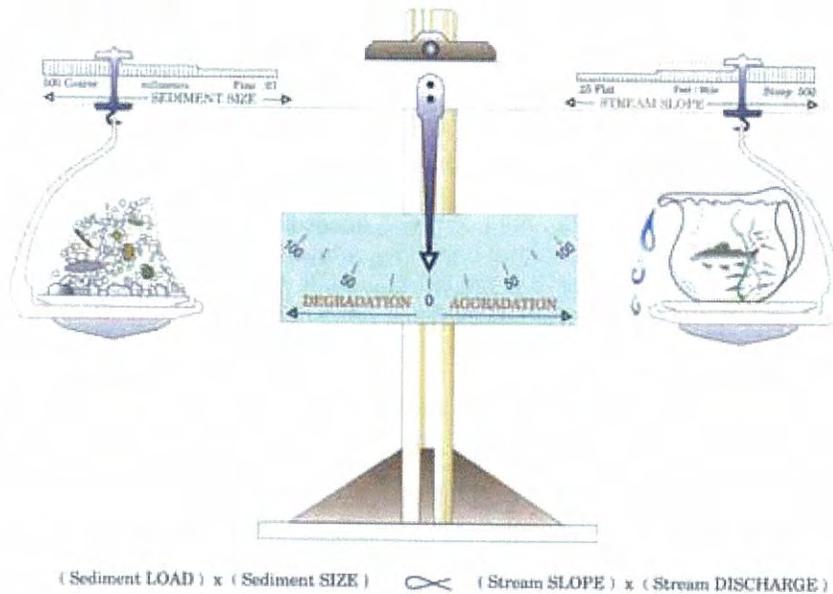

**Figure 5 - Schematic of the Lane Relationship**

After Lane (1955) as cited in Rosgen (1996)

Stream slope multiplied by stream discharge (the right side of the scale) is essentially an approximation of stream power, a unifying concept in fluvial geomorphology (Bledsoe 1999). Urbanization generally increases stream power and affects the resisting forces in a channel (sediment load and sediment size represented on the left side of the scale).

During construction, sediment loads can increase from 2 to 40,000 times over pre-construction levels.<sup>28</sup> Most of this sediment is delivered to stream channels during large, episodic rain events.<sup>29</sup> This increased sediment load leads to an initial aggradation phase where stream depths may decrease as sediment fills the channel, leading to a decrease in channel capacity and increase in flooding and overbank deposition. A degradation phase initiates after construction is completed.

Schumm et. al (1984) developed a channel evolution model that describes the series of adjustments from initial downcutting, to widening, to establishing new floodplains at lower elevations (Figure 6).

<sup>28</sup> Goldman S.J., K. Jackson, and T.A. Bursztynsky. 1986. Erosion and Sediment Control Handbook. McGraw Hill. San Francisco.

<sup>29</sup> Wolman 1967 as cited in Paul, M.P. and J.L. Meyer. 2001. Streams in the Urban Landscape. *Annu. Rev.Ecol. Syst.* 32: 333-365.

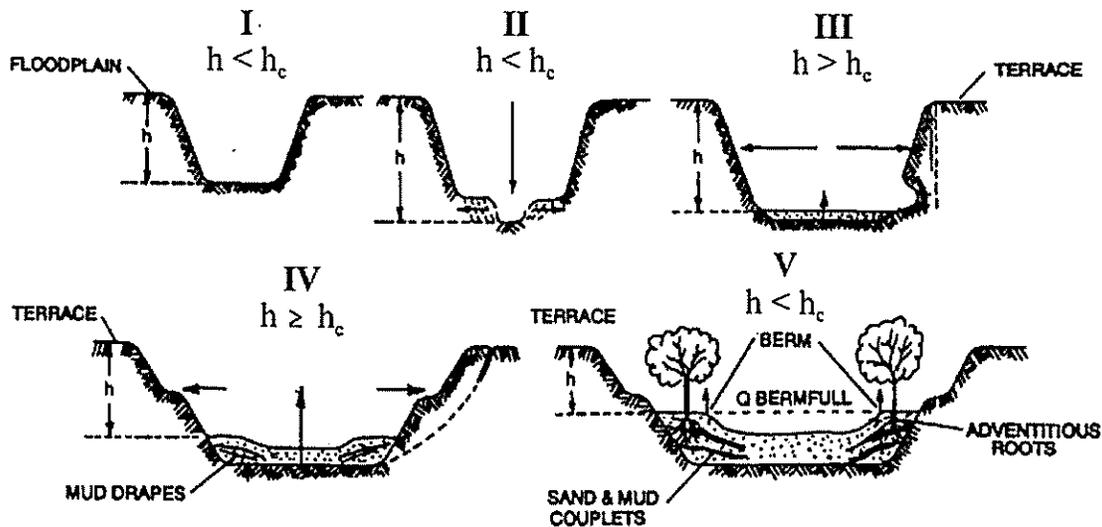


Figure 6 - Channel Changes Associated with Urbanization

After Incised Channel Evolution Sequence in Schumm et. al 1984

Channel incision (Stage II) and widening (Stages III and to a lesser degree, Stage IV) are due to a number of fundamental changes on the landscape. Connected impervious area and compaction of pervious surfaces increase the frequency and volume of bankfull discharges.<sup>30</sup> Increased drainage density (miles of stream length per square mile of watershed) also negatively impacts receiving stream channels.<sup>31</sup> Increased drainage density and hydraulic efficiency leads to an increase in the frequency and volume of bankfull discharges because the time of concentration is shortened. Flows from engineered pipes and channels are also often "sediment starved" and seek to replenish their sediment supply from the channel.

Encroachment of stream channels can also lead to an increase in stream slope, which leads to an increase in stream power. In addition, watershed sediment loads and sediment size (with size generally represented as the median bed and bank particle size, or  $d_{50}$ ) decrease during urbanization.<sup>32</sup> This means that even if pre- and post-development stream power are the same, more erosion will occur in the post-development stage because the smaller particles are less resistant (provided they are non-cohesive).

<sup>30</sup> Booth, D. B. and C. R. Jackson. 1997. Urbanization of Aquatic Systems: Degradation Thresholds, Storm Water Detection, and the Limits of Mitigation. *Journal of the American Water Resources Association* Vol. 33, No.5, pp. 1077-1089.

<sup>31</sup> May, C.W. 1998. Cumulative effects of urbanization on small streams in the Puget Sound Lowland ecoregion. Conference proceedings from Puget Sound Research '98 held March 12, 13 1998 in Seattle, WA; Santa Clara Valley Urban Runoff Pollution Prevention Program. 2002. Hydromodification Management Plan Literature Review. 80 pp.

<sup>32</sup> Finkenbine, J.K., D.S. Atwater, and D.S. Mavinic. 2000. Stream health after urbanization. *J. Am. Water Resour. Assoc.* 36:1149-60;

Pizzuto, J.E. W.S. Hession, and M. McBride. 2000. Comparing gravel-bed rivers in paired urban and rural catchments of southeastern Pennsylvania. *Geology* 28:79-82.

As shown in Stages II and III, the channel deepens and widens to accommodate the increased stream power<sup>33</sup> and decrease in sediment load and sediment size. Channels may actually narrow as entrained sediment from incision is deposited laterally in the channel. After incised channels begin to migrate laterally (Stage III), bank erosion begins, which leads to general channel widening.<sup>34</sup> At this point, a majority of the sediment that leaves a drainage area comes from within the channel, as opposed to the background and construction related hillslope contribution. Stage IV is characterized by more aggradation and localized bank instability. Stage V represents a new quasi-equilibrium channel morphology in balance with the new flow and sediment supply regime. In other words, stream power is in balance with sediment load and sediment size.

The magnitude of the channel morphology changes discussed above varies along a stream network as well as with the age of development, slope, geology (sand-bedded channels may cycle through the evolution sequence in a matter of decades whereas clay-dominated channels may take much longer), watershed sediment load and size, type of urbanization, and land use history. It is also dependent on a channel's stage in the channel evolution sequence when urbanization occurs. Management strategies must take into account a channel's stage of adjustment and account for future changes in the evolution of channel form (Stein and Zaleski 2005).<sup>35</sup>

Traditional structural water quality BMPs (e.g. detention basins and other devices used to store volumes of runoff) unless they are highly engineered to provide adequate flow duration control, do not adequately protect receiving waters from accelerated channel bed and bank erosion, do not address post-development increases in runoff volume, and do not mitigate the decline in benthic macroinvertebrate communities in the receiving waters<sup>36</sup> suggest that structural BMPs are not as effective in protecting aquatic communities as a continuous riparian buffer of native vegetation. This is supported by the findings of Zucker and White<sup>37</sup>, where instream biological metrics were correlated with the extent of forested buffers.

This General Permit requires dischargers to maintain pre-development drainage densities and times of concentration in order to protect channels and encourages dischargers to implement setbacks to reduce channel slope and velocity changes that can lead to aquatic habitat degradation.

There are a number of other approaches for modeling fluvial systems, including statistical and physical models and simpler stream power models.<sup>38</sup> The use of these models in California is described in Stein and Zaleski (2005).<sup>39</sup> Rather than prescribe a specific one-size-fits-all modeling method in this permit, the State Water Board intends to develop a stream power and channel evolution model-based framework to assess channels and develop a hierarchy of suitable analysis methods and management strategies. In time, this framework may become a State Water Board water quality control policy.

---

<sup>33</sup> Hammer 1973 as cited in Delaware Department of Natural Resources (DDNR). 2004. Green Technology: The Delaware Urban Runoff Management Approach. Dover, DE. 117 pp;

Booth, D.B. 1990. Stream Channel Incision Following Drainage Basin Urbanization. *Water Resour. Bull.* 26:407-417.

<sup>34</sup> Trimble, S.W. 1997. Contribution of Stream Channel Erosion to Sediment Yield from an Urbanizing Watershed. *Science*: Vol. 278 (21), pp. 1442-1444.

<sup>35</sup> Stein, E.S. and S. Zaleski. 2005. Managing runoff to protect natural stream: the latest developments on investigation and management of hydromodification in California. Southern California Coastal Water Research Project Technical Report 475. 26 pp.

<sup>36</sup> Horner, R.R. 2006. Investigation of the Feasibility and Benefits of Low-Impact Site Design Practices (LID) for the San Diego Region. Available at: [http://www.projectcleanwater.org/pdf/permit/case-study\\_lid.pdf](http://www.projectcleanwater.org/pdf/permit/case-study_lid.pdf).

<sup>37</sup> Delaware Department of Natural Resources (DDNR). 2004. Green Technology: The Delaware Urban Runoff Management Approach. Dover, DE. 117 pp.

<sup>38</sup> Finlayson, D.P. and D.R. Montgomery. 2003. Modeling large-scale fluvial erosion in geographic information systems. *Geomorphology* (53), pp. 147-164).

<sup>39</sup> Stein, E.S. and S. Zaleski. 2005. Managing runoff to protect natural stream: the latest developments on investigation and management of hydromodification in California. Southern California Coastal Water Research Project Technical Report 475. 26 pp.

#### Permit Linkage to Overbank and Extreme Flood Protection

Site design BMPs (e.g. rooftop and impervious disconnection, vegetated swales, setbacks and buffers) filter and settle out pollutants and provide for more infiltration than is possible for traditional centralized structural BMPs placed at the lowest point in a site. They provide source control for runoff and lead to a reduction in pollutant loads. When implemented, they also help reduce the magnitude and volume of larger, less frequent storm events (e.g., 10-yr, 24-hour storm and larger), thereby reducing the need for expensive flood control infrastructure. Nonstructural BMPs can also be a landscape amenity, instead of a large isolated structure requiring substantial area for ancillary access, buffering, screening and maintenance facilities.<sup>25</sup> The multiple benefits of using non-structural benefits will be critically important as the state's population increases and imposes strains upon our existing water resources.

Maintaining predevelopment drainage densities and times of concentration will help reduce post-development peak flows and volumes in areas not covered under a municipal permit. The most effective way to preserve drainage areas and maximize time of concentration is to implement landform grading, incorporate site design BMPs and implement distributed structural BMPs (e.g., bioretention cells, rain gardens, rain cisterns).

### M. Storm Water Pollution Prevention Plans

USEPA's Construction General Permit requires that qualified personnel conduct inspections. USEPA defines qualified personnel as "a person knowledgeable in the principles and practice of erosion and sediment controls who possesses the skills to assess conditions at the construction site that could impact storm water quality and to assess the effectiveness of any sediment and erosion control measures selected to control the quality of storm water discharges from the construction activity."<sup>40</sup> USEPA also suggests that qualified personnel prepare SWPPPs and points to numerous states that require certified professionals to be on construction sites at all times. States that currently have certification programs are Washington, Georgia, Florida, Delaware, Maryland, and New Jersey. The Permit 99-08-DWQ did not require that qualified personnel prepare SWPPPs or conduct inspections. However, to ensure that water quality is being protected, this General Permit requires that all SWPPPs be written, amended, and certified by a Qualified SWPPP Developer. A Qualified SWPPP Developer must possess one of the eight certifications and or registrations specified in this General Permit and effective two years after the adoption date of this General Permit, must have attended a State Water Board-sponsored or approved Qualified SWPPP Developer training course. Table 9 provides an overview of the criteria used in determining qualified certification titles for a QSD and QSP.

---

<sup>40</sup> US Environmental Protection Agency. Stormwater Pollution Prevention Plans for Construction Activities. <<http://cfpub.epa.gov/npdes/stormwater/swpppp.cfm>> and <[http://www.epa.gov/npdes/pubs/sw\\_swpppp\\_guide.pdf](http://www.epa.gov/npdes/pubs/sw_swpppp_guide.pdf)>.

Table 9 - Qualified SWPPP Developer/ Qualified SWPPP Practitioner Certification Criteria

Certification/ Title	Registered By	QSD/QSP	Certification Criteria
Professional Civil Engineer	California	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites
Professional Geologist or Engineering Geologist	California	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites
Landscape Architect	California	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites
Professional Hydrologist	American Institute of Hydrology	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites
Certified Professional in Erosion and Sediment Control™ (CPESC)	Enviro Cert International Inc.	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites 5. Continuing Education
Certified Inspector of Sediment and Erosion Control™ (CISEC)	Certified Inspector of Sediment and Erosion Control, Inc.	QSP	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites 5. Continuing Education
Certified Erosion, Sediment and Storm Water Inspector™ (CESSWI)	Enviro Cert International Inc.	QSP	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites 5. Continuing Education
Certified Professional in Storm Water Quality™ (CPSWQ)	Enviro Cert International Inc.	Both	1. Approval Process 2. Code of Ethics 3. Accountability 4. Pre-requisites 5. Continuing Education

The previous versions of the General Permit required development and implementation of a SWPPP as the primary compliance mechanism. The SWPPP has two major objectives: (1) to help identify the sources of sediment and other pollutants that affect the quality of storm water discharges; and (2) to describe and ensure the implementation of BMPs to reduce or eliminate sediment and other pollutants in storm water and non-storm water discharges. The SWPPP must include BMPs that address source control, BMPs that address pollutant control, and BMPs that address treatment control.

This General Permit shifts some of the measures that were covered by this general requirement to specific permit requirements, each individually enforceable as a permit term. This General Permit emphasizes the use of appropriately selected, correctly installed and maintained pollution reduction BMPs. This approach provides the flexibility necessary to establish BMPs that can effectively address source control of pollutants during changing construction activities. These specific requirements also improve both the clarity and the enforceability of the General Permit so that the dischargers understand, and the public can determine whether the discharges are in compliance with, permit requirements.

The SWPPP must be implemented at the appropriate level to protect water quality at all times throughout the life of the project. The SWPPP must remain on the site during construction activities, commencing with the initial mobilization and ending with the termination of coverage under the General Permit. For LUPs the discharger shall make the SWPPP available at the construction site during working hours while construction is occurring and shall be made available upon request by a State or Municipal inspector. When the original SWPPP is retained by a crewmember in a construction vehicle and is not currently at the construction site, current copies of the BMPs and map/drawing will be left with the field crew and the original SWPPP shall be made available via a request by radio or telephone. Once construction activities are complete, until stabilization is achieved, the SWPPP shall be available from the SWPPP contact listed in the PRDs

A SWPPP must be appropriate for the type and complexity of a project and will be developed and implemented to address project specific conditions. Some projects may have similarities or complexities, yet each project is unique in its progressive state that requires specific description and selection of BMPs needed to address all possible generated pollutants

## **N. Regional Water Board Authorities**

Because this General Permit will be issued to thousands of construction sites across the State, the Regional Water Boards retain discretionary authority over certain issues that may arise from the discharges in their respective regions. This General Permit does not grant the Regional Water Boards any authority they do not otherwise have; rather, it merely emphasizes that the Regional Water Boards can take specific actions related to this General Permit. For example, the Regional Water Boards will be enforcing this General Permit and may need to adjust some requirements for a discharger based on the discharger's compliance history.



Linda S. Adams  
Secretary for  
Environmental Protection

# State Water Resources Control Board

## Division of Water Quality

1001 I Street • Sacramento, California 95814 • (916) 341-5455  
Mailing Address: P.O. Box 100 • Sacramento, California • 95812-0100  
Fax (916) 341-5463 • <http://www.waterboards.ca.gov>



Arnold Schwarzenegger  
Governor

NATIONAL POLLUTANT DISCHARGE ELIMINATION SYSTEM (NPDES)  
GENERAL PERMIT FOR  
STORM WATER DISCHARGES  
ASSOCIATED WITH CONSTRUCTION AND LAND DISTURBANCE  
ACTIVITIES

ORDER NO. 2009-0009-DWQ  
NPDES NO. **CAS000002**

This Order was adopted by the State Water Resources Control Board on:	<b>September 2, 2009</b>
This Order shall become effective on:	<b>July 1, 2010</b>
This Order shall expire on:	<b>September 2, 2014</b>

IT IS HEREBY ORDERED, that this Order supersedes [Order No. 99-08-DWQ](#) except for enforcement purposes. The Discharger shall comply with the requirements in this Order to meet the provisions contained in Division 7 of the California Water Code (commencing with section 13000) and regulations adopted thereunder, and the provisions of the federal Clean Water Act and regulations and guidelines adopted thereunder.

I, Jeanine Townsend, Clerk to the Board, do hereby certify that this Order with all attachments is a full, true, and correct copy of an Order adopted by the State Water Resources Control Board, on September 2, 2009.

AYE: Vice Chair Frances Spivy-Weber  
Board Member Arthur G. Baggett, Jr.  
Board Member Tam M. Doduc

NAY: Chairman Charles R. Hoppin

ABSENT: None

ABSTAIN: None

Jeanine Townsend  
Clerk to the Board

## TABLE OF CONTENTS

I.	FINDINGS .....	1
II.	CONDITIONS FOR PERMIT COVERAGE.....	14
III.	DISCHARGE PROHIBITIONS.....	20
IV.	SPECIAL PROVISIONS.....	22
V.	EFFLUENT STANDARDS .....	29
VI.	RECEIVING WATER LIMITATIONS .....	32
VII.	TRAINING QUALIFICATIONS AND CERTIFICATION REQUIREMENTS.....	33
VIII.	RISK DETERMINATION .....	34
IX.	RISK LEVEL 1 REQUIREMENTS.....	35
X.	RISK LEVEL 2 REQUIREMENTS.....	35
XI.	RISK LEVEL 3 REQUIREMENTS.....	35
XII.	ACTIVE TREATMENT SYSTEMS (ATS).....	35
XIII.	POST-CONSTRUCTION STANDARDS .....	36
XIV.	SWPPP REQUIREMENTS .....	38
XV.	REGIONAL WATER BOARD AUTHORITIES.....	39
XVI.	ANNUAL REPORTING REQUIREMENTS.....	40

## LIST OF ATTACHMENTS

Attachment A – Linear Underground/Overhead Requirements  
Attachment A.1 – LUP Type Determination  
Attachment A.2 – LUP Permit Registration Documents  
Attachment B – Permit Registration Documents  
Attachment C – Risk Level 1 Requirements  
Attachment D – Risk Level 2 Requirements  
Attachment E – Risk Level 3 Requirements  
Attachment F – Active Treatment System (ATS) Requirements

## LIST OF APPENDICES

Appendix 1 – Risk Determination Worksheet  
Appendix 2 – Post-Construction Water Balance Performance Standard  
Appendix 2.1 – Post-Construction Water Balance Performance Standard Spreadsheet  
Appendix 3 – Bioassessment Monitoring Guidelines  
Appendix 4 – Adopted/Implemented Sediment TMDLs  
Appendix 5 – Glossary  
Appendix 6 – Acronyms  
Appendix 7 – State and Regional Water Resources Control Board Contacts

**STATE WATER RESOURCES CONTROL BOARD  
ORDER NO. 2009-0009-DWQ  
NATIONAL POLLUTANT DISCHARGE ELIMINATION SYSTEM  
GENERAL PERMIT NO. CAS000002**

**WASTE DISCHARGE REQUIREMENTS  
FOR  
DISCHARGES OF STORM WATER RUNOFF ASSOCIATED WITH  
CONSTRUCTION AND LAND DISTURBANCE ACTIVITIES**

**I. FINDINGS**

**A. General Findings**

The State Water Resources Control Board (State Water Board) finds that:

1. The federal Clean Water Act (CWA) prohibits certain discharges of storm water containing pollutants except in compliance with a National Pollutant Discharge Elimination System (NPDES) permit (Title 33 United States Code (U.S.C.) §§ 1311 and 1342(p); also referred to as Clean Water Act (CWA) §§ 301 and 402(p)). The U.S. Environmental Protection Agency (U.S. EPA) promulgates federal regulations to implement the CWA's mandate to control pollutants in storm water runoff discharges. (Title 40 Code of Federal Regulations (C.F.R.) Parts 122, 123, and 124). The federal statutes and regulations require discharges to surface waters comprised of storm water associated with construction activity, including demolition, clearing, grading, and excavation, and other land disturbance activities (except operations that result in disturbance of less than one acre of total land area and which are not part of a larger common plan of development or sale), to obtain coverage under an NPDES permit. The NPDES permit must require implementation of Best Available Technology Economically Achievable (BAT) and Best Conventional Pollutant Control Technology (BCT) to reduce or eliminate pollutants in storm water runoff. The NPDES permit must also include additional requirements necessary to implement applicable water quality standards.
2. This General Permit authorizes discharges of storm water associated with construction activity so long as the dischargers comply with all requirements, provisions, limitations and prohibitions in the permit. In addition, this General Permit regulates the discharges of storm water associated with construction activities from all Linear Underground/Overhead Projects resulting in the disturbance of greater than or equal to one acre (Attachment A).

3. This General Permit regulates discharges of pollutants in storm water associated with construction activity (storm water discharges) to waters of the United States from construction sites that disturb one or more acres of land surface, or that are part of a common plan of development or sale that disturbs more than one acre of land surface.
4. This General Permit does not preempt or supersede the authority of local storm water management agencies to prohibit, restrict, or control storm water discharges to municipal separate storm sewer systems or other watercourses within their jurisdictions.
5. This action to adopt a general NPDES permit is exempt from the provisions of Chapter 3 of the California Environmental Quality Act (CEQA) (Public Resources Code Section 21100, et seq.), pursuant to Section 13389 of the California Water Code.
6. Pursuant to 40 C.F.R. § 131.12 and State Water Board [Resolution No. 68-16](#),<sup>1</sup> which incorporates the requirements of § 131.12 where applicable, the State Water Board finds that discharges in compliance with this General Permit will not result in the lowering of water quality standards, and are therefore consistent with those provisions. Compliance with this General Permit will result in improvements in water quality.
7. This General Permit serves as an NPDES permit in compliance with CWA § 402 and will take effect on July 1, 2010 by the State Water Board provided the Regional Administrator of the U.S. EPA has no objection. If the U.S. EPA Regional Administrator objects to its issuance, the General Permit will not become effective until such objection is withdrawn.
8. Following adoption and upon the effective date of this General Permit, the Regional Water Quality Control Boards (Regional Water Boards) shall enforce the provisions herein.
9. Regional Water Boards establish water quality standards in Basin Plans. The State Water Board establishes water quality standards in various statewide plans, including the California Ocean Plan. U.S. EPA establishes water quality standards in the National Toxic Rule (NTR) and the California Toxic Rule (CTR).

---

<sup>1</sup> Resolution No. 68-16 generally requires that existing water quality be maintained unless degradation is justified based on specific findings.

10. This General Permit does not authorize discharges of fill or dredged material regulated by the U.S. Army Corps of Engineers under CWA § 404 and does not constitute a waiver of water quality certification under CWA § 401.
11. The primary storm water pollutant at construction sites is excess sediment. Excess sediment can cloud the water, which reduces the amount of sunlight reaching aquatic plants, clog fish gills, smother aquatic habitat and spawning areas, and impede navigation in our waterways. Sediment also transports other pollutants such as nutrients, metals, and oils and greases.
12. Construction activities can impact a construction site's runoff sediment supply and transport characteristics. These modifications, which can occur both during and after the construction phase, are a significant cause of degradation of the beneficial uses established for water bodies in California. Dischargers can avoid these effects through better construction site design and activity practices.
13. This General Permit recognizes four distinct phases of construction activities. The phases are Grading and Land Development Phase, Streets and Utilities Phase, Vertical Construction Phase, and Final Landscaping and Site Stabilization Phase. Each phase has activities that can result in different water quality effects from different water quality pollutants. This General Permit also recognizes inactive construction as a category of construction site type.
14. Compliance with any specific limits or requirements contained in this General Permit does not constitute compliance with any other applicable requirements.
15. Following public notice in accordance with State and Federal laws and regulations, the State Water Board heard and considered all comments and testimony in a public hearing on 06/03/2009. The State Water Board has prepared written responses to all significant comments.
16. Construction activities obtaining coverage under the General Permit may have multiple discharges subject to requirements that are specific to general, linear, and/or active treatment system discharge types.
17. The State Water Board may reopen the permit if the U.S. EPA adopts a final effluent limitation guideline for construction activities.

**B. Activities Covered Under the General Permit**

18. Any construction or demolition activity, including, but not limited to, clearing, grading, grubbing, or excavation, or any other activity that results in a land disturbance of equal to or greater than one acre.
19. Construction activity that results in land surface disturbances of less than one acre if the construction activity is part of a larger common plan of development or the sale of one or more acres of disturbed land surface.
20. Construction activity related to residential, commercial, or industrial development on lands currently used for agriculture including, but not limited to, the construction of buildings related to agriculture that are considered industrial pursuant to U.S. EPA regulations, such as dairy barns or food processing facilities.
21. Construction activity associated with Linear Underground/Overhead Utility Projects (LUPs) including, but not limited to, those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment and associated ancillary facilities) and include, but are not limited to, underground utility mark-out, potholing, concrete and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/tower pad and cable/wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/or pavement repair or replacement, and stockpile/borrow locations.
22. Discharges of sediment from construction activities associated with oil and gas exploration, production, processing, or treatment operations or transmission facilities.<sup>2</sup>
23. Storm water discharges from dredge spoil placement that occur outside of U.S. Army Corps of Engineers jurisdiction (upland sites) and that disturb one or more acres of land surface from construction activity are covered by this General Permit. Construction sites that intend to disturb one or more acres of land within the jurisdictional boundaries of a CWA § 404 permit should contact the appropriate Regional Water Board to determine whether this permit applies to the site.

---

<sup>2</sup> Pursuant to the Ninth Circuit Court of Appeals' decision in *NRDC v. EPA* (9th Cir. 2008) 526 F.3d 591, and subsequent denial of the U.S. EPA's petition for reconsideration in November 2008, oil and gas construction activities discharging storm water contaminated only with sediment are no longer exempt from the NPDES program.

**C. Activities Not Covered Under the General Permit**

24. Routine maintenance to maintain original line and grade, hydraulic capacity, or original purpose of the facility.
25. Disturbances to land surfaces solely related to agricultural operations such as disking, harrowing, terracing and leveling, and soil preparation.
26. Discharges of storm water from areas on tribal lands; construction on tribal lands is regulated by a federal permit.
27. Construction activity and land disturbance involving discharges of storm water within the Lake Tahoe Hydrologic Unit. The Lahontan Regional Water Board has adopted its own permit to regulate storm water discharges from construction activity in the Lake Tahoe Hydrologic Unit (Regional Water Board 6SLT). Owners of construction sites in this watershed must apply for the Lahontan Regional Water Board permit rather than the statewide Construction General Permit.
28. Construction activity that disturbs less than one acre of land surface, and that is not part of a larger common plan of development or the sale of one or more acres of disturbed land surface.
29. Construction activity covered by an individual NPDES Permit for storm water discharges.
30. Discharges from small (1 to 5 acre) construction activities with an approved Rainfall Erosivity Waiver authorized by U.S. EPA Phase II regulations certifying to the State Board that small construction activity will occur only when the Rainfall Erosivity Factor is less than 5 ("R" in the Revised Universal Soil Loss Equation).
31. Landfill construction activity that is subject to the Industrial General Permit.
32. Construction activity that discharges to Combined Sewer Systems.
33. Conveyances that discharge storm water runoff combined with municipal sewage.
34. Discharges of storm water identified in CWA § 402(f)(2), 33 U.S.C. § 1342(f)(2).

35. Discharges occurring in basins that are not tributary or hydrologically connected to waters of the United States (for more information contact your Regional Water Board).

#### **D. Obtaining and Modifying General Permit Coverage**

36. This General Permit requires all dischargers to electronically file all Permit Registration Documents (PRDs), Notices of Termination (NOT), changes of information, annual reporting, and other compliance documents required by this General Permit through the State Water Board's Storm water Multi-Application and Report Tracking System (SMARTS) website.
37. Any information provided to the Regional Water Board shall comply with the Homeland Security Act and any other federal law that concerns security in the United States; any information that does not comply should not be submitted.
38. This General Permit grants an exception from the Risk Determination requirements for existing sites covered under Water Quality Orders No. 99-08-DWQ, and [No. 2003-0007-DWQ](#). For certain sites, adding additional requirements may not be cost effective. Construction sites covered under Water Quality Order No. 99-08-DWQ shall obtain permit coverage at the Risk Level 1. LUPs covered under Water Quality Order No. 2003-0007-DWQ shall obtain permit coverage as a Type 1 LUP. The Regional Water Boards have the authority to require Risk Determination to be performed on sites currently covered under Water Quality Orders No. 99-08-DWQ and No. 2003-0007-DWQ where they deem it necessary. The State Water Board finds that there are two circumstances when it may be appropriate for the Regional Water Boards to require a discharger that had filed an NOI under State Water Board Order No. 99-08-DWQ to recalculate the site's risk level. These circumstances are: (1) when the discharger has a demonstrated history of noncompliance with State Water Board Order No. 99-08-DWQ or; (2) when the discharger's site poses a significant risk of causing or contributing to an exceedance of a water quality standard without the implementation of the additional Risk Level 2 or 3 requirements.

#### **E. Prohibitions**

39. All discharges are prohibited except for the storm water and non-storm water discharges specifically authorized by this General Permit or another NPDES permit. Non-storm water discharges include a wide variety of sources, including improper dumping, spills, or leakage from storage tanks or transfer areas. Non-storm water discharges may

contribute significant pollutant loads to receiving waters. Measures to control spills, leakage, and dumping, and to prevent illicit connections during construction must be addressed through structural as well as non-structural Best Management Practices (BMPs)<sup>3</sup>. The State Water Board recognizes, however, that certain non-storm water discharges may be necessary for the completion of construction.

40. This General Permit prohibits all discharges which contain a hazardous substance in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
41. This General Permit incorporates discharge prohibitions contained in water quality control plans, as implemented by the State Water Board and the nine Regional Water Boards.
42. Pursuant to the Ocean Plan, discharges to Areas of Special Biological Significance (ASBS) are prohibited unless covered by an exception that the State Water Board has approved.
43. This General Permit prohibits the discharge of any debris<sup>4</sup> from construction sites. Plastic and other trash materials can cause negative impacts to receiving water beneficial uses. The State Water Board encourages the use of more environmentally safe, biodegradable materials on construction sites to minimize the potential risk to water quality.

## **F. Training**

44. In order to improve compliance with and to maintain consistent enforcement of this General Permit, all dischargers are required to appoint two positions - the Qualified SWPPP Developer (QSD) and the Qualified SWPPP Practitioner (QSP) - who must obtain appropriate training. Together with the key stakeholders, the State and Regional Water Boards are leading the development of this curriculum through a collaborative organization called The Construction General Permit (CGP) Training Team.
45. The Professional Engineers Act (Bus. & Prof. Code section 6700, et seq.) requires that all engineering work must be performed by a California licensed engineer.

---

<sup>3</sup> BMPs are scheduling of activities, prohibitions of practices, maintenance procedures, and other management practices to prevent or reduce the discharge of pollutants to waters of the United States. BMPs also include treatment requirements, operating procedures, and practice to control site runoff, spillage or leaks, sludge or waste disposal, or drainage from raw material storage.

<sup>4</sup> Litter, rubble, discarded refuse, and remains of destroyed inorganic anthropogenic waste.

## G. Determining and Reducing Risk

46. The risk of accelerated erosion and sedimentation from wind and water depends on a number of factors, including proximity to receiving water bodies, climate, topography, and soil type.
47. This General Permit requires dischargers to assess the risk level of a site based on both sediment transport and receiving water risk. This General Permit contains requirements for Risk Levels 1, 2 and 3, and LUP Risk Type 1, 2, and 3 (Attachment A). Risk levels are established by determining two factors: first, calculating the site's sediment risk; and second, receiving water risk during periods of soil exposure (i.e. grading and site stabilization). Both factors are used to determine the site-specific Risk Level(s). LUPs can be determined to be Type 1 based on the flowchart in Attachment A.1.
48. Although this General Permit does not mandate specific setback distances, dischargers are encouraged to set back their construction activities from streams and wetlands whenever feasible to reduce the risk of impacting water quality (e.g., natural stream stability and habitat function). Because there is a reduced risk to receiving waters when setbacks are used, this General Permit gives credit to setbacks in the risk determination and post-construction storm water performance standards. The risk calculation and runoff reduction mechanisms in this General Permit are expected to facilitate compliance with any Regional Water Board and local agency setback requirements, and to encourage voluntary setbacks wherever practicable.
49. Rain events can occur at any time of the year in California. Therefore, a Rain Event Action Plan (REAP) is necessary for Risk Level 2 and 3 traditional construction projects (LUPs exempt) to ensure that active construction sites have adequate erosion and sediment controls implemented prior to the onset of a storm event, even if construction is planned only during the dry season.
50. Soil particles smaller than 0.02 millimeters (mm) (i.e., finer than medium silt) do not settle easily using conventional measures for sediment control (i.e., sediment basins). Given their long settling time, dislodging these soils results in a significant risk that fine particles will be released into surface waters and cause unacceptable downstream impacts. If operated correctly, an Active Treatment System (ATS)<sup>5</sup> can prevent or reduce the release of fine particles from construction sites.

---

<sup>5</sup> An ATS is a treatment system that employs chemical coagulation, chemical flocculation, or electro coagulation in order to reduce turbidity caused by fine suspended sediment.

Use of an ATS can effectively reduce a site's risk of impacting receiving waters.

51. Dischargers located in a watershed area where a Total Maximum Daily Load (TMDL) has been adopted or approved by the Regional Water Board or U.S. EPA may be required by a separate Regional Water Board action to implement additional BMPs, conduct additional monitoring activities, and/or comply with an applicable waste load allocation and implementation schedule. Such dischargers may also be required to obtain an individual Regional Water Board permit specific to the area.

#### **H. Effluent Standards**

52. The State Water Board convened a blue ribbon panel of storm water experts that submitted a report entitled, "The Feasibility of Numeric Effluent Limits Applicable to Discharges of Storm Water Associated with Municipal, Industrial and Construction Activities," dated June 19, 2006. The panel concluded that numeric limits or action levels are technically feasible to control construction storm water discharges, provided that certain conditions are considered. The panel also concluded that numeric effluent limitations (NELs) are feasible for discharges from construction sites that utilize an ATS. The State Water Board has incorporated the expert panel's suggestions into this General Permit, which includes both numeric action levels (NALs) and NELs for pH and turbidity, and special numeric limits for ATS discharges.

##### **Numeric Effluent Limitations**

53. Discharges of storm water from construction activities may become contaminated from alkaline construction materials resulting in high pH (greater than pH 7). Alkaline construction materials include, but are not limited to, hydrated lime, concrete, mortar, cement kiln dust (CKD), Portland cement treated base (CTB), fly ash, recycled concrete, and masonry work. This General Permit includes an NEL for pH (6.0-9.0) that applies only at sites that exhibit a "high risk of high pH discharge." A "high risk of high pH discharge" can occur during the complete utilities phase, the complete vertical build phase, and any portion of any phase where significant amounts of materials are placed directly on the land at the site in a manner that could result in significant alterations to the background pH of any discharges.
54. For Risk Level 3 discharges, this General Permit establishes technology-based, numeric effluent limitations (NELs) for turbidity of 500 NTU. Exceedances of the turbidity NEL constitutes a violation of this General Permit.

55. This General Permit establishes a 5 year, 24 hour (expressed in inches of rainfall) Compliance Storm Event exemption from the technology-based NELs for Risk Level 3 dischargers.

**Determining Compliance with Numeric Limitations**

56. This General Permit sets a pH NAL of 6.5 to 8.5, and a turbidity NAL of 250 NTU. The purpose of the NAL and its associated monitoring requirement is to provide operational information regarding the performance of the measures used at the site to minimize the discharge of pollutants and to protect beneficial uses and receiving waters from the adverse effects of construction-related storm water discharges. The NALs in this General Permit for pH and turbidity are not directly enforceable and do not constitute NELs.

57. This General Permit requires dischargers with NAL exceedances to immediately implement additional BMPs and revise their Storm Water Pollution Prevention Plans (SWPPPs) accordingly to either prevent pollutants and authorized non-storm water discharges from contaminating storm water, or to substantially reduce the pollutants to levels consistently below the NALs. NAL exceedances are reported in the State Water Boards SMARTS system, and the discharger is required to provide an NAL Exceedance Report when requested by a Regional Water Board.

58. If run-on is caused by a forest fire or any other natural disaster, then NELs do not apply.

59. Exceedances of the NELs are a violation of this Permit. This General Permit requires dischargers with NEL exceedances to implement additional monitoring, BMPs, and revise their SWPPPs accordingly. Dischargers are required to notify the State and Regional Water Boards of the violation through the State Water Boards SMARTS system, and provide an NEL Violation Report sharing additional information concerning the NEL exceedance.

**I. Receiving Water Limitations**

60. This General Permit requires all enrolled dischargers to determine the receiving waters potentially affected by their discharges and to comply with all applicable water quality standards, including any more stringent standards applicable to a water body.

**J. Sampling, Monitoring, Reporting and Record Keeping**

61. Visual monitoring of storm water and non-storm water discharges is required for all sites subject to this General Permit.

62. Records of all visual monitoring inspections are required to remain on-site during the construction period and for a minimum of three years.
63. For all Risk Level 3 and Risk Level 2 sites, this General Permit requires effluent monitoring for pH and turbidity. Sampling, analysis and monitoring requirements for effluent monitoring for pH and turbidity are contained in this General Permit.
64. Risk Level 3 sites in violation of the Numeric Effluent Limitations contained in this General Permit and with direct discharges to receiving water are required to conduct receiving water monitoring.
65. For Risk Level 3 sites larger than 30 acres and with direct discharges to receiving waters, this General Permit requires bioassessment sampling before and after site completion to determine if significant degradation to the receiving water's biota has occurred. Bioassessment sampling guidelines are contained in this General Permit.
66. A summary and evaluation of the sampling and analysis results will be submitted in the Annual Reports.
67. This General Permit contains sampling, analysis and monitoring requirements for non-visible pollutants at all sites subject to this General Permit.
68. Compliance with the General Permit relies upon dischargers to electronically self-report any discharge violations and to comply with any Regional Water Board enforcement actions.
69. This General Permit requires that all dischargers maintain a paper or electronic copy of all required records for three years from the date generated or date submitted, whichever is last. These records must be available at the construction site until construction is completed. For LUPs, these documents may be retained in a crew member's vehicle and made available upon request.

#### **K. Active Treatment System (ATS) Requirements**

70. Active treatment systems add chemicals to facilitate flocculation, coagulation and filtration of suspended sediment particles. The uncontrolled release of these chemicals to the environment can negatively affect the beneficial uses of receiving waters and/or degrade water quality (e.g., acute and chronic toxicity). Additionally, the batch storage and treatment of storm water through an ATS' can potentially

cause physical impacts on receiving waters if storage volume is inadequate or due to sudden releases of the ATS batches and improperly designed outfalls.

71. If designed, operated and maintained properly an ATS can achieve very high removal rates of suspended sediment (measured as turbidity), albeit at sometimes significantly higher costs than traditional erosion/sediment control practices. As a result, this General Permit establishes NELs consistent with the expected level of typical ATS performance.
72. This General Permit requires discharges of storm water associated with construction activity that undergo active treatment to comply with special operational and effluent limitations to ensure that these discharges do not adversely affect the beneficial uses of the receiving waters or cause degradation of their water quality.
73. For ATS discharges, this General Permit establishes technology-based NELs for turbidity.
74. This General Permit establishes a 10 year, 24 hour (expressed in inches of rainfall) Compliance Storm Event exemption from the technology-based numeric effluent limitations for ATS discharges. Exceedances of the ATS turbidity NEL constitutes a violation of this General Permit.

#### **L. Post-Construction Requirements**

75. This General Permit includes performance standards for post-construction that are consistent with State Water Board [Resolution No. 2005-0006](#), "Resolution Adopting the Concept of Sustainability as a Core Value for State Water Board Programs and Directing Its Incorporation," and [2008-0030](#), "Requiring Sustainable Water Resources Management." The requirement for all construction sites to match pre-project hydrology will help ensure that the physical and biological integrity of aquatic ecosystems are sustained. This "runoff reduction" approach is analogous in principle to Low Impact Development (LID) and will serve to protect related watersheds and waterbodies from both hydrologic-based and pollution impacts associated with the post-construction landscape.
76. LUP projects are not subject to post-construction requirements due to the nature of their construction to return project sites to pre-construction conditions.

**M. Storm Water Pollution Prevention Plan Requirements**

- 77. This General Permit requires the development of a site-specific SWPPP. The SWPPP must include the information needed to demonstrate compliance with all requirements of this General Permit, and must be kept on the construction site and be available for review. The discharger shall ensure that a QSD develops the SWPPP.
- 78. To ensure proper site oversight, this General Permit requires a Qualified SWPPP Practitioner to oversee implementation of the BMPs required to comply with this General Permit.

**N. Regional Water Board Authorities**

- 79. Regional Water Boards are responsible for implementation and enforcement of this General Permit. A general approach to permitting is not always suitable for every construction site and environmental circumstances. Therefore, this General Permit recognizes that Regional Water Boards must have some flexibility and authority to alter, approve, exempt, or rescind permit authority granted under this General Permit in order to protect the beneficial uses of our receiving waters and prevent degradation of water quality.

**IT IS HEREBY ORDERED** that all dischargers subject to this General Permit shall comply with the following conditions and requirements (including all conditions and requirements as set forth in Attachments A, B, C, D, E and F)<sup>6</sup>:

## **II. CONDITIONS FOR PERMIT COVERAGE**

### **A. Linear Underground/Overhead Projects (LUPs)**

1. Linear Underground/Overhead Projects (LUPs) include, but are not limited to, any conveyance, pipe, or pipeline for the transportation of any gaseous, liquid (including water and wastewater for domestic municipal services), liquescent, or slurry substance; any cable line or wire for the transmission of electrical energy; any cable line or wire for communications (e.g. telephone, telegraph, radio or television messages); and associated ancillary facilities. Construction activities associated with LUPs include, but are not limited to, (a) those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment, and associated ancillary facilities); and include, but are not limited to, (b) underground utility mark-out, potholing, concrete and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/tower pad and cable/wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/ or pavement repair or replacement, and stockpile/borrow locations.
2. The utility company, municipality, or other public or private company or agency that owns or operates the linear underground/overhead project is responsible for obtaining coverage under the General Permit where the construction of pipelines, utility lines, fiber-optic cables, or other linear underground/overhead projects will occur across several properties unless the LUP construction activities are covered under another construction storm water permit.
3. Only LUPs shall comply with the conditions and requirements in Attachment A, A.1 & A.2 of this Order. The balance of this Order is not applicable to LUPs except as indicated in Attachment A.

### **B. Obtaining Permit Coverage Traditional Construction Sites**

---

<sup>6</sup> These attachments are part of the General Permit itself and are not separate documents that are capable of being updated independently by the State Water Board.

1. The Legally Responsible Person (LRP) (see Special Provisions, Electronic Signature and Certification Requirements, Section IV.I.1) must obtain coverage under this General Permit.
2. To obtain coverage, the LRP must electronically file Permit Registration Documents (PRDs) prior to the commencement of construction activity. Failure to obtain coverage under this General Permit for storm water discharges to waters of the United States is a violation of the CWA and the California Water Code.
3. PRDs shall consist of:
  - a. Notice of Intent (NOI)
  - b. Risk Assessment (Section VIII)
  - c. Site Map
  - d. Storm Water Pollution Prevention Plan (Section XIV)
  - e. Annual Fee
  - f. Signed Certification Statement

Any information provided to the Regional Water Board shall comply with the Homeland Security Act and any other federal law that concerns security in the United States; any information that does not comply should not be submitted.

Attachment B contains additional PRD information. Dischargers must electronically file the PRDs, and mail the appropriate annual fee to the State Water Board.

4. This permit is effective on July 1, 2010.
  - a. **Dischargers Obtaining Coverage On or After July 1, 2010:** All dischargers requiring coverage on or after July 1, 2010, shall electronically file their PRDs prior to the commencement of construction activities, and mail the appropriate annual fee no later than seven days prior to the commencement of construction activities. Permit coverage shall not commence until the PRDs and the annual fee are received by the State Water Board, and a WDID number is assigned and sent by SMARTS.
  - b. **Dischargers Covered Under 99-08-DWQ and 2003-0007-DWQ:** Existing dischargers subject to State Water Board Order No. 99-08-DWQ (existing dischargers) will continue coverage under 99-08-DWQ until July 1, 2010. After July 1, 2010, all NOIs subject to State Water Board Order No. 99-08-DWQ will be terminated. Existing dischargers shall electronically file their PRDs no later than

July 1, 2010. If an existing discharger's site acreage subject to the annual fee has changed, it shall mail a revised annual fee no less than seven days after receiving the revised annual fee notification, **or else lose permit coverage**. All existing dischargers shall be exempt from the risk determination requirements in Section VIII of this General Permit until two years after permit adoption. All existing dischargers are therefore subject to Risk Level 1 requirements regardless of their site's sediment and receiving water risks. However, a Regional Board retains the authority to require an existing discharger to comply with the Section VIII risk determination requirements.

5. The discharger is only considered covered by this General Permit upon receipt of a Waste Discharger Identification (WDID) number assigned and sent by the State Water Board Storm water Multi-Application and Report Tracking System (SMARTS). In order to demonstrate compliance with this General Permit, the discharger must obtain a WDID number and must present documentation of a valid WDID upon demand.
6. During the period this permit is subject to review by the U.S. EPA, the prior permit (State Water Board Order No. 99-08-DWQ) remains in effect. Existing dischargers under the prior permit will continue to have coverage under State Water Board Order No. 99-08-DWQ until this General Permit takes effect on July 1, 2010. Dischargers who complete their projects and electronically file an NOT prior to July 1, 2010, are not required to obtain coverage under this General Permit.
7. Small Construction Rainfall Erosivity Waiver

EPA's Small Construction Erosivity Waiver applies to sites between one and five acres demonstrating that there are no adverse water quality impacts.

Dischargers eligible for a Rainfall Erosivity Waiver based on low erosivity potential shall complete the electronic Notice of Intent (NOI) and Sediment Risk form through the State Water Board's SMARTS system, certifying that the construction activity will take place during a period when the value of the rainfall erosivity factor is less than five. Where the LRP changes or another LRP is added during construction, the new LRP must also submit a waiver certification through the SMARTS system.

If a small construction site continues beyond the projected completion date given on the waiver certification, the LRP shall recalculate the rainfall erosivity factor for the new project duration and submit this

information through the SMARTS system. If the new R factor is below five (5), the discharger shall update through SMARTS all applicable information on the waiver certification and retain a copy of the revised waiver onsite. The LRP shall submit the new waiver certification 30 days prior to the projected completion date listed on the original waiver form to assure exemption from permitting requirements is uninterrupted. If the new R factor is five (5) or above, the LRP shall be required to apply for coverage under this Order.

8. In the case of a public emergency that requires immediate construction activities, a discharger shall submit a brief description of the emergency construction activity within five days of the onset of construction, and then shall submit all PRDs within thirty days.

### **C. Revising Permit Coverage for Change of Acreage or New Ownership**

1. The discharger may reduce or increase the total acreage covered under this General Permit when a portion of the site is complete and/or conditions for termination of coverage have been met (See Section II.D Conditions for Termination of Coverage); when ownership of a portion of the site is sold to a different entity; or when new acreage, subject to this General Permit, is added to the site.
2. Within 30 days of a reduction or increase in total disturbed acreage, the discharger shall electronically file revisions to the PRDs that include:
  - a. A revised NOI indicating the new project size;
  - b. A revised site map showing the acreage of the site completed, acreage currently under construction, acreage sold/transferred or added, and acreage currently stabilized in accordance with the Conditions for Termination of Coverage in Section II.D below.
  - c. SWPPP revisions, as appropriate; and
  - d. Certification that any new landowners have been notified of applicable requirements to obtain General Permit coverage. The certification shall include the name, address, telephone number, and e-mail address of the new landowner.
  - e. If the project acreage has increased, dischargers shall mail payment of revised annual fees within 14 days of receiving the revised annual fee notification.

3. The discharger shall continue coverage under the General Permit for any parcel that has not achieved "Final Stabilization" as defined in Section II.D.
4. When an LRP owns property with active General Permit coverage, and the LRP sells the property, or a parcel thereof, to another person, that person shall become an LRP with respect to whatever parcel was sold. The existing LRP shall inform the new LRP of the General Permit's requirements. In order for the new LRP to continue the construction activity on its parcel of property, the new LRP, or the new LRP's approved signatory, must submit PRDs in accordance with this General Permit's requirements.

#### **D. Conditions for Termination of Coverage**

1. Within 90 days of when construction is complete or ownership has been transferred, the discharger shall electronically file a Notice of Termination (NOT), a final site map, and photos through the State Water Boards SMARTS system. Filing a NOT certifies that all General Permit requirements have been met. The Regional Water Board will consider a construction site complete only when all portions of the site have been transferred to a new owner, or all of the following conditions have been met:
  - a. For purposes of "final stabilization," the site will not pose any additional sediment discharge risk than it did prior to the commencement of construction activity;
  - b. There is no potential for construction-related storm water pollutants to be discharged into site runoff;
  - c. Final stabilization has been reached;
  - d. Construction materials and wastes have been disposed of properly;
  - e. Compliance with the Post-Construction Standards in Section XIII of this General Permit has been demonstrated;
  - f. Post-construction storm water management measures have been installed and a long-term maintenance plan<sup>7</sup> has been established; and

---

<sup>7</sup> For the purposes of this requirement a long-term maintenance plan will be designed for a minimum of five years, and will describe the procedures to ensure that the post-construction storm water management measures are adequately maintained.

- g. All construction-related equipment, materials and any temporary BMPs no longer needed are removed from the site.
2. The discharger shall certify that final stabilization conditions are satisfied in their NOT. Failure to certify shall result in continuation of permit coverage and annual billing.
3. The NOT must demonstrate through photos, RUSLE or RUSLE2, or results of testing and analysis that the site meets all of the conditions above (Section II.D.1) and the final stabilization condition (Section II.D.1.a) is attained by one of the following methods:
  - a. "70% final cover method," no computational proof required
  - OR:**
  - b. "RUSLE or RUSLE2 method," computational proof required
  - OR:**
  - c. "Custom method", the discharger shall demonstrate in some other manner than a or b, above, that the site complies with the "final stabilization" requirement in Section II.D.1.a.

### III. DISCHARGE PROHIBITIONS

- A.** Dischargers shall not violate any discharge prohibitions contained in applicable Basin Plans or statewide water quality control plans. Waste discharges to Areas of Special Biological Significance (ASBS) are prohibited by the California Ocean Plan, unless granted an exception issued by the State Water Board.
- B.** All discharges are prohibited except for the storm water and non-storm water discharges specifically authorized by this General Permit or another NPDES permit.
- C.** Authorized non-storm water discharges may include those from de-chlorinated potable water sources such as: fire hydrant flushing, irrigation of vegetative erosion control measures, pipe flushing and testing, water to control dust, uncontaminated ground water from dewatering, and other discharges not subject to a separate general NPDES permit adopted by a Regional Water Board. The discharge of non-storm water is authorized under the following conditions:
1. The discharge does not cause or contribute to a violation of any water quality standard;
  2. The discharge does not violate any other provision of this General Permit;
  3. The discharge is not prohibited by the applicable Basin Plan;
  4. The discharger has included and implemented specific BMPs required by this General Permit to prevent or reduce the contact of the non-storm water discharge with construction materials or equipment.
  5. The discharge does not contain toxic constituents in toxic amounts or (other) significant quantities of pollutants;
  6. The discharge is monitored and meets the applicable NALs and NELs; and
  7. The discharger reports the sampling information in the Annual Report.

If any of the above conditions are not satisfied, the discharge is not authorized by this General Permit. The discharger shall notify the Regional Water Board of any anticipated non-storm water discharges not already authorized by this General Permit or another NPDES permit, to determine whether a separate NPDES permit is necessary.

- D. Debris resulting from construction activities are prohibited from being discharged from construction sites.
- E. When soil contamination is found or suspected and a responsible party is not identified, or the responsible party fails to promptly take the appropriate action, the discharger shall have those soils sampled and tested to ensure proper handling and public safety measures are implemented. The discharger shall notify the appropriate local, State, and federal agency(ies) when contaminated soil is found at a construction site, and will notify the appropriate Regional Water Board.

## **IV. SPECIAL PROVISIONS**

### **A. Duty to Comply**

1. The discharger shall comply with all of the conditions of this General Permit. Any permit noncompliance constitutes a violation of the Clean Water Act (CWA) and the Porter-Cologne Water Quality Control Act and is grounds for enforcement action and/or removal from General Permit coverage.
2. The discharger shall comply with effluent standards or prohibitions established under Section 307(a) of the CWA for toxic pollutants within the time provided in the regulations that establish these standards or prohibitions, even if this General Permit has not yet been modified to incorporate the requirement.

### **B. General Permit Actions**

1. This General Permit may be modified, revoked and reissued, or terminated for cause. The filing of a request by the discharger for a General Permit modification, revocation and reissuance, or termination, or a notification of planned changes or anticipated noncompliance does not annul any General Permit condition.
2. If any toxic effluent standard or prohibition (including any schedule of compliance specified in such effluent standard or prohibition) is promulgated under Section 307(a) of the CWA for a toxic pollutant which is present in the discharge and that standard or prohibition is more stringent than any limitation on the pollutant in this General Permit, this General Permit shall be modified or revoked and reissued to conform to the toxic effluent standard or prohibition and the dischargers so notified.

### **C. Need to Halt or Reduce Activity Not a Defense**

It shall not be a defense for a discharger in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of this General Permit.

### **D. Duty to Mitigate**

The discharger shall take all responsible steps to minimize or prevent any discharge in violation of this General Permit, which has a reasonable likelihood of adversely affecting human health or the environment.

### **E. Proper Operation and Maintenance**

The discharger shall at all times properly operate and maintain any facilities and systems of treatment and control (and related appurtenances) which are installed or used by the discharger to achieve compliance with the conditions of this General Permit. Proper operation and maintenance also includes adequate laboratory controls and appropriate quality assurance procedures. Proper operation and maintenance may require the operation of backup or auxiliary facilities or similar systems installed by a discharger when necessary to achieve compliance with the conditions of this General Permit.

### **F. Property Rights**

This General Permit does not convey any property rights of any sort or any exclusive privileges, nor does it authorize any injury to private property or any invasion of personal rights, nor does it authorize any infringement of Federal, State, or local laws or regulations.

### **G. Duty to Maintain Records and Provide Information**

1. The discharger shall maintain a paper or electronic copy of all required records, including a copy of this General Permit, for three years from the date generated or date submitted, whichever is last. These records shall be available at the construction site until construction is completed.
2. The discharger shall furnish the Regional Water Board, State Water Board, or U.S. EPA, within a reasonable time, any requested information to determine compliance with this General Permit. The discharger shall also furnish, upon request, copies of records that are required to be kept by this General Permit.

### **H. Inspection and Entry**

The discharger shall allow the Regional Water Board, State Water Board, U.S. EPA, and/or, in the case of construction sites which discharge through a municipal separate storm sewer, an authorized representative of the municipal operator of the separate storm sewer system receiving the discharge, upon the presentation of credentials and other documents as may be required by law, to:

1. Enter upon the discharger's premises at reasonable times where a regulated construction activity is being conducted or where records must be kept under the conditions of this General Permit;

2. Access and copy at reasonable times any records that must be kept under the conditions of this General Permit;
3. Inspect at reasonable times the complete construction site, including any off-site staging areas or material storage areas, and the erosion/sediment controls; and
4. Sample or monitor at reasonable times for the purpose of ensuring General Permit compliance.

**I. Electronic Signature and Certification Requirements**

1. All Permit Registration Documents (PRDs) and Notice of Terminations (NOTs) shall be electronically signed, certified, and submitted via SMARTS to the State Water Board. Either the Legally Responsible Person (LRP) or a person legally authorized to sign and certify PRDs and NOTs on behalf of the LRP (the LRP's Approved Signatory) must submit all information electronically via SMARTS.
  - a. The LRP's Approved Signatory must be one of the following:
    - i. For a corporation: a responsible corporate officer. For the purpose of this section, a responsible corporate officer means: (a) a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy or decision-making functions for the corporation; or (b) the manager of the facility if authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures;
    - ii. For a partnership or sole proprietorship: a general partner or the proprietor, respectively;
    - iii. For a municipality, State, Federal, or other public agency: either a principal executive officer or ranking elected official. The principal executive officer of a Federal agency includes the chief executive officer of the agency or the senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., Regional Administrators of U.S. EPA);
    - iv. For the military: Any military officer who has been designated.
    - v. For a public university: An authorized university official

- b. Changes to Authorization. If an approved signatory's authorization is no longer accurate, a new authorization satisfying the requirements of paragraph (a) of this section must be submitted via SMARTS prior to or together with any reports, information or applications to be signed by an approved signatory.
2. All Annual Reports, or other information required by the General Permit (other than PRDs and NOTs) or requested by the Regional Water Board, State Water Board, U.S. EPA, or local storm water management agency shall be certified and submitted by the LRP or the LRP's approved signatory as described above.

#### **J. Certification**

Any person signing documents under Section IV.I above, shall make the following certification:

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

#### **K. Anticipated Noncompliance**

The discharger shall give advance notice to the Regional Water Board and local storm water management agency of any planned changes in the construction activity, which may result in noncompliance with General Permit requirements.

#### **L. Bypass**

Bypass<sup>8</sup> is prohibited. The Regional Water Board may take enforcement action against the discharger for bypass unless:

1. Bypass was unavoidable to prevent loss of life, personal injury or severe property damage;<sup>9</sup>

---

<sup>8</sup> The intentional diversion of waste streams from any portion of a treatment facility

<sup>9</sup> Severe property damage means substantial physical damage to property, damage to the treatment facilities that causes them to become inoperable, or substantial and permanent loss of natural resources that can reasonably be expected to occur in the absence of a bypass. Severe property damage does not mean economic loss caused by delays in production.

2. There were no feasible alternatives to bypass, such as the use of auxiliary treatment facilities, retention of untreated waste, or maintenance during normal periods of equipment downtime. This condition is not satisfied if adequate back-up equipment should have been installed in the exercise of reasonable engineering judgment to prevent a bypass that could occur during normal periods of equipment downtime or preventative maintenance;
3. The discharger submitted a notice at least ten days in advance of the need for a bypass to the Regional Water Board; or
4. The discharger may allow a bypass to occur that does not cause effluent limitations to be exceeded, but only if it is for essential maintenance to assure efficient operation. In such a case, the above bypass conditions are not applicable. The discharger shall submit notice of an unanticipated bypass as required.

#### **M. Upset**

1. A discharger that wishes to establish the affirmative defense of an upset<sup>10</sup> in an action brought for noncompliance shall demonstrate, through properly signed, contemporaneous operating logs, or other relevant evidence that:
  - a. An upset occurred and that the discharger can identify the cause(s) of the upset
  - b. The treatment facility was being properly operated by the time of the upset
  - c. The discharger submitted notice of the upset as required; and
  - d. The discharger complied with any remedial measures required
2. No determination made before an action of noncompliance occurs, such as during administrative review of claims that noncompliance was caused by an upset, is final administrative action subject to judicial review.
3. In any enforcement proceeding, the discharger seeking to establish the occurrence of an upset has the burden of proof

---

<sup>10</sup> An exceptional incident in which there is unintentional and temporary noncompliance the technology based numeric effluent limitations because of factors beyond the reasonable control of the discharger. An upset does not include noncompliance to the extent caused by operational error, improperly designed treatment facilities, inadequate treatment facilities, lack of preventative maintenance, or careless or improper operation.

#### **N. Penalties for Falsification of Reports**

Section 309(c)(4) of the CWA provides that any person who knowingly makes any false material statement, representation, or certification in any record or other document submitted or required to be maintained under this General Permit, including reports of compliance or noncompliance shall upon conviction, be punished by a fine of not more than \$10,000 or by imprisonment for not more than two years or by both.

#### **O. Oil and Hazardous Substance Liability**

Nothing in this General Permit shall be construed to preclude the institution of any legal action or relieve the discharger from any responsibilities, liabilities, or penalties to which the discharger is or may be subject to under Section 311 of the CWA.

#### **P. Severability**

The provisions of this General Permit are severable; and, if any provision of this General Permit or the application of any provision of this General Permit to any circumstance is held invalid, the application of such provision to other circumstances and the remainder of this General Permit shall not be affected thereby.

#### **Q. Reopener Clause**

This General Permit may be modified, revoked and reissued, or terminated for cause due to promulgation of amended regulations, receipt of U.S. EPA guidance concerning regulated activities, judicial decision, or in accordance with 40 Code of Federal Regulations (CFR) 122.62, 122.63, 122.64, and 124.5.

#### **R. Penalties for Violations of Permit Conditions**

1. Section 309 of the CWA provides significant penalties for any person who violates a permit condition implementing Sections 301, 302, 306, 307, 308, 318, or 405 of the CWA or any permit condition or limitation implementing any such section in a permit issued under Section 402. Any person who violates any permit condition of this General Permit is subject to a civil penalty not to exceed \$37,500<sup>11</sup> per calendar day of such violation, as well as any other appropriate sanction provided by Section 309 of the CWA.

---

<sup>11</sup> May be further adjusted in accordance with the Federal Civil Penalties Inflation Adjustment Act.

2. The Porter-Cologne Water Quality Control Act also provides for civil and criminal penalties, which in some cases are greater than those under the CWA.

**S. Transfers**

This General Permit is not transferable.

**T. Continuation of Expired Permit**

This General Permit continues in force and effect until a new General Permit is issued or the SWRCB rescinds this General Permit. Only those dischargers authorized to discharge under the expiring General Permit are covered by the continued General Permit.

## V. EFFLUENT STANDARDS

### A. Narrative Effluent Limitations

1. Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
2. Dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.

### B. Numeric Effluent Limitations (NELs)

Table 1- Numeric Effluent Limitations, Numeric Action Levels, Test Methods, Detection Limits, and Reporting Units

Parameter	Test Method	Discharge Type	Min. Detection Limit	Units	Numeric Action Level	Numeric Effluent Limitation
pH	Field test with calibrated portable instrument	Risk Level 2	0.2	pH units	lower NAL = 6.5 upper NAL = 8.5	N/A
		Risk Level 3			lower NAL = 6.5 upper NAL = 8.5	lower NEL = 6.0 upper NEL = 9.0
Turbidity	EPA 0180.1 and/or field test with calibrated portable instrument	Risk Level 2	1	NTU	250 NTU	N/A
		Risk Level 3			250 NTU	500 NTU

#### 1. Numeric Effluent Limitations (NELs):

- a. **Storm Event, Daily Average pH Limits** – For Risk Level 3 dischargers, the pH of storm water and non-storm water discharges

shall be within the ranges specified in Table 1 during any site phase where there is a "high risk of pH discharge."<sup>12</sup>

- b. **Storm Event Daily Average Turbidity Limit** – For Risk Level 3 dischargers, the turbidity of storm water and non-storm water discharges shall not exceed 500 NTU.
2. If daily average sampling results are outside the range of pH NELs (i.e., is below the lower NEL for pH or exceeds the upper NEL for pH) or exceeds the turbidity NEL (as listed in Table 1), the discharger is in violation of this General Permit and shall electronically file monitoring results in violation within 5 business days of obtaining the results.
3. **Compliance Storm Event:**

Discharges of storm water from Risk Level 3 sites shall comply with applicable NELs (above) unless the storm event causing the discharges is determined after the fact to be equal to or larger than the Compliance Storm Event (expressed in inches of rainfall). The Compliance Storm Event for Risk Level 3 discharges is the 5 year, 24 hour storm (expressed in tenths of an inch of rainfall), as determined by using these maps:

<http://www.wrcc.dri.edu/pcpnfreq/nca5y24.gif>

<http://www.wrcc.dri.edu/pcpnfreq/sca5y24.gif>

Compliance storm event verification shall be done by reporting on-site rain gauge readings as well as nearby governmental rain gauge readings.

4. Dischargers shall not be required to comply with NELs if the site receives run-on from a forest fire or any other natural disaster.

### C. Numeric Action Levels (NALs)

1. For Risk Level 2 and 3 dischargers, the lower storm event average NAL for pH is 6.5 pH units and the upper storm event average NAL for pH is 8.5 pH units. The discharger shall take actions as described below if the discharge is outside of this range of pH values.

---

<sup>12</sup> A period of high risk of pH discharge is defined as a project's complete utilities phase, complete vertical build phase, and any portion of any phase where significant amounts of materials are placed directly on the land at the site in a manner that could result in significant alterations of the background pH of the discharges.

2. For Risk Level 2 and 3 dischargers, the NAL storm event daily average for turbidity is 250 NTU. The discharger shall take actions as described below if the discharge is outside of this range of turbidity values.
3. Whenever the results from a storm event daily average indicate that the discharge is below the lower NAL for pH, exceeds the upper NAL for pH, or exceeds the turbidity NAL (as listed in Table 1), the discharger shall conduct a construction site and run-on evaluation to determine whether pollutant source(s) associated with the site's construction activity may have caused or contributed to the NAL exceedance and shall immediately implement corrective actions if they are needed.
4. The site evaluation shall be documented in the SWPPP and specifically address whether the source(s) of the pollutants causing the exceedance of the NAL:
  - a. Are related to the construction activities and whether additional BMPs are required to (1) meet BAT/BCT requirements; (2) reduce or prevent pollutants in storm water discharges from causing exceedances of receiving water objectives; and (3) determine what corrective action(s) were taken or will be taken and with a description of the schedule for completion.

**AND/OR:**

- b. Are related to the run-on associated with the construction site location and whether additional BMPs measures are required to (1) meet BAT/BCT requirements; (2) reduce or prevent pollutants in storm water discharges from causing exceedances of receiving water objectives; and (3) what corrective action(s) were taken or will be taken with a description of the schedule for completion.

## **VI. RECEIVING WATER LIMITATIONS**

- A.** The discharger shall ensure that storm water discharges and authorized non-storm water discharges to any surface or ground water will not adversely affect human health or the environment.
- B.** The discharger shall ensure that storm water discharges and authorized non-storm water discharges will not contain pollutants in quantities that threaten to cause pollution or a public nuisance.
- C.** The discharger shall ensure that storm water discharges and authorized non-storm water discharges will not contain pollutants that cause or contribute to an exceedance of any applicable water quality objectives or water quality standards (collectively, WQS) contained in a Statewide Water Quality Control Plan, the California Toxics Rule, the National Toxics Rule, or the applicable Regional Water Board's Water Quality Control Plan (Basin Plan).
- D.** Dischargers located within the watershed of a CWA § 303(d) impaired water body, for which a TMDL has been approved by the U.S. EPA, shall comply with the approved TMDL if it identifies "construction activity" or land disturbance as a source of the pollution.

## VII. TRAINING QUALIFICATIONS AND CERTIFICATION REQUIREMENTS

### A. General

The discharger shall ensure that all persons responsible for implementing requirements of this General Permit shall be appropriately trained in accordance with this Section. Training should be both formal and informal, occur on an ongoing basis, and should include training offered by recognized governmental agencies or professional organizations. Those responsible for preparing and amending SWPPPs shall comply with the requirements in this Section VII.

The discharger shall provide documentation of all training for persons responsible for implementing the requirements of this General Permit in the Annual Reports.

### B. SWPPP Certification Requirements

1. **Qualified SWPPP Developer:** The discharger shall ensure that SWPPPs are written, amended and certified by a Qualified SWPPP Developer (QSD). A QSD shall have one of the following registrations or certifications, and appropriate experience, as required for:
  - a. A California registered professional civil engineer;
  - b. A California registered professional geologist or engineering geologist;
  - c. A California registered landscape architect;
  - d. A professional hydrologist registered through the American Institute of Hydrology;
  - e. A Certified Professional in Erosion and Sediment Control (CPESC)<sup>TM</sup> registered through Enviro Cert International, Inc.;
  - f. A Certified Professional in Storm Water Quality (CPSWQ)<sup>TM</sup> registered through Enviro Cert International, Inc.; or
  - g. A professional in erosion and sediment control registered through the National Institute for Certification in Engineering Technologies (NICET);

Effective two years after the adoption date of this General Permit, a QSD shall have attended a State Water Board-sponsored or approved QSD training course.

2. The discharger shall list the name and telephone number of the currently designated Qualified SWPPP Developer(s) in the SWPPP.
3. **Qualified SWPPP Practitioner:** The discharger shall ensure that all BMPs required by this General Permit are implemented by a Qualified SWPPP Practitioner (QSP). A QSP is a person responsible for non-storm water and storm water visual observations, sampling and analysis. Effective two years from the date of adoption of this General Permit, a QSP shall be either a QSD or have one of the following certifications:
  - a. A certified erosion, sediment and storm water inspector registered through Enviro Cert International, Inc.; or
  - b. A certified inspector of sediment and erosion control registered through Certified Inspector of Sediment and Erosion Control, Inc.

Effective two years after the adoption date of this General Permit, a QSP shall have attended a State Water Board-sponsored or approved QSP training course.

4. The LRP shall list in the SWPPP, the name of any Approved Signatory, and provide a copy of the written agreement or other mechanism that provides this authority from the LRP in the SWPPP.
5. The discharger shall include, in the SWPPP, a list of names of all contractors, subcontractors, and individuals who will be directed by the Qualified SWPPP Practitioner. This list shall include telephone numbers and work addresses. Specific areas of responsibility of each subcontractor and emergency contact numbers shall also be included.
6. The discharger shall ensure that the SWPPP and each amendment will be signed by the Qualified SWPPP Developer. The discharger shall include a listing of the date of initial preparation and the date of each amendment in the SWPPP.

## VIII. RISK DETERMINATION

The discharger shall calculate the site's sediment risk and receiving water risk during periods of soil exposure (i.e. grading and site stabilization) and use the calculated risks to determine a Risk Level(s) using the methodology in

Appendix 1. For any site that spans two or more planning watersheds,<sup>13</sup> the discharger shall calculate a separate Risk Level for each planning watershed. The discharger shall notify the State Water Board of the site's Risk Level determination(s) and shall include this determination as a part of submitting the PRDs. If a discharger ends up with more than one Risk Level determination, the Regional Water Board may choose to break the project into separate levels of implementation.

## **IX. RISK LEVEL 1 REQUIREMENTS**

Risk Level 1 Dischargers shall comply with the requirements included in Attachment C of this General Permit.

## **X. RISK LEVEL 2 REQUIREMENTS**

Risk Level 2 Dischargers shall comply with the requirements included in Attachment D of this General Permit.

## **XI. RISK LEVEL 3 REQUIREMENTS**

Risk Level 3 Dischargers shall comply with the requirements included in Attachment E of this General Permit.

## **XII. ACTIVE TREATMENT SYSTEMS (ATS)**

Dischargers choosing to implement an ATS on their site shall comply with all of the requirements in Attachment F of this General Permit.

---

<sup>13</sup> Planning watershed: defined by the Calwater Watershed documents as a watershed that ranges in size from approximately 3,000 to 10,000 acres <http://cain.ice.ucdavis.edu/calwater/calwfaq.html>, <http://gis.ca.gov/catalog/BrowseRecord.epi?id=22175>.

### XIII. POST-CONSTRUCTION STANDARDS

- A. All dischargers shall comply with the following runoff reduction requirements unless they are located within an area subject to post-construction standards of an active Phase I or II municipal separate storm sewer system (MS4) permit that has an approved Storm Water Management Plan.
1. This provision shall take effect three years from the adoption date of this permit, or later at the discretion of the Executive Officer of the Regional Board.
  2. The discharger shall demonstrate compliance with the requirements of this section by submitting with their NOI a map and worksheets in accordance with the instructions in Appendix 2. The discharger shall use non-structural controls unless the discharger demonstrates that non-structural controls are infeasible or that structural controls will produce greater reduction in water quality impacts.
  3. The discharger shall, through the use of non-structural and structural measures as described in Appendix 2, replicate the pre-project water balance (for this permit, defined as the volume of rainfall that ends up as runoff) for the smallest storms up to the 85<sup>th</sup> percentile storm event (or the smallest storm event that generates runoff, whichever is larger). Dischargers shall inform Regional Water Board staff at least 30 days prior to the use of any structural control measure used to comply with this requirement. Volume that cannot be addressed using non-structural practices shall be captured in structural practices and approved by the Regional Water Board. When seeking Regional Board approval for the use of structural practices, dischargers shall document the infeasibility of using non-structural practices on the project site, or document that there will be fewer water quality impacts through the use of structural practices.
  4. For sites whose disturbed area exceeds two acres, the discharger shall preserve the pre-construction drainage density (miles of stream length per square mile of drainage area) for all drainage areas within the area serving a first order stream<sup>14</sup> or larger stream and ensure that post-project time of runoff concentration is equal or greater than pre-project time of concentration.

---

<sup>14</sup> A first order stream is defined as a stream with no tributaries.

- B.** All dischargers shall implement BMPs to reduce pollutants in storm water discharges that are reasonably foreseeable after all construction phases have been completed at the site (Post-construction BMPs).

#### **XIV. SWPPP REQUIREMENTS**

- A.** The discharger shall ensure that the Storm Water Pollution Prevention Plans (SWPPPs) for all traditional project sites are developed and amended or revised by a QSD. The SWPPP shall be designed to address the following objectives:
1. All pollutants and their sources, including sources of sediment associated with construction, construction site erosion and all other activities associated with construction activity are controlled;
  2. Where not otherwise required to be under a Regional Water Board permit, all non-storm water discharges are identified and either eliminated, controlled, or treated;
  3. Site BMPs are effective and result in the reduction or elimination of pollutants in storm water discharges and authorized non-storm water discharges from construction activity to the BAT/BCT standard;
  4. Calculations and design details as well as BMP controls for site run-on are complete and correct, and
  5. Stabilization BMPs installed to reduce or eliminate pollutants after construction are completed.
- B.** To demonstrate compliance with requirements of this General Permit, the QSD shall include information in the SWPPP that supports the conclusions, selections, use, and maintenance of BMPs.
- C.** The discharger shall make the SWPPP available at the construction site during working hours while construction is occurring and shall be made available upon request by a State or Municipal inspector. When the original SWPPP is retained by a crewmember in a construction vehicle and is not currently at the construction site, current copies of the BMPs and map/drawing will be left with the field crew and the original SWPPP shall be made available via a request by radio/telephone.

## **XV. REGIONAL WATER BOARD AUTHORITIES**

- A.** In the case where the Regional Water Board does not agree with the discharger's self-reported risk level (e.g., they determine themselves to be a Level 1 Risk when they are actually a Level 2 Risk site), Regional Water Boards may either direct the discharger to reevaluate the Risk Level(s) for their site or terminate coverage under this General Permit.
- B.** Regional Water Boards may terminate coverage under this General Permit for dischargers who fail to comply with its requirements or where they determine that an individual NPDES permit is appropriate.
- C.** Regional Water Boards may require dischargers to submit a Report of Waste Discharge / NPDES permit application for Regional Water Board consideration of individual requirements.
- D.** Regional Water Boards may require additional Monitoring and Reporting Program Requirements, including sampling and analysis of discharges to sediment-impaired water bodies.
- E.** Regional Water Boards may require dischargers to retain records for more than the three years required by this General Permit.

## **XVI. ANNUAL REPORTING REQUIREMENTS**

- A.** All dischargers shall prepare and electronically submit an Annual Report no later than September 1 of each year.
- B.** The discharger shall certify each Annual Report in accordance with the Special Provisions.
- C.** The discharger shall retain an electronic or paper copy of each Annual Report for a minimum of three years after the date the annual report is filed.
- D.** The discharger shall include storm water monitoring information in the Annual Report consisting of:
  - 1. a summary and evaluation of all sampling and analysis results, including copies of laboratory reports;
  - 2. the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as "less than the method detection limit");
  - 3. a summary of all corrective actions taken during the compliance year;
  - 4. identification of any compliance activities or corrective actions that were not implemented;
  - 5. a summary of all violations of the General Permit;
  - 6. the names of individual(s) who performed the facility inspections, sampling, visual observation (inspections), and/or measurements;
  - 7. the date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation (rain gauge); and
  - 8. the visual observation and sample collection exception records and reports specified in Attachments C, D, and E.
- E.** The discharger shall provide training information in the Annual Report consisting of:
  - 1. documentation of all training for individuals responsible for all activities associated with compliance with this General Permit;

2. documentation of all training for individuals responsible for BMP installation, inspection, maintenance, and repair; and
3. documentation of all training for individuals responsible for overseeing, revising, and amending the SWPPP.

**ATTACHMENT A**  
**Linear Underground/ Overhead Requirements**

A.	DEFINITION OF LINEAR UNDERGROUND/OVERHEAD PROJECTS ....	1
B.	LINEAR PROJECT PERMIT REGISTRATION DOCUMENTS (PRDs) .....	3
C.	LINEAR PROJECT TERMINATION OF COVERAGE REQUIREMENTS ..	4
D.	DISCHARGE PROHIBITIONS .....	6
E.	SPECIAL PROVISIONS .....	8
F.	EFFLUENT STANDARDS.....	13
G.	RECEIVING WATER LIMITATIONS .....	16
H.	TRAINING QUALIFICATIONS .....	17
I.	TYPES OF LINEAR PROJECTS .....	19
J.	LUP TYPE-SPECIFIC REQUIREMENTS .....	20
K.	STORM WATER POLLUTION PREVENTION PLAN (SWPPP) REQUIREMENTS .....	28
L.	REGIONAL WATER BOARD AUTHORITIES .....	29
M.	MONITORING AND REPORTING REQUIREMENTS .....	31

All Linear Underground/Overhead project dischargers who submit permit registration documents (PRDs) indicating their intention to be regulated under the provisions of this General Permit shall comply with the following:

**A. DEFINITION OF LINEAR UNDERGROUND/OVERHEAD PROJECTS**

1. Linear Underground/Overhead Projects (LUPs) include, but are not limited to, any conveyance, pipe, or pipeline for the transportation of any gaseous, liquid (including water and wastewater for domestic municipal services), liquescent, or slurry substance; any cable line or wire for the transmission of electrical energy; any cable line or wire for communications (e.g., telephone, telegraph, radio, or television messages); and associated ancillary facilities. Construction activities associated with LUPs include, but are not limited to, (a) those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment, and associated ancillary facilities); and include, but are not limited to, (b) underground utility mark-out, potholing, concrete and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/tower pad and cable/wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/or pavement repair or replacement, and stockpile/borrow locations.
2. LUP evaluation shall consist of two tasks:

- a. Confirm that the project or project section(s) qualifies as an LUP. The State Water Board website contains a project determination guidance flowchart.  
[http://www.waterboards.ca.gov/water\\_issues/programs/stormwater/constructionpermits.shtml](http://www.waterboards.ca.gov/water_issues/programs/stormwater/constructionpermits.shtml)
  - b. Identify which Type(s) (1, 2 or 3 described in Section I below) are applicable to the project or project sections based on project sediment and receiving water risk. (See Attachment A.1)
3. A Legally Responsible Person (LRP) for a Linear Underground/Overhead project is required to obtain CGP coverage under one or more permit registration document (PRD) electronic submittals to the State Water Board's Storm Water Multi-Application and Report Tracking (SMARTs) system. Attachment A.1 contains a flow chart to be used when determining if a linear project qualifies for coverage and to determine LUP Types. Since a LUP may be constructed within both developed and undeveloped locations and portions of LUPs may be constructed by different contractors, LUPs may be broken into logical permit sections. Sections may be determined based on portions of a project conducted by one contractor. Other situations may also occur, such as the time period in which the sections of a project will be constructed (e.g. project phases), for which separate permit coverage is possible. For projects that are broken into separate sections, a description of how each section relates to the overall project and the definition of the boundaries between sections shall be clearly stated.
  4. Where construction activities transverse or enter into different Regional Water Board jurisdictions, LRPs shall obtain permit coverage for each Regional Water Board area involved prior to the commencement of construction activities.
  5. Small Construction Rainfall Erosivity Waiver

EPA's Small Construction Erosivity Waiver applies to sites between one and five acres demonstrating that there are no adverse water quality impacts.

Dischargers eligible for a Rainfall Erosivity Waiver based on low erosivity potential shall complete the electronic Notice of Intent (NOI) and Sediment Risk form through the State Water Board's SMARTS system, certifying that the construction activity will take place during a period when the value of the rainfall erosivity factor is less than five. Where the LRP changes or another LRP is added during construction, the new LRP must also submit a waiver certification through the SMARTS system.

If a small linear construction site continues beyond the projected completion date given on the waiver certification, the LRP shall recalculate the rainfall erosivity factor for the new project duration and submit this information through the SMARTS system. If the new R factor is below five (5), the discharger shall update through SMARTS all applicable information on the waiver certification and retain a copy of the revised waiver onsite. The LRP shall submit the new waiver certification 30 days prior to the projected completion date listed on the original waiver form to assure exemption from permitting requirements is uninterrupted. If the new R factor is five (5) or above, the LRP shall be required to apply for coverage under this Order.

## **B. LINEAR PROJECT PERMIT REGISTRATION DOCUMENTS (PRDs)**

Any information provided to the Regional Water Board shall comply with the Homeland Security Act and any other federal law that concerns security in the United States; any information that does not comply should not be submitted. PRDs shall consist of the following:

### **1. Notice of Intent (NOI)**

Prior to construction activities, the LRP of a proposed linear underground/overhead project shall utilize the processes and methods provided in Attachment A.2, Permit Registration Documents (PRDs) – General Instructions for Linear Underground/Overhead Projects to comply with the Construction General Permit.

### **2. Site Maps**

LRPs submitting PRDs shall include at least 3 maps. The first map will be a zoomed<sup>1</sup> 1000-1500 ft vicinity map that shows the starting point of the project. The second will be a zoomed map of 1000-1500 ft showing the ending location of the project. The third will be a larger view vicinity map, 1000 ft to 2000 ft, displaying the entire project location depending on the project size, and indicating the LUP type (1, 2 or 3) areas within the total project footprint.

### **3. Drawings**

LRPs submitting PRDs shall include a construction drawing(s) or other appropriate drawing(s) or map(s) that shows the locations of storm drain

---

<sup>1</sup> An image with a close-up/enhanced detailed view of site features that show minute details such as streets and neighboring structures.

Or: An image with a close-up/enhanced detailed view of the site's surrounding infrastructure.

Or: An image with a close up detailed view of the project and its surroundings.

inlets and waterbodies<sup>2</sup> that may receive discharges from the construction activities and that shows the locations of BMPs to be installed for all those BMPs that can be illustrated on the revisable drawing(s) or map(s). If storm drain inlets, waterbodies, and/or BMPs cannot be adequately shown on the drawing(s) or map(s) they should be described in detail within the SWPPP.

#### **4. Storm Water Pollution Prevention Plan (SWPPP)**

LUP dischargers shall comply with the SWPPP Preparation, Implementation, and Oversight requirements in Section K of this Attachment.

#### **5. Contact information**

LUP dischargers shall include contact information for all contractors (or subcontractors) responsible for each area of an LUP project. This should include the names, telephone numbers, and addresses of contact personnel. Specific areas of responsibility of each contact, and emergency contact numbers should also be included.

6. In the case of a public emergency that requires immediate construction activities, a discharger shall submit a brief description of the emergency construction activity within five days of the onset of construction, and then shall submit all PRDs within thirty days.

### **C. LINEAR PROJECT TERMINATION OF COVERAGE REQUIREMENTS**

The LRP may terminate coverage of an LUP when construction activities are completed by submitting an electronic notice of termination (NOT) through the State Water Board's SMARTS system. Termination requirements are different depending on the complexity of the LUP. An LUP is considered complete when: (a) there is no potential for construction-related storm water pollution; (b) all elements of the SWPPP have been completed; (c) construction materials and waste have been disposed of properly; (d) the site is in compliance with all local storm water management requirements; and (e) the LRP submits a notice of termination (NOT) and has received approval for termination from the appropriate Regional Water Board office.

#### **1. LUP Stabilization Requirements**

The LUP discharger shall ensure that all disturbed areas of the construction site are stabilized prior to termination of coverage under this General Permit. Final stabilization for the purposes of submitting an NOT

---

<sup>2</sup> Includes basin(s) that the MS4 storm sewer systems may drain to for Hydromodification or Hydrological Conditional of Concerns under the MS4 permits.

is satisfied when all soil disturbing activities are completed and one of the following criteria is met:

- a. In disturbed areas that were vegetated prior to construction activities of the LUP, the area disturbed must be re-established to a uniform vegetative cover equivalent to 70 percent coverage of the preconstruction vegetative conditions. Where preconstruction vegetation covers less than 100 percent of the surface, such as in arid areas, the 70 percent coverage criteria is adjusted as follows: if the preconstruction vegetation covers 50 percent of the ground surface, 70 percent of 50 percent ( $.70 \times .50 = .35$ ) would require 35 percent total uniform surface coverage; or
- b. Where no vegetation is present prior to construction, the site is returned to its original line and grade and/or compacted to achieve stabilization; or
- c. Equivalent stabilization measures have been employed. These measures include, but are not limited to, the use of such BMPs as blankets, reinforced channel liners, soil cement, fiber matrices, geotextiles, or other erosion resistant soil coverings or treatments.

## **2. LUP Termination of Coverage Requirements**

The LRP shall file an NOT through the State Water Board's SMARTS system. By submitting an NOT, the LRP is certifying that construction activities for an LUP are complete and that the project is in full compliance with requirements of this General Permit and that it is now compliant with soil stabilization requirements where appropriate. Upon approval by the appropriate Regional Water Board office, permit coverage will be terminated.

## **3. Revising Coverage for Change of Acreage**

When the LRP of a portion of an LUP construction project changes, or when a phase within a multi-phase project is completed, the LRP may reduce the total acreage covered by this General Permit. In reducing the acreage covered by this General Permit, the LRP shall electronically file revisions to the PRDs that include:

- a. a revised NOI indicating the new project size;
- b. a revised site map showing the acreage of the project completed, acreage currently under construction, acreage sold, transferred or added, and acreage currently stabilized.
- c. SWPPP revisions, as appropriate; and
- d. certification that any new LRPs have been notified of applicable requirements to obtain General Permit coverage. The certification shall include the name, address, telephone number, and e-mail address (if known) of the new LRP.

If the project acreage has increased, dischargers shall mail payment of revised annual fees within 14 days of receiving the revised annual fee notification.

#### **D. DISCHARGE PROHIBITIONS**

1. LUP dischargers shall not violate any discharge prohibitions contained in applicable Basin Plans or statewide water quality control plans. Waste discharges to Areas of Special Biological Significance (ASBS) are prohibited by the California Ocean Plan, unless granted an exception issued by the State Water Board.
2. LUP dischargers are prohibited from discharging non-storm water that is not otherwise authorized by this General Permit. Non-storm water discharges authorized by this General Permit<sup>3</sup> may include, fire hydrant flushing, irrigation of vegetative erosion control measures, pipe flushing and testing, water to control dust, street cleaning, dewatering,<sup>4</sup> uncontaminated groundwater from dewatering, and other discharges not subject to a separate general NPDES permit adopted by a Regional Water Board. Such discharges are allowed by this General Permit provided they are not relied upon to clean up failed or inadequate construction or post-construction BMPs designed to keep materials on site. These authorized non-storm water discharges:

---

<sup>3</sup> Dischargers must identify all authorized non-storm water discharges in the LUP's SWPPP and identify BMPs that will be implemented to either eliminate or reduce pollutants in non-storm water discharges. Regional Water Boards may direct the discharger to discontinue discharging such non-storm water discharges if determined that such discharges discharge significant pollutants or threaten water quality.

<sup>4</sup>Dewatering activities may be prohibited or need coverage under a separate permit issued by the Regional Water Boards. Dischargers shall check with the appropriate Regional Water Boards for any required permit or basin plan conditions prior to initial dewatering activities to land, storm drains, or waterbodies.

- a. Shall not cause or contribute to a violation of any water quality standard;
- b. Shall not violate any other provision of this General Permit;
- c. Shall not violate any applicable Basin Plan;
- d. Shall comply with BMPs as described in the SWPPP;
- e. Shall not contain toxic constituents in toxic amounts or (other) significant quantities of pollutants;
- f. Shall be monitored and meets the applicable NALs and NELs; and
- g. Shall be reported by the discharger in the Annual Report.

If any of the above conditions are not satisfied, the discharge is not authorized by this General Permit. The discharger shall notify the Regional Water Board of any anticipated non-storm water discharges not authorized by this General Permit to determine the need for a separate NPDES permit.

Additionally, some LUP dischargers may be required to obtain a separate permit if the applicable Regional Water Board has adopted a General Permit for dewatering discharges. Wherever feasible, alternatives, that do not result in the discharge of non-storm water, shall be implemented in accordance with this Attachment's Section K.2 - SWPPP Implementation Schedule.

3. LUP dischargers shall ensure that trench spoils or any other soils disturbed during construction activities that are contaminated<sup>5</sup> are not discharged with storm water or non-storm water discharges into any storm drain or water body except pursuant to an NPDES permit.

When soil contamination is found or suspected and a responsible party is not identified, or the responsible party fails to promptly take the appropriate action, the LUP discharger shall have those soils sampled and tested to ensure that proper handling and public safety measures are

---

<sup>5</sup> Contaminated soil contains pollutants in concentrations that exceed the appropriate thresholds that various regulatory agencies set for those substances. Preliminary testing of potentially contaminated soils will be based on odor, soil discoloration, or prior history of the site's chemical use and storage and other similar factors. When soil contamination is found or suspected and a responsible party is not identified, or the responsible party fails to promptly take the appropriate action, the discharger shall have those soils sampled and tested to ensure proper handling and public safety measures are implemented. The legally responsible person will notify the appropriate local, State, or federal agency(ies) when contaminated soil is found at a construction site, and will notify the Regional Water Board by submitting an NOT at the completion of the project.

implemented. The LUP discharger shall notify the appropriate local, State, and federal agency(ies) when contaminated soil is found at a construction site, and will notify the appropriate Regional Water Board.

4. Discharging any pollutant-laden water that will cause or contribute to an exceedance of the applicable Regional Water Board's Basin Plan from a dewatering site or sediment basin into any receiving water or storm drain is prohibited.
5. Debris<sup>6</sup> resulting from construction activities are prohibited from being discharged from construction project sites.

## **E. SPECIAL PROVISIONS**

### **1. Duty to Comply**

- a. The LUP discharger must comply with all of the conditions of this General Permit. Any permit noncompliance constitutes a violation of the Clean Water Act (CWA) and the Porter-Cologne Water Quality Control Act and is grounds for enforcement action and/or removal from General Permit coverage.
- b. The LUP discharger shall comply with effluent standards or prohibitions established under Section 307(a) of the CWA for toxic pollutants within the time provided in the regulations that establish these standards or prohibitions, even if this General Permit has not yet been modified to incorporate the requirement.

### **2. General Permit Actions**

- a. This General Permit may be modified, revoked and reissued, or terminated for cause. The filing of a request by the discharger for a General Permit modification, revocation and reissuance, or termination, or a notification of planned changes or anticipated noncompliance does not annul any General Permit condition.

---

<sup>6</sup> Litter, rubble, discarded refuse, and remains of something destroyed.

- b. If any toxic effluent standard or prohibition (including any schedule of compliance specified in such effluent standard or prohibition) is promulgated under Section 307(a) of the CWA for a toxic pollutant which is present in the discharge and that standard or prohibition is more stringent than any limitation on the pollutant in this General Permit, this General Permit shall be modified or revoked and reissued to conform to the toxic effluent standard or prohibition and the dischargers so notified.

### **3. Need to Halt or Reduce Activity Not a Defense**

It shall not be a defense for an LUP discharger in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of this General Permit.

### **4. Duty to Mitigate**

The LUP discharger shall take all responsible steps to minimize or prevent any discharge in violation of this General Permit, which has a reasonable likelihood of adversely affecting human health or the environment.

### **5. Proper Operation and Maintenance**

The LUP discharger shall at all times properly operate and maintain any facilities and systems of treatment and control (and related appurtenances) which are installed or used by the discharger to achieve compliance with the conditions of this General Permit and with the requirements of the Storm Water Pollution Prevention Plan (SWPPP). Proper operation and maintenance also includes adequate laboratory controls and appropriate quality assurance procedures. Proper operation and maintenance may require the operation of backup or auxiliary facilities or similar systems installed by a discharger when necessary to achieve compliance with the conditions of this General Permit.

### **6. Property Rights**

This General Permit does not convey any property rights of any sort or any exclusive privileges, nor does it authorize any injury to private property or any invasion of personal rights, nor does it authorize any infringement of Federal, State, or local laws or regulations.

### **7. Duty to Maintain Records and Provide Information**

- a. The LUP discharger shall maintain a paper or electronic copy of all required records, including a copy of this General Permit, for three years from the date generated or date submitted, whichever is last. These records shall be kept at the construction site or in a crew

member's vehicle until construction is completed, and shall be made available upon request.

- b. The LUP discharger shall furnish the Regional Water Board, State Water Board, or USEPA, within a reasonable time, any requested information to determine compliance with this General Permit. The LUP discharger shall also furnish, upon request, copies of records that are required to be kept by this General Permit.

## **8. Inspection and Entry**

The LUP discharger shall allow the Regional Water Board, State Water Board, USEPA, and/or, in the case of construction sites which discharge through a municipal separate storm sewer, an authorized representative of the municipal operator of the separate storm sewer system receiving the discharge, upon the presentation of credentials and other documents as may be required by law, to:

- a. Enter upon the discharger's premises at reasonable times where a regulated construction activity is being conducted or where records must be kept under the conditions of this General Permit;
- b. Access and copy at reasonable times any records that must be kept under the conditions of this General Permit;
- c. Inspect at reasonable times the complete construction site, including any off-site staging areas or material storage areas, and the erosion/sediment controls; and
- d. Sample or monitor at reasonable times for the purpose of ensuring General Permit compliance.

## **9. Electronic Signature and Certification Requirements**

- a. All Permit Registration Documents (PRDs) and Notices of Termination (NOTs) shall be electronically signed, certified, and submitted via SMARTS to the State Water Board. Either the Legally Responsible Person (LRP) or a person legally authorized to sign and certify PRDs and NOTs on behalf of the LRP (the LRP's Approved Signatory) must submit all information electronically via SMARTS. For Linear Underground/Overhead projects, the Legally Responsible Person is the person in charge of the utility company, municipality, or other public or private company or agency that owns or operates the LUP. The LRP's Approved Signatory must be one of the following:
  - i For a corporation: a responsible corporate officer. For the purpose of this section, a responsible corporate officer means:

- (1) a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy or decision-making functions for the corporation; or
  - (2) the manager of the facility if authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures;
- ii For a partnership or sole proprietorship: a general partner or the proprietor, respectively; or
  - iii For a municipality, State, Federal, or other public agency: either a principal executive officer or ranking elected official. The principal executive officer of a Federal agency includes the chief executive officer of the agency or the senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., Regional Administrators of U.S. EPA).
- b. Changes to Authorization. If an approved signatory's authorization is no longer accurate, a new authorization satisfying the requirements of paragraph (a) of this section must be submitted via SMARTS prior to or together with any reports, information or applications to be signed by an approved signatory.
  - c. All SWPPP revisions, annual reports, or other information required by the General Permit (other than PRDs and NOTs) or requested by the Regional Water Board, State Water Board, USEPA, or local storm water management agency shall be certified and submitted by the LRP or the LRP's approved signatory as described above.

## 10. Certification

Any person signing documents under Section E.9 above, shall make the following certification:

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

**11. Anticipated Noncompliance**

The LUP discharger shall give advance notice to the Regional Water Board and local storm water management agency of any planned changes in the construction activity, which may result in noncompliance with General Permit requirements.

**12. Penalties for Falsification of Reports**

Section 309(c)(4) of the CWA provides that any person who knowingly makes any false material statement, representation, or certification in any record or other document submitted or required to be maintained under this General Permit, including reports of compliance or noncompliance shall upon conviction, be punished by a fine of not more than \$10,000 or by imprisonment for not more than two years or by both.

**13. Oil and Hazardous Substance Liability**

Nothing in this General Permit shall be construed to preclude the institution of any legal action or relieve the discharger from any responsibilities, liabilities, or penalties to which the LUP discharger is or may be subject to under Section 311 of the CWA.

**14. Severability**

The provisions of this General Permit are severable; and, if any provision of this General Permit or the application of any provision of this General Permit to any circumstance is held invalid, the application of such provision to other circumstances and the remainder of this General Permit shall not be affected thereby.

**15. Reopener Clause**

This General Permit may be modified, revoked and reissued, or terminated for cause due to promulgation of amended regulations, receipt of USEPA guidance concerning regulated activities, judicial decision, or in accordance with 40 Code of Federal Regulations (CFR) 122.62, 122.63, 122.64, and 124.5.

**16. Penalties for Violations of Permit Conditions**

- a. Section 309 of the CWA provides significant penalties for any person who violates a permit condition implementing Sections 301, 302, 306, 307, 308, 318, or 405 of the CWA or any permit condition or limitation implementing any such section in a permit issued under Section 402. Any person who violates any permit condition of this General Permit is

subject to a civil penalty not to exceed \$37,500<sup>7</sup> per calendar day of such violation, as well as any other appropriate sanction provided by Section 309 of the CWA.

- b. The Porter-Cologne Water Quality Control Act also provides for civil and criminal penalties, which in some cases are greater than those under the CWA.

### **17. Transfers**

This General Permit is not transferable. A new LRP of an ongoing construction activity must submit PRDs in accordance with the requirements of this General Permit to be authorized to discharge under this General Permit. An LRP who is a property owner with active General Permit coverage who sells a fraction or all the land shall inform the new property owner(s) of the requirements of this General Permit.

### **18. Continuation of Expired Permit**

This General Permit continues in force and effect until a new General Permit is issued or the SWRCB rescinds this General Permit. Only those dischargers authorized to discharge under the expiring General Permit are covered by the continued General Permit.

## **F. EFFLUENT STANDARDS**

### **1. Narrative Effluent Limitations**

- a. LUP dischargers shall ensure that storm water discharges and authorized non-storm water discharges regulated by this General Permit do not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
- b. LUP dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of structural or non-structural controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.

---

<sup>7</sup> May be further adjusted in accordance with the Federal Civil Penalties Inflation Adjustment Act

## 2. Numeric Effluent Limitations (NELs)

Table 1. Numeric Effluent Limitations, Numeric Action Levels, Test Methods, Detection Limits, and Reporting Units

Parameter	Test Method	Discharge Type	Min. Detection Limit	Units	Numeric Action Level	Numeric Effluent Limitation
pH	Field test with calibrated portable instrument	LUP Type 2	0.2	pH units	lower NAL = 6.5 upper NAL = 8.5	N/A
		LUP Type 3			lower NAL = 6.5 upper NAL = 8.5	lower NEL = 6.0 upper NEL = 9.0
Turbidity EPA	0180.1 and/or field test with calibrated portable instrument	LUP Type 2	1 NTU		250 NTU	N/A
		LUP Type 3			250 NTU	500 NTU

### a. Numeric Effluent Limitations (NELs):

- i **Storm Event, Daily Average pH Limits** – For LUP Type 3 dischargers, the daily average pH of storm water and non-storm water discharges shall be within the ranges specified in Table 1 during any project phase where there is a "high risk of pH discharge."<sup>8</sup>
- ii **Storm Event Daily Average Turbidity Limit** – For LUP Type 3 dischargers, the daily average turbidity of storm water and non-storm water discharges shall not exceed 500 NTU.

<sup>8</sup> A period of high risk of pH discharge is defined as a project's complete utilities phase, complete vertical build phase, and any portion of any phase where significant amounts of materials are placed directly on the land at the site in a manner that could result in significant alterations of the background pH of the discharges.

- b. If a daily average sample result is outside the range of pH NELs (i.e., is below the lower NEL for pH or exceeds the upper NEL for pH) or exceeds the turbidity NEL (as listed in Table 1), the discharger is in violation of this General Permit and shall electronically file the results in violation within 5 business days of obtaining the results.
- c. Compliance Storm Event:

Discharges of storm water from LUP Type 3 sites shall comply with applicable NELs (above) unless the storm event causing the discharges is determined after the fact to be equal to or larger than the Compliance Storm Event (expressed in inches of rainfall). The Compliance Storm Event for LUP Type 3 discharges is the 5-year, 24-hour storm (expressed in tenths of an inch of rainfall), as determined by using these maps:

<http://www.wrcc.dri.edu/pcpnfreq/nca5y24.gif>

<http://www.wrcc.dri.edu/pcpnfreq/sca5y24.gif>

Compliance storm event verification shall be done by reporting on-site rain gauge readings as well as nearby governmental rain gauge readings.

- d. Dischargers shall not be required to comply with NELs if the site receives run-on from a forest fire or any other natural disaster.

### 3. Numeric Action Levels (NALs)

- a. For LUP Type 2 and 3 dischargers, the lower storm event daily average NAL for pH is 6.5 pH units and the upper storm event daily average NAL for pH is 8.5 pH units. The LUP discharger shall take actions as described below if the storm event daily average discharge is outside of this range of pH values.
- b. For LUP Type 2 and 3 dischargers, the storm event daily average NAL for turbidity is 250 NTU. The discharger shall take actions as described below if the storm event daily average discharge is outside of this range of turbidity values.
- c. Whenever daily average analytical effluent monitoring results indicate that the discharge is below the lower NAL for pH, exceeds the upper NAL for pH, or exceeds the turbidity NAL (as listed in Table 1), the LUP discharger shall conduct a construction site and run-on evaluation to determine whether pollutant source(s) associated with the site's construction activity may have caused or contributed to the NAL

exceedance and shall immediately implement corrective actions if they are needed.

- d. The site evaluation will be documented in the SWPPP and specifically address whether the source(s) of the pollutants causing the exceedance of the NAL:
- i Are related to the construction activities and whether additional BMPs or SWPPP implementation measures are required to (1) meet BAT/BCT requirements; (2) reduce or prevent pollutants in storm water discharges from causing exceedances of receiving water objectives; and (3) determine what corrective action(s) were taken or will be taken and with a description of the schedule for completion.

**AND/OR:**

- ii Are related to the run-on associated with the construction site location and whether additional BMPs or SWPPP implementation measures are required to (1) meet BAT/BCT requirements; (2) reduce or prevent pollutants in storm water discharges from causing exceedances of receiving water objectives; and (3) decide what corrective action(s) were taken or will be taken, including a description of the schedule for completion.

**G. RECEIVING WATER LIMITATIONS**

1. LUP dischargers shall ensure that storm water discharges and authorized non-storm water discharges to any surface or ground water will not adversely affect human health or the environment.
2. LUP dischargers shall ensure that storm water discharges and authorized non-storm water discharges will not contain pollutants in quantities that threaten to cause pollution or a public nuisance.
3. LUP dischargers shall ensure that storm water discharges and authorized non-storm water discharges will not contain pollutants that cause or contribute to an exceedance of any applicable water quality objectives or water quality standards (collectively, WQS) contained in a Statewide Water Quality Control Plan, the California Toxics Rule, the National Toxics Rule, or the applicable Regional Water Board's Water Quality Control Plan (Basin Plan).

## H. TRAINING QUALIFICATIONS

### 1. General

All persons responsible for implementing requirements of this General Permit shall be appropriately trained. Training should be both formal and informal, occur on an ongoing basis, and should include training offered by recognized governmental agencies or professional organizations. Persons responsible for preparing, amending and certifying SWPPPs shall comply with the requirements in this Section H.

### 2. SWPPP Certification Requirements

- a. **Qualified SWPPP Developer:** The LUP discharger shall ensure that all SWPPPs be written, amended and certified by a Qualified SWPPP Developer (QSD). A QSD shall have one of the following registrations or certifications, and appropriate experience, as required for:
- i A California registered professional civil engineer;
  - ii A California registered professional geologist or engineering geologist;
  - iii A California registered landscape architect;
  - iv A professional hydrologist registered through the American Institute of Hydrology;
  - v A certified professional in erosion and sediment control (CPESC)<sup>™</sup> registered through Enviro Cert International, Inc;
  - vi A certified professional in storm water quality (CPSWQ)<sup>™</sup> registered through Enviro Cert International, Inc.; or
  - vii A certified professional in erosion and sediment control registered through the National Institute for Certification in Engineering Technologies (NICET).

Effective two years after the adoption date of this General Permit, a QSD shall have attended a State Water Board-sponsored or approved QSD training course.

- b. The LUP discharger shall ensure that the SWPPP is written and amended, as needed, to address the specific circumstances for each construction site covered by this General Permit prior to commencement of construction activity for any stage.
- c. The LUP discharger shall list the name and telephone number of the currently designated Qualified SWPPP Developer(s) in the SWPPP.
- d. **Qualified SWPPP Practitioner:** The LUP discharger shall ensure that all elements of any SWPPP for each project will be implemented by a Qualified SWPPP Practitioner (QSP). A QSP is a person responsible for non-storm water and storm water visual observations, sampling and analysis, and for ensuring full compliance with the permit and implementation of all elements of the SWPPP. Effective two years from the date of adoption of this General Permit, a QSP shall be either a QSD or have one of the following certifications:
  - i A certified erosion, sediment and storm water inspector registered through Certified Professional in Erosion and Sediment Control, Inc.; or
  - ii A certified inspector of sediment and erosion control registered through Certified Inspector of Sediment and Erosion Control, Inc.

Effective two years after the adoption date of this General Permit, a QSP shall have attended a State Water Board-sponsored or approved QSP training course.
- e. The LUP discharger shall ensure that the SWPPP include a list of names of all contractors, subcontractors, and individuals who will be directed by the Qualified SWPPP Practitioner, and who is ultimately responsible for implementation of the SWPPP. This list shall include telephone numbers and work addresses. Specific areas of responsibility of each subcontractor and emergency contact numbers shall also be included.
- f. The LUP discharger shall ensure that the SWPPP and each amendment be signed by the Qualified SWPPP Developer. The LUP discharger shall include a listing of the date of initial preparation and the dates of each amendment in the SWPPP.

## I. TYPES OF LINEAR PROJECTS

This attachment establishes three types (Type 1, 2 & 3) of complexity for areas within an LUP or project section based on threat to water quality. Project area Types are determined through Attachment A.1.

The Type 1 requirements below establish the baseline requirements for all LUPs subject to this General Permit. Additional requirements for Type 2 and Type 3 LUPs are labeled.

### 1. Type 1 LUPs:

LUP dischargers with areas of a LUP designated as Type 1 shall comply with the requirements in this Attachment. Type 1 LUPs are:

- a. Those construction areas where 70 percent or more of the construction activity occurs on a paved surface and where areas disturbed during construction will be returned to preconstruction conditions or equivalent protection established at the end of the construction activities for the day; or
- b. Where greater than 30 percent of construction activities occur within the non-paved shoulders or land immediately adjacent to paved surfaces, or where construction occurs on unpaved improved roads, including their shoulders or land immediately adjacent to them where:
  - i Areas disturbed during construction will be returned to preconstruction conditions or equivalent protection is established at the end of the construction activities for the day to minimize the potential for erosion and sediment deposition, and
  - ii Areas where established vegetation was disturbed during construction will be stabilized and re-vegetated by the end of project. When required, adequate temporary stabilization BMPs will be installed and maintained until vegetation is established to meet minimum cover requirements established in this General Permit for final stabilization.
- c. Where the risk determination is as follows:
  - i Low sediment risk, low receiving water risk, or
  - ii Low sediment risk, medium receiving water risk, or
  - iii Medium sediment risk, low receiving water risk

**2. Type 2 LUPs:**

Type 2 LUPs are determined by the Combined Risk Matrix in Attachment A.1. Type 2 LUPs have the specified combination of risk:

- d. High sediment risk, low receiving water risk, or
- e. Medium sediment risk, medium receiving water risk, or
- f. Low sediment risk, high receiving water risk

Receiving water risk is either considered “Low” for those areas of the project that are not in close proximity to a sensitive receiving watershed, “Medium” for those areas of the project within a sensitive receiving watershed yet outside of the flood plain of a sensitive receiving water body, and “High” where the soil disturbance is within close proximity to a sensitive receiving water body. Project sediment risk is calculated based on the Risk Factor Worksheet in Attachment C of this General Permit.

**3. Type 3 LUPs:**

Type 3 LUPs are determined by the Combined Risk Matrix in Attachment A.1. Type 3 LUPs have the specified combination of risk:

- a. High sediment risk, high receiving water risk, or
- b. High sediment risk, medium receiving water risk, or
- c. Medium sediment risk, high receiving water risk

Receiving water risk is either considered “Medium” for those areas of the project within a sensitive receiving watershed yet outside of the flood plain of a sensitive receiving water body, or “High” where the soil disturbance is within close proximity to a sensitive receiving water body. Project sediment risk is calculated based on the Risk Factor Worksheet in Attachment C.

**J. LUP TYPE-SPECIFIC REQUIREMENTS****1. Effluent Standards**

- a. Narrative – LUP dischargers shall comply with the narrative effluent standards below.

- i Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
  - ii LUP dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.
- b. Numeric – LUP Type 1 dischargers are not subject to a numeric effluent standard
  - c. Numeric –LUP Type 2 dischargers are subject to a pH NAL of 6.5-8.5, and a turbidity NAL of 250 NTU.
  - d. Numeric – LUP Type 3 dischargers are subject to a pH NAL of 6.5-8.5, and a turbidity NAL of 250 NTU. In addition, LUP Type 3 dischargers are subject to a pH NEL of 6.0-9.0 and a turbidity NEL of 500 NTU.

## 2. Good Site Management "Housekeeping"

- a. LUP dischargers shall implement good site management (i.e., "housekeeping") measures for construction materials that could potentially be a threat to water quality if discharged. At a minimum, the good housekeeping measures shall consist of the following:
  - i Identify the products used and/or expected to be used and the end products that are produced and/or expected to be produced. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - ii Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).
  - iii Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).
  - iv Minimize exposure of construction materials to precipitation (not applicable to materials designed to be outdoors and exposed to the environment).

- v Implement BMPs to control the off-site tracking of loose construction and landscape materials.
- b. LUP dischargers shall implement good housekeeping measures for waste management, which, at a minimum, shall consist of the following:
- i Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.
  - ii Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.
  - iii Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.
  - iv Cover waste disposal containers at the end of every business day and during a rain event.
  - v Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.
  - vi Contain and securely protect stockpiled waste material from wind and rain at all times unless actively being used.
  - vii Implement procedures that effectively address hazardous and non-hazardous spills.
  - viii Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require that:
    - (1) Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly; and
    - (2) Appropriate spill response personnel are assigned and trained.
  - ix Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.

- c. LUP dischargers shall implement good housekeeping for vehicle storage and maintenance, which, at a minimum, shall consist of the following:
- i Prevent oil, grease, or fuel from leaking into the ground, storm drains or surface waters.
  - ii Implement appropriate BMPs whenever equipment or vehicles are fueled, maintained or stored.
  - iii Clean leaks immediately and disposing of leaked materials properly.
- d. LUP dischargers shall implement good housekeeping for landscape materials, which, at a minimum, shall consist of the following:
- i Contain stockpiled materials such as mulches and topsoil when they are not actively being used.
  - ii Contain fertilizers and other landscape materials when they are not actively being used.
  - iii Discontinue the application of any erodible landscape material at least 2 days before a forecasted rain event<sup>9</sup> or during periods of precipitation.
  - iv Applying erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.
  - v Stacking erodible landscape material on pallets and covering or storing such materials when not being used or applied.
- e. LUP dischargers shall conduct an assessment and create a list of potential pollutant sources and identify any areas of the site where additional BMPs are necessary to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges. This potential pollutant list shall be kept with the SWPPP and shall identify all non-visible pollutants which are known, or should be known, to occur on the construction site. At a minimum, when developing BMPs, LUP dischargers shall do the following:

---

<sup>9</sup> 50% or greater chance of producing precipitation.

- i Consider the quantity, physical characteristics (e.g., liquid, powder, solid), and locations of each potential pollutant source handled, produced, stored, recycled, or disposed of at the site.
  - ii Consider the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water.
  - iii Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas.
  - iv Ensure retention of sampling, visual observation, and inspection records.
  - v Ensure effectiveness of existing BMPs to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges.
- f. LUP dischargers shall implement good housekeeping measures on the construction site to control the air deposition of site materials and from site operations.

### **3. Non-Storm Water Management**

- a. LUP dischargers shall implement measures to control all non-storm water discharges during construction.
- b. LUP dischargers shall wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.
- c. LUP dischargers shall clean streets in such a manner as to prevent unauthorized non-storm water discharges from reaching surface water or MS4 drainage systems.

### **4. Erosion Control**

- a. LUP dischargers shall implement effective wind erosion control.
- b. LUP dischargers shall provide effective soil cover for inactive<sup>10</sup> areas and all finished slopes, and utility backfill.

---

<sup>10</sup> Areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days

- c. LUP dischargers shall limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the discharger shall consider the use of plastic materials resistant to solar degradation.

## 5. Sediment Controls

- a. LUP dischargers shall establish and maintain effective perimeter controls as needed, and implement effective BMPs for all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.
- b. On sites where sediment basins are to be used, LUP dischargers shall, at minimum, design sediment basins according to the guidance provided in CASQA's Construction BMP Handbook.
- c. **Additional LUP Type 2 & 3 Requirement:** LUP Type 2 & 3 dischargers shall apply linear sediment controls along the toe of the slope, face of the slope, and at the grade breaks of exposed slopes to comply with sheet flow lengths<sup>11</sup> in accordance with Table 2 below.

**Table 2 – Critical Slope/Sheet Flow Length Combinations**

Slope Percentage	Sheet flow length not to exceed
0-25%	20 feet
25-50%	15 feet
Over 50%	10 feet

- d. **Additional LUP Type 2 & 3 Requirement:** LUP Type 2 & 3 dischargers shall ensure that construction activity traffic to and from the project is limited to entrances and exits that employ effective controls to prevent off-site tracking of sediment.
- e. **Additional LUP Type 2 & 3 Requirement:** LUP Type 2 & 3 dischargers shall ensure that all storm drain inlets and perimeter controls, runoff control BMPs, and pollutant controls at entrances and exits (e.g. tire washoff locations) are maintained and protected from activities that reduce their effectiveness.
- f. **Additional LUP Type 2 & 3 Requirement:** LUP Type 2 & 3 dischargers shall inspect all immediate access roads. At a minimum daily and prior to any rain event, the discharger shall remove any

<sup>11</sup> Sheet flow length is the length that shallow, low velocity flow travels across a site.

sediment or other construction activity-related materials that are deposited on the roads (by vacuuming or sweeping).

- g. **Additional LUP Type 3 Requirement:** The Regional Water Board may require LUP Type 3 dischargers to implement additional site-specific sediment control requirements if the implementation of the other requirements in this section are not adequately protecting the receiving waters.

## 6. Run-on and Run-off Controls

- a. LUP dischargers shall effectively manage all run-on, all runoff within the site and all runoff that discharges off the site. Run-on from off site shall be directed away from all disturbed areas or shall collectively be in compliance with the effluent limitations in this Attachment.
- b. Run-on and runoff controls are not required for Type 1 LUPs unless the evaluation of quantity and quality of run-on and runoff deems them necessary or visual inspections show that the site requires such controls.

## 7. Inspection, Maintenance and Repair

- a. All inspection, maintenance repair and sampling activities at the discharger's LUP location shall be performed or supervised by a QSP representing the discharger. The QSP may delegate any or all of these activities to an employee trained to do the task(s) appropriately, but shall ensure adequate deployment.
- b. LUP dischargers shall conduct visual inspections and observations daily during working hours (not recorded). At least once each 24-hour period during extended storm events, **LUP Type 2 & 3 dischargers** shall conduct visual inspections to identify and record BMPs that need maintenance to operate effectively, that have failed, or that could fail to operate as intended. Inspectors shall be the QSP or be trained by the QSP.

- c. Upon identifying failures or other shortcomings, as directed by the QSP, LUP dischargers shall begin implementing repairs or design changes to BMPs within 72 hours of identification and complete the changes as soon as possible.
- d. For each pre- and post-rain event inspection required, LUP dischargers shall complete an inspection checklist, using a form provided by the State Water Board or Regional Water Board or in an alternative format that includes the information described below.
- e. The LUP discharger shall ensure that the checklist remains on-site or with the SWPPP. At a minimum, an inspection checklist should include:
  - i. Inspection date and date the inspection report was written.
  - ii. Weather information, including presence or absence of precipitation, estimate of beginning of qualifying storm event, duration of event, time elapsed since last storm, and approximate amount of rainfall in inches.
  - iii. Site information, including stage of construction, activities completed, and approximate area of the site exposed.
  - iv. A description of any BMPs evaluated and any deficiencies noted.
  - v. If the construction site is safely accessible during inclement weather, list the observations of all BMPs: erosion controls, sediment controls, chemical and waste controls, and non-storm water controls. Otherwise, list the results of visual inspections at all relevant outfalls, discharge points, downstream locations and any projected maintenance activities.
  - vi. Report the presence of noticeable odors or of any visible sheen on the surface of any discharges.
  - vii. Any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates.
  - viii. Photographs taken during the inspection, if any.
  - ix. Inspector's name, title, and signature.

**K. STORM WATER POLLUTION PREVENTION PLAN (SWPPP)  
REQUIREMENTS****1. Objectives**

SWPPPs for all LUPs shall be developed and amended or revised by a QSD. The SWPPP shall be designed to address the following objectives:

- a. All pollutants and their sources, including sources of sediment, associated with construction activities associated with LUP activity are controlled;
- b. All non-storm water discharges are identified and either eliminated, controlled, or treated;
- c. BMPs are effective and result in the reduction or elimination of pollutants in storm water discharges and authorized non-storm water discharges from LUPs during construction; and
- d. Stabilization BMPs installed to reduce or eliminate pollutants after construction is completed are effective and maintained.

**2. SWPPP Implementation Schedule**

- a. LUPs for which PRDs have been submitted to the State Water Board shall develop a site/project location SWPPP prior to the start of land-disturbing activity in accordance with this Section and shall implement the SWPPP concurrently with commencement of soil-disturbing activities.
- b. For an ongoing LUP involving a change in the LRP, the new LRP shall review the existing SWPPP and amend it, if necessary, or develop a new SWPPP within 15 calendar days to conform to the requirements set forth in this General Permit.

**3. Availability**

The SWPPP shall be available at the construction site during working hours while construction is occurring and shall be made available upon request by a State or Municipal inspector. When the original SWPPP is retained by a crewmember in a construction vehicle and is not currently at the construction site, copies of the BMPs and map/drawing will be left with the field crew and the original SWPPP shall be made available via a request by radio/telephone.

**L. REGIONAL WATER BOARD AUTHORITIES**

1. Regional Water Boards shall administer the provisions of this General Permit. Administration of this General Permit may include, but is not limited to, requesting the submittal of SWPPPs, reviewing SWPPPs, reviewing monitoring and sampling and analysis reports, conducting compliance inspections, gathering site information by any medium including sampling, photo and video documentation, and taking enforcement actions.
2. Regional Water Boards may terminate coverage under this General Permit for dischargers who fail to comply with its requirements or where they determine that an individual NPDES permit is appropriate.
3. Regional Water Boards may issue separate permits for discharges of storm water associated with construction activity to individual dischargers, categories of dischargers, or dischargers in a geographic area. Upon issuance of such permits by a Regional Water Board, dischargers subject to those permits shall no longer be regulated by this General Permit.
4. Regional Water Boards may direct the discharger to reevaluate the LUP Type(s) for the project (or elements/areas of the project) and impose the appropriate level of requirements.
5. Regional Water Boards may terminate coverage under this General Permit for dischargers who negligently or with willful intent incorrectly determine or report their LUP Type (e.g., they determine themselves to be a LUP Type 1 when they are actually a Type 2).
6. Regional Water Boards may review PRDs and reject or accept applications for permit coverage or may require dischargers to submit a Report of Waste Discharge / NPDES permit application for Regional Water Board consideration of individual requirements.
7. Regional Water Boards may impose additional requirements on dischargers to satisfy TMDL implementation requirements or to satisfy provisions in their Basin Plans.
8. Regional Water Boards may require additional Monitoring and Reporting Program Requirements, including sampling and analysis of discharges to sediment-impaired water bodies.
9. Regional Water Boards may require dischargers to retain records for more than the three years required by this General Permit.

10. Based on an LUP's threat to water quality and complexity, the Regional Water Board may determine on a case-by-case basis that an LUP, or a portion of an LUP, is not eligible for the linear project requirements contained in this Attachment, and require that the discharger comply with all standard requirements in this General Permit.
11. The Regional Water Board may require additional monitoring and reporting program requirements including sampling and analysis of discharges to CWA § 303(d)-listed water bodies. Additional requirements imposed by the Regional Water Board shall be consistent with the overall monitoring effort in the receiving waters.

**M. MONITORING AND REPORTING REQUIREMENTS****Table 3. LUP Summary of Monitoring Requirements**

LUP Type	Visual Inspections				Sample Collection		
	Daily Site BMP	Pre-storm Event	Daily Storm BMP	Post Storm	Storm Water Discharge	Receiving Water	Non-Visible (when applicable)
		Baseline					
1	X						X
2	X	X	X	X	X		X
3	X	X	X	X	X	X	X

**1. Objectives**

LUP dischargers shall prepare a monitoring and reporting program (M&RP) prior to the start of construction and immediately implement the program at the start of construction for LUPs. The monitoring program must be implemented at the appropriate level to protect water quality at all times throughout the life of the project. The M&RP must be a part of the SWPPP, included as an appendix or separate SWPPP chapter.

**2. M&RP Implementation Schedule**

- a. LUP dischargers shall implement the requirements of this Section at the time of commencement of construction activity. LUP dischargers are responsible for implementing these requirements until construction activity is complete and the site is stabilized.
- b. LUP dischargers shall revise the M&RP when:
  - i. Site conditions or construction activities change such that a change in monitoring is required to comply with the requirements and intent of this General Permit.
  - ii. The Regional Water Board requires the discharger to revise its M&RP based on its review of the document. Revisions may include, but not be limited to, conducting additional site inspections, submitting reports, and certifications. Revisions shall be submitted via postal mail or electronic e-mail.

- iii The Regional Water Board may require additional monitoring and reporting program requirements including sampling and analysis of discharges to CWA § 303(d)-listed water bodies. Additional requirements imposed by the Regional Water Board shall be consistent with the overall monitoring effort in the receiving waters.

### 3. LUP Type 1 Monitoring and Reporting Requirements

#### a. LUP Type 1 Inspection Requirements

- i LUP Type 1 dischargers shall ensure that all inspections are conducted by trained personnel. The name(s) and contact number(s) of the assigned inspection personnel should be listed in the SWPPP.
- ii LUP Type 1 dischargers shall ensure that all visual inspections are conducted daily during working hours and in conjunction with other daily activities in areas where active construction is occurring.
- iii LUP Type 1 dischargers shall ensure that photographs of the site taken before, during, and after storm events are taken during inspections, and submitted through the State Water Board's SMARTS website once every three rain events.
- iv LUP Type 1 dischargers shall conduct daily visual inspections to verify that:
  - (1) Appropriate BMPs for storm water and non-storm water are being implemented in areas where active construction is occurring (including staging areas);
  - (2) Project excavations are closed, with properly protected spoils, and that road surfaces are cleaned of excavated material and construction materials such as chemicals by either removing or storing the material in protective storage containers at the end of every construction day;
  - (3) Land areas disturbed during construction are returned to pre-construction conditions or an equivalent protection is used at the end of each workday to eliminate or minimize erosion and the possible discharge of sediment or other pollutants during a rain event.
- v Inspections may be discontinued in non-active construction areas where soil-disturbing activities are completed and final soil stabilization is achieved (e.g., paving is completed, substructures

are installed, vegetation meets minimum cover requirements for final stabilization, or other stabilization requirements are met).

- vi Inspection programs are required for LUP Type 1 projects where temporary and permanent stabilization BMPs are installed and are to be monitored after active construction is completed. Inspection activities shall continue until adequate permanent stabilization is established and, in areas where re-vegetation is chosen, until minimum vegetative coverage is established in accordance with Section C.1 of this Attachment.

b. LUP Type 1 Monitoring Requirements for Non-Visible Pollutants

LUP Type 1 dischargers shall implement sampling and analysis requirements to monitor non-visible pollutants associated with (1) construction sites; (2) activities producing pollutants that are not visually detectable in storm water discharges; and (3) activities which could cause or contribute to an exceedance of water quality objectives in the receiving waters.

- i Sampling and analysis for non-visible pollutants is only required where the LUP Type 1 discharger believes pollutants associated with construction activities have the potential to be discharged with storm water runoff due to a spill or in the event there was a breach, malfunction, failure and/or leak of any BMP. Also, failure to implement BMPs may require sample collection.
  - (1) Visual observations made during the monitoring program described above will help the LUP Type 1 discharger determine when to collect samples.
  - (2) The LUP Type 1 discharger is not required to sample if one of the conditions described above (e.g., breach or spill) occurs and the site is cleaned of material and pollutants and/or BMPs are implemented prior to the next storm event.
- ii LUP Type 1 dischargers shall collect samples down-gradient from all discharge locations where the visual observations were made triggering the monitoring, and which can be safely accessed. For sites where sampling and analysis is required, personnel trained in water quality sampling procedures shall collect storm water samples.
- iii If sampling for non-visible pollutant parameters is required, LUP Type 1 dischargers shall ensure that samples be analyzed for parameters indicating the presence of pollutants identified in the pollutant source assessment required in Section J.2.a.i.

- iv LUP Type 1 dischargers shall collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff.
  - v LUP Type 1 dischargers shall ensure that a sufficiently large sample of storm water that has not come into contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample<sup>12</sup>) will be collected for comparison with the discharge sample. Samples shall be collected during the first two hours of discharge from rain events that occur during daylight hours and which generate runoff.
  - vi LUP Type 1 dischargers shall compare the uncontaminated sample to the samples of discharge using field analysis or through laboratory analysis. Analyses may include, but are not limited to, indicator parameters such as: pH, specific conductance, dissolved oxygen, conductivity, salinity, and Total Dissolved Solids (TDS).
  - vii For laboratory analyses, all sampling, sample preservation, and other analyses must be conducted according to test procedures pursuant to 40 C.F.R. Part 136. LUP Type 1 dischargers shall ensure that field samples are collected and analyzed according to manufacturer specifications of the sampling devices employed. Portable meters shall be calibrated according to manufacturer's specification.
  - viii LUP Type 1 dischargers shall ensure that all field and/or analytical data are kept in the SWPPP document.
- c. LUP Type 1 Visual Observation Exceptions
- i LUP Type 1 dischargers shall be prepared to collect samples and conduct visual observation (inspections) to meet the minimum visual observation requirements of this Attachment. The Type 1 LUP discharger is not required to physically collect samples or conduct visual observation (inspections) under the following conditions:
    - (1) During dangerous weather conditions such as flooding and electrical storms;
    - (2) Outside of scheduled site business hours.
    - (3) When access to the site is unsafe due to storm events.

---

<sup>12</sup> Sample collected at a location unaffected by construction activities.

- ii If the LUP Type 1 discharger does not collect the required samples or visual observation (inspections) due to these exceptions, an explanation why the sampling or visual observation (inspections) were not conducted shall be included in both the SWPPP and the Annual Report.

d. Particle Size Analysis for Risk Justification

LUP Type 1 dischargers utilizing justifying an alternative project risk shall report a soil particle size analysis used to determine the RUSLE K-Factor. ASTM D-422 (Standard Test Method for Particle-Size Analysis of Soils), as revised, shall be used to determine the percentages of sand, very fine sand, silt, and clay on the site.

#### **4. LUP Type 2 & 3 Monitoring and Reporting Requirements**

a. LUP Type 2 & 3 Inspection Requirements

- i LUP Type 2 & 3 dischargers shall ensure that all inspections are conducted by trained personnel. The name(s) and contact number(s) of the assigned inspection personnel should be listed in the SWPPP.
- ii LUP Type 2 & 3 dischargers shall ensure that all visual inspections are conducted daily during working hours and in conjunction with other daily activities in areas where active construction is occurring.
- iii LUP Type 2 & 3 dischargers shall ensure that photographs of the site taken before, during, and after storm events are taken during inspections, and submitted through the State Water Board's SMARTS website once every three rain events.
- iv LUP Type 2 & 3 dischargers shall conduct daily visual inspections to verify that appropriate BMPs for storm water and non-storm water are being implemented and in place in areas where active construction is occurring (including staging areas).
- v LUP Type 2 & 3 dischargers shall conduct inspections of the construction site prior to anticipated storm events, during extended storm events, and after actual storm events to identify areas contributing to a discharge of storm water associated with construction activity. Pre-storm inspections are to ensure that BMPs are properly installed and maintained; post-storm inspections are to assure that BMPs have functioned adequately. During

extended storm events, inspections shall be required during normal working hours for each 24-hour period.

- vi Inspections may be discontinued in non-active construction areas where soil-disturbing activities are completed and final soil stabilization is achieved (e.g., paving is completed, substructures are installed, vegetation meets minimum cover requirements for final stabilization, or other stabilization requirements are met).
- vii LUP Type 2 & 3 dischargers shall implement a monitoring program for inspecting projects that require temporary and permanent stabilization BMPs after active construction is complete. Inspections shall ensure that the BMPs are adequate and maintained. Inspection activities shall continue until adequate permanent stabilization is established and, in vegetated areas, until minimum vegetative coverage is established in accordance with Section C.1 of this Attachment.
- viii If possible, LUP Type 2 & 3 dischargers shall install a rain gauge on-site at an accessible and secure location with readings made during all storm event inspections. When readings are unavailable, data from the closest rain gauge with publically available data may be used.
- ix LUP Type 2 & 3 dischargers shall include and maintain a log of the inspections conducted in the SWPPP. The log will provide the date and time of the inspection and who conducted the inspection.

b. LUP Type 2 & 3 Storm Water Effluent Monitoring Requirements

**Table 4. LUP Type 2 & 3 Effluent Monitoring Requirements**

<b>LUP Type</b>	<b>Frequency</b>	<b>Effluent Monitoring</b>
<b>2</b>	Minimum of 3 samples per day characterizing discharges associated with construction activity from the project active areas of construction.	Turbidity, pH, and non-visible pollutant parameters (if applicable)
<b>3</b>	Minimum of 3 samples per day characterizing discharges associated with construction activity from the project active areas of construction.	turbidity, pH, suspended sediment concentrations (SSC) <sup>13</sup> (only if turbidity NEL exceeded), plus non-visible pollutant parameters (if applicable)

- i LUP Type 2 & 3 dischargers shall collect storm water grab samples from sampling locations characterizing discharges associated with

<sup>13</sup> Suspended Sediment Concentration monitoring is required for any Type 3 area that exceeds its turbidity NEL.

activity from the LUP active areas of construction. At a minimum, 3 samples shall be collected per day of discharge.

- ii LUP Type 2 & 3 dischargers shall collect samples of stored or contained storm water that is discharged subsequent to a storm event producing precipitation of ½ inch or more at the time of discharge.
- iii LUP Type 2 & 3 dischargers shall ensure that storm water grab sample(s) obtained be representative of the flow and characteristics of the discharge.
- iv LUP Type 2 & 3 dischargers shall analyze their effluent samples for:
  - (1) pH and turbidity
  - (2) Any additional parameter for which monitoring is required by the Regional Water Board.
- v LUP Type 3 dischargers that have violated the turbidity daily average NEL shall analyze subsequent effluent samples for turbidity and SSC.

c. LUP Type 2 & 3 Storm Water Effluent Sampling Locations

- i LUP Type 2 & 3 dischargers shall perform sampling and analysis of storm water discharges to characterize discharges associated with construction activity from the entire disturbed project or area.
- ii LUP Type 2 & 3 dischargers may monitor and report run-on from surrounding areas if there is reason to believe run-on may contribute to exceedance of NALs or NELs (applicable to Type 3).
- iii LUP Type 2 & 3 dischargers shall select analytical test methods from the list provided in Table 5 below.
- iv LUP Type 2 & 3 dischargers shall ensure that all storm water sample collection preservation and handling shall be conducted in accordance with the “Storm Water Sample Collection and Handling Instructions” below.

d. LUP Type 3 Receiving Water Monitoring Requirements

- i In the event that an LUP Type 3 discharger violates an applicable NEL contained in this General Permit and has a direct discharge to receiving waters, the LUP discharger shall subsequently sample Receiving Waters (RWs) for turbidity, pH (if applicable) and SSC.

- ii LUP Type 3 dischargers that meet the project criteria in Appendix 3 of this General Permit and have more than 30 acres of soil disturbance in the project area or project section area designated as Type 3, shall comply with the Bioassessment requirements prior to commencement of construction activity.
  - iii LUP Type 3 dischargers shall obtain RW samples in accordance with the requirements of the Receiving Water Sampling Locations section (Section M.4.d of this Attachment).
- e. LUP Type 3 Receiving Water Sampling Locations
- i **Upstream/up-gradient RW samples:** LUP Type 3 dischargers shall obtain any required upstream/up-gradient receiving water samples from a representative and accessible location as close as possible to and upstream from the effluent discharge point.
  - ii **Downstream/down-gradient RW samples:** LUP Type 3 dischargers shall obtain any required downstream/down-gradient receiving water samples from a representative and accessible location as close as possible to and downstream from the effluent discharge point.
  - iii If two or more discharge locations discharge to the same receiving water, LUP Type 3 dischargers may sample the receiving water at a single upstream and downstream location.
- f. LUP Type 2 & 3 Monitoring Requirements for Non-Visible Pollutants

LUP Type 2 & 3 dischargers shall implement sampling and analysis requirements to monitor non-visible pollutants associated with (1) construction sites; (2) activities producing pollutants that are not visually detectable in storm water discharges; and (3) activities which could cause or contribute to an exceedance of water quality objectives in the receiving waters.

- i Sampling and analysis for non-visible pollutants is only required where LUP Type 2 & 3 dischargers believe pollutants associated with construction activities have the potential to be discharged with storm water runoff due to a spill or in the event there was a breach, malfunction, failure and/or leak of any BMP. Also, failure to implement BMPs may require sample collection.
  - (1) Visual observations made during the monitoring program described above will help LUP Type 2 & 3 dischargers determine when to collect samples.

- (2) LUP Type 2 & 3 dischargers are not required to sample if one of the conditions described above (e.g., breach or spill) occurs and the site is cleaned of material and pollutants and/or BMPs are implemented prior to the next storm event.
- ii LUP Type 2 & 3 dischargers shall collect samples down-gradient from the discharge locations where the visual observations were made triggering the monitoring and which can be safely accessed. For sites where sampling and analysis is required, personnel trained in water quality sampling procedures shall collect storm water samples.
  - iii If sampling for non-visible pollutant parameters is required, LUP Type 2 & 3 dischargers shall ensure that samples be analyzed for parameters indicating the presence of pollutants identified in the pollutant source assessment required in Section J.2.a.i.
  - iv LUP Type 2 & 3 dischargers shall collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff.
  - v LUP Type 2 & 3 dischargers shall ensure that a sufficiently large sample of storm water that has not come into contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample<sup>14</sup>) will be collected for comparison with the discharge sample. Samples shall be collected during the first two hours of discharge from rain events that occur during daylight hours and which generate runoff.
  - vi LUP Type 2 & 3 dischargers shall compare the uncontaminated sample to the samples of discharge using field analysis or through laboratory analysis. Analyses may include, but are not limited to, indicator parameters such as: pH, specific conductance, dissolved oxygen, conductivity, salinity, and Total Dissolved Solids (TDS).
  - vii For laboratory analyses, all sampling, sample preservation, and other analyses must be conducted according to test procedures pursuant to 40 C.F.R. Part 136. LUP Type 2 & 3 dischargers shall ensure that field samples are collected and analyzed according to manufacturer specifications of the sampling devices employed. Portable meters shall be calibrated according to manufacturer's specification.
  - viii LUP Type 2 & 3 dischargers shall ensure that all field and/or analytical data are kept in the SWPPP document.

---

<sup>14</sup> Sample collected at a location unaffected by construction activities

g. LUP Type 2 & 3 Visual Observation and Sample Collection Exceptions

- i LUP Type 2 & 3 dischargers shall be prepared to collect samples and conduct visual observation (inspections) to meet the minimum visual observation requirements of this Attachment. Type 2 & 3 LUP dischargers are not required to physically collect samples or conduct visual observation (inspections) under the following conditions:
  - (1) During dangerous weather conditions such as flooding and electrical storms;
  - (2) Outside of scheduled site business hours.
  - (3) When access to the site is unsafe due to storm events.
- ii If the LUP Type 2 or 3 discharger does not collect the required samples or visual observation (inspections) due to these exceptions, an explanation why the sampling or visual observation (inspections) were not conducted shall be included in both the SWPPP and the Annual Report.

h. LUP Type 2 & 3 Storm Water Sample Collection and Handling Instructions

LUP Type 2 & 3 dischargers shall refer to Table 5 below for test Methods, detection Limits, and reporting Units. During storm water sample collection and handling, the LUP Type 2 & 3 discharger shall:

- i Identify the parameters required for testing and the number of storm water discharge points that will be sampled. Request the laboratory to provide the appropriate number of sample containers, types of containers, sample container labels, blank chain of custody forms, and sample preservation instructions.
- ii Determine how to ship the samples to the laboratory. The testing laboratory should receive samples within 48 hours of the physical sampling (unless otherwise required by the laboratory). The options are to either deliver the samples to the laboratory, arrange to have the laboratory pick them up, or ship them overnight to the laboratory.
- iii Use only the sample containers provided by the laboratory to collect and store samples. Use of any other type of containers could contaminate your samples.

- iv Prevent sample contamination, by not touching, or putting anything into the sample containers before collecting storm water samples.
- v Not overfilling sample containers. Overfilling can change the analytical results.
- vi Tightly screw the cap of each sample container without stripping the threads of the cap.
- vii Complete and attach a label to each sample container. The label shall identify the date and time of sample collection, the person taking the sample, and the sample collection location or discharge point. The label should also identify any sample containers that have been preserved.
- viii Carefully pack sample containers into an ice chest or refrigerator to prevent breakage and maintain temperature during shipment. Remember to place frozen ice packs into the shipping container. Samples should be kept as close to 4° C (39° F) as possible until arriving at the laboratory. Do not freeze samples.
- ix Complete a Chain of Custody form for each set of samples. The Chain of Custody form shall include the discharger's name, address, and phone number, identification of each sample container and sample collection point, person collecting the samples, the date and time each sample container was filled, and the analysis that is required for each sample container.
- x Upon shipping/delivering the sample containers, obtain both the signatures of the persons relinquishing and receiving the sample containers.
- xi Designate and train personnel to collect, maintain, and ship samples in accordance with the above sample protocols and good laboratory practices.
- xii Refer to the Surface Water Ambient Monitoring Program's (SWAMP) Quality Assurance Management Plan (QAMP) for more information on sampling collection and analysis. See [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/](http://www.waterboards.ca.gov/water_issues/programs/swamp/)<sup>15</sup>  
QAMP Link:  
[http://www.waterboards.ca.gov/water\\_issues/programs/swamp/qamp.p.shtml](http://www.waterboards.ca.gov/water_issues/programs/swamp/qamp.p.shtml)

---

<sup>15</sup> Additional information regarding QAMP can be found at <http://mpsl.mlml.calstate.edu/swqacompare.htm>.

**Table 5. Test Methods, Detection Limits, Reporting Units and Applicable NALs/NELs**

Parameter	Test Method	Discharge Type	Min. Detection Limit	Reporting Units	Numeric Action Levels	Numeric Effluent Limitation (LUP Type 3)
<b>pH</b>	Field test with calibrated portable instrument	Type 2 & 3	0.2	pH units	Lower = 6.5 upper = 8.5	Lower = 6.0 upper = 9.0
<b>Turbidity</b>	EPA 0180.1 and/or field test with calibrated portable instrument	Type 2 & 3	1	NTU	250 NTU	500 NTU
<b>SSC</b>	ASTM Method D 3977-97 <sup>16</sup>	Type 3 if NEL is exceeded	5 Mg/L		N/A	N/A
<b>Bioassessment</b>	(STE) Level I of (SAFIT), <sup>17</sup> fixed-count of 600 org/sample	Type 3 LUPs > 30 acres	N/A N/A		N/A	N/A

i. LUP Type 2 & 3 Monitoring Methods

- i The LUP Type 2 or 3 discharger's project M&RP shall include a description of the following items:
- (1) Visual observation locations, visual observation procedures, and visual observation follow-up and tracking procedures.
  - (2) Sampling locations, and sample collection and handling procedures. This shall include detailed procedures for sample collection, storage, preservation, and shipping to the testing lab to assure that consistent quality control and quality assurance is maintained. Dischargers shall attach to the monitoring program a copy of the Chain of Custody form used when handling and shipping samples.

<sup>16</sup> ASTM, 1999, Standard Test Method for Determining Sediment Concentration in Water Samples: American Society of Testing and Materials, D 3977-97, Vol. 11.02, pp. 389-394

<sup>17</sup> The current SAFIT STEs (28 November 2006) list requirements for both the Level I and Level II taxonomic effort, and are located at: [http://www.swrcb.ca.gov/swamp/docs/safit/ste\\_list.pdf](http://www.swrcb.ca.gov/swamp/docs/safit/ste_list.pdf). When new editions are published by SAFIT, they will supersede all previous editions. All editions will be posted at the State Water Board's SWAMP website.

- (3) Identification of the analytical methods and related method detection limits (if applicable) for each parameter required in Section M.4.f above.
- ii LUP Type 2 & 3 dischargers shall ensure that all sampling and sample preservation be in accordance with the current edition of "Standard Methods for the Examination of Water and Wastewater" (American Public Health Association). All monitoring instruments and equipment (including a discharger's own field instruments for measuring pH and turbidity) shall be calibrated and maintained in accordance with manufacturers' specifications to ensure accurate measurements. All laboratory analyses shall be conducted according to test procedures under 40 CFR Part 136, unless other test procedures have been specified in this General Permit or by the Regional Water Board. With the exception of field analysis conducted by the discharger for turbidity and pH, all analyses shall be sent to and conducted at a laboratory certified for such analyses by the State Department of Health Services (SSC exception). The LUP discharger shall conduct its own field analysis of pH and may conduct its own field analysis of turbidity if the discharger has sufficient capability (qualified and trained employees, properly calibrated and maintained field instruments, etc.) to adequately perform the field analysis.
- j. LUP Type 2 & 3 Analytical Methods

LUP Type 2 & 3 dischargers shall refer to Table 5 above for test Methods, detection Limits, and reporting Units.

- i **pH:** LUP Type 2 & 3 dischargers shall perform pH analysis on-site with a calibrated pH meter or pH test kit. The LUP discharger shall record pH monitoring results on paper and retain these records in accordance with Section M.4.o, below.
- ii **Turbidity:** LUP Type 2 & 3 dischargers shall perform turbidity analysis using a calibrated turbidity meter (turbidimeter), either on-site or at an accredited lab. Acceptable test methods include Standard Method 2130 or USEPA Method 180.1. The results shall be recorded in the site log book in Nephelometric Turbidity Units (NTU).
- iii **Suspended sediment concentration (SSC):** LUP Type 3 dischargers exceeding their NEL, shall perform SSC analysis using ASTM Method D3977-97.

- iv **Bioassessment:** LUP Type 3 dischargers shall perform bioassessment sampling and analysis according to Appendix 3 of this General Permit.

- k. Watershed Monitoring Option

If an LUP Type 2 or 3 discharger is part of a qualified regional watershed-based monitoring program the LUP Type 2 or 3 discharger may be eligible for relief from the monitoring requirements in this Attachment. The Regional Water Board may approve proposals to substitute an acceptable watershed-based monitoring program if it determines that the watershed-based monitoring program will provide information to determine each discharger's compliance with the requirements of this General Permit.

- l. Particle Size Analysis for Risk Justification

LUP Type 2 & 3 dischargers justifying an alternative project risk shall report a soil particle size analysis used to determine the RUSLE K-Factor. ASTM D-422 (Standard Test Method for Particle-Size Analysis of Soils), as revised, shall be used to determine the percentages of sand, very fine sand, silt, and clay on the site.

- m. NAL Exceedance Report

- i In the event that any effluent sample exceeds an applicable NAL, the Regional Water Boards may require LUP Type 2 & 3 dischargers to submit NAL Exceedance Reports.
- ii LUP Type 2 & 3 dischargers shall certify each NAL Exceedance Report in accordance with the Special Provisions for Construction Activity.
- iii LUP Type 2 & 3 dischargers shall retain an electronic or paper copy of each NAL Exceedance Report for a minimum of three years after the date the exceedance report is filed.
- iv LUP Type 2 & 3 dischargers shall include in the NAL Exceedance Report:
  - (1) the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as "less than the method detection limit"); and
  - (2) the date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation.

- (3) Description of the current BMPs associated with the effluent sample that exceeded the NAL and the proposed corrective actions taken.

n. NEL Violation Report

- i All LUP Type 3 dischargers shall electronically submit all storm event sampling results to the State Water Board no later than 5 days after the conclusion of the storm event.
- ii In the event that a LUP Type 3 discharger has violated an applicable NEL, the discharger shall submit an NEL Violation Report to the State Water Board no later than 24 hours after the NEL exceedance has been identified.
- iii The LUP Type 3 discharger shall certify each NEL Violation Report in accordance with the Special Provisions for Construction Activity.
- iv The LUP Type 3 discharger shall retain an electronic or paper copy of each NEL Violation Report for a minimum of three years after the date the violation report is filed.
- v The LUP Type 3 discharger shall include in the NEL Violation Report:
  - (1) the analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as "less than the method detection limit"); and
  - (2) the date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation.
  - (3) Description of the current on-site BMPs, and the proposed corrective actions taken to manage the NEL exceedance.
- vi Compliance Storm Exemption:

In the event that an applicable NEL has been exceeded during a storm event equal to or larger than the Compliance Storm Event (see Section F.2.c of this Attachment), the LUP Type 3 discharger shall report the on-site rain gauge and nearby governmental rain gauge readings for verification.


o. Monitoring Records

LUP Type 2 & 3 dischargers shall ensure that records of all storm water monitoring information and copies of all reports (including Annual Reports) required by this General Permit be retained for a period of at least three years. LUP Type 2 & 3 dischargers may retain records off-

site and make them available upon request. These records shall include:

- i The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation (rain gauge);
- ii The individual(s) who performed the facility inspections, sampling, visual observation (inspections), and or measurements;
- iii The date and approximate time of analyses;
- iv The individual(s) who performed the analyses;
- v A summary of all analytical results from the last three years, the method detection limits and reporting units, the analytical techniques or methods used, and all chain of custody forms;
- vi Quality assurance/quality control records and results;
- vii Non-storm water discharge inspections and visual observation (inspections) and storm water discharge visual observation records (see Section M.4.a above);
- viii Visual observation and sample collection exception records (see Section M.4.g above); and
- ix The records of any corrective actions and follow-up activities that resulted from analytical results, visual observation (inspections), or inspections.


## ATTACHMENT A.1 LUP Project Area or Project Section Area Type Determination

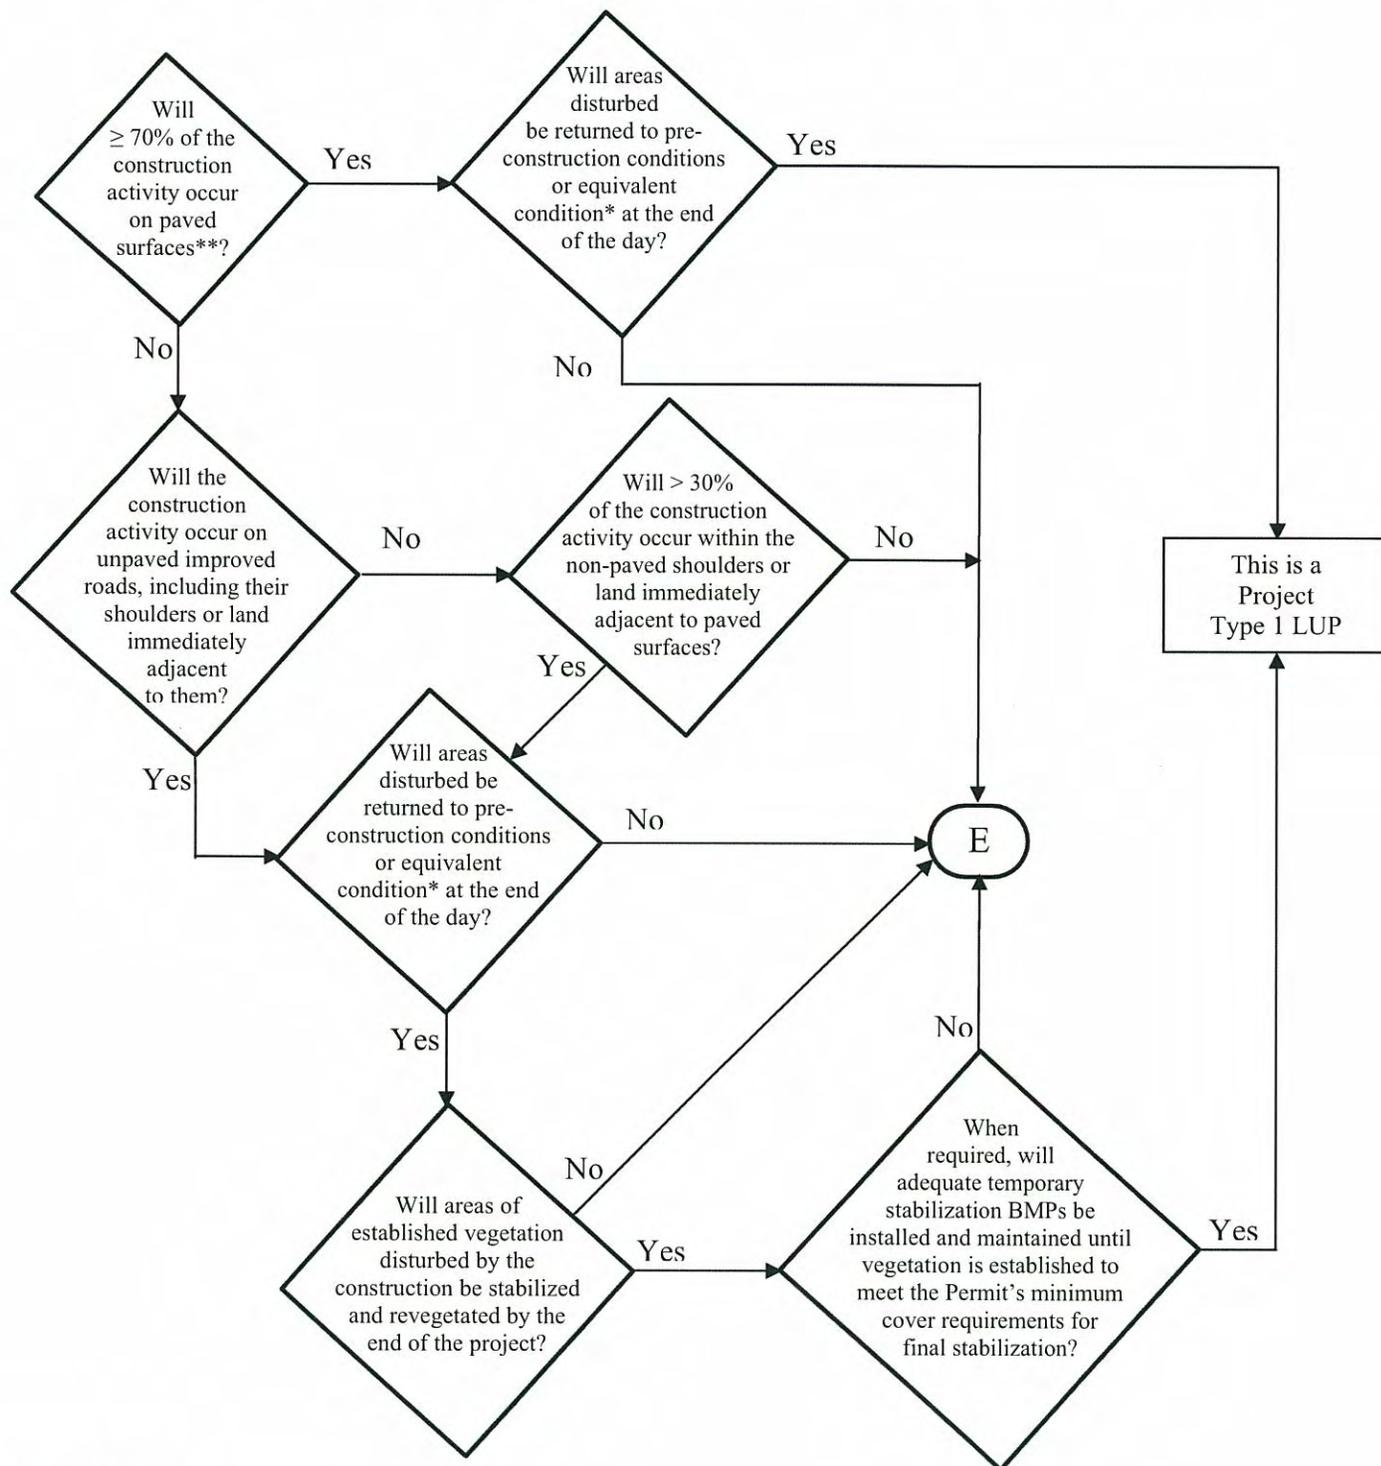

\*See Definition of Terms

\*\* Or: "Will < 30% of the soil disturbance occur on unpaved surfaces?"

### ATTACHMENT A.1 LUP Project Area or Project Section Area Type Determination

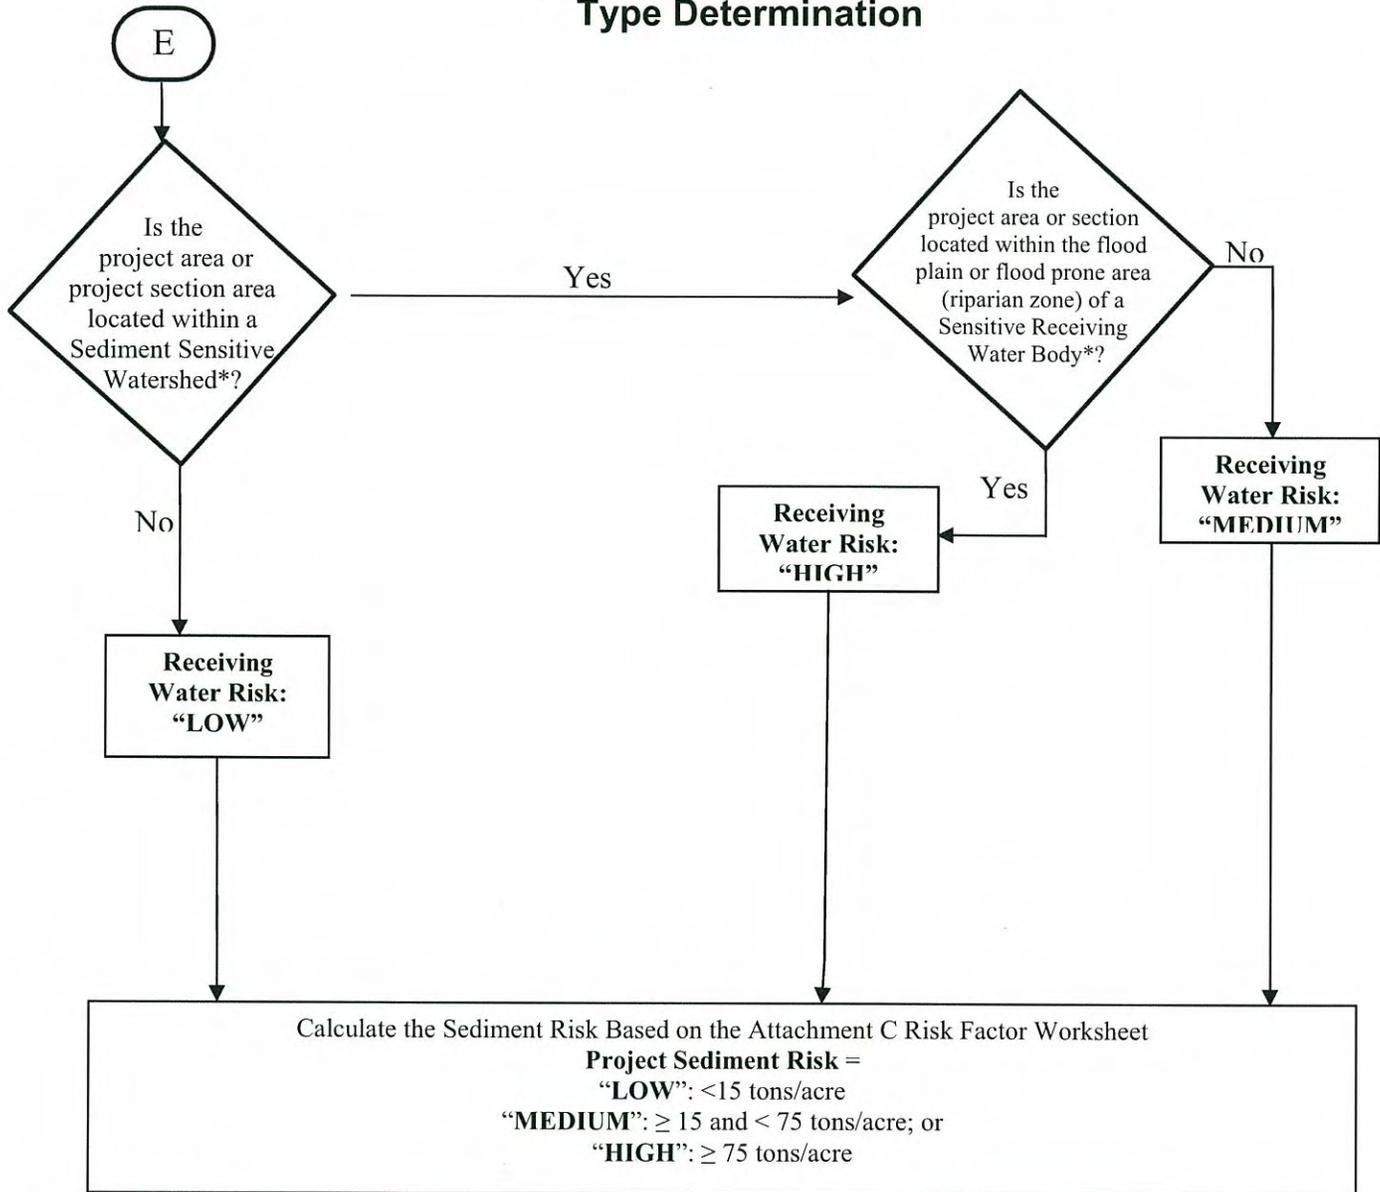

\* See Definition of Terms

#### PROJECT SEDIMENT RISK

<u>RECEIVING WATER RISK</u>	<u>LOW</u>	<u>MEDIUM</u>	<u>HIGH</u>
<u>LOW</u>	Type 1	Type 1	Type 2
<u>MEDIUM</u>	Type 1	Type 2	Type 3
<u>HIGH</u>	Type 2	Type 3	Type 3

## ATTACHMENT A.1

### Definition of Terms

1. **Equivalent Condition** – Means disturbed soils such as those from trench excavation are required to be hauled away, backfilled into the trench, and/or covered (e.g., metal plates, pavement, plastic covers over spoil piles) at the end of the construction day.
2. **Linear Construction Activity** – Linear construction activity consists of underground/ overhead facilities that typically include, but are not limited to, any conveyance, pipe or pipeline for the transportation of any gaseous, liquid (including water, wastewater for domestic municipal services), liquescent, or slurry substance; any cable line or wire for the transmission of electrical energy; any cable line or wire for communications (e.g., telephone, telegraph, radio or television messages); and associated ancillary facilities. Construction activities associated with LUPs include, but are not limited to those activities necessary for the installation of underground and overhead linear facilities (e.g., conduits, substructures, pipelines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment and associated ancillary facilities) and include, but are not limited to, underground utility mark-out, potholing, concrete and asphalt cutting and removal, trenching, excavation, boring and drilling, access road and pole/ tower pad and cable/ wire pull station, substation construction, substructure installation, construction of tower footings and/or foundations, pole and tower installations, pipeline installations, welding, concrete and/or pavement repair or replacement, and stockpile/ borrow locations.
3. **Sediment Sensitive Receiving Water Body** – Defined as a water body segment that is listed on EPA's approved CWA 303(d) list for sedimentation/siltation, turbidity, or is designated with beneficial uses of SPAWN, MIGRATORY, and COLD.
4. **Sediment Sensitive Watershed** – Defined as a watershed draining into a receiving water body listed on EPA's approved CWA 303(d) list for sedimentation/siltation, turbidity, or a water body designated with beneficial uses of SPAWN, MIGRATORY, and COLD.

**ATTACHMENT A.2  
PERMIT REGISTRATION DOCUMENTS (PRDs)  
GENERAL INSTRUCTIONS FOR LINEAR UNDERGROUND/OVERHEAD PROJECTS TO  
COMPLY WITH THE CONSTRUCTION GENERAL PERMIT**

**GENERAL INSTRUCTIONS**

**Who Must Submit**

This permit is effective on July 1, 2010.

The Legally Responsible Person (LRP) for construction activities associated with linear underground/overhead project (LUP) must electronically apply for coverage under this General Permit on or after July 1, 2010. If it is determined that the LUP construction activities require an NPDES permit, the Legally Responsible Person<sup>1</sup> (LRP) shall submit PRDs for this General Permit in accordance with the following:

*LUPs associated with Private or Municipal Development Projects*

1. For LUPs associated with pre-development and pre-redevelopment construction activities:

The LRP must obtain coverage<sup>2</sup> under this General Permit for its pre-development and pre-redevelopment construction activities where the total disturbed land area of these construction activities is greater than 1 acre.

2. For LUPs associated with new development and redevelopment construction projects:

The LRP must obtain coverage under this General Permit for LUP construction activities associated with new development and redevelopment projects where the total disturbed land area of the LUP is greater than 1 acre. Coverage under this permit is not required where the same LUP construction activities are covered by another NPDES permit.

*LUPs not associated with private or municipal new development or redevelopment projects:*

The LRP must obtain coverage under this General Permit on or after July 1, 2010 for its LUP construction activities where the total disturbed land area is greater than 1 acre.

**PRD Submittal Requirements**

Prior to the start of construction activities a LRP must submit PRDs and fees to the State Water Board for each LUP.

*New and Ongoing LUPs*

Dischargers of new LUPs that commence construction activities after the adoption date of this General Permit shall file PRDs prior to the commencement of construction and implement the SWPPP upon the start of construction.

<sup>1</sup> person possessing the title of the land on which the construction activities will occur for the regulated site

<sup>2</sup> obtain coverage means filing PRDs for the project.

**PERMIT REGISTRATION DOCUMENTS (PRDs)  
GENERAL INSTRUCTIONS (CONTINUED)**

Dischargers of ongoing LUPs that are currently covered under State Water Board Order No. 2003-0007 (Small LUP General Permit) shall electronically file Permit Registration Documents no later than July 1, 2010. After July 1, 2010, all NOIs subject to State Water Board Order No. 2003-0007-DWQ will be terminated. All existing dischargers shall be exempt from the risk determination requirements in Attachment A. All existing dischargers are therefore subject to LUP Type 1 requirements regardless of their project's sediment and receiving water risks. However, a Regional Board retains the authority to require an existing discharger to comply with the risk determination requirements in Attachment A.

Where to Apply

The Permit Registration Documents (PRDs) can be found at [www.waterboards.ca.gov/water\\_issues/programs/stormwater/](http://www.waterboards.ca.gov/water_issues/programs/stormwater/)

Fees

The annual fee for storm water permits are established through the State of California Code of Regulations.

When Permit Coverage Commences

To obtain coverage under the General Permit, the LRP must include the complete PRDs and the annual fee. All PRDs deemed incomplete will be rejected with an explanation as to what is required to complete submittal. Upon receipt of complete PRDs and associated fee, each discharger will be sent a waste discharger's identification (WDID) number.

**Projects and Activities Not Defined As Construction Activity**

1. LUP construction activity does not include routine maintenance projects to maintain original line and grade, hydraulic capacity, or original purpose of the facility. Routine maintenance projects are projects associated with operations and maintenance activities that are conducted on existing lines and facilities and within existing right-of-way, easements, franchise agreements or other legally binding agreements of the discharger. Routine maintenance projects include, but are not limited to projects that are conducted to:
  - Maintain the original purpose of the facility, or hydraulic capacity.
  - Update existing lines<sup>3</sup> and facilities to comply with applicable codes, standards and regulations regardless if such projects result in increased capacity.
  - Repairing leaks.

Routine maintenance does not include construction of new<sup>4</sup> lines or facilities resulting from compliance with applicable codes, standards and regulations.

<sup>3</sup> Update existing lines includes replacing existing lines with new materials or pipes.

<sup>4</sup> New lines are those that are not associated with existing facilities and are not part of a project to update or replace existing lines.

**PERMIT REGISTRATION DOCUMENTS (PRDs)  
GENERAL INSTRUCTIONS (CONTINUED)**

Routine maintenance projects do not include those areas of maintenance projects that are outside of an existing right-of-way, franchise, easements, or agreements. When a project must acquire new areas, those areas may be subject to this General Permit based on the area of disturbed land outside the original right-of-way, easement or agreement.

2. LUP construction activity does not include field activities associated with the planning and design of a project (e.g., activities associated with route selection).
3. Tie-ins conducted immediately adjacent to “energized” or “pressurized” facilities by the discharger are not considered small construction activities where all other LUP construction activities associated with the tie-in are covered by a NOI and SWPPP of a third party or municipal agency.

**Calculating Land Disturbance Areas of LUPs**

The total land area disturbed for LUPs is the sum of the:

- Surface areas of trenches, laterals and ancillary facilities, plus
- Area of the base of stockpiles on unpaved surfaces, plus
- Surface area of the borrow area, plus
- Areas of paved surfaces constructed for the project, plus
- Areas of new roads constructed or areas of major reconstruction to existing roads (e.g. improvements to two-track surfaces or road widening) for the sole purpose of accessing construction activities or as part of the final project, plus
- Equipment and material storage, staging, and preparation areas (laydown areas) not on paved surfaces, plus
- Soil areas outside the surface area of trenches, laterals and ancillary facilities that will be graded, and/or disturbed by the use of construction equipment, vehicles and machinery during construction activities.

*Stockpiling Areas*

Stockpiling areas, borrow areas and the removal of soils from a construction site may or may not be included when calculating the area of disturbed soil for a site depending on the following conditions:

- For stockpiling of soils onsite or immediately adjacent to a LUP site and the stockpile is not on a paved surface, the area of the base of the stockpile is to be included in the disturbed area calculation.
- The surface area of borrow areas that are onsite or immediately adjacent to a project site are to be included in the disturbed area calculation.
- For soil that is hauled offsite to a location owned or operated by the discharger that is not a paved surface, the area of the base of the stockpile is to be included in the disturbed area calculation except when the offsite location is already subject to a separate storm water permit.

**PERMIT REGISTRATION DOCUMENTS (PRDs)  
GENERAL INSTRUCTIONS (CONTINUED)**

- For soil that is brought to the project from an off-site location owned or operated by the discharger the surface area of the borrow pit is to be included in the disturbed area calculation except when the offsite location is already subject to a separate storm water permit.
- Trench spoils on a paved surface that are either returned to the trench or excavation or hauled away from the project daily for disposal or reuse will not be included in the disturbed area calculation.

If you have any questions concerning submittal of PRDs, please call the State Water Board at (866) 563-3107.

**ATTACHMENT B**  
**PERMIT REGISTRATION DOCUMENTS (PRDs) TO COMPLY WITH THE TERMS**  
**OF THE GENERAL PERMIT TO DISCHARGE STORM WATER**  
**ASSOCIATED WITH CONSTRUCTION ACTIVITY**

**GENERAL INSTRUCTIONS**

---

**A.** All Linear Construction Projects shall comply with the PRD requirements in Attachment A.2 of this Order.

**B. Who Must Submit**

Discharges of storm water associated with construction that results in the disturbance of one acre or more of land must apply for coverage under the General Construction Storm Water Permit (General Permit). Any construction activity that is a part of a larger common plan of development or sale must also be permitted, regardless of size. (For example, if 0.5 acre of a 20-acre subdivision is disturbed by the construction activities of discharger A and the remaining 19.5 acres is to be developed by discharger B, discharger A must obtain a General Storm Water Permit for the 0.5 acre project).

Other discharges from construction activities that are covered under this General Permit can be found in the General Permit Section II.B.

It is the LRP's responsibility to obtain coverage under this General Permit by electronically submitting complete PRDs (Permit Registration Documents).

In all cases, the proper procedures for submitting the PRDs must be completed before construction can commence.

**C. Construction Activity Not Covered By This General Permit**

Discharges from construction that are not covered under this General Permit can be found in the General Permit Sections II.A & B..

**D. Annual Fees and Fee Calculation**

Annual fees are calculated based upon the total area of land to be disturbed not the total size of the acreage owned. However, the calculation includes all acres to be disturbed during the duration of the project. For example, if 10 acres are scheduled to be disturbed the first year and 10 in each subsequent year for 5 years, the annual fees would be based upon 50 acres of disturbance. The State Water Board will evaluate adding acreage to an existing Permit Waste Discharge Identification (WDID) number on a case-by-case basis. In general, any acreage to be considered must be contiguous to the permitted land area and the existing

SWPPP must be appropriate for the construction activity and topography of the acreage under consideration. As acreage is built out and stabilized or sold, the Change of Information (COI) form enables the applicant to remove those acres from inclusion in the annual fee calculation. Checks should be made payable to: State Water Board.

The Annual fees are established through regulations adopted by the State Water Board. The total annual fee is the current base fee plus applicable surcharges for all construction sites submitting an NOI, based on the total acreage to be disturbed during the life of the project. Annual fees are subject to change by regulation.

Dischargers that apply for and satisfy the Small Construction Erosivity Wavier requirements shall pay a fee of \$200.00 plus an applicable surcharge, see the General Permit Section II.B.7.

#### **E. When to Apply**

LRP's proposing to conduct construction activities subject to this General Permit must submit their PRDs prior to the commencement of construction activity.

#### **F. Requirements for Completing Permit Registration Documents (PRDs)**

All dischargers required to comply with this General Permit shall electronically submit the required PRDs for their type of construction as defined below.

#### **G. Standard PRD Requirements (All Dischargers)**

1. Notice of Intent
2. Risk Assessment (Standard or Site-Specific)
3. Site Map
4. SWPPP
5. Annual Fee
6. Certification

#### **H. Additional PRD Requirements Related to Construction Type**

1. Discharger in unincorporated areas of the State (not covered under an adopted Phase I or II SUSMP requirements) and that are not a linear project shall also submit a completed:
  - a. Post-Construction Water Balance Calculator (Appendix 2).
2. Dischargers who are proposing to implement ATS shall submit:
  - a. Complete ATS Plan in accordance with Attachment F at least 14 days prior to the planned operation of the ATS and a paper copy shall be available onsite during ATS operation.

- b. Certification proof that design done by a professional in accordance with Attachment F.
3. Dischargers who are proposing an alternate Risk Justification:
  - a. Particle Size Analysis.

#### **I. Exceptions to Standard PRD Requirements**

Construction sites with an R value less than 5 as determined in the Risk Assessment are not required to submit a SWPPP.

#### **J. Description of PRDs**

1. Notice of Intent (NOI)
2. Site Map(s) Includes:
  - a. The project's surrounding area (vicinity)
  - b. Site layout
  - c. Construction site boundaries
  - d. Drainage areas
  - e. Discharge locations
  - f. Sampling locations
  - g. Areas of soil disturbance (temporary or permanent)
  - h. Active areas of soil disturbance (cut or fill)
  - i. Locations of all runoff BMPs
  - j. Locations of all erosion control BMPs
  - k. Locations of all sediment control BMPs
  - l. ATS location (if applicable)
  - m. Locations of sensitive habitats, watercourses, or other features which are not to be disturbed
  - n. Locations of all post-construction BMPs
  - o. Locations of storage areas for waste, vehicles, service, loading/unloading of materials, access (entrance/exits) points to construction site, fueling, and water storage, water transfer for dust control and compaction practices
3. **SWPPPs**

A site-specific SWPPP shall be developed by each discharger and shall be submitted with the PRDs.
4. **Risk Assessment**

All dischargers shall use the Risk Assessment procedure as describe in the General Permit Appendix 1.

  - a. The Standard Risk Assessment includes utilization of the following:
    - i. Receiving water Risk Assessment interactive map

- ii. EPA Rainfall Erosivity Factor Calculator Website
  - iii. Sediment Risk interactive map
  - iv. Sediment sensitive water bodies list
- b. The Site-Specific Risk Assessment includes the completion of the hand calculated R value Risk Calculator
5. **Post-Construction Water Balance Calculator**  
All dischargers subject to this requirement shall complete the Water Balance Calculator (in Appendix 2) in accordance with the instructions.
6. **ATS Design Document and Certification**  
All dischargers using ATS must submit electronically their system design (as well as any supporting documentation) and proof that the system was designed by a qualified ATS design professional (See Attachment F).

To obtain coverage under the General Permit PRDs must be included and completed. If any of the required items are missing, the PRD submittal is considered incomplete and will be rejected. Upon receipt of a complete PRD submittal, the State Water Board will process the application package in the order received and assign a (WDID) number.

Questions?

If you have any questions on completing the PRDs please email [stormwater@waterboards.ca.gov](mailto:stormwater@waterboards.ca.gov) or call (866) 563-3107.

## ATTACHMENT C RISK LEVEL 1 REQUIREMENTS

### A. Effluent Standards

*[These requirements are the same as those in the General Permit order.]*

1. Narrative – Risk Level 1 dischargers shall comply with the narrative effluent standards listed below:
  - a. Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
  - b. Dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.
2. Numeric – Risk Level 1 dischargers are not subject to a numeric effluent standard.

### B. Good Site Management "Housekeeping"

1. Risk Level 1 dischargers shall implement good site management (i.e., "housekeeping") measures for construction materials that could potentially be a threat to water quality if discharged. At a minimum, Risk Level 1 dischargers shall implement the following good housekeeping measures:
  - a. Conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - b. Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).

- c. Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).
  - d. Minimize exposure of construction materials to precipitation. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - e. Implement BMPs to prevent the off-site tracking of loose construction and landscape materials.
2. Risk Level 1 dischargers shall implement good housekeeping measures for waste management, which, at a minimum, shall consist of the following:
- a. Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.
  - b. Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.
  - c. Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.
  - d. Cover waste disposal containers at the end of every business day and during a rain event.
  - e. Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.
  - f. Contain and securely protect stockpiled waste material from wind and rain at all times unless actively being used.
  - g. Implement procedures that effectively address hazardous and non-hazardous spills.
  - h. Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require that:
    - i. Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly; and

- ii. Appropriate spill response personnel are assigned and trained.
  - i. Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.
3. Risk Level 1 dischargers shall implement good housekeeping for vehicle storage and maintenance, which, at a minimum, shall consist of the following:
  - a. Prevent oil, grease, or fuel to leak in to the ground, storm drains or surface waters.
  - b. Place all equipment or vehicles, which are to be fueled, maintained and stored in a designated area fitted with appropriate BMPs.
  - c. Clean leaks immediately and disposing of leaked materials properly.
4. Risk Level 1 dischargers shall implement good housekeeping for landscape materials, which, at a minimum, shall consist of the following:
  - a. Contain stockpiled materials such as mulches and topsoil when they are not actively being used.
  - b. Contain fertilizers and other landscape materials when they are not actively being used.
  - c. Discontinue the application of any erodible landscape material within 2 days before a forecasted rain event or during periods of precipitation.
  - d. Apply erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.
  - e. Stack erodible landscape material on pallets and covering or storing such materials when not being used or applied.
5. Risk Level 1 dischargers shall conduct an assessment and create a list of potential pollutant sources and identify any areas of the site where additional BMPs are necessary to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges. This potential pollutant list shall be kept with the SWPPP and shall identify

all non-visible pollutants which are known, or should be known, to occur on the construction site. At a minimum, when developing BMPs, Risk Level 1 dischargers shall do the following:

- a. Consider the quantity, physical characteristics (e.g., liquid, powder, solid), and locations of each potential pollutant source handled, produced, stored, recycled, or disposed of at the site.
  - b. Consider the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water.
  - c. Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas.
  - d. Ensure retention of sampling, visual observation, and inspection records.
  - e. Ensure effectiveness of existing BMPs to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges.
6. Risk Level 1 dischargers shall implement good housekeeping measures on the construction site to control the air deposition of site materials and from site operations. Such particulates can include, but are not limited to, sediment, nutrients, trash, metals, bacteria, oil and grease and organics.

### **C. Non-Storm Water Management**

1. Risk Level 1 dischargers shall implement measures to control all non-storm water discharges during construction.
2. Risk Level 1 dischargers shall wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.
3. Risk Level 1 dischargers shall clean streets in such a manner as to prevent unauthorized non-storm water discharges from reaching surface water or MS4 drainage systems.

**D. Erosion Control**

1. Risk Level 1 dischargers shall implement effective wind erosion control.
2. Risk Level 1 dischargers shall provide effective soil cover for inactive<sup>1</sup> areas and all finished slopes, open space, utility backfill, and completed lots.
3. Risk Level 1 dischargers shall limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the discharger shall consider the use of plastic materials resistant to solar degradation.

**E. Sediment Controls**

1. Risk Level 1 dischargers shall establish and maintain effective perimeter controls and stabilize all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.
2. On sites where sediment basins are to be used, Risk Level 1 dischargers shall, at minimum, design sediment basins according to the method provided in CASQA's Construction BMP Guidance Handbook.

**F. Run-on and Runoff Controls**

Risk Level 1 dischargers shall effectively manage all run-on, all runoff within the site and all runoff that discharges off the site. Run-on from off site shall be directed away from all disturbed areas or shall collectively be in compliance with the effluent limitations in this General Permit.

**G. Inspection, Maintenance and Repair**

1. Risk Level 1 dischargers shall ensure that all inspection, maintenance repair and sampling activities at the project location shall be performed or supervised by a Qualified SWPPP Practitioner (QSP) representing the discharger. The QSP may delegate any or all of these activities to an employee trained to do the task(s) appropriately, but shall ensure adequate deployment.
2. Risk Level 1 dischargers shall perform weekly inspections and observations, and at least once each 24-hour period during extended

---

<sup>1</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

storm events, to identify and record BMPs that need maintenance to operate effectively, that have failed, or that could fail to operate as intended. Inspectors shall be the QSP or be trained by the QSP.

3. Upon identifying failures or other shortcomings, as directed by the QSP, Risk Level 1 dischargers shall begin implementing repairs or design changes to BMPs within 72 hours of identification and complete the changes as soon as possible.
4. For each inspection required, Risk Level 1 dischargers shall complete an inspection checklist, using a form provided by the State Water Board or Regional Water Board or in an alternative format.
5. Risk Level 1 dischargers shall ensure that checklists shall remain onsite with the SWPPP and at a minimum, shall include:
  - a. Inspection date and date the inspection report was written.
  - b. Weather information, including presence or absence of precipitation, estimate of beginning of qualifying storm event, duration of event, time elapsed since last storm, and approximate amount of rainfall in inches.
  - c. Site information, including stage of construction, activities completed, and approximate area of the site exposed.
  - d. A description of any BMPs evaluated and any deficiencies noted.
  - e. If the construction site is safely accessible during inclement weather, list the observations of all BMPs: erosion controls, sediment controls, chemical and waste controls, and non-storm water controls. Otherwise, list the results of visual inspections at all relevant outfalls, discharge points, downstream locations and any projected maintenance activities.
  - f. Report the presence of noticeable odors or of any visible sheen on the surface of any discharges.
  - g. Any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates.
  - h. Photographs taken during the inspection, if any.
  - i. Inspector's name, title, and signature.

**H. Rain Event Action Plan**

Not required for Risk Level 1 dischargers.

## I. Risk Level 1 Monitoring and Reporting Requirements

Table 1- Summary of Monitoring Requirements

Risk Level	Visual Inspections				Sample Collection		
	Quarterly Non-storm Water Discharge	Pre-storm Event		Daily Storm BMP	Post Storm	Storm Water Discharge	Receiving Water
		Baseline	REAP				
1	X	X		X	X		

### 1. Construction Site Monitoring Program Requirements

- a. Pursuant to Water Code Sections 13383 and 13267, all dischargers subject to this General Permit shall develop and implement a written site-specific Construction Site Monitoring Program (CSMP) in accordance with the requirements of this Section. The CSMP shall include all monitoring procedures and instructions, location maps, forms, and checklists as required in this section. The CSMP shall be developed prior to the commencement of construction activities, and revised as necessary to reflect project revisions. The CSMP shall be a part of the Storm Water Pollution Prevention Plan (SWPPP), included as an appendix or separate SWPPP chapter.
- b. Existing dischargers registered under the State Water Board Order No. 99-08-DWQ shall make and implement necessary revisions to their Monitoring Programs to reflect the changes in this General Permit in a timely manner, but no later than July 1, 2010. Existing dischargers shall continue to implement their existing Monitoring Programs in compliance with State Water Board Order No. 99-08-DWQ until the necessary revisions are completed according to the schedule above.
- c. When a change of ownership occurs for all or any portion of the construction site prior to completion or final stabilization, the new discharger shall comply with these requirements as of the date the ownership change occurs.

### 2. Objectives

The CSMP shall be developed and implemented to address the following objectives:

- a. To demonstrate that the site is in compliance with the Discharge Prohibitions;

- b. To determine whether non-visible pollutants are present at the construction site and are causing or contributing to exceedances of water quality objectives;
  - c. To determine whether immediate corrective actions, additional Best Management Practice (BMP) implementation, or SWPPP revisions are necessary to reduce pollutants in storm water discharges and authorized non-storm water discharges; and
  - d. To determine whether BMPs included in the SWPPP are effective in preventing or reducing pollutants in storm water discharges and authorized non-storm water discharges.
3. **Risk Level 1 - Visual Monitoring (Inspection) Requirements for Qualifying Rain Events**
- a. Risk Level 1 dischargers shall visually observe (inspect) storm water discharges at all discharge locations within two business days (48 hours) after each qualifying rain event.
  - b. Risk Level 1 dischargers shall visually observe (inspect) the discharge of stored or contained storm water that is derived from and discharged subsequent to a qualifying rain event producing precipitation of ½ inch or more at the time of discharge. Stored or contained storm water that will likely discharge after operating hours due to anticipated precipitation shall be observed prior to the discharge during operating hours.
  - c. Risk Level 1 dischargers shall conduct visual observations (inspections) during business hours only.
  - d. Risk Level 1 dischargers shall record the time, date and rain gauge reading of all qualifying rain events.
  - e. Within 2 business days (48 hours) prior to each qualifying rain event, Risk Level 1 dischargers shall visually observe (inspect):
    - i. All storm water drainage areas to identify any spills, leaks, or uncontrolled pollutant sources. If needed, the discharger shall implement appropriate corrective actions.
    - ii. All BMPs to identify whether they have been properly implemented in accordance with the SWPPP. If needed, the discharger shall implement appropriate corrective actions.

- iii. Any storm water storage and containment areas to detect leaks and ensure maintenance of adequate freeboard.
- f. For the visual observations (inspections) described in e.i and e.iii above, Risk Level 1 dischargers shall observe the presence or absence of floating and suspended materials, a sheen on the surface, discolorations, turbidity, odors, and source(s) of any observed pollutants.
- g. Within two business days (48 hours) after each qualifying rain event, Risk Level 1 dischargers shall conduct post rain event visual observations (inspections) to (1) identify whether BMPs were adequately designed, implemented, and effective, and (2) identify additional BMPs and revise the SWPPP accordingly.
- h. Risk Level 1 dischargers shall maintain on-site records of all visual observations (inspections), personnel performing the observations, observation dates, weather conditions, locations observed, and corrective actions taken in response to the observations.

#### **4. Risk Level 1 – Visual Observation Exemptions**

- a. Risk Level 1 dischargers shall be prepared to conduct visual observation (inspections) until the minimum requirements of Section I.3 above are completed. Risk Level 1 dischargers are not required to conduct visual observation (inspections) under the following conditions:
  - i. During dangerous weather conditions such as flooding and electrical storms.
  - ii. Outside of scheduled site business hours.
- b. If no required visual observations (inspections) are collected due to these exceptions, Risk Level 1 dischargers shall include an explanation in their SWPPP and in the Annual Report documenting why the visual observations (inspections) were not conducted.

#### **5. Risk Level 1 – Monitoring Methods**

Risk Level 1 dischargers shall include a description of the visual observation locations, visual observation procedures, and visual observation follow-up and tracking procedures in the CSMP.

#### **6. Risk Level 1 – Non-Storm Water Discharge Monitoring Requirements**

- a. Visual Monitoring Requirements:
  - i. Risk Level 1 dischargers shall visually observe (inspect) each drainage area for the presence of (or indications of prior) unauthorized and authorized non-storm water discharges and their sources.
  - ii. Risk Level 1 dischargers shall conduct one visual observation (inspection) quarterly in each of the following periods: January-March, April-June, July-September, and October-December. Visual observation (inspections) are only required during daylight hours (sunrise to sunset).
  - iii. Risk Level 1 dischargers shall ensure that visual observations (inspections) document the presence or evidence of any non-storm water discharge (authorized or unauthorized), pollutant characteristics (floating and suspended material, sheen, discoloration, turbidity, odor, etc.), and source. Risk Level 1 dischargers shall maintain on-site records indicating the personnel performing the visual observation (inspections), the dates and approximate time each drainage area and non-storm water discharge was observed, and the response taken to eliminate unauthorized non-storm water discharges and to reduce or prevent pollutants from contacting non-storm water discharges.

#### **7. Risk Level 1 – Non-Visible Pollutant Monitoring Requirements**

- a. Risk Level 1 dischargers shall collect one or more samples during any breach, malfunction, leakage, or spill observed during a visual inspection which could result in the discharge of pollutants to surface waters that would not be visually detectable in storm water.
- b. Risk Level 1 dischargers shall ensure that water samples are large enough to characterize the site conditions.
- c. Risk Level 1 dischargers shall collect samples at all discharge locations that can be safely accessed.
- d. Risk Level 1 dischargers shall collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff.
- e. Risk Level 1 dischargers shall analyze samples for all non-visible pollutant parameters (if applicable) - parameters indicating the

presence of pollutants identified in the pollutant source assessment required (Risk Level 1 dischargers shall modify their CSMPs to address these additional parameters in accordance with any updated SWPPP pollutant source assessment).

- f. Risk Level 1 dischargers shall collect a sample of storm water that has not come in contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample) for comparison with the discharge sample.
- g. Risk Level 1 dischargers shall compare the uncontaminated sample to the samples of discharge using field analysis or through laboratory analysis.<sup>2</sup>
- h. Risk Level 1 dischargers shall keep all field /or analytical data in the SWPPP document.

#### **8. Risk Level 1 – Particle Size Analysis for Project Risk Justification**

Risk Level 1 dischargers justifying an alternative project risk shall report a soil particle size analysis used to determine the RUSLE K-Factor. ASTM D-422 (Standard Test Method for Particle-Size Analysis of Soils), as revised, shall be used to determine the percentages of sand, very fine sand, silt, and clay on the site.

#### **9. Risk Level 1 – Records**

Risk Level 1 dischargers shall retain records of all storm water monitoring information and copies of all reports (including Annual Reports) for a period of at least three years. Risk Level 1 dischargers shall retain all records on-site while construction is ongoing. These records include:

- a. The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation.
- b. The individual(s) who performed the facility inspections, sampling, visual observation (inspections), and or measurements.
- c. The date and approximate time of analyses.
- d. The individual(s) who performed the analyses.

---

<sup>2</sup> For laboratory analysis, all sampling, sample preservation, and analyses must be conducted according to test procedures under 40 CFR Part 136. Field discharge samples shall be collected and analyzed according to the specifications of the manufacturer of the sampling devices employed.

- e. A summary of all analytical results from the last three years, the method detection limits and reporting units, and the analytical techniques or methods used.
- f. Rain gauge readings from site inspections.
- g. Quality assurance/quality control records and results.
- h. Non-storm water discharge inspections and visual observation (inspections) and storm water discharge visual observation records (see Sections I.3 and I.6 above).
- i. Visual observation and sample collection exception records (see Section I.4 above).
- j. The records of any corrective actions and follow-up activities that resulted from analytical results, visual observation (inspections), or inspections.

## ATTACHMENT D RISK LEVEL 2 REQUIREMENTS

### A. Effluent Standards

*[These requirements are the same as those in the General Permit order.]*

1. Narrative – Risk Level 2 dischargers shall comply with the narrative effluent standards listed below:
  - a. Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
  - b. Dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.
2. Numeric – Risk level 2 dischargers are subject to a pH NAL of 6.5-8.5, and a turbidity NAL of 250 NTU.

### B. Good Site Management "Housekeeping"

1. Risk Level 2 dischargers shall implement good site management (i.e., "housekeeping") measures for construction materials that could potentially be a threat to water quality if discharged. At a minimum, Risk Level 2 dischargers shall implement the following good housekeeping measures:
  - a. Conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - b. Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).

- c. Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).
  - d. Minimize exposure of construction materials to precipitation. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - e. Implement BMPs to prevent the off-site tracking of loose construction and landscape materials.
2. Risk Level 2 dischargers shall implement good housekeeping measures for waste management, which, at a minimum, shall consist of the following:
- a. Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.
  - b. Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.
  - c. Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.
  - d. Cover waste disposal containers at the end of every business day and during a rain event.
  - e. Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.
  - f. Contain and securely protect stockpiled waste material from wind and rain at all times unless actively being used.
  - g. Implement procedures that effectively address hazardous and non-hazardous spills.
  - h. Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require:
    - i. Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly.

- ii. Appropriate spill response personnel are assigned and trained.
  - i. Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.
3. Risk Level 2 dischargers shall implement good housekeeping for vehicle storage and maintenance, which, at a minimum, shall consist of the following:
  - a. Prevent oil, grease, or fuel to leak in to the ground, storm drains or surface waters.
  - b. Place all equipment or vehicles, which are to be fueled, maintained and stored in a designated area fitted with appropriate BMPs.
  - c. Clean leaks immediately and disposing of leaked materials properly.
4. Risk Level 2 dischargers shall implement good housekeeping for landscape materials, which, at a minimum, shall consist of the following:
  - a. Contain stockpiled materials such as mulches and topsoil when they are not actively being used.
  - b. Contain all fertilizers and other landscape materials when they are not actively being used.
  - c. Discontinue the application of any erodible landscape material within 2 days before a forecasted rain event or during periods of precipitation.
  - d. Apply erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.
  - e. Stack erodible landscape material on pallets and covering or storing such materials when not being used or applied.
5. Risk Level 2 dischargers shall conduct an assessment and create a list of potential pollutant sources and identify any areas of the site where additional BMPs are necessary to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges. This potential pollutant list shall be kept with the SWPPP and shall identify

all non-visible pollutants which are known, or should be known, to occur on the construction site. At a minimum, when developing BMPs, Risk Level 2 dischargers shall do the following:

- a. Consider the quantity, physical characteristics (e.g., liquid, powder, solid), and locations of each potential pollutant source handled, produced, stored, recycled, or disposed of at the site.
  - b. Consider the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water.
  - c. Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas.
  - d. Ensure retention of sampling, visual observation, and inspection records.
  - e. Ensure effectiveness of existing BMPs to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges.
6. Risk Level 2 dischargers shall implement good housekeeping measures on the construction site to control the air deposition of site materials and from site operations. Such particulates can include, but are not limited to, sediment, nutrients, trash, metals, bacteria, oil and grease and organics.
7. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall document all housekeeping BMPs in the SWPPP and REAP(s) in accordance with the nature and phase of the construction project. Construction phases at traditional land development projects include Grading and Land Development Phase, Streets and Utilities, or Vertical Construction for traditional land development projects.

### **C. Non-Storm Water Management**

1. Risk Level 2 dischargers shall implement measures to control all non-storm water discharges during construction.
2. Risk Level 2 dischargers shall wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.

3. Risk Level 2 dischargers shall clean streets in such a manner as to prevent unauthorized non-storm water discharges from reaching surface water or MS4 drainage systems.

#### D. Erosion Control

1. Risk Level 2 dischargers shall implement effective wind erosion control.
2. Risk Level 2 dischargers shall provide effective soil cover for inactive<sup>1</sup> areas and all finished slopes, open space, utility backfill, and completed lots.
3. Risk Level 2 dischargers shall limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the discharger shall consider the use of plastic materials resistant to solar degradation.

#### E. Sediment Controls

1. Risk Level 2 dischargers shall establish and maintain effective perimeter controls and stabilize all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.
2. On sites where sediment basins are to be used, Risk Level 2 dischargers shall, at minimum, design sediment basins according to the method provided in CASQA's Construction BMP Guidance Handbook.
3. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall implement appropriate erosion control BMPs (runoff control and soil stabilization) in conjunction with sediment control BMPs for areas under active<sup>2</sup> construction.
4. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall apply linear sediment controls along the toe of the slope, face of the slope, and at the grade breaks of exposed slopes to comply with sheet flow lengths<sup>3</sup> in accordance with Table 1.

**Table 1 - Critical Slope/Sheet Flow Length Combinations**

Slope Percentage	Sheet flow length not
------------------	-----------------------

<sup>1</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

<sup>2</sup> Active areas of construction are areas undergoing land surface disturbance. This includes construction activity during the preliminary stage, mass grading stage, streets and utilities stage and the vertical construction stage.

<sup>3</sup> Sheet flow length is the length that shallow, low velocity flow travels across a site.

	to exceed
0-25% 20	feet
25-50% 15	feet
Over 50%	10 feet

5. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall ensure that construction activity traffic to and from the project is limited to entrances and exits that employ effective controls to prevent offsite tracking of sediment.
6. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall ensure that all storm drain inlets and perimeter controls, runoff control BMPs, and pollutant controls at entrances and exits (e.g. tire washoff locations) are maintained and protected from activities that reduce their effectiveness.
7. **Additional Risk Level 2 Requirement:** Risk Level 2 dischargers shall inspect on a daily basis all immediate access roads daily. At a minimum daily (when necessary) and prior to any rain event, the discharger shall remove any sediment or other construction activity-related materials that are deposited on the roads (by vacuuming or sweeping).

#### F. Run-on and Run-off Controls

Risk Level 2 dischargers shall effectively manage all run-on, all runoff within the site and all runoff that discharges off the site. Run-on from off site shall be directed away from all disturbed areas or shall collectively be in compliance with the effluent limitations in this General Permit.

#### G. Inspection, Maintenance and Repair

1. Risk Level 2 dischargers shall ensure that all inspection, maintenance repair and sampling activities at the project location shall be performed or supervised by a Qualified SWPPP Practitioner (QSP) representing the discharger. The QSP may delegate any or all of these activities to an employee appropriately trained to do the task(s).
2. Risk Level 2 dischargers shall perform weekly inspections and observations, and at least once each 24-hour period during extended storm events, to identify and record BMPs that need maintenance to operate effectively, that have failed, or that could fail to operate as intended. Inspectors shall be the QSP or be trained by the QSP.
3. Upon identifying failures or other shortcomings, as directed by the QSP, Risk Level 2 dischargers shall begin implementing repairs or

design changes to BMPs within 72 hours of identification and complete the changes as soon as possible.

4. For each inspection required, Risk Level 2 dischargers shall complete an inspection checklist, using a form provided by the State Water Board or Regional Water Board or in an alternative format.
5. Risk Level 2 dischargers shall ensure that checklists shall remain onsite with the SWPPP and at a minimum, shall include:
  - a. Inspection date and date the inspection report was written.
  - b. Weather information, including presence or absence of precipitation, estimate of beginning of qualifying storm event, duration of event, time elapsed since last storm, and approximate amount of rainfall in inches.
  - c. Site information, including stage of construction, activities completed, and approximate area of the site exposed.
  - d. A description of any BMPs evaluated and any deficiencies noted.
  - e. If the construction site is safely accessible during inclement weather, list the observations of all BMPs: erosion controls, sediment controls, chemical and waste controls, and non-storm water controls. Otherwise, list the results of visual inspections at all relevant outfalls, discharge points, downstream locations and any projected maintenance activities.
  - f. Report the presence of noticeable odors or of any visible sheen on the surface of any discharges.
  - g. Any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates.
  - h. Photographs taken during the inspection, if any.
  - i. Inspector's name, title, and signature.

#### H. Rain Event Action Plan

1. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP develop a Rain Event Action Plan (REAP) 48 hours prior to any likely precipitation event. A likely precipitation event is any weather pattern that is forecast to have a 50% or greater probability of producing precipitation in the project area. The discharger shall

ensure a QSP obtain a printed copy of precipitation forecast information from the National Weather Service Forecast Office (e.g., by entering the zip code of the project's location at <http://www.srh.noaa.gov/forecast>).

2. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP develop the REAPs for all phases of construction (i.e., Grading and Land Development, Streets and Utilities, Vertical Construction, Final Landscaping and Site Stabilization).
3. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP ensure that the REAP include, at a minimum, the following site information:
  - a. Site Address
  - b. Calculated Risk Level (2 or 3)
  - c. Site Storm Water Manager Information including the name, company, and 24-hour emergency telephone number
  - d. Erosion and Sediment Control Provider information including the name, company, and 24-hour emergency telephone number
  - e. Storm Water Sampling Agent information including the name, company, and 24-hour emergency telephone number
4. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP include in the REAP, at a minimum, the following project phase information:
  - a. Activities associated with each construction phase
  - b. Trades active on the construction site during each construction phase
  - c. Trade contractor information
  - d. Suggested actions for each project phase
5. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP develop additional REAPs for project sites where construction activities are indefinitely halted or postponed (Inactive Construction). At a minimum, Inactive Construction REAPs must include:
  - a. Site Address
  - b. Calculated Risk Level (2 or 3)
  - c. Site Storm Water Manager Information including the name, company, and 24-hour emergency telephone number
  - d. Erosion and Sediment Control Provider information including the name, company, and 24-hour emergency telephone number
  - e. Storm Water Sampling Agent information including the name, company, and 24-hour emergency telephone number

- f. Trades active on site during Inactive Construction
  - g. Trade contractor information
  - h. Suggested actions for inactive construction sites
6. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP begin implementation and make the REAP available onsite no later than 24 hours prior to the likely precipitation event.
7. **Additional Risk Level 2 Requirement:** The discharger shall ensure a QSP maintain onsite a paper copy of each REAP onsite in compliance with the record retention requirements of the Special Provisions in this General Permit.

## I. Risk Level 2 Monitoring and Reporting Requirements

**Table 2- Summary of Monitoring Requirements**

Risk Level	Visual Inspections					Sample Collection	
	Quarterly Non-storm Water Discharge	Pre-storm Event		Daily Storm BMP	Post Storm	Storm Water Discharge	Receiving Water
		Baseline	REAP				
2	X	X	X	X	X	X	

### 1. Construction Site Monitoring Program Requirements

- a. Pursuant to Water Code Sections 13383 and 13267, all dischargers subject to this General Permit shall develop and implement a written site-specific Construction Site Monitoring Program (CSMP) in accordance with the requirements of this Section. The CSMP shall include all monitoring procedures and instructions, location maps, forms, and checklists as required in this section. The CSMP shall be developed prior to the commencement of construction activities, and revised as necessary to reflect project revisions. The CSMP shall be a part of the Storm Water Pollution Prevention Plan (SWPPP), included as an appendix or separate SWPPP chapter.
- b. Existing dischargers registered under the State Water Board Order No. 99-08-DWQ shall make and implement necessary revisions to their Monitoring Program to reflect the changes in this General Permit in a timely manner, but no later than July 1, 2010. Existing dischargers shall continue to implement their existing Monitoring Programs in compliance with State Water Board Order No. 99-08-DWQ until the necessary revisions are completed according to the schedule above.
- c. When a change of ownership occurs for all or any portion of the construction site prior to completion or final stabilization, the new discharger shall comply with these requirements as of the date the ownership change occurs.

### 2. Objectives

The CSMP shall be developed and implemented to address the following objectives:

- a. To demonstrate that the site is in compliance with the Discharge Prohibitions and applicable Numeric Action Levels (NALs)/Numeric Effluent Limitations (NELs) of this General Permit.
  - b. To determine whether non-visible pollutants are present at the construction site and are causing or contributing to exceedances of water quality objectives.
  - c. To determine whether immediate corrective actions, additional Best Management Practice (BMP) implementation, or SWPPP revisions are necessary to reduce pollutants in storm water discharges and authorized non-storm water discharges.
  - d. To determine whether BMPs included in the SWPPP/Rain Event Action Plan (REAP) are effective in preventing or reducing pollutants in storm water discharges and authorized non-storm water discharges.
3. **Risk Level 2 – Visual Monitoring (Inspection) Requirements for Qualifying Rain Events**
- a. Risk Level 2 dischargers shall visually observe (inspect) storm water discharges at all discharge locations within two business days (48 hours) after each qualifying rain event.
  - b. Risk Level 2 dischargers shall visually observe (inspect) the discharge of stored or contained storm water that is derived from and discharged subsequent to a qualifying rain event producing precipitation of ½ inch or more at the time of discharge. Stored or contained storm water that will likely discharge after operating hours due to anticipated precipitation shall be observed prior to the discharge during operating hours.
  - c. Risk Level 2 dischargers shall conduct visual observations (inspections) during business hours only.
  - d. Risk Level 2 dischargers shall record the time, date and rain gauge reading of all qualifying rain events.
  - e. Within 2 business days (48 hours) prior to each qualifying rain event, Risk Level 2 dischargers shall visually observe (inspect):
    - i. all storm water drainage areas to identify any spills, leaks, or uncontrolled pollutant sources. If needed, the discharger shall implement appropriate corrective actions.

- ii. all BMPs to identify whether they have been properly implemented in accordance with the SWPPP/REAP. If needed, the discharger shall implement appropriate corrective actions.
- iii. any storm water storage and containment areas to detect leaks and ensure maintenance of adequate freeboard.
- f. For the visual observations (inspections) described in c.i and c.iii above, Risk Level 2 dischargers shall observe the presence or absence of floating and suspended materials, a sheen on the surface, discolorations, turbidity, odors, and source(s) of any observed pollutants.
- g. Within two business days (48 hours) after each qualifying rain event, Risk Level 2 dischargers shall conduct post rain event visual observations (inspections) to (1) identify whether BMPs were adequately designed, implemented, and effective, and (2) identify additional BMPs and revise the SWPPP accordingly.
- h. Risk Level 2 dischargers shall maintain on-site records of all visual observations (inspections), personnel performing the observations, observation dates, weather conditions, locations observed, and corrective actions taken in response to the observations.

#### **4. Risk Level 2 – Water Quality Sampling and Analysis**

- a. Risk Level 2 dischargers shall collect storm water grab samples from sampling locations, as defined in Section 1.5. The storm water grab sample(s) obtained shall be representative of the flow and characteristics of the discharge.
- b. At minimum, Risk Level 2 dischargers shall collect 3 samples per day of the qualifying event.
- c. Risk Level 2 dischargers shall ensure that the grab samples collected of stored or contained storm water are from discharges subsequent to a qualifying rain event (producing precipitation of ½ inch or more at the time of discharge).

#### **Storm Water Effluent Monitoring Requirements**

- d. Risk Level 2 dischargers shall analyze their effluent samples for:
  - i. pH and turbidity.

- ii. Any additional parameters for which monitoring is required by the Regional Water Board.

## 5. Risk Level 2 – Storm Water Discharge Water Quality Sampling Locations

### Effluent Sampling Locations

- a. Risk Level 2 dischargers shall perform sampling and analysis of storm water discharges to characterize discharges associated with construction activity from the entire project disturbed area.
- b. Risk Level 2 dischargers shall collect effluent samples at all discharge points where storm water is discharged off-site.
- c. Risk Level 2 dischargers shall ensure that storm water discharge collected and observed represent<sup>4</sup> the effluent in each drainage area based on visual observation of the water and upstream conditions.
- d. Risk Level 2 dischargers shall monitor and report site run-on from surrounding areas if there is reason to believe run-on may contribute to an exceedance of NALs or NELs.
- e. Risk Level 2 dischargers who deploy an ATS on their site, or a portion on their site, shall collect ATS effluent samples and measurements from the discharge pipe or another location representative of the nature of the discharge.
- f. Risk Level 2 dischargers shall select analytical test methods from the list provided in Table 3 below.
- g. All storm water sample collection preservation and handling shall be conducted in accordance with Section 1.7 “Storm Water Sample Collection and Handling Instructions” below.

## 6. Risk Level 2 – Visual Observation and Sample Collection Exemptions

- a. Risk Level 2 dischargers shall be prepared to collect samples and conduct visual observation (inspections) until the minimum requirements of Sections 1.3 and 1.4 above are completed. Risk

---

<sup>4</sup> For example, if there has been concrete work recently in an area, or drywall scrap is exposed to the rain, a pH sample shall be taken of drainage from the relevant work area. Similarly, if sediment laden water is flowing through some parts of a silt fence, samples shall be taken of the sediment-laden water even if most water flowing through the fence is clear.

Level 2 dischargers are not required to physically collect samples or conduct visual observation (inspections) under the following conditions:

- i. During dangerous weather conditions such as flooding and electrical storms.
  - ii. Outside of scheduled site business hours.
- b. If no required samples or visual observation (inspections) are collected due to these exceptions, Risk Level 2 dischargers shall include an explanation in their SWPPP and in the Annual Report documenting why the sampling or visual observation (inspections) were not conducted.

#### **7. Risk Level 2 – Storm Water Sample Collection and Handling Instructions**

- a. Risk Level 2 dischargers shall refer to Table 3 below for test methods, detection limits, and reporting units.
- b. Risk Level 2 dischargers shall ensure that testing laboratories will receive samples within 48 hours of the physical sampling (unless otherwise required by the laboratory), and shall use only the sample containers provided by the laboratory to collect and store samples.
- c. Risk Level 2 dischargers shall designate and train personnel to collect, maintain, and ship samples in accordance with the Surface Water Ambient Monitoring Program's (SWAMP) 2008 Quality Assurance Program Plan (QAPrP).<sup>5</sup>

#### **8. Risk Level 2 – Monitoring Methods**

- a. Risk Level 2 dischargers shall include a description of the following items in the CSMP:
  - i. Visual observation locations, visual observation procedures, and visual observation follow-up and tracking procedures.
  - ii. Sampling locations, and sample collection and handling procedures. This shall include detailed procedures for sample

<sup>5</sup> Additional information regarding SWAMP's QAPrP and QAMP can be found at [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/](http://www.waterboards.ca.gov/water_issues/programs/swamp/).  
 QAPrP: [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/docs/qapp/swamp\\_qapp\\_master090108a.pdf](http://www.waterboards.ca.gov/water_issues/programs/swamp/docs/qapp/swamp_qapp_master090108a.pdf).  
 QAMP: [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/qamp.shtml](http://www.waterboards.ca.gov/water_issues/programs/swamp/qamp.shtml).

collection, storage, preservation, and shipping to the testing lab to assure that consistent quality control and quality assurance is maintained. Dischargers shall attach to the monitoring program an example Chain of Custody form used when handling and shipping samples.

- iii. Identification of the analytical methods and related method detection limits (if applicable) for each parameter required in Section I.4 above.
- b. Risk Level 2 dischargers shall ensure that all sampling and sample preservation are in accordance with the current edition of "Standard Methods for the Examination of Water and Wastewater" (American Public Health Association). All monitoring instruments and equipment (including a discharger's own field instruments for measuring pH and turbidity) should be calibrated and maintained in accordance with manufacturers' specifications to ensure accurate measurements. Risk Level 2 dischargers shall ensure that all laboratory analyses are conducted according to test procedures under 40 CFR Part 136, unless other test procedures have been specified in this General Permit or by the Regional Water Board. With the exception of field analysis conducted by the discharger for turbidity and pH, all analyses should be sent to and conducted at a laboratory certified for such analyses by the State Department of Health Services. Risk Level 2 dischargers shall conduct their own field analysis of pH and may conduct their own field analysis of turbidity if the discharger has sufficient capability (qualified and trained employees, properly calibrated and maintained field instruments, etc.) to adequately perform the field analysis.

#### 9. Risk Level 2 – Analytical Methods

- a. Risk Level 2 dischargers shall refer to Table 3 below for test methods, detection limits, and reporting units.
- b. **pH:** Risk Level 2 dischargers shall perform pH analysis on-site with a calibrated pH meter or a pH test kit. Risk Level 2 dischargers shall record pH monitoring results on paper and retain these records in accordance with Section I.14, below.
- c. **Turbidity:** Risk Level 2 dischargers shall perform turbidity analysis using a calibrated turbidity meter (turbidimeter), either on-site or at an accredited lab. Acceptable test methods include Standard Method 2130 or USEPA Method 180.1. The results will be recorded in the site log book in Nephelometric Turbidity Units (NTU).

## 10. Risk Level 2 - Non-Storm Water Discharge Monitoring Requirements

### a. Visual Monitoring Requirements:

- i. Risk Level 2 dischargers shall visually observe (inspect) each drainage area for the presence of (or indications of prior) unauthorized and authorized non-storm water discharges and their sources.
- ii. Risk Level 2 dischargers shall conduct one visual observation (inspection) quarterly in each of the following periods: January-March, April-June, July-September, and October-December. Visual observation (inspections) are only required during daylight hours (sunrise to sunset).
- iii. Risk Level 2 dischargers shall ensure that visual observations (inspections) document the presence or evidence of any non-storm water discharge (authorized or unauthorized), pollutant characteristics (floating and suspended material, sheen, discoloration, turbidity, odor, etc.), and source. Risk Level 2 dischargers shall maintain on-site records indicating the personnel performing the visual observation (inspections), the dates and approximate time each drainage area and non-storm water discharge was observed, and the response taken to eliminate unauthorized non-storm water discharges and to reduce or prevent pollutants from contacting non-storm water discharges.

### b. Effluent Sampling Locations:

- i. Risk Level 2 dischargers shall sample effluent at all discharge points where non-storm water and/or authorized non-storm water is discharged off-site.
- ii. Risk Level 2 dischargers shall send all non-storm water sample analyses to a laboratory certified for such analyses by the State Department of Health Services.
- iii. Risk Level 2 dischargers shall monitor and report run-on from surrounding areas if there is reason to believe run-on may contribute to an exceedance of NALs.

## 11. Risk Level 2 – Non-Visible Pollutant Monitoring Requirements

- a. Risk Level 2 dischargers shall collect one or more samples during any breach, malfunction, leakage, or spill observed during a visual inspection which could result in the discharge of pollutants to surface waters that would not be visually detectable in storm water.
- b. Risk Level 2 dischargers shall ensure that water samples are large enough to characterize the site conditions.
- c. Risk Level 2 dischargers shall collect samples at all discharge locations that can be safely accessed.
- d. Risk Level 2 dischargers shall collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff.
- e. Risk Level 2 dischargers shall analyze samples for all non-visible pollutant parameters (if applicable) - parameters indicating the presence of pollutants identified in the pollutant source assessment required (Risk Level 2 dischargers shall modify their CSMPs to address these additional parameters in accordance with any updated SWPPP pollutant source assessment).
- f. Risk Level 2 dischargers shall collect a sample of storm water that has not come in contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample) for comparison with the discharge sample.
- g. Risk Level 2 dischargers shall compare the uncontaminated sample to the samples of discharge using field analysis or through laboratory analysis.<sup>6</sup>
- h. Risk Level 2 dischargers shall keep all field /or analytical data in the SWPPP document.

## 12. Risk Level 2 – Watershed Monitoring Option

Risk Level 2 dischargers who are part of a qualified regional watershed-based monitoring program may be eligible for relief from the requirements in Sections I.5. The Regional Water Board may approve proposals to substitute an acceptable watershed-based monitoring program by determining if the watershed-based monitoring program

---

<sup>6</sup> For laboratory analysis, all sampling, sample preservation, and analyses must be conducted according to test procedures under 40 CFR Part 136. Field discharge samples shall be collected and analyzed according to the specifications of the manufacturer of the sampling devices employed.

will provide substantially similar monitoring information in evaluating discharger compliance with the requirements of this General Permit.

### **13. Risk Level 2 – Particle Size Analysis for Project Risk Justification**

Risk Level 2 dischargers justifying an alternative project risk shall report a soil particle size analysis used to determine the RUSLE K-Factor. ASTM D-422 (Standard Test Method for Particle-Size Analysis of Soils), as revised, shall be used to determine the percentages of sand, very fine sand, silt, and clay on the site.

### **14. Risk Level 2 – Records**

Risk Level 2 dischargers shall retain records of all storm water monitoring information and copies of all reports (including Annual Reports) for a period of at least three years. Risk Level 2 dischargers shall retain all records on-site while construction is ongoing. These records include:

- a. The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation.
- b. The individual(s) who performed the facility inspections, sampling, visual observation (inspections), and or measurements.
- c. The date and approximate time of analyses.
- d. The individual(s) who performed the analyses.
- e. A summary of all analytical results from the last three years, the method detection limits and reporting units, the analytical techniques or methods used, and the chain of custody forms.
- f. Rain gauge readings from site inspections;
- g. Quality assurance/quality control records and results.
- h. Non-storm water discharge inspections and visual observation (inspections) and storm water discharge visual observation records (see Sections I.3 and I.10 above).
- i. Visual observation and sample collection exception records (see Section I.6 above).

- j. The records of any corrective actions and follow-up activities that resulted from analytical results, visual observation (inspections), or inspections.

#### 15. Risk Level 2 – NAL Exceedance Report

- a. In the event that any effluent sample exceeds an applicable NAL, Risk Level 2 dischargers shall electronically submit all storm event sampling results to the State Water Board no later than 10 days after the conclusion of the storm event. The Regional Boards have the authority to require the submittal of an NAL Exceedance Report.
- b. Risk Level 2 dischargers shall certify each NAL Exceedance Report in accordance with the Special Provisions for Construction Activity.
- c. Risk Level 2 dischargers shall retain an electronic or paper copy of each NAL Exceedance Report for a minimum of three years after the date the annual report is filed.
- d. Risk Level 2 dischargers shall include in the NAL Exceedance Report:
  - i. The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as “less than the method detection limit”).
  - ii. The date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation.
  - iii. A description of the current BMPs associated with the effluent sample that exceeded the NAL and the proposed corrective actions taken.

**Table 3 – Risk Level 2 Test Methods, Detection Limits, Reporting Units and Applicable NALs/NELs**

Parameter	Test Method / Protocol	Discharge Type	Min. Detection Limit	Reporting Units	Numeric Action Level
pH	Field test with calibrated portable instrument	Risk Level 2 Discharges	0.2 pH	units	lower NAL = 6.5 upper NAL = 8.5
Turbidity EPA	0180.1 and/or field test with calibrated portable instrument	Risk Level 2 Discharges other than ATS	1 NTU		250 NTU
		For ATS discharges	1 NTU		N/A

## ATTACHMENT E RISK LEVEL 3 REQUIREMENTS

### A. Effluent Standards

*[These requirements are the same as those in the General Permit order.]*

1. Narrative – Risk Level 3 dischargers shall comply with the narrative effluent standards listed below:
  - a. Storm water discharges and authorized non-storm water discharges regulated by this General Permit shall not contain a hazardous substance equal to or in excess of reportable quantities established in 40 C.F.R. §§ 117.3 and 302.4, unless a separate NPDES Permit has been issued to regulate those discharges.
  - b. Dischargers shall minimize or prevent pollutants in storm water discharges and authorized non-storm water discharges through the use of controls, structures, and management practices that achieve BAT for toxic and non-conventional pollutants and BCT for conventional pollutants.
2. Numeric –Risk Level 3 dischargers are subject to a pH NAL of 6.5-8.5, and a turbidity NAL of 250 NTU. In addition, Risk Level 3 dischargers are subject to a pH NEL of 6.0-9.0 and a turbidity NEL of 500 NTU.

### B. Good Site Management "Housekeeping"

1. Risk Level 3 dischargers shall implement good site management (i.e., "housekeeping") measures for construction materials that could potentially be a threat to water quality if discharged. At a minimum, Risk Level 3 dischargers shall implement the following good housekeeping measures:
  - a. Conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - b. Cover and berm loose stockpiled construction materials that are not actively being used (i.e. soil, spoils, aggregate, fly-ash, stucco, hydrated lime, etc.).

- c. Store chemicals in watertight containers (with appropriate secondary containment to prevent any spillage or leakage) or in a storage shed (completely enclosed).
  - d. Minimize exposure of construction materials to precipitation. This does not include materials and equipment that are designed to be outdoors and exposed to environmental conditions (i.e. poles, equipment pads, cabinets, conductors, insulators, bricks, etc.).
  - e. Implement BMPs to prevent the off-site tracking of loose construction and landscape materials.
2. Risk Level 3 dischargers shall implement good housekeeping measures for waste management, which, at a minimum, shall consist of the following:
- a. Prevent disposal of any rinse or wash waters or materials on impervious or pervious site surfaces or into the storm drain system.
  - b. Ensure the containment of sanitation facilities (e.g., portable toilets) to prevent discharges of pollutants to the storm water drainage system or receiving water.
  - c. Clean or replace sanitation facilities and inspecting them regularly for leaks and spills.
  - d. Cover waste disposal containers at the end of every business day and during a rain event.
  - e. Prevent discharges from waste disposal containers to the storm water drainage system or receiving water.
  - f. Contain and securely protecting stockpiled waste material from wind and rain at all times unless actively being used.
  - g. Implement procedures that effectively address hazardous and non-hazardous spills.
  - h. Develop a spill response and implementation element of the SWPPP prior to commencement of construction activities. The SWPPP shall require that:
    - i. Equipment and materials for cleanup of spills shall be available on site and that spills and leaks shall be cleaned up immediately and disposed of properly; and

- ii. Appropriate spill response personnel are assigned and trained.
  - i. Ensure the containment of concrete washout areas and other washout areas that may contain additional pollutants so there is no discharge into the underlying soil and onto the surrounding areas.
3. Risk Level 3 dischargers shall implement good housekeeping for vehicle storage and maintenance, which, at a minimum, shall consist of the following:
  - a. Prevent oil, grease, or fuel to leak in to the ground, storm drains or surface waters.
  - b. Place all equipment or vehicles, which are to be fueled, maintained and stored in a designated area fitted with appropriate BMPs.
  - c. Clean leaks immediately and disposing of leaked materials properly.
4. Risk Level 3 dischargers shall implement good housekeeping for landscape materials, which, at a minimum, shall consist of the following:
  - a. Contain stockpiled materials such as mulches and topsoil when they are not actively being used.
  - b. Contain fertilizers and other landscape materials when they are not actively being used.
  - c. Discontinuing the application of any erodible landscape material within 2 days before a forecasted rain event or during periods of precipitation.
  - d. Applying erodible landscape material at quantities and application rates according to manufacture recommendations or based on written specifications by knowledgeable and experienced field personnel.
  - e. Stacking erodible landscape material on pallets and covering or storing such materials when not being used or applied.
5. Risk Level 3 dischargers shall conduct an assessment and create a list of potential pollutant sources and identify any areas of the site where additional BMPs are necessary to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges. This potential pollutant list shall be kept with the SWPPP and shall identify

all non-visible pollutants which are known, or should be known, to occur on the construction site. At a minimum, when developing BMPs, Risk Level 3 dischargers shall do the following:

- a. Consider the quantity, physical characteristics (e.g., liquid, powder, solid), and locations of each potential pollutant source handled, produced, stored, recycled, or disposed of at the site.
  - b. Consider the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water.
  - c. Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas.
  - d. Ensure retention of sampling, visual observation, and inspection records.
  - e. Ensure effectiveness of existing BMPs to reduce or prevent pollutants in storm water discharges and authorized non-storm water discharges.
6. Risk Level 3 dischargers shall implement good housekeeping measures on the construction site to control the air deposition of site materials and from site operations. Such particulates can include, but are not limited to, sediment, nutrients, trash, metals, bacteria, oil and grease and organics.
7. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall document all housekeeping BMPs in the SWPPP and REAP(s) in accordance with the nature and phase of the construction project. Construction phases at traditional land development projects include Grading and Land Development Phase, Streets and Utilities, or Vertical Construction for traditional land development projects.

### C. Non-Storm Water Management

1. Risk Level 3 dischargers shall implement measures to control all non-storm water discharges during construction.
2. Risk Level 3 dischargers shall wash vehicles in such a manner as to prevent non-storm water discharges to surface waters or MS4 drainage systems.

3. Risk Level 3 dischargers shall clean streets in such a manner as to prevent unauthorized non-storm water discharges from reaching surface water or MS4 drainage systems.

#### D. Erosion Control

1. Risk Level 3 dischargers shall implement effective wind erosion control.
2. Risk Level 3 dischargers shall provide effective soil cover for inactive<sup>1</sup> areas and all finished slopes, open space, utility backfill, and completed lots.
3. Dischargers shall limit the use of plastic materials when more sustainable, environmentally friendly alternatives exist. Where plastic materials are deemed necessary, the discharger shall consider the use of plastic materials resistant to solar degradation.

#### E. Sediment Controls

1. Risk Level 3 dischargers shall establish and maintain effective perimeter controls and stabilize all construction entrances and exits to sufficiently control erosion and sediment discharges from the site.
2. On sites where sediment basins are to be used, Risk Level 3 dischargers shall, at minimum, design sediment basins according to the method provided in CASQA's Construction BMP Guidance Handbook.
3. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall implement appropriate erosion control BMPs (runoff control and soil stabilization) in conjunction with sediment control BMPs for areas under active<sup>2</sup> construction.
4. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall apply linear sediment controls along the toe of the slope, face of the slope, and at the grade breaks of exposed slopes to comply with sheet flow lengths<sup>3</sup> in accordance with Table 1.

---

<sup>1</sup> Inactive areas of construction are areas of construction activity that have been disturbed and are not scheduled to be re-disturbed for at least 14 days.

<sup>2</sup> Active areas of construction are areas undergoing land surface disturbance. This includes construction activity during the preliminary stage, mass grading stage, streets and utilities stage and the vertical construction stage

<sup>3</sup> Sheet flow length is the length that shallow, low velocity flow travels across a site.

**Table 1 - Critical Slope/Sheet Flow Length Combinations**

<b>Slope Percentage</b>	<b>Sheet flow length not to exceed</b>
0-25% 20	feet
25-50% 15	feet
Over 50%	10 feet

5. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall ensure that construction activity traffic to and from the project is limited to entrances and exits that employ effective controls to prevent offsite tracking of sediment.
6. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall ensure that all storm drain inlets and perimeter controls, runoff control BMPs, and pollutant controls at entrances and exits (e.g. tire washoff locations) are maintained and protected from activities that reduce their effectiveness.
7. **Additional Risk Level 3 Requirement:** Risk Level 3 dischargers shall inspect on a daily basis all immediate access roads daily. At a minimum daily (when necessary) and prior to any rain event, the discharger shall remove any sediment or other construction activity-related materials that are deposited on the roads (by vacuuming or sweeping).
8. **Additional Risk Level 3 Requirement:** The Regional Water Board may require Risk Level 3 dischargers to implement additional site-specific sediment control requirements if the implementation of the other requirements in this section are not adequately protecting the receiving waters.

#### **F. Run-on and Run-off Controls**

Risk Level 3 dischargers shall effectively manage all run-on, all runoff within the site and all runoff that discharges off the site. Run-on from off site shall be directed away from all disturbed areas or shall collectively be in compliance with the effluent limitations in this General Permit.

#### **G. Inspection, Maintenance and Repair**

1. Risk Level 3 dischargers shall ensure that all inspection, maintenance repair and sampling activities at the project location shall be performed or supervised by a Qualified SWPPP Practitioner (QSP) representing the discharger. The QSP may delegate any or all of these activities to an employee appropriately trained to do the task(s).

2. Risk Level 3 dischargers shall perform weekly inspections and observations, and at least once each 24-hour period during extended storm events, to identify and record BMPs that need maintenance to operate effectively, that have failed, or that could fail to operate as intended. Inspectors shall be the QSP or be trained by the QSP.
3. Upon identifying failures or other shortcomings, as directed by the QSP, Risk Level 3 dischargers shall begin implementing repairs or design changes to BMPs within 72 hours of identification and complete the changes as soon as possible.
4. For each inspection required, Risk Level 3 dischargers shall complete an inspection checklist, using a form provided by the State Water Board or Regional Water Board or in an alternative format.
5. Risk Level 3 dischargers shall ensure that checklists shall remain onsite with the SWPPP and at a minimum, shall include:
  - a. Inspection date and date the inspection report was written.
  - b. Weather information, including presence or absence of precipitation, estimate of beginning of qualifying storm event, duration of event, time elapsed since last storm, and approximate amount of rainfall in inches.
  - c. Site information, including stage of construction, activities completed, and approximate area of the site exposed.
  - d. A description of any BMPs evaluated and any deficiencies noted.
  - e. If the construction site is safely accessible during inclement weather, list the observations of all BMPs: erosion controls, sediment controls, chemical and waste controls, and non-storm water controls. Otherwise, list the results of visual inspections at all relevant outfalls, discharge points, downstream locations and any projected maintenance activities.
  - f. Report the presence of noticeable odors or of any visible sheen on the surface of any discharges.
  - g. Any corrective actions required, including any necessary changes to the SWPPP and the associated implementation dates.
  - h. Photographs taken during the inspection, if any.

- i. Inspector's name, title, and signature.

## H. Rain Event Action Plan

1. **Additional Risk Level 3 Requirement:** The discharger shall ensure a QSP develop a Rain Event Action Plan (REAP) 48 hours prior to any likely precipitation event. A likely precipitation event is any weather pattern that is forecast to have a 50% or greater probability of producing precipitation in the project area. The QSP shall obtain a printed copy of precipitation forecast information from the National Weather Service Forecast Office (e.g., by entering the zip code of the project's location at <http://www.srh.noaa.gov/forecast>).
2. **Additional Risk Level 3 Requirement:** The discharger shall ensure a QSP develop the REAPs for all phases of construction (i.e., Grading and Land Development, Streets and Utilities, Vertical Construction, Final Landscaping and Site Stabilization).
3. **Additional Risk Level 3 Requirement:** The discharger shall ensure a QSP ensure that the REAP include, at a minimum, the following site information:
  - a. Site Address.
  - b. Calculated Risk Level (2 or 3).
  - c. Site Storm Water Manager Information including the name, company, and 24-hour emergency telephone number.
  - d. Erosion and Sediment Control Provider information including the name, company, and 24-hour emergency telephone number.
  - e. Storm Water Sampling Agent information including the name, company, and 24-hour emergency telephone number.
4. **Additional Risk Level 3 Requirement:** The QSP shall include in the REAP, at a minimum, the following project phase information:
  - a. Activities associated with each construction phase.
  - b. Trades active on the construction site during each construction phase.
  - c. Trade contractor information.
  - d. Suggested actions for each project phase.
5. **Additional Risk Level 3 Requirement:** The QSP shall develop additional REAPs for project sites where construction activities are indefinitely halted or postponed (Inactive Construction). At a minimum, Inactive Construction REAPs must include:

- a. Site Address.
  - b. Calculated Risk Level (2 or 3).
  - c. Site Storm Water Manager Information including the name, company, and 24-hour emergency telephone number.
  - d. Erosion and Sediment Control Provider information including the name, company, and 24-hour emergency telephone number.
  - e. Storm Water Sampling Agent information including the name, company, and 24-hour emergency telephone number.
  - f. Trades active on site during Inactive Construction.
  - g. Trade contractor information.
  - h. Suggested actions for inactive construction sites.
6. **Additional Risk Level 3 Requirement:** The discharger shall ensure a QSP begin implementation and make the REAP available onsite no later than 24 hours prior to the likely precipitation event.
7. **Additional Risk Level 3 Requirement:** The discharger shall ensure a QSP maintain onsite a paper copy of each REAP onsite in compliance with the record retention requirements of the Special Provisions in this General Permit.

## I. Risk Level 3 Monitoring and Reporting Requirements

Table 2- Summary of Monitoring Requirements

Risk Level	Visual Inspections				Sample Collection		
	Quarterly Non-storm Water Discharge	Pre-storm Event		Daily Storm BMP	Post Storm	Storm Water Discharge	Receiving Water
		Baseline	REAP				
3	X	X	X	X	X	X	X <sup>4</sup>

### 1. Construction Site Monitoring Program Requirements

- a. Pursuant to Water Code Sections 13383 and 13267, all dischargers subject to this General Permit shall develop and implement a written site-specific Construction Site Monitoring Program (CSMP) in accordance with the requirements of this Section. The CSMP shall include all monitoring procedures and instructions, location maps, forms, and checklists as required in this section. The CSMP shall be developed prior to the commencement of construction activities, and revised as necessary to reflect project revisions. The CSMP shall be a part of the Storm Water Pollution Prevention Plan (SWPPP), included as an appendix or separate SWPPP chapter.
- b. Existing dischargers registered under the State Water Board Order No. 99-08-DWQ shall make and implement necessary revisions to their Monitoring Program to reflect the changes in this General Permit in a timely manner, but no later than July 1, 2010. Existing dischargers shall continue to implement their existing Monitoring Program in compliance with State Water Board Order No. 99-08-DWQ until the necessary revisions are completed according to the schedule above.
- c. When a change of ownership occurs for all or any portion of the construction site prior to completion or final stabilization, the new discharger shall comply with these requirements as of the date the ownership change occurs.

### 2. Objectives

The CSMP shall be developed and implemented to address the following objectives:

<sup>4</sup> When NEL exceeded

- a. To demonstrate that the site is in compliance with the Discharge Prohibitions and applicable Numeric Action Levels (NALs)/Numeric Effluent Limitations (NELs) of this General Permit.
  - b. To determine whether non-visible pollutants are present at the construction site and are causing or contributing to exceedances of water quality objectives.
  - c. To determine whether immediate corrective actions, additional Best Management Practice (BMP) implementation, or SWPPP revisions are necessary to reduce pollutants in storm water discharges and authorized non-storm water discharges.
  - d. To determine whether BMPs included in the SWPPP/Rain Event Action Plan (REAP) are effective in preventing or reducing pollutants in storm water discharges and authorized non-storm water discharges.
- 3. Risk Level 3 – Visual Monitoring (Inspection) Requirements for Qualifying Rain Events**
- a. Risk Level 3 dischargers shall visually observe (inspect) storm water discharges at all discharge locations within two business days (48 hours) after each qualifying rain event.
  - b. Risk Level 3 dischargers shall visually observe (inspect) the discharge of stored or contained storm water that is derived from and discharged subsequent to a qualifying rain event producing precipitation of ½ inch or more at the time of discharge. Stored or contained storm water that will likely discharge after operating hours due to anticipated precipitation shall be observed prior to the discharge during operating hours.
  - c. Risk Level 3 dischargers shall conduct visual observations (inspections) during business hours only.
  - d. Risk Level 3 dischargers shall record the time, date and rain gauge reading of all qualifying rain events.
  - e. Within 2 business days (48 hours) prior to each qualifying rain event, Risk Level 3 dischargers shall visually observe (inspect):
    - i. all storm water drainage areas to identify any spills, leaks, or uncontrolled pollutant sources. If needed, the discharger shall implement appropriate corrective actions.

- ii. all BMPs to identify whether they have been properly implemented in accordance with the SWPPP/REAP. If needed, the discharger shall implement appropriate corrective actions.
  - iii. any storm water storage and containment areas to detect leaks and ensure maintenance of adequate freeboard.
- f. For the visual observations (inspections) described in c.i. and c.iii above, Risk Level 3 dischargers shall observe the presence or absence of floating and suspended materials, a sheen on the surface, discolorations, turbidity, odors, and source(s) of any observed pollutants.
- g. Within two business days (48 hours) after each qualifying rain event, Risk Level 3 dischargers shall conduct post rain event visual observations (inspections) to (1) identify whether BMPs were adequately designed, implemented, and effective, and (2) identify additional BMPs and revise the SWPPP accordingly.
- h. Risk Level 3 dischargers shall maintain on-site records of all visual observations (inspections), personnel performing the observations, observation dates, weather conditions, locations observed, and corrective actions taken in response to the observations.

#### **4. Risk Level 3 – Water Quality Sampling and Analysis**

- a. Risk Level 3 dischargers shall collect storm water grab samples from sampling locations, as defined in Section I.5. The storm water grab sample(s) obtained shall be representative of the flow and characteristics of the discharge.
- b. At minimum, Risk Level 3 dischargers shall collect 3 samples per day of the qualifying event.
- c. Risk Level 3 dischargers shall ensure that the grab samples collected of stored or contained storm water are from discharges subsequent to a qualifying rain event (producing precipitation of ½ inch or more at the time of discharge).

#### Storm Water Effluent Monitoring Requirements

- d. Risk Level 3 dischargers shall analyze their effluent samples for:
  - i. pH and turbidity.

- ii. Any additional parameters for which monitoring is required by the Regional Water Board.
- e. Risk 3 dischargers shall electronically submit all storm event sampling results to the State Water Board no later than 5 days after the conclusion of the storm event.
- f. Risk Level 3 discharger sites that have violated the turbidity daily average NEL shall analyze subsequent effluent samples for all the parameters specified in Section I.4.e, above, and Suspended Sediment Concentration (SSC).

#### Receiving Water Monitoring Requirements

- g. In the event that a Risk Level 3 discharger violates an NEL contained in this General Permit and has a direct discharge into receiving waters, the Risk Level 3 discharger shall subsequently sample receiving waters (RWs) for all parameter(s) required in Section I.4.e above for the duration of coverage under this General Permit.
- h. Risk Level 3 dischargers disturbing 30 acres or more of the landscape and with direct discharges into receiving waters shall conduct or participate in benthic macroinvertebrate bioassessment of RWs prior to commencement of construction activity (See Appendix 3).
- i. Risk Level 3 dischargers shall obtain RW samples in accordance with the Receiving Water sampling location section (Section I.5), below.

#### **5. Risk Level 3 – Storm Water Discharge Water Quality Sampling Locations**

##### Effluent Sampling Locations

- a. Risk Level 3 dischargers shall perform sampling and analysis of storm water discharges to characterize discharges associated with construction activity from the entire project disturbed area.
- b. Risk Level 3 dischargers shall collect effluent samples at all discharge points where storm water is discharged off-site.

- c. Risk Level 3 dischargers shall ensure that storm water discharge collected and observed represent<sup>5</sup> the effluent in each drainage area based on visual observation of the water and upstream conditions.
- d. Risk Level 3 dischargers shall monitor and report site run-on from surrounding areas if there is reason to believe run-on may contribute to an exceedance of NALs or NELs.
- e. Risk Level 3 dischargers who deploy an ATS on their site, or a portion on their site, shall collect ATS effluent samples and measurements from the discharge pipe or another location representative of the nature of the discharge.
- f. Risk Level 3 dischargers shall select analytical test methods from the list provided in Table 3 below.
- g. All storm water sample collection preservation and handling shall be conducted in accordance with Section I.7 "Storm Water Sample Collection and Handling Instructions" below.

#### Receiving Water Sampling Locations

- h. **Upstream/up-gradient RW samples:** Risk Level 3 dischargers shall obtain any required upstream/up-gradient receiving water samples from a representative and accessible location as close as possible and upstream from the effluent discharge point.
- i. **Downstream/down-gradient RW samples:** Risk Level 3 dischargers shall obtain any required downstream/down-gradient receiving water samples from a representative and accessible location as close as possible and downstream from the effluent discharge point.
- j. If two or more discharge locations discharge to the same receiving water, Risk Level 3 dischargers may sample the receiving water at a single upstream and downstream location.

---

<sup>5</sup> For example, if there has been concrete work recently in an area, or drywall scrap is exposed to the rain, a pH sample shall be taken of drainage from the relevant work area. Similarly, if sediment-laden water is flowing through some parts of a silt fence, samples shall be taken of the sediment laden water even if most water flowing through the fence is clear.

## 6. Risk Level 3 – Visual Observation and Sample Collection Exemptions

- a. Risk Level 3 dischargers shall be prepared to collect samples and conduct visual observation (inspections) until the minimum requirements of Sections I.3 and I.4 above are completed. Risk Level 3 dischargers are not required to physically collect samples or conduct visual observation (inspections) under the following conditions:
  - i. During dangerous weather conditions such as flooding and electrical storms.
  - ii. Outside of scheduled site business hours.
- b. If no required samples or visual observation (inspections) are collected due to these exceptions, Risk Level 3 dischargers shall include an explanation in their SWPPP and in the Annual Report documenting why the sampling or visual observation (inspections) were not conducted.

## 7. Risk Level 3 – Storm Water Sample Collection and Handling Instructions

- a. Risk Level 3 dischargers shall refer to Table 3 below for test methods, detection limits, and reporting units.
- b. Risk Level 3 dischargers shall ensure that testing laboratories will receive samples within 48 hours of the physical sampling (unless otherwise required by the laboratory), and shall use only the sample containers provided by the laboratory to collect and store samples.
- c. Risk Level 3 dischargers shall designate and train personnel to collect, maintain, and ship samples in accordance with the Surface Water Ambient Monitoring Program's (SWAMP) 2008 Quality Assurance Program Plan (QAPrP).<sup>6</sup>

---

<sup>6</sup> Additional information regarding SWAMP's QAPrP and QAMP can be found at [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/](http://www.waterboards.ca.gov/water_issues/programs/swamp/).

QAPrP: [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/docs/qapp/swamp\\_qapp\\_master090108a.pdf](http://www.waterboards.ca.gov/water_issues/programs/swamp/docs/qapp/swamp_qapp_master090108a.pdf)

QAMP: [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/qamp.shtml](http://www.waterboards.ca.gov/water_issues/programs/swamp/qamp.shtml)

## 8. Risk Level 3 – Monitoring Methods

- a. Risk Level 3 dischargers shall include a description of the following items in the CSMP:
  - i. Visual observation locations, visual observation procedures, and visual observation follow-up and tracking procedures.
  - ii. Sampling locations, and sample collection and handling procedures. This shall include detailed procedures for sample collection, storage, preservation, and shipping to the testing lab to assure that consistent quality control and quality assurance is maintained. Dischargers shall attach to the monitoring program an example Chain of Custody form used when handling and shipping samples.
  - iii. Identification of the analytical methods and related method detection limits (if applicable) for each parameter required in Section I.4 above.
- b. Risk Level 3 dischargers shall ensure that all sampling and sample preservation are in accordance with the current edition of "Standard Methods for the Examination of Water and Wastewater" (American Public Health Association). All monitoring instruments and equipment (including a discharger's own field instruments for measuring pH and turbidity) should be calibrated and maintained in accordance with manufacturers' specifications to ensure accurate measurements. Risk Level 3 dischargers shall ensure that all laboratory analyses are conducted according to test procedures under 40 CFR Part 136, unless other test procedures have been specified in this General Permit or by the Regional Water Board. With the exception of field analysis conducted by the discharger for turbidity and pH, all analyses should be sent to and conducted at a laboratory certified for such analyses by the State Department of Health Services (SSC exception). Risk Level 3 dischargers shall conduct their own field analysis of pH and may conduct their own field analysis of turbidity if the discharger has sufficient capability (qualified and trained employees, properly calibrated and maintained field instruments, etc.) to adequately perform the field analysis.

## 9. Risk Level 3 – Analytical Methods

- a. Risk Level 3 dischargers shall refer to Table 3 below for test methods, detection limits, and reporting units.

- b. **pH:** Risk Level 3 dischargers shall perform pH analysis on-site with a calibrated pH meter or a pH test kit. Risk Level 3 dischargers shall record pH monitoring results on paper and retain these records in accordance with Section I.14, below.
- c. **Turbidity:** Risk Level 3 dischargers shall perform turbidity analysis using a calibrated turbidity meter (turbidimeter), either on-site or at an accredited lab. Acceptable test methods include Standard Method 2130 or USEPA Method 180.1. The results will be recorded in the site log book in Nephelometric Turbidity Units (NTU).
- d. **Suspended sediment concentration (SSC):** Risk Level 3 dischargers shall perform SSC analysis using ASTM Method D3977-97.
- e. **Bioassessment:** Risk Level 3 dischargers shall perform bioassessment sampling and analysis according to Appendix 3 of this General Permit.

#### 10. Risk Level 3 - Non-Storm Water Discharge Monitoring Requirements

- a. Visual Monitoring Requirements:
  - i. Risk Level 3 dischargers shall visually observe (inspect) each drainage area for the presence of (or indications of prior) unauthorized and authorized non-storm water discharges and their sources.
  - ii. Risk Level 3 dischargers shall conduct one visual observation (inspection) quarterly in each of the following periods: January-March, April-June, July-September, and October-December. Visual observation (inspections) are only required during daylight hours (sunrise to sunset).
  - iii. Risk Level 3 dischargers shall ensure that visual observations (inspections) document the presence or evidence of any non-storm water discharge (authorized or unauthorized), pollutant characteristics (floating and suspended material, sheen, discoloration, turbidity, odor, etc.), and source. Risk Level 3 dischargers shall maintain on-site records indicating the personnel performing the visual observation (inspections), the dates and approximate time each drainage area and non-storm water discharge was observed, and the response taken to eliminate unauthorized non-storm water discharges and to

reduce or prevent pollutants from contacting non-storm water discharges.

- b. Effluent Sampling Locations:
  - i. Risk Level 3 dischargers shall sample effluent at all discharge points where non-storm water and/or authorized non-storm water is discharged off-site.
  - ii. Risk Level 3 dischargers shall send all non-storm water sample analyses to a laboratory certified for such analyses by the State Department of Health Services.
  - iii. Risk Level 3 dischargers shall monitor and report run-on from surrounding areas if there is reason to believe run-on may contribute to an exceedance of NALs or NELs.

#### **11. Risk Level 3 – Non-Visible Pollutant Monitoring Requirements**

- a. Risk Level 3 dischargers shall collect one or more samples during any breach, malfunction, leakage, or spill observed during a visual inspection which could result in the discharge of pollutants to surface waters that would not be visually detectable in storm water.
- b. Risk Level 3 dischargers shall ensure that water samples are large enough to characterize the site conditions.
- c. Risk Level 3 dischargers shall collect samples at all discharge locations that can be safely accessed.
- d. Risk Level 3 dischargers shall collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff.
- e. Risk Level 3 dischargers shall analyze samples for all non-visible pollutant parameters (if applicable) - parameters indicating the presence of pollutants identified in the pollutant source assessment required (Risk Level 3 dischargers shall modify their CSMPs to address these additional parameters in accordance with any updated SWPPP pollutant source assessment).
- f. Risk Level 3 dischargers shall collect a sample of storm water that has not come in contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample) for comparison with the discharge sample.

- g. Risk Level 3 dischargers shall compare the uncontaminated sample to the samples of discharge using field analysis or through laboratory analysis.<sup>7</sup>
- h. Risk Level 3 dischargers shall keep all field /or analytical data in the SWPPP document.

### **12. Risk Level 3 – Watershed Monitoring Option**

Risk Level 3 dischargers who are part of a qualified regional watershed-based monitoring program may be eligible for relief from the requirements in Sections I.5. The Regional Water Board may approve proposals to substitute an acceptable watershed-based monitoring program by determining if the watershed-based monitoring program will provide substantially similar monitoring information in evaluating discharger compliance with the requirements of this General Permit.

### **13. Risk Level 3 – Particle Size Analysis for Project Risk Justification**

Risk Level 3 dischargers justifying an alternative project risk shall report a soil particle size analysis used to determine the RUSLE K-Factor. ASTM D-422 (Standard Test Method for Particle-Size Analysis of Soils), as revised, shall be used to determine the percentages of sand, very fine sand, silt, and clay on the site.

### **14. Risk Level 3 – Records**

Risk Level 3 dischargers shall retain records of all storm water monitoring information and copies of all reports (including Annual Reports) for a period of at least three years. Risk Level 3 dischargers shall retain all records on-site while construction is ongoing. These records include:

- a. The date, place, time of facility inspections, sampling, visual observation (inspections), and/or measurements, including precipitation.
- b. The individual(s) who performed the facility inspections, sampling, visual observation (inspections), and or measurements.
- c. The date and approximate time of analyses.

---

<sup>7</sup> For laboratory analysis, all sampling, sample preservation, and analyses must be conducted according to test procedures under 40 CFR Part 136. Field discharge samples shall be collected and analyzed according to the specifications of the manufacturer of the sampling devices employed.

- d. The individual(s) who performed the analyses.
- e. A summary of all analytical results from the last three years, the method detection limits and reporting units, the analytical techniques or methods used, and the chain of custody forms.
- f. Rain gauge readings from site inspections.
- g. Quality assurance/quality control records and results.
- h. Non-storm water discharge inspections and visual observation (inspections) and storm water discharge visual observation records (see Sections I.3 and I.10 above).
- i. Visual observation and sample collection exception records (see Section I.6 above).
- j. The records of any corrective actions and follow-up activities that resulted from analytical results, visual observation (inspections), or inspections.

#### **15. Risk Level 3 – NAL Exceedance Report**

- a. In the event that any effluent sample exceeds an applicable NAL, Risk Level 3 dischargers shall electronically submit all storm event sampling results to the State Water Board no later than 10 days after the conclusion of the storm event. The Regional Boards have the authority to require the submittal of an NAL Exceedance Report.
- b. Risk Level 3 dischargers shall certify each NAL Exceedance Report in accordance with the Special Provisions for Construction Activity In this General Permit.
- c. Risk Level 3 dischargers shall retain an electronic or paper copy of each NAL Exceedance Report for a minimum of three years after the date the annual report is filed.
- d. Risk Level 3 dischargers shall include in the NAL Exceedance Report:
  - i. The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as “less than the method detection limit”).

- ii. The date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation.
- iii. A description of the current BMPs associated with the effluent sample that exceeded the NAL and the proposed corrective actions taken.

#### 16. Risk Level 3 – NEL Violation Report

- a. Risk Level 3 dischargers shall electronically submit all storm event sampling results to the State Water Board no later than 5 days after the conclusion of the storm event.
- b. In the event that a discharger has violated an applicable NEL, Risk Level 3 dischargers shall submit an NEL Violation Report to the State Water Board within 24 hours after the NEL exceedance has been identified.
- c. Risk Level 3 dischargers shall certify each NEL Violation Report in accordance with the Special Provisions for Construction Activity in this General Permit.
- d. Risk Level 3 dischargers shall retain an electronic or paper copy of each NEL Violation Report for a minimum of three years after the date the annual report is filed.
- e. Risk Level 3 dischargers shall include in the NEL Violation Report:
  - i. The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as “less than the method detection limit”);
  - ii. The date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation; and
  - iii. A Description of the current onsite BMPs, and the proposed corrective actions taken to manage the NEL exceedance.
- f. Compliance Storm Exemption - In the event that an applicable NEL has been exceeded during a storm event equal to or larger than the Compliance Storm Event, Risk level 3 discharger shall report the on-site rain gauge reading and nearby governmental rain gauge readings for verification.

**17. Risk Level 3 – Bioassessment**

- a. Risk Level 3 dischargers with a total project-related ground disturbance exceeding 30 acres shall:
  - i. Conduct bioassessment monitoring, as described in Appendix 3.
  - ii. Include the collection and reporting of specified in stream biological data and physical habitat.
  - iii. Use the bioassessment sample collection and Quality Assurance & Quality Control (QA/QC) protocols developed by the State of California's Surface Water Ambient Monitoring Program (SWAMP).<sup>8</sup>
- b. Risk Level 3 dischargers qualifying for bioassessment, where construction commences out of an index period for the site location shall:
  - i. Receive Regional Board approval for the sampling exception.
  - ii. Conduct bioassessment monitoring, as described in Appendix 3.
  - iii. Include the collection and reporting of specified instream biological data and physical habitat.
  - iv. Use the bioassessment sample collection and Quality Assurance & Quality Control (QA/QC) protocols developed by the State of California's Surface Water Ambient Monitoring Program (SWAMP).

OR

- v. Make a check payable to: Cal State Chico Foundation (SWAMP Bank Account) or San Jose State Foundation (SWAMP Bank Account) and include the WDID# on the check for the amount calculated for the exempted project.
- vi. Send a copy of the check to the Regional Water Board office for the site's region.
- vii. Invest **\$7,500.00 X The number of samples required** into the SWAMP program as compensation (upon regional board approval).

---

<sup>8</sup> [http://www.waterboards.ca.gov/water\\_issues/programs/swamp/](http://www.waterboards.ca.gov/water_issues/programs/swamp/).

**Table 3 – Risk Level 3 Test Methods, Detection Limits, Reporting Units and Applicable NALs/NELs**

Parameter	Test Method / Protocol	Discharge Type	Min. Detection Limit	Reporting Units	Numeric Action Level	Numeric Effluent Limitation
pH	Field test with calibrated portable instrument	Risk Level 3 Discharges	0.2 pH	units	lower NAL = 6.5 upper NAL = 8.5	lower NEL = 6.0 upper NEL = 9.0
Turbidity EPA	0180.1 and/or field test with calibrated portable instrument	Risk Level 3 Discharges other than ATS	1	NTU	250 NTU	500 NTU
		For ATS discharges	1 NTU		N/A	10 NTU for Daily Weighted Average & 20 NTU for Any Single Sample
SSC ASTM	Method D 3977-97 <sup>9</sup>	Risk Level 3 (if NEL exceeded)	5 mg/L		N/A	N/A
Bioassessment	(STE) Level I of (SAFIT), <sup>10</sup> fixed-count of 600 org/sample	Risk Level 3 projects > 30 acres	N/A N/A		N/A	N/A

<sup>9</sup> ASTM, 1999, Standard Test Method for Determining Sediment Concentration in Water Samples: American Society of Testing and Materials, D 3977-97, Vol. 11.02, pp. 389-394.

<sup>10</sup> The current SAFIT STEs (28 November 2006) list requirements for both the Level I and Level II taxonomic effort, and are located at: [http://www.swrcb.ca.gov/swamp/docs/safit/ste\\_list.pdf](http://www.swrcb.ca.gov/swamp/docs/safit/ste_list.pdf). When new editions are published by SAFIT, they will supersede all previous editions. All editions will be posted at the State Water Board's SWAMP website.

## ATTACHMENT F: Active Treatment System (ATS) Requirements

**Table 1 – Numeric Effluent Limitations, Numeric Action Levels, Test Methods, Detection Limits, and Reporting Units**

Parameter	Test Method	Discharge Type	Min. Detection Limit	Units	Numeric Action Level	Numeric Effluent Limitation
Turbidity	EPA 0180.1 and/or field test with a calibrated portable instrument	For ATS discharges	1 NTU		N/A	10 NTU for Daily Flow-Weighted Average & 20 NTU for Any Single Sample

- A.** Dischargers choosing to implement an Active Treatment System (ATS) on their site shall comply with all of the requirements in this Attachment.
- B.** The discharger shall maintain a paper copy of each ATS specification onsite in compliance with the record retention requirements in the Special Provisions of this General Permit.
- C. ATS Design, Operation and Submittals**
1. The ATS shall be designed and approved by a Certified Professional in Erosion and Sediment Control (CPESC), a Certified Professional in Storm Water Quality (CPSWQ); a California registered civil engineer; or any other California registered engineer.
  2. The discharger shall ensure that the ATS is designed in a manner to preclude the accidental discharge of settled floc<sup>1</sup> during floc pumping or related operations.
  3. The discharger shall design outlets to dissipate energy from concentrated flows.
  4. The discharger shall install and operate an ATS by assigning a lead person (or project manager) who has either a minimum of five years construction storm

<sup>1</sup> Floc is defined as a clump of solids formed by the chemical action in ATS systems.

water experience or who is a licensed contractor specifically holding a California Class A Contractors license.<sup>2</sup>

5. The discharger shall prepare an ATS Plan that combines the site-specific data and treatment system information required to safely and efficiently operate an ATS. The ATS Plan shall be electronically submitted to the State Water Board at least 14 days prior to the planned operation of the ATS and a paper copy shall be available onsite during ATS operation. At a minimum, the ATS Plan shall include:
  - a. ATS Operation and Maintenance Manual for All Equipment.
  - b. ATS Monitoring, Sampling & Reporting Plan, including Quality Assurance/Quality Control (QA/QC).
  - c. ATS Health and Safety Plan.
  - d. ATS Spill Prevention Plan.
6. The ATS shall be designed to capture and treat (within a 72-hour period) a volume equivalent to the runoff from a 10-year, 24-hour storm event using a watershed runoff coefficient of 1.0.

#### **D. Treatment – Chemical Coagulation/Flocculation**

1. Jar tests shall be conducted using water samples selected to represent typical site conditions and in accordance with ASTM D2035-08 (2003).
2. The discharger shall conduct, at minimum, six site-specific jar tests (per polymer with one test serving as a control) for each project to determine the proper polymer and dosage levels for their ATS.
3. Single field jar tests may also be conducted during a project if conditions warrant, for example if construction activities disturb changing types of soils, which consequently cause change in storm water and runoff characteristics.

#### **E. Residual Chemical and Toxicity Requirements**

1. The discharger shall utilize a residual chemical test method that has a method detection limit (MDL) of 10% or less than the maximum allowable threshold

---

<sup>2</sup> Business and Professions Code Division 3, Chapter 9, Article 4, Class A Contractor: A general engineering contractor is a contractor whose principal contracting business is in connection with fixed works requiring specialized engineering knowledge and skill. [<http://www.cslb.ca.gov/General-Information/library/licensing-classifications.asp>].

concentration<sup>3</sup> (MATC) for the specific coagulant in use and for the most sensitive species of the chemical used.

2. The discharger shall utilize a residual chemical test method that produces a result within one hour of sampling.
3. The discharger shall have a California State certified laboratory validate the selected residual chemical test. Specifically the lab will review the test protocol, test parameters, and the detection limit of the coagulant. The discharger shall electronically submit this documentation as part of the ATS Plan.
4. If the discharger cannot utilize a residual chemical test method that meets the requirements above, the discharger shall operate the ATS in Batch Treatment<sup>4</sup> mode.
5. A discharger planning to operate in Batch Treatment mode shall perform toxicity testing in accordance with the following:
  - a. The discharger shall initiate acute toxicity testing on effluent samples representing effluent from each batch prior to discharge<sup>5</sup>. All bioassays shall be sent to a laboratory certified by the Department of Health Services (DHS) Environmental Laboratory Accreditation Program (ELAP). The required field of testing number for Whole Effluent Toxicity (WET) testing is E113.<sup>6</sup>
  - b. Acute toxicity tests shall be conducted with the following species and protocols. The methods to be used in the acute toxicity testing shall be those outlined for a 96-hour acute test in "Methods for Measuring the Acute Toxicity of Effluents and Receiving Water to Freshwater and Marine Organisms, USEPA-841-R-02-012" for Fathead minnow, *Pimephales promelas* (fathead minnow). Acute toxicity for *Oncorhynchus mykiss* (Rainbow Trout) may be used as a substitute for testing fathead minnows.
  - c. All toxicity tests shall meet quality assurance criteria and test acceptability criteria in the most recent versions of the EPA test method for WET testing.
  - d. The discharger shall electronically report all acute toxicity testing.

<sup>3</sup> The Maximum Allowable Threshold Concentration (MATC) is the allowable concentration of residual, or dissolved, coagulant/flocculant in effluent. The MATC shall be coagulant/flocculant-specific, and based on toxicity testing conducted by an independent, third-party laboratory. A typical MATC would be:

The MATC is equal to the geometric mean of the NOEC (No Observed Effect Concentration) and LOEC (Lowest Observed Effect Concentration) Acute and Chronic toxicity results for most sensitive species determined for the specific coagulant. The most sensitive species test shall be used to determine the MATC.

<sup>4</sup> Batch Treatment mode is defined as holding or recirculating the treated water in a holding basin or tank(s) until treatment is complete or the basin or storage tank(s) is full.

<sup>5</sup> This requirement only requires that the test be initiated prior to discharge.

<sup>6</sup> [http://www.dhs.ca.gov/ps/ls/elap/pdf/FOT\\_Desc.pdf](http://www.dhs.ca.gov/ps/ls/elap/pdf/FOT_Desc.pdf).

**F. Filtration**

1. The ATS shall include a filtration step between the coagulant treatment train and the effluent discharge. This is commonly provided by sand, bag, or cartridge filters, which are sized to capture suspended material that might pass through the clarifier tanks.
2. Differential pressure measurements shall be taken to monitor filter loading and confirm that the final filter stage is functioning properly.

**G. Residuals Management**

1. Sediment shall be removed from the storage or treatment cells as necessary to ensure that the cells maintain their required water storage (i.e., volume) capability.
2. Handling and disposal of all solids generated during ATS operations shall be done in accordance with all local, state, and federal laws and regulations.

**H. ATS Instrumentation**

1. The ATS shall be equipped with instrumentation that automatically measures and records effluent water quality data and flow rate.
2. The minimum data recorded shall be consistent with the Monitoring and Reporting requirements below, and shall include:
  - a. Influent Turbidity
  - b. Effluent Turbidity
  - c. Influent pH
  - d. Effluent pH
  - e. Residual Chemical
  - f. Effluent Flow rate
  - g. Effluent Flow volume
3. Systems shall be equipped with a data recording system, such as data loggers or webserver-based systems, which records each measurement on a frequency no longer than once every 15 minutes.

4. Cumulative flow volume shall be recorded daily. The data recording system shall have the capacity to record a minimum of seven days continuous data.
5. Instrumentation systems shall be interfaced with system control to provide auto shutoff or recirculation in the event that effluent measurements exceed turbidity or pH.
6. The system shall also assure that upon system upset, power failure, or other catastrophic event, the ATS will default to a recirculation mode or safe shut down.
7. Instrumentation (flow meters, probes, valves, streaming current detectors, controlling computers, etc.) shall be installed and maintained per manufacturer's recommendations, which shall be included in the QA/QC plan.
8. The QA/QC plan shall also specify calibration procedures and frequencies, instrument method detection limit or sensitivity verification, laboratory duplicate procedures, and other pertinent procedures.
9. The instrumentation system shall include a method for controlling coagulant dose, to prevent potential overdosing. Available technologies include flow/turbidity proportional metering, periodic jar testing and metering pump adjustment, and ionic charge measurement controlling the metering pump.

#### **I. ATS Effluent Discharge**

1. ATS effluent shall comply with all provisions and prohibitions in this General Permit, specifically the NELs.
2. NELs for discharges from an ATS:
  - a. Turbidity of all ATS discharges shall be less than 10 NTU for daily flow-weighted average of all samples and 20 NTU for any single sample.
  - b. Residual Chemical shall be < 10% of MATC<sup>7</sup> for the most sensitive species of the chemical used.
3. If an analytical effluent sampling result is outside the range of pH NELs (i.e., is below the lower NEL for pH or exceeds the upper NEL for pH) or exceeds the turbidity NEL (as listed in Table 1), the discharger is in violation of this General

---

<sup>7</sup> The Maximum Allowable Threshold Concentration (MATC) is the allowable concentration of residual, or dissolved, coagulant/flocculant in effluent. The MATC shall be coagulant/flocculant-specific, and based on toxicity testing conducted by an independent, third-party laboratory. The MATC is equal to the geometric mean of the NOEC (No Observed Effect Concentration) and LOEC (Lowest Observed Effect Concentration) Acute and Chronic toxicity results for most sensitive species determined for the specific coagulant. The most sensitive species test shall be used to determine the MATC.

Permit and shall electronically file the results in violation within 24-hours of obtaining the results.

4. If ATS effluent is authorized to discharge into a sanitary sewer system, the discharger shall comply with any pre-treatment requirements applicable for that system. The discharger shall include any specific criteria required by the municipality in the ATS Plan.
5. Compliance Storm Event:

Discharges of storm water from ATS shall comply with applicable NELs (above) unless the storm event causing the discharges is determined after the fact to be equal to or larger than the Compliance Storm Event (expressed in inches of rainfall). The Compliance Storm Event for ATS discharges is the 10 year, 24 hour storm, as determined using these maps:

<http://www.wrcc.dri.edu/pcpnfreq/nca10y24.gif>  
<http://www.wrcc.dri.edu/pcpnfreq/sca10y24.gif>

This exemption is dependent on the submission of rain gauge data verifying the storm event is equal to or larger than the Compliance Storm.

#### **J. Operation and Maintenance Plan**

1. Each Project shall have a site-specific Operation and Maintenance (O&M) Manual covering the procedures required to install, operate and maintain the ATS.<sup>8</sup>
2. The O&M Manual shall only be used in conjunction with appropriate project-specific design specifications that describe the system configuration and operating parameters.
3. The O&M Manual shall have operating manuals for specific pumps, generators, control systems, and other equipment.

#### **K. Sampling and Reporting Quality Assurance/ Quality Check (QA/QC) Plan**

4. A project-specific QA/QC Plan shall be developed for each project. The QA/QC Plan shall include at a minimum:
  - a. Calibration – Calibration methods and frequencies for all system and field instruments shall be specified.
  - b. Method Detection Limits (MDLs) – The methods for determining MDLs shall be specified for each residual coagulant measurement method. Acceptable

<sup>8</sup> The manual is typically in a modular format covering generalized procedures for each component that is utilized in a particular system.

minimum MDLs for each method, specific to individual coagulants, shall be specified.

- c. Laboratory Duplicates – Requirements for monthly laboratory duplicates for residual coagulant analysis shall be specified.

#### **L. Personnel Training**

1. Operators shall have training specific to using an ATS and liquid coagulants for storm water discharges in California.
2. The training shall be in the form of a formal class with a certificate and requirements for testing and certificate renewal.
3. Training shall include a minimum of eight hours classroom and 32 hours field training. The course shall cover the following topics:
  - a. Coagulation Basics –Chemistry and physical processes
  - b. ATS System Design and Operating Principles
  - c. ATS Control Systems
  - d. Coagulant Selection – Jar testing, dose determination, etc.
  - e. Aquatic Safety/Toxicity of Coagulants, proper handling and safety
  - f. Monitoring, Sampling, and Analysis
  - g. Reporting and Recordkeeping
  - h. Emergency Response

#### **M. Active Treatment System (ATS) Monitoring Requirements**

Any discharger who deploys an ATS on their site shall conduct the following:

1. Visual Monitoring
  - a. A designated responsible person shall be on site daily at all times during treatment operations.
  - b. Daily on-site visual monitoring of the system for proper performance shall be conducted and recorded in the project data log.

- i. The log shall include the name and phone number of the person responsible for system operation and monitoring.
- ii. The log shall include documentation of the responsible person's training.

## 2. Operational and Compliance Monitoring

- a. Flow shall be continuously monitored and recorded at not greater than 15-minute intervals for total volume treated and discharged.
- b. Influent and effluent pH must be continuously monitored and recorded at not greater than 15-minute intervals.
- c. Influent and effluent turbidity (expressed in NTU) must be continuously monitored and recorded at not greater than 15-minute intervals.
- d. The type and amount of chemical used for pH adjustment, if any, shall be monitored and recorded.
- e. Dose rate of chemical used in the ATS system (expressed in mg/L) shall be monitored and reported 15-minutes after startup and every 8 hours of operation.
- f. Laboratory duplicates – monthly laboratory duplicates for residual coagulant analysis must be performed and records shall be maintained onsite.
- g. Effluent shall be monitored and recorded for residual chemical/additive levels.
- h. If a residual chemical/additive test does not exist and the ATS is operating in a batch treatment mode of operation refer to the toxicity monitoring requirements below.

## 3. Toxicity Monitoring

A discharger operating in batch treatment mode shall perform toxicity testing in accordance with the following:

- a. The discharger shall initiate acute toxicity testing on effluent samples representing effluent from each batch prior to discharge.<sup>9</sup> All bioassays shall be sent to a laboratory certified by the Department of Health Services (DHS) Environmental Laboratory Accreditation Program (ELAP). The required field of testing number for Whole Effluent Toxicity (WET) testing is E113.<sup>10</sup>

<sup>9</sup> This requirement only requires that the test be initiated prior to discharge.

<sup>10</sup> [http://www.dhs.ca.gov/ps/ls/elap/pdf/FOT\\_Desc.pdf](http://www.dhs.ca.gov/ps/ls/elap/pdf/FOT_Desc.pdf).

- b. Acute toxicity tests shall be conducted with the following species and protocols. The methods to be used in the acute toxicity testing shall be those outlined for a 96-hour acute test in “Methods for Measuring the Acute Toxicity of Effluents and Receiving Water to Freshwater and Marine Organisms, USEPA-841-R-02-012” for Fathead minnow, *Pimephales promelas* or Rainbow trout *Oncorhynchus mykiss* may be used as a substitute for fathead minnow.
- c. All toxicity tests shall meet quality assurance criteria and test acceptability criteria in the most recent versions of the EPA test method for WET testing.<sup>11</sup>

#### 4. Reporting and Recordkeeping

At a minimum, every 30 days a LRP representing the discharger shall access the State Water Boards Storm Water Multi-Application and Report Tracking system (SMARTS) and electronically upload field data from the ATS. Records must be kept for three years after the project is completed .

#### 5. Non-compliance Reporting

- a. Any indications of toxicity or other violations of water quality objectives shall be reported to the appropriate regulatory agency as required by this General Permit.
- b. Upon any measurements that exceed water quality standards, the system operator shall immediately notify his supervisor or other responsible parties, who shall notify the Regional Water Board.
- c. If any monitoring data exceeds any applicable NEL in this General Permit, the discharger shall electronically submit a NEL Violation Report to the State Water Board within 24 hours after the NEL exceedance has been identified.
  - i. ATS dischargers shall certify each NEL Violation Report in accordance with the Special Provisions for Construction Activity in this General Permit.
  - ii. ATS dischargers shall retain an electronic or paper copy of each NEL Violation Report for a minimum of three years after the date the annual report is filed.
  - iii. ATS dischargers shall include in the NEL Violation Report:
    - (1) The analytical method(s), method reporting unit(s), and method detection limit(s) of each analytical parameter (analytical results that are less than the method detection limit shall be reported as “less than the method detection limit”);

<sup>11</sup> <http://www.epa.gov/waterscience/methods/wet/>.

- (2) The date, place, time of sampling, visual observation (inspections), and/or measurements, including precipitation; and
  - (3) A description of the current onsite BMPs, and the proposed corrective actions taken to manage the NEL exceedance.
- iv. Compliance Storm Exemption - In the event that an applicable NEL has been exceeded during a storm event equal to or larger than the Compliance Storm Event, ATS dischargers shall report the on-site rain gauge reading and nearby governmental rain gauge readings for verification.

# Risk Determination Worksheet

**Step**

- 1** Determine Sediment Risk via one of the options listed:
- [1. GIS Map Method - EPA Rainfall Erosivity Calculator & GIS map](#)
  - [2. Individual Method - EPA Rainfall Erosivity Calculator & Individual Data](#)

- Step 2** Determine Receiving Water Risk via one of the options listed:


- [1. GIS map of Sediment Sensitive Watersheds provided \(in development\)](#)
- [2. List of Sediment Sensitive Watersheds provided](#)

**Step**

- 3** [Determine Combined Risk Level](#)

Sediment Risk Factor Worksheet		Entry
<b>A) R Factor</b>		
<p>Analyses of data indicated that when factors other than rainfall are held constant, soil loss is directly proportional to a rainfall factor composed of total storm kinetic energy (E) times the maximum 30-min intensity (I30) (Wischmeier and Smith, 1958). The numerical value of R is the average annual sum of EI30 for storm events during a rainfall record of at least 22 years. "Isoerodent" maps were developed based on R values calculated for more than 1000 locations in the Western U.S. Refer to the link below to determine the R factor for the project site.</p> <p><a href="http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm">http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm</a></p>		
R Factor Value		0
<b>B) K Factor (weighted average, by area, for all site soils)</b>		
<p>The soil-erodibility factor K represents: (1) susceptibility of soil or surface material to erosion, (2) transportability of the sediment, and (3) the amount and rate of runoff given a particular rainfall input, as measured under a standard condition. Fine-textured soils that are high in clay have low K values (about 0.05 to 0.15) because the particles are resistant to detachment. Coarse-textured soils, such as sandy soils, also have low K values (about 0.05 to 0.2) because of high infiltration resulting in low runoff even though these particles are easily detached. Medium-textured soils, such as a silt loam, have moderate K values (about 0.25 to 0.45) because they are moderately susceptible to particle detachment and they produce runoff at moderate rates. Soils having a high silt content are especially susceptible to erosion and have high K values, which can exceed 0.45 and can be as large as 0.65. Silt-size particles are easily detached and tend to crust, producing high rates and large volumes of runoff. Use Site-specific data must be submitted.</p> <p><a href="#">Site-specific K factor guidance</a></p>		
K Factor Value		0
<b>C) LS Factor (weighted average, by area, for all slopes)</b>		
<p>The effect of topography on erosion is accounted for by the LS factor, which combines the effects of a hillslope-length factor, L, and a hillslope-gradient factor, S. Generally speaking, as hillslope length and/or hillslope gradient increase, soil loss increases. As hillslope length increases, total soil loss and soil loss per unit area increase due to the progressive accumulation of runoff in the downslope direction. As the hillslope gradient increases, the velocity and erosivity of runoff increases. Use the LS table located in separate tab of this spreadsheet to determine LS factors. Estimate the weighted LS for the site prior to construction.</p> <p><a href="#">LS Table</a></p>		
LS Factor Value		0
Watershed Erosion Estimate (=R <sub>x</sub> K <sub>x</sub> LS) in tons/acre		0
<b>Site Sediment Risk Factor</b> Low Sediment Risk: < 15 tons/acre Medium Sediment Risk: >=15 and <75 tons/acre High Sediment Risk: >= 75 tons/acre		Low

For the GIS Map Method, the R factor for the project is calculated using the online calculator at (see cell to right). The product of K and LS are shown on the figure below. To determine soil loss in tons per acre, multiply the R factor times the value for K times LS from the map.  
<http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm>

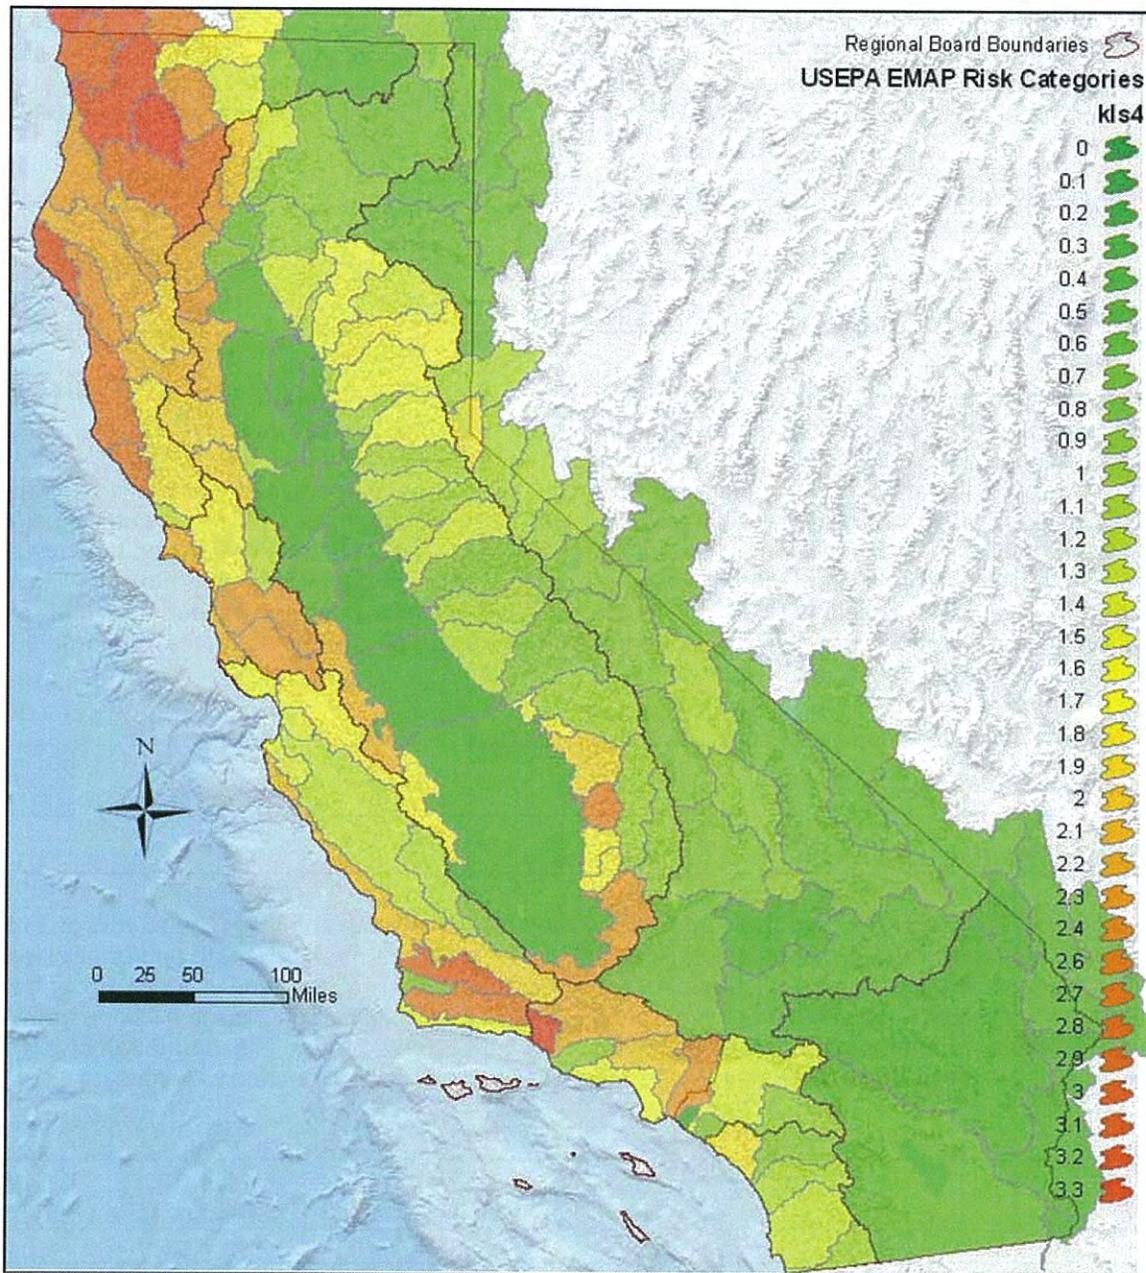

State Water Resources Control Board, January 15, 2008

Receiving Water (RW) Risk Factor Worksheet	Entry	Score
<b>A. Watershed Characteristics</b>	yes/no	
A.1. Does the disturbed area discharge (either directly or indirectly) to a <b>303(d)-listed waterbody impaired by sediment</b> ? (For help with impaired waterbodies please check the attached worksheet or visit the link below) or has a <b>USEPA approved TMDL implementation plan for sediment</b> ?	<b>Yes</b>	<b>High</b>
<a href="#">2006 Approved Sediment-impaired WBs Worksheet</a>		
<a href="http://www.waterboards.ca.gov/water_issues/programs/tmdl/303d_lists2006_epa.shtml">http://www.waterboards.ca.gov/water_issues/programs/tmdl/303d_lists2006_epa.shtml</a>		
<b>OR</b>		
A.2. Does the disturbed area discharge to a waterbody with designated beneficial uses of SPAWN & COLD & MIGRATORY?		
<a href="http://www.ice.ucdavis.edu/geowbs/asp/wbquse.asp">http://www.ice.ucdavis.edu/geowbs/asp/wbquse.asp</a>		

		Sediment Risk		
		Low	Medium	High
Receiving Water Risk	Low	Level 1	Level 2	
	High	Level 2		Level 3


Project Sediment Risk: **Low**

Project RW Risk: **High**

Project Combined Risk: **Level 2**

### Soil Erodibility Factor (K)

The K factor can be determined by using the nomograph method, which requires that a particle size analysis (ASTM D-422) be done to determine the percentages of sand, very fine sand, silt and clay. Use the figure below to determine appropriate K value.

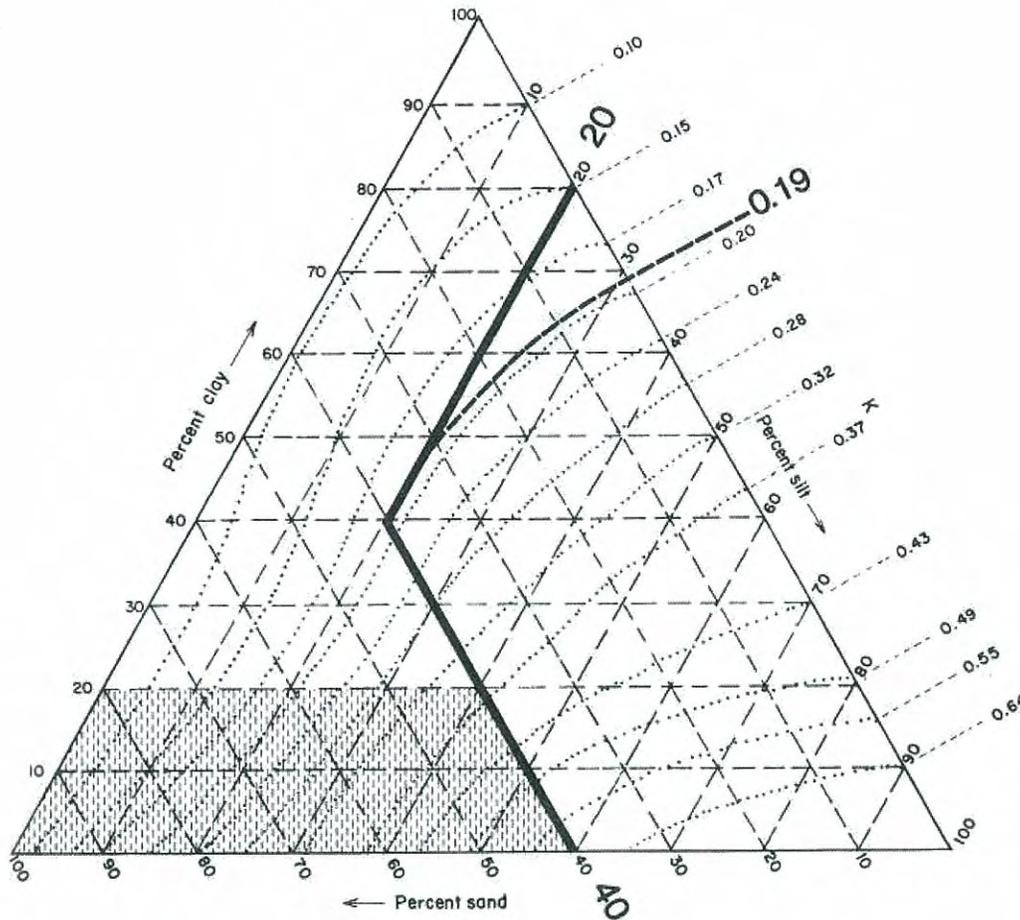

Erickson triangular nomograph used to estimate soil erodibility (K) factor.

The figure above is the USDA nomograph used to determine the K factor for a soil, based on its texture (% silt plus very fine sand, % sand, % organic matter, soil structure, and permeability).

*Nomograph from Erickson 1977 as referenced in Goldman et. al., 1986.*

Sheet Flow Length (ft)	Average Watershed Slope (%)													
	0.2	0.5	1.0	2.0	3.0	4.0	5.0	6.0	8.0	10.0	12.0	14.0	16.0	20.0
<3	0.05	0.07	0.09	0.13	0.17	0.20	0.23	0.26	0.32	0.35	0.36	0.38	0.39	0.41
6	0.05	0.07	0.09	0.13	0.17	0.20	0.23	0.26	0.32	0.37	0.41	0.45	0.49	0.56
9	0.05	0.07	0.09	0.13	0.17	0.20	0.23	0.26	0.32	0.38	0.45	0.51	0.56	0.67
12	0.05	0.07	0.09	0.13	0.17	0.20	0.23	0.26	0.32	0.39	0.47	0.55	0.62	0.76
15	0.05	0.07	0.09	0.13	0.17	0.20	0.23	0.26	0.32	0.40	0.49	0.58	0.67	0.84
25	0.05	0.07	0.10	0.16	0.21	0.26	0.31	0.36	0.45	0.57	0.71	0.85	0.98	1.24
50	0.05	0.08	0.13	0.21	0.30	0.38	0.46	0.54	0.70	0.91	1.15	1.40	1.64	2.10
75	0.05	0.08	0.14	0.25	0.36	0.47	0.58	0.69	0.91	1.20	1.54	1.87	2.21	2.86
100	0.05	0.09	0.15	0.28	0.41	0.55	0.68	0.82	1.10	1.46	1.88	2.31	2.73	3.57
150	0.05	0.09	0.17	0.33	0.50	0.68	0.86	1.05	1.43	1.92	2.51	3.09	3.68	4.85
200	0.06	0.10	0.18	0.37	0.57	0.79	1.02	1.25	1.72	2.34	3.07	3.81	4.56	6.04
250	0.06	0.10	0.19	0.40	0.64	0.89	1.16	1.43	1.99	2.72	3.60	4.48	5.37	7.16
300	0.06	0.10	0.20	0.43	0.69	0.98	1.28	1.60	2.24	3.09	4.09	5.11	6.15	8.23
400	0.06	0.11	0.22	0.48	0.80	1.14	1.51	1.90	2.70	3.75	5.01	6.30	7.60	10.24
600	0.06	0.12	0.24	0.56	0.96	1.42	1.91	2.43	3.52	4.95	6.67	8.45	10.26	13.94
800	0.06	0.12	0.26	0.63	1.10	1.65	2.25	2.89	4.24	6.03	8.17	10.40	12.69	17.35
1000	0.06	0.13	0.27	0.69	1.23	1.86	2.55	3.30	4.91	7.02	9.57	12.23	14.96	20.57

LS Factors for Construction Sites. *Table from Renard et. al., 1997.*

NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	1510	Range Grazing-Riparian	2019	Water Quality Attainment strategy is attempting to increase voluntary measures for attainment of standards & objectives, as was done in the Estero de San Antoni		
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	7000	Hydromodification	2019	Water Quality Attainment Strategy, adopted by NCRWQCB in Dec. 97.		
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	Water Quality Attainment strategy is attempting to increase voluntary measures for attainment of standards & objectives, as was done in the Estero de San Antoni		
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	Water Quality Attainment strategy is attempting to increase voluntary measures for attainment of standards & objectives, as was done in the Estero de San Antoni		
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Water Quality Attainment Strategy, adopted by NCRWQCB in Dec. 97.		
E	Estuaries	Bodega HU, Estero Americano HA, estuary	11530012	199 A	Acres	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	Water Quality Attainment Strategy, adopted by NCRWQCB in Dec. 97.		
R	Rivers/Streams	Eel River HU, Lower Eel River HA, Eel River Delta	11110000	426 M	Miles	1100	Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2019			
R	Rivers/Streams	Eel River HU, Lower Eel River HA, Eel River Delta	11110000	426 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019			
R	Rivers/Streams	Eel River HU, Lower Eel River HA, Eel River Delta	11110000	426 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	1510	Range Grazing-Riparian	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	1520	Range Grazing-Upland	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	2300	Harvesting, Restoration, Residue Management	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	3000	Logging Road Construction/Maintenance	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	3200	Construction/Land Development	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	7000	Land Development	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	7550	Hydromodification	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	7600	Habitat Modification	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	7700	Removal of Riparian Vegetation	2004			
R	Rivers/Streams	Eel River HU, Middle Main HF	11140000	674 M	Miles	1100	Sedimentation/Siltation	7820	Streambank Modification/Destabilization	2004			
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	1935	Erosion/Siltation	2004			
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	2000	Agriculture-grazing	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	2100	Silviculture	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	2300	Harvesting, Restoration, Residue Management	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	2300	Logging Road Construction/Maintenance	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	2400	Silvicultural Point Sources	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eel River HU, Upper Main HA (includes Tomk Creek)	11160000	1141 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	USEPA will develop a TMDL for Eel River, Upper Main Fork.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	2100	Harvesting, Restoration, Residue Management	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	2300	Logging Road Construction/Maintenance	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Elk River	11000000	88 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	The Eureka Plain HU, Elk River, includes the following Calwater Planning Watersheds (PWS): 110.00021, 110.00030, 110.00032, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	2100	Harvesting, Restoration, Residue Management	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	2300	Logging Road Construction/Maintenance	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00042. Sedimentation, sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding due to see NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		

NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00044, and 110.00048 threat of sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding d damage. NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00044, and 110.00048 threat of sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding d damage. NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00048 threat of sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding d damage. NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00048 threat of sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding d damage. NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Eureka Plain HU, Freshwater Creek	11000000	84 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	The Eureka Plain HU, Freshwater Creek, includes the following Calwater Planning Watersheds (PWS): 110.00011, 110.00012, 110.00014, 110.00040, and 110.00048 threat of sedimentation, impaired irrigation water quality, impaired domestic supply water quality, impaired spawning habitat, increased rate and depth of flooding d damage. NCRWQCB and California Department of forestry staff are involved in ongoing efforts to attain adherence to Forest Practice Rules.		
R	Rivers/Streams	Klamath River HU, Lower HA, Klamath Glen HSA	10511000	609 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown	2019	If this listing is determined to be on tribal lands, USEPA should place this water body and pollutant on the section 303d list for the tribal lands. It is not the State W this listing affect other actions related to decommissioning and removal of dams on the Klamath River		
R	Rivers/Streams	Mad River HU, Mad River	10900000	654 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	USEPA will develop TMDL for the Mad River. Sediment TMDLS will be developed for the area tributary to and including: (1) the Mad River (North Fork), (2) the m (3) the Mad River (Middle).		
R	Rivers/Streams	Mad River HU, Mad River	10900000	654 M	Miles	1100	Sedimentation/Siltation	5000	Resource Extraction	2019	USEPA will develop TMDL for the Mad River. Sediment TMDLS will be developed for the area tributary to and including: (1) the Mad River (North Fork), (2) the m (3) the Mad River (Middle).		
R	Rivers/Streams	Mad River HU, Mad River	10900000	654 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	USEPA will develop TMDL for the Mad River. Sediment TMDLS will be developed for the area tributary to and including: (1) the Mad River (North Fork), (2) the m (3) the Mad River (Middle).		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Austr Creek HSA	11412000	81 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Austr Creek HSA	11412000	81 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Austr Creek HSA	11412000	81 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Austr Creek HSA	11412000	81 M	Miles	1100	Sedimentation/Siltation	7300	Dam Construction	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Austr Creek HSA	11412000	81 M	Miles	1100	Sedimentation/Siltation	7400	Flow Regulation/Modification	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	1200	Irrigated Crop Production	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	1300	Specialty Crop Production	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	1915	Agriculture-storm runoff	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	1935	Agriculture-grazing	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	3200	Land Development	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7000	Hydromodification	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7100	Channelization	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7300	Dam Construction	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7350	Upstream Impoundment	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7400	Flow Regulation/Modification	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7550	Habitat Modification	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7800	Drainage/Filling Of Wetlands	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7810	Channel Erosion	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Lower Russian River HA, Guerneville HSA	11411000	195 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Middle Russian River HA, Big Sulphur Creek HSA	11426000	85 M	Miles	1100	Sedimentation/Siltation	3210	Geothermal Development	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Middle Russian River HA, Big Sulphur Creek HSA	11426000	85 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		
R	Rivers/Streams	Russian River HU, Middle Russian River HA, Big Sulphur Creek HSA	11426000	85 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	Sediment impacts in Russian River tributaries prompted listing entire Russian River watershed for sediment.		



NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Mark West Creek HSA	11423000	99 M	Miles	1100		Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Mark West Creek HSA	11423000	99 M	Miles	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Mark West Creek HSA	11423000	99 M	Miles	1100		Sedimentation/Siltation	7800	Drainage/Filling Of Wetlands	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Mark West Creek HSA	11423000	99 M	Miles	1100		Sedimentation/Siltation	7810	Channel Erosion	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	4300	Other Urban Runoff	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	4500	Highway/Road/Bridge Runoff	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7000	Hydromodification	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7100	Channelization	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7800	Drainage/Filling Of Wetlands	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7810	Channel Erosion	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	8050	Erosion From Derelict Land	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	8300	Highway Maintenance and Runoff	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
.t	R	Rivers/Streams	Laguna de Santa Rosa	11421000	96 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
.t	R	Rivers/Streams	San Vicente Creek	30411023	9.11953 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2019	Entire Russian River watershed (including Laguna de Santa Rosa) is listed for sedimentation.
.t	R	Rivers/Streams	Santa Ynez River (below city of Lompoc to Ocean)	31410040	3.8 M	Miles	1100		Sedimentation/Siltation	1000	Agriculture	2019	
.t	R	Rivers/Streams	Santa Ynez River (below city of Lompoc to Ocean)	31410040	3.8 M	Miles	1100		Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2019	
.t	R	Rivers/Streams	Santa Ynez River (below city of Lompoc to Ocean)	31410040	3.8 M	Miles	1100		Sedimentation/Siltation	5000	Resource Extraction	2019	
.t	R	Rivers/Streams	Santa Ynez River (Cachuma Lake to below city c Lompoc)	31440050	43 M	Miles	1100		Sedimentation/Siltation	1000	Agriculture	2019	
.t	R	Rivers/Streams	Santa Ynez River (Cachuma Lake to below city c Lompoc)	31440050	43 M	Miles	1100		Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2019	
.t	R	Rivers/Streams	Santa Ynez River (Cachuma Lake to below city c Lompoc)	31440050	43 M	Miles	1100		Sedimentation/Siltation	5000	Resource Extraction	2019	
.t	R	Rivers/Streams	Shuman Canyon Creek	31300041	8.5496 M	Miles	1100		Sedimentation/Siltation	9000	Source Unknown	2019	
.t	R	Rivers/Streams	Valencia Creek	30413023	6.19 M	Miles	1100		Sedimentation/Siltation	1000	Agriculture	2008	
.t	R	Rivers/Streams	Valencia Creek	30413023	6.19 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2008	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	1000	Agriculture	2019	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2019	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	3110	Road Construction	2019	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)	2019	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	7620	Erosion/Siltation	2019	
.t	R	Rivers/Streams	Zayante Creek	30412040	9.20875 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2019	
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Mark West Creek HSA	11423000	99 M	Miles	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1000	Agriculture	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1100	Nonirrigated Crop Production	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1200	Irrigated Crop Production	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1300	Specialty Crop Production	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1400	Pasture Grazing-Riparian and/or Upland	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1510	Range Grazing-Riparian	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1520	Range Grazing-Upland	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	1940	Dairies	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	3200	Land Development	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	4100	Urban Runoff--Non-industrial Permitted	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	4300	Other Urban Runoff	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.
R	Rivers/Streams		Russian River HU, Middle Russian River HA, Santa Rosa Creek	11422000	87 M	Miles	1100		Sedimentation/Siltation	4501	Surface Runoff	2019	Entire Russian River watershed (including Santa Rosa Creek) is listed for sedimentation.



NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Coyote Valley HSA	11432000	171 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Forsythe Creek HSA	11433000	122 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Forsythe Creek HSA	11433000	122 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	5000	Resource Extraction	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7550	Habitat Modification	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7600	Removal of Riparian Vegetation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7800	Drainage/Filling Of Wetlands	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7810	Channel Erosion	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	8300	Highway Maintenance and Runoff	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
R	Rivers/Streams	Russian River HU, Upper Russian River HA, Ukiah HSA	11431000	460 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources	2019	Russian River Watershed tributary sediment impairments led to listing of entire watershed for sediment.		
Bay	Bays and Harbors	Tomes Bay	20114033	8545.46 A	Acres	1100	Sedimentation/Siltation	1000	Agriculture	2008	TMDL will be developed as part of ongoing watershed management effort. Tributary streams, Lagunitas Creek and Walker Creek, must be managed first. Additional assessment needed.		
Bay	Bays and Harbors	Tomes Bay	20114033	8545.46 A	Acres	1100	Sedimentation/Siltation	7350	Upstream Impoundment	2008	TMDL will be developed as part of ongoing watershed management effort. Tributary streams, Lagunitas Creek and Walker Creek, must be managed first. Additional assessment needed.		
Bay	Rivers/Streams	Butano Creek	20240031	3,627.74 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	Impairment to steelhead habita		
Bay	Rivers/Streams	Lagunitas Creek	20113020	16.75 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2009	Tributary to Tomales Bay. TMDLs will be developed as part of evolving watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Lagunitas Creek	20113020	16.75 M	Miles	1100	Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2009	Tributary to Tomales Bay. TMDLs will be developed as part of evolving watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Napa River	20650010	65.33 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2006	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Napa River	20650010	65.33 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2006	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Napa River	20650010	65.33 M	Miles	1100	Sedimentation/Siltation	2000	Land Development	2006	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Napa River	20650010	65.33 M	Miles	1100	Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2006	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Pescadero Creek	20240013	26.03 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019	If California Department of Fish and Game and the National Marine Fisheries Service find that for this water body fish populations are not impacted, the State Water removing this water body and pollutant from the list.		
Bay	Rivers/Streams	Petaluma River	20630020	21,566 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2019	Impairment to steelhead habita		
Bay	Rivers/Streams	Petaluma River	20630020	21,566 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Petaluma River	20630020	21,566 M	Miles	1100	Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2019	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	San Francisco Creek	20550040	12.05 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2008	Impairment to steelhead habita		
Bay	Rivers/Streams	San Gregorio Creek	20230014	11.14 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2008	Impairment to steelhead habita		
Bay	Rivers/Streams	Sonoma Creek	20640050	30.23 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2008	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Sonoma Creek	20640050	30.23 M	Miles	1100	Sedimentation/Siltation	3000	Construction/Land Development	2008	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Sonoma Creek	20640050	30.23 M	Miles	1100	Sedimentation/Siltation	3200	Land Development	2008	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Sonoma Creek	20640050	30.23 M	Miles	1100	Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2008	TMDL will be developed as part of ongoing watershed management effort. Additional monitoring and assessment nee		
Bay	Rivers/Streams	Walker Creek	20112013	15,835.2 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture	2009	Tributary to Tomales Bay. TMDLs will be developed as part of evolving watershed management effort. Additional monitoring and assessment nee		
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	1000	Agriculture	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	1200	Irrigated Crop Production	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	1915	Agriculture-storm runoff	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	7000	Hydromodification	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	7200	Dredging	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	7810	Channel Erosion	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019			
B	Bays and Harbors	Moss Landing Harbor	30600014	79,272.6 A	Acres	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019			
E	Estuaries	Elkhorn Slough	30600014	2033.73 A	Acres	1100	Sedimentation/Siltation	1000	Agriculture	2015			
E	Estuaries	Elkhorn Slough	30600014	2033.73 A	Acres	1100	Sedimentation/Siltation	1200	Irrigated Crop Production	2015			
E	Estuaries	Elkhorn Slough	30600014	2033.73 A	Acres	1100	Sedimentation/Siltation	1915	Agriculture-storm runoff	2015			
E	Estuaries	Elkhorn Slough	30600014	2033.73 A	Acres	1100	Sedimentation/Siltation	7810	Channel Erosion	2015			
E	Estuaries	Elkhorn Slough	30600014	2033.73 A	Acres	1100	Sedimentation/Siltation	9100	Nonpoint Source	2015			
E	Estuaries	Moro Cojo Slough	30913011	62,494.9 A	Acres	1100	Sedimentation/Siltation	1000	Agriculture	2019			
E	Estuaries	Moro Cojo Slough	30913011	62,494.9 A	Acres	1100	Sedimentation/Siltation	1200	Irrigated Crop Production	2019			
E	Estuaries	Moro Cojo Slough	30913011	62,494.9 A	Acres	1100	Sedimentation/Siltation	1915	Agriculture-storm runoff	2019			
E	Estuaries	Moro Cojo Slough	30913011	62,494.9 A	Acres	1100	Sedimentation/Siltation	3000	Construction/Land Development	2019			
E	Estuaries	Moro Cojo Slough	30913011	62,494.9 A	Acres	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019			
E	Estuaries	Soquel Lagor	30413014	1,158.73 A	Acres	1100	Sedimentation/Siltation	3000	Construction/Land Development	2011			
R	Rivers/Streams	Aptos Creek	30413023	8,405.89 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)	2008			
R	Rivers/Streams	Aptos Creek	30413023	8,405.89 M	Miles	1100	Sedimentation/Siltation	7810	Channel Erosion	2008			
R	Rivers/Streams	Bean Creek	30412041	8,907.07 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction	2019			
R	Rivers/Streams	Bean Creek	30412041	8,907.07 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)	2019			
R	Rivers/Streams	Bean Creek	30412041	8,907.07 M	Miles	1100	Sedimentation/Siltation	5000	Resource Extraction	2019			
R	Rivers/Streams	Bean Creek	30412041	8,907.07 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation	2019			
R	Rivers/Streams	Bean Creek	30412041	8,907.07 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019			
R	Rivers/Streams	Bear Creek(Santa Cruz County)	30412030	6,315.31 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019			
R	Rivers/Streams	Bear Creek(Santa Cruz County)	30412030	6,315.31 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction	2019			
R	Rivers/Streams	Bear Creek(Santa Cruz County)	30412030	6,315.31 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)	2019			
R	Rivers/Streams	Bear Creek(Santa Cruz County)	30412030	6,315.31 M	Miles	1100	Sedimentation/Siltation	9100	Erosion/Siltation	2019			
R	Rivers/Streams	Bear Creek(Santa Cruz County)	30412030	6,315.31 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019			
R	Rivers/Streams	Boulder Creek	30412020	7,559.58 M	Miles	1100	Sedimentation/Siltation	1300	Specialty Crop Production	2019			
R	Rivers/Streams	Boulder Creek	30412020	7,559.58 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019			

NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
t	R	Rivers/Streams	Boulder Creek	30412020	7.55958 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Boulder Creek	30412020	7.55958 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)		2019	
t	R	Rivers/Streams	Boulder Creek	30412020	7.55958 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Boulder Creek	30412020	7.55958 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Brancoforte Creek	30412051	5.78 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture		2019	
t	R	Rivers/Streams	Brancoforte Creek	30412051	5.78 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Brancoforte Creek	30412051	5.78 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Casmalia Canyon Creek	31300040	4.96262 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
t	R	Rivers/Streams	Fall Creek	30412022	5.07242 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Fall Creek	30412022	5.07242 M	Miles	1100	Sedimentation/Siltation	7550	Habitat Modification		2019	
t	R	Rivers/Streams	Fall Creek	30412022	5.07242 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Fall Creek	30412022	5.07242 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Fall Creek	30412021	4.36837 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture		2019	
t	R	Rivers/Streams	Kings Creek	30412011	4.36837 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Kings Creek	30412011	4.36837 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)		2019	
t	R	Rivers/Streams	Kings Creek	30412011	4.36837 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Kings Creek	30412011	4.36837 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Love Creek	30412021	3.78816 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Mountain Charlie Gulch	30412040	3.92844 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture		2019	
t	R	Rivers/Streams	Mountain Charlie Gulch	30412040	3.92844 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Mountain Charlie Gulch	30412040	3.92844 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Mountain Charlie Gulch	30412040	3.92844 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	3110	Road Construction		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	3215	Disturbed Sites (Land Develop.)		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	7810	Channel Erosion		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	7820	Erosion/Siltation		2019	
t	R	Rivers/Streams	Newell Creek (Upper	30412031	3.50199 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2019	
t	R	Rivers/Streams	Las Virgenes Creek	40422010	11.62 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
t	R	Rivers/Streams	Malibu Creek	40421000	10.85 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
R	Rivers/Streams	Medea Creek Reach 1 (Lake to Confl. with Lindero Rd	40424000		2.57 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
R	Rivers/Streams	Calleguas Creek Reach 2 (estuary to Potrero Rd											
R	Rivers/Streams	Calleguas Creek Reaches 1 and 2 on 1998	40312000		4.31213 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 2 (estuary to Potrero Rd											
R	Rivers/Streams	Calleguas Creek Reaches 1 and 2 on 1998	40312000		4.31213 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 3 (Potrero Road upstream											
R	Rivers/Streams	to confluence with Conejo Creek on 1998 303d list)	40312000		3.46697 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 3 (Potrero Road upstream											
R	Rivers/Streams	to confluence with Conejo Creek on 1998 303d list)	40312000		3.46697 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 4 (was Revolon Slough											
R	Rivers/Streams	Main Branch: Mugu Lagoon to Central Avenue on											
R	Rivers/Streams	1998 303d list)	40311000		7.18751 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 4 (was Revolon Slough											
R	Rivers/Streams	Main Branch: Mugu Lagoon to Central Avenue on											
R	Rivers/Streams	1998 303d list)	40311000		7.18751 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 5 (was Beardsley Channe											
R	Rivers/Streams	on 1998 303d list)	40311000		4.34088 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 5 (was Beardsley Channe											
R	Rivers/Streams	on 1998 303d list)	40311000		4.34088 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 6 ( was Arroyo Las Posa:											
R	Rivers/Streams	Reaches 1 and 2 on 1998 303d list)	40362000		15.2966 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 6 ( was Arroyo Las Posa:											
R	Rivers/Streams	Reaches 1 and 2 on 1998 303d list)	40362000		15.2966 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 7 ( was Arroyo Simi											
R	Rivers/Streams	Reaches 1 and 2 on 1998 303d list)	40367000		13.9129 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 7 ( was Arroyo Simi											
R	Rivers/Streams	Reaches 1 and 2 on 1998 303d list)	40367000		13.9129 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 8 ( was Tapo Canyon											
R	Rivers/Streams	Reach 1)	40366000		7.18869 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 11 (Arroyo Santa Rosa											
R	Rivers/Streams	was part of Conejo Creek Reach 3 on 1998 303d											
R	Rivers/Streams	list)	40365000		8.68888 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Calleguas Creek Reach 11 (Arroyo Santa Rosa											
R	Rivers/Streams	was part of Conejo Creek Reach 3 on 1998 303d											
R	Rivers/Streams	list)	40365000		8.68888 M	Miles	1100	Sedimentation/Siltation	8600	Natural Sources		2005	For 2006, sedimentation/siltation was moved by USEPA from the being addressed list back to the 303(d) list pending completion and USEPA approval of a TMDL
R	Rivers/Streams	Medea Creek Reach 2 (Abv Confl. with Linderc											
R	Rivers/Streams	Triunfo Canyon Creek Reach 1	40423000		5.41 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
R	Rivers/Streams	Triunfo Canyon Creek Reach 1	40424000		2.51 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
R	Rivers/Streams	Triunfo Canyon Creek Reach 2	40424000		3.32 M	Miles	1100	Sedimentation/Siltation	9000	Source Unknown		2019	
y	R	Rivers/Streams	Fall River (Pit)	52641031	8.61219 M	Miles	1100	Sedimentation/Siltation	2105	Historical Land Management Activities		2016	The sedimentation is accumulated sand size sediment in the upper Fall River. The historic land management activities include logging, grazing, channelization, ro
y	R	Rivers/Streams	Humbug Creek	51732030	2.20272 M	Miles	1100	Sedimentation/Siltation	5000	Resource Extraction		2012	All resource extraction sources are abandoned mine
y	R	Rivers/Streams	Panoche Creek (Silver Creek to Belmont Avenue)	55112000	17.6357 M	Miles	1100	Sedimentation/Siltation	1000	Agriculture		2007	
y	R	Rivers/Streams	Panoche Creek (Silver Creek to Belmont Avenue)	55112000	17.6357 M	Miles	1100	Sedimentation/Siltation	1935	Agriculture-grazing		2007	

NAME	WATER BODY TYPE ABBR	WATER BODY TYPE	WATER BODY NAME	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
y	R	Rivers/Streams	Panache Creek (Silver Creek to Belmont Avenue)	55112000	17.6357 M	Miles	1100		Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2007	
	L	Lakes/Reservoirs	Bridgeport Reservoir	63030050	2614.34 A	Acres	1100		Sedimentation/Siltation	1350	Grazing-Related Sources	2006	
	L	Lakes/Reservoirs	Bridgeport Reservoir	63030050	2614.34 A	Acres	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2006	
	L	Lakes/Reservoirs	Bridgeport Reservoir	63030050	2614.34 A	Acres	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2006	
	L	Lakes/Reservoirs	Bridgeport Reservoir	63030050	2614.34 A	Acres	1100		Sedimentation/Siltation	8540	Sediment Resuspension	2006	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	1350	Grazing-Related Sources	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	2000	Silviculture	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	3200	Land Development	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	4300	Other Urban Runoff	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	4500	Highway/Road/Bridge Runoff	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	4600	Urban Runoff-Erosion and Sedimentation	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7000	Hydromodification	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7100	Channelization	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7200	Removal of Riparian Vegetation	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7810	Channel Erosion	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	8100	Atmospheric Deposition	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	8540	Sediment Resuspension	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	8600	Natural Sources	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	8700	Recreational and Tourism Activities (non-boating)	2007	
	L	Lakes/Reservoirs	Tahoe, Lake	63430010	85364.1 A	Acres	1100		Sedimentation/Siltation	9100	Nonpoint Source	2007	
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	4501	Surface Runoff	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	5000	Resource Extraction	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	7000	Hydromodification	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	8100	Atmospheric Deposition	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	8600	Natural Sources	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	8700	Recreational and Tourism Activities (non-boating)	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Blackwood Creel	63420021	5.87001 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2008	Creek affected by past gravel quarry operations and other watershed disturbance including grazing and timber har
	R	Rivers/Streams	Bronco Creek	63520053	1.34403 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2006	Watershed disturbance in naturally highly erosive watershe
	R	Rivers/Streams	Bronco Creek	63520053	1.34403 M	Miles	1100		Sedimentation/Siltation	8600	Natural Sources	2006	Watershed disturbance in naturally highly erosive watershe
	R	Rivers/Streams	Bronco Creek	63520053	1.34403 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2006	Watershed disturbance in naturally highly erosive watershe
	R	Rivers/Streams	Clearwater Creel	63040051	12.4874 M	Miles	1100		Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2006	Listed on basis of limited information; additional monitoring may support delist
	R	Rivers/Streams	Clearwater Creel	63040051	12.4874 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2006	Listed on basis of limited information; additional monitoring may support delist
	R	Rivers/Streams	Clearwater Creel	63040051	12.4874 M	Miles	1100		Sedimentation/Siltation	8300	Highway Maintenance and Runoff	2006	Listed on basis of limited information; additional monitoring may support delist
	R	Rivers/Streams	Clearwater Creel	63040051	12.4874 M	Miles	1100		Sedimentation/Siltation	1350	Grazing-Related Sources	2019	
	R	Rivers/Streams	East Walker River, below Bridgeport Reservo	63030050	8.00973 M	Miles	1100		Sedimentation/Siltation	4500	Highway/Road/Bridge Runoff	2019	
	R	Rivers/Streams	East Walker River, below Bridgeport Reservo	63030050	8.00973 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2019	
	R	Rivers/Streams	East Walker River, below Bridgeport Reservo	63030050	8.00973 M	Miles	1100		Sedimentation/Siltation	7350	Urban Runoff-Erosion and Sedimentation	2019	
	R	Rivers/Streams	East Walker River, below Bridgeport Reservo	63030050	8.00973 M	Miles	1100		Sedimentation/Siltation	7500	Upstream Impoundment	2019	
	R	Rivers/Streams	East Walker River, below Bridgeport Reservo	63030050	8.00973 M	Miles	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2019	
	R	Rivers/Streams	Gray Creek (Nevada County)	63520052	2.8033 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2006	Sediment from disturbance of naturally highly erosive watershe
	R	Rivers/Streams	Gray Creek (Nevada County)	63520052	2.8033 M	Miles	1100		Sedimentation/Siltation	8600	Natural Sources	2006	Sediment from disturbance of naturally highly erosive watershe
	R	Rivers/Streams	Gray Creek (Nevada County)	63520052	2.8033 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2006	Sediment from disturbance of naturally highly erosive watershe
	R	Rivers/Streams	Heavenly Valley Creek (USFS boundary to Trou	63410031	1.44732 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2019	
	R	Rivers/Streams	Heavenly Valley Creek (USFS boundary to Trou	63410031	1.44732 M	Miles	1100		Sedimentation/Siltation	3200	Land Development	2019	
	R	Rivers/Streams	Heavenly Valley Creek (USFS boundary to Trou	63410031	1.44732 M	Miles	1100		Sedimentation/Siltation	7000	Hydromodification	2019	
	R	Rivers/Streams	Heavenly Valley Creek (USFS boundary to Trou	63410031	1.44732 M	Miles	1100		Sedimentation/Siltation	7550	Habitat Modification	2019	
	R	Rivers/Streams	Heavenly Valley Creek (USFS boundary to Trou	63410031	1.44732 M	Miles	1100		Sedimentation/Siltation	8700	Recreational and Tourism Activities (non-boating)	2019	
	R	Rivers/Streams	Hot Springs Canyon Cree	63030042	2.8612 M	Miles	1100		Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2008	Listed on basis of limited data; further monitoring may support delist
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	4300	Other Urban Runoff	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	7000	Hydromodification	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	7800	Drainage/Filling Of Wetlands	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	8300	Highway Maintenance and Runoff	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	8600	Natural Sources	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	8700	Recreational and Tourism Activities (non-boating)	2006	
	R	Rivers/Streams	Squaw Cree	63520011	5.8 M	Miles	1100		Sedimentation/Siltation	9100	Nonpoint Source	2006	
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	2000	Silviculture	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	3000	Construction/Land Development	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	3100	Highway/Road/Bridge Construction	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	7700	Streambank Modification/Destabilization	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	7810	Channel Erosion	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	7820	Erosion/Siltation	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	8600	Natural Sources	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	8700	Recreational and Tourism Activities (non-boating)	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Tuckee River	63510010	39.1307 M	Miles	1100		Sedimentation/Siltation	9100	Snow Sking activities	2006	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100		Sedimentation/Siltation	2000	Nonpoint Source	2008	Watershed disturbance including ski resorts, silvicultural activities, urban development, reservoir construction and management; highly erosive subwaters
	R	Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100		Sedimentation/Siltation	3200	Land Development	2008	
	R	Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100		Sedimentation/Siltation	4000	Urban Runoff/Storm Sewers	2008	

WATER BODY NAME	WATER BODY TYPE	CALWATER WATERSHED	ESTIMATED SIZE AFFECTED	UNIT ABBR	UNIT	POLLUTANT CODE	POLLUTANT	SOURCE CODE	POTENTIAL SOURCES	PROPOSED TMDL COMPLETION	COMMENTS
Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100	Sedimentation/Siltation	4500	Highway/Road/Bridge Runoff	2008		
Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100	Sedimentation/Siltation	7810	Channel Erosion	2008		
Rivers/Streams	Ward Creek	63420020	5.675 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2008		
Rivers/Streams	Wolf Creek (Alpine County)	63210031	11.8207 M	Miles	1100	Sedimentation/Siltation	1500	Range Grazing-Riparian and/or Upland	2019		
Rivers/Streams	Wolf Creek (Alpine County)	63210031	11.8207 M	Miles	1100	Sedimentation/Siltation	2000	Silviculture	2019		
Rivers/Streams	Wolf Creek (Alpine County)	63210031	11.8207 M	Miles	1100	Sedimentation/Siltation	9100	Nonpoint Source	2019		
Lakes/Reservoirs	Big Bear Lake	80171000	2865.01 A	Acres	1100	Sedimentation/Siltation	3000	Construction/Land Development	2006		
Lakes/Reservoirs	Big Bear Lake	80171000	2865.01 A	Acres	1100	Sedimentation/Siltation	8710	Snow skiing activities	2006		
Lakes/Reservoirs	Big Bear Lake	80171000	2865.01 A	Acres	1100	Sedimentation/Siltation	9105	Unknown Nonpoint Source	2006		
Rivers/Streams	Rathbone (Rathbun) Creei	80171000	4.68 M	Miles	1100	Sedimentation/Siltation	8710	Snow skiing activities	2006		
Rivers/Streams	Rathbone (Rathbun) Creei	80171000	4.68 M	Miles	1100	Sedimentation/Siltation	9105	Unknown Nonpoint Source	2006		
Estuaries	Agua Hedionda Lagoon	90431000	6.83187 A	Acres	1100	Sedimentation/Siltation	9201	Nonpoint/Point Source	2019		
Estuaries	Buena Vista Lagoon	90421000	202.298 A	Acres	1100	Sedimentation/Siltation	9201	Nonpoint/Point Source	2019		
Estuaries	Los Penasquitos Lagoon	90610000	468.918 A	Acres	1100	Sedimentation/Siltation	9201	Nonpoint/Point Source	2019		
Estuaries	San Elijo Lagoon	90461000	565.804 A	Acres	1100	Sedimentation/Siltation	9201	Nonpoint/Point Source	2019		Estimated size of impairment is 150 acres



**Porous Pavement Credit Worksheet**

Please fill out a porous pavement credit worksheet for each project sub-watershed.

For the **PROPOSED Development**:

Proposed Porous Pavement	Runoff Reduction*	Fill in either Acres or SqFt		
		In SqFt.	In Acres	Equivalent Acres
Area of <b>Brick without Grout</b> on <u>less than 12 inches</u> of base with at least 20% void space over soil	0.45			0.00
Area of <b>Brick without Grout</b> on <u>more than 12 inches</u> of base with at least 20% void space over soil	0.90			0.00
Area of <b>Cobbles</b> <u>less than 12 inches deep</u> and over soil	0.30			0.00
Area of <b>Cobbles</b> <u>less than 12 inches deep</u> and over soil	0.60			0.00
Area of <b>Reinforced Grass Pavement</b> on <u>less than 12 inches</u> of base with at least 20% void space over soil	0.45			0.00
Area of <b>Reinforced Grass Pavement</b> on <u>at least 12 inches</u> of base with at least 20% void space over soil	0.90			0.00
Area of <b>Porous Gravel Pavement</b> on <u>less than 12 inches</u> of base with at least 20% void space over soil	0.38			0.00
Area of <b>Porous Gravel Pavement</b> on <u>at least 12 inches</u> of base with at least 20% void space over soil	0.75			0.00
Area of <b>Poured Porous Concrete or Asphalt Pavement</b> with <u>less than 4 inches</u> of gravel base (washed stone)	0.40			0.00
Area of <b>Poured Porous Concrete or Asphalt Pavement</b> with <u>4 to 8 inches</u> of gravel base (washed stone)	0.60			0.00
Area of <b>Poured Porous Concrete or Asphalt Pavement</b> with <u>8 to 12 inches</u> of gravel base (washed stone)	0.80			0.00
Area of <b>Poured Porous Concrete or Asphalt Pavement</b> with <u>12 or more</u> inches of gravel base (washed stone)	1.00			0.00

\*=1-Rv\*\*

[Return to Calculator](#)

\*\*Using Site Design Techniques to meet Development Standards for Stormwater Quality (BASMAA 2003)

\*\*NCDENR Stormwater BMP Manual (2007)

**Tree Planting Credit Worksheet**

Please fill out a tree canopy credit worksheet for each project sub-watershed.

Tree Canopy Credit Criteria	Number of Trees Planted	Credit (acres)
Number of proposed evergreen trees to be planted (credit = number of trees x 0.005)*	0	0.00
Number of proposed deciduous trees to be planted (credit = number of trees x 0.0025)*		0.00
	Square feet Under Canopy	
Square feet under an existing tree canopy, that will remain on the property, with an average diameter at 4.5 ft above grade (i.e., diameter at breast height or DBH) is LESS than 12 in diameter.		0.00
Square feet under an existing tree canopy that will remain on the property, with an average diameter at 4.5 ft above grade (i.e., diameter at breast height or DBH) is 12 in diameter or GREATER.		0.00
Please describe below how the project will ensure that these trees will be maintained.		

0

[Return to Calculator](#)

\* credit amount based on credits from Stormwater Quality Design Manual for the Sacramento and South Placer Regions

### Downspout Disconnection Credit Worksheet

Please fill out a downspout disconnection credit worksheet for each project subwatershed. If you answer yes to all questions, all rooftop area draining to each downspout will be subtracted from your proposed rooftop impervious coverage.

Downspout Disconnection Credit Criteria					
Do downspouts and any extensions extend at least six feet from a basement and two feet from a crawl space or concrete slab?				<input type="radio"/> Yes	<input checked="" type="radio"/> No
Is the area of rooftop connecting to each disconnected downspout 600 square feet or less?				<input type="radio"/> Yes	<input checked="" type="radio"/> No
Is the roof runoff from the design storm event fully contained in a raised bed or planter box or does it drain as sheet flow to a landscaped area large enough to contain the roof runoff from the design storm event?				<input type="radio"/> Yes	<input checked="" type="radio"/> No
The Stream Buffer and/or Vegetated Swale credits <b>will not</b> be taken in this sub-watershed area?				<input type="radio"/> Yes	<input checked="" type="radio"/> No
Percentage of existing	0.00	Acres	of rooftop surface has disconnected downspouts		
Percentage of the proposed	0.00	Acres	of rooftop surface has disconnected downspouts	50	
				<a href="#">Return to Calculator</a>	

**Impervious Area Disconnection Credit Worksheet**

Please fill out an impervious area disconnection credit worksheet for each project sub-watershed. If you answer yes to all questions, all non-rooftop impervious surface area will be subtracted from your proposed non-rooftop impervious coverage.

Non-Rooftop Disconnection Credit Criteria	Response
Is the maximum contributing impervious flow path length less than 75 feet or, if equal or greater than 75 feet, is a storage device (e.g. French drain, bioretention area, gravel trench) implemented to achieve the required disconnection length?	<input checked="" type="radio"/> Yes <input type="radio"/> No
Is the impervious area to any one discharge location less than 5,000 square feet?	<input checked="" type="radio"/> Yes <input type="radio"/> No
The Stream Buffer credit <b>will not</b> be taken in this sub-watershed area?	<input checked="" type="radio"/> Yes <input type="radio"/> No

Percentage of existing	0.00 Acres non-rooftop surface area disconnected	
Percentage of the proposed	0.00 Acres non-rooftop surface area disconnected	70

[Return to Calculator](#)

## Green Roof Credit Worksheet

Please fill out a greenroof credit worksheet for each project sub-watershed. If you answer yes to all questions, 70% of the greenroof area will be subtracted from your proposed rooftop impervious coverage.

Green Roof Credit Criteria		Response
Is the roof slope less than 15% or does it have a grid to hold the substrate in place until it forms a thick vegetation mat?		<input checked="" type="radio"/> <b>Yes</b> <input type="radio"/> <b>No</b>
Has a professional engineer assessed the necessary load reserves and designed a roof structure to meet state and local codes?		<input checked="" type="radio"/> <b>Yes</b> <input type="radio"/> <b>No</b>
Is the irrigation needed for plant establishment and/or to sustain the green roof during extended dry periods, is the source from stored, recycled, reclaimed, or reused water?		<input checked="" type="radio"/> <b>Yes</b> <input type="radio"/> <b>No</b>
Percentage of existing	0.0 0 Acres rooftop surface area in greenroof	
Percentage of the proposed	0.0 0 Acres rooftop surface area in greenroof	
		<a href="#">Return to Calculator</a>

## Stream Buffer Credit Worksheet

Please fill out a stream buffer credit worksheet for each project sub-watershed. If you answer yes to all questions, you may subtract all impervious surface draining to each stream buffer that has not been addressed using the Downspout and/or Impervious Area Disconnection credits.

Stream Buffer Credit Criteria				Response
Does runoff enter the floodprone width* or within 500 feet (whichever is larger) of a stream channel as sheet flow**?				<input type="radio"/> Yes <input checked="" type="radio"/> No
Is the contributing overland slope 5% or less, or if greater than 5%, is a level spreader used?				<input type="radio"/> Yes <input checked="" type="radio"/> No
Is the buffer area protected from vehicle or other traffic barriers to reduce compaction?				<input type="radio"/> Yes <input checked="" type="radio"/> No
Will the stream buffer be maintained in an ungraded and uncompacted condition and will the vegetation be maintained in a natural condition?				<input type="radio"/> Yes <input checked="" type="radio"/> No
Percentage of existing	0.00	Acres	impervious surface area draining into a stream buffer:	
Percentage of the proposed	0.00	Acres	impervious surface area that will drain into a stream buffer:	
Please describe below how the project will ensure that the buffer areas will remain in ungraded and uncompacted condition and that the vegetation will be maintained in a natural condition.				

[Return to Calculator](#)

\* floodprone width is the width at twice the bankfull depth.

\*\* the maximum contributing length shall be 75 feet for impervious area

### Vegetated Swale Credit Worksheet

Please fill out a vegetated swale worksheet for each project subwatershed. If you answer yes to all questions, you may subtract all impervious surface draining to each stream buffer that has not been addressed using the Downspout Disconnection credit.

#### Vegetated Swale Credit Criteria

Have all vegetated swales been designed in accordance with Treatment Control BMP 30 (TC-30 - Vegetated Swale) from the California Stormwater BMP Handbook, New Development and Redevelopment (available at [www.cabmphandbooks.com](http://www.cabmphandbooks.com))?

<input type="radio"/> Yes	<input checked="" type="radio"/> No
---------------------------	-------------------------------------

Is the maximum flow velocity for runoff from the design storm event less than or equal to 1.0 foot per second?

<input type="radio"/> Yes	<input checked="" type="radio"/> No
---------------------------	-------------------------------------

Percentage of existing	0.00	Acres of impervious area draining to a vegetated swale	
Percentage of the proposed	0.00	Acres of impervious area draining to a vegetated swale	

[Return to Calculator](#)

### Rain Barrel/Cistern Credit Worksheet

Please fill out a rain barrel/cistern worksheet for each project sub-watershed.

Rain Barrel/Cistern Credit Criteria	Response
Total number of rain barrel(s)/cisterns	
Average capacity of rain barrel(s)/cistern(s) (in gallons)	
Total capacity rain barrel(s)/cistern(s) (in cu ft) <sup>1</sup>	0

<sup>1</sup> accounts for 10% loss

[Return to Calculator](#)

Please fill out a soil quality worksheet for each project sub-watershed.

	Response
Will the landscaped area be lined with an impervious membrane?	
Will the soils used for landscaping meet the ideal bulk densities listed in Table 1 below? <sup>1</sup>	<input type="radio"/> Yes <input checked="" type="radio"/> No
If you answered yes to the question above, and you know the area-weighted bulk density within the top 12 inches for soils used for landscaping (in g/cm <sup>3</sup> )*, fill in the cell to the right and skip to cell G11. If not select from the drop-down menu in G10.	1.3
If you answered yes to the question above, but you do not know the exact bulk density, which of the soil types in the drop down menu to the right best describes the top 12 inches for soils used for landscaping (in g/cm <sup>3</sup> ).	Sandy loams, loams
What is the average depth of your landscaped soil media meeting the above criteria (inches)?	12
What is the total area of the landscaped areas meeting the above criteria (in acres)?	2.97

[Return to Calculator](#)

Table 1

Sands, loamy sands	<1.6
Sandy loams, loams	<1.4
Sandy clay loams, loams, clay loams	<1.4
Silts, silt loams	<1.3
Silt loams, silty clay loams	<1.1
Sandy clays, silty clays, some clay loams (35-45% clay)	<1.1
Clays (>45% clay)	<1.1

Porosity (%) 50.94%

Mineral grains in many soils are mainly quartz and feldspar, so 2.65 a good average for particle density. To determine percent porosity, use the formula: Porosity (%) = (1-Bulk Density/2.65) X 100

<sup>1</sup> USDA NRCS. "Soil Quality Urban Technical Note No.2-Urban Soil Compaction". March 2000.

[http://soils.usda.gov/sqi/management/files/sq\\_utn\\_2.pdf](http://soils.usda.gov/sqi/management/files/sq_utn_2.pdf)

\* To determine how to calculate density see:

<http://www.globe.gov/tctq/bulkden.pdf?sectionID=94>

## **APPENDIX 2: Post-Construction Water Balance Performance Standard Spreadsheet**

The discharger shall submit with their Notice of Intent (NOI) the following information to demonstrate compliance with the New and Re-Development Water Balance Performance Standard.

### **Map Instructions**

The discharger must submit a small-scale topographic map of the site to show the existing contour elevations, pre- and post-construction drainage divides, and the total length of stream in each watershed area. Recommended scales include 1 in. = 20 ft., 1 in. = 30 ft., 1 in. = 40 ft., or 1 in. = 50 ft. The suggested contour interval is usually 1 to 5 feet, depending upon the slope of the terrain. The contour interval may be increased on steep slopes. Other contour intervals and scales may be appropriate given the magnitude of land disturbance.

### **Spreadsheet Instructions**

The intent of the spreadsheet is to help dischargers calculate the project-related increase in runoff volume and select impervious area and runoff reduction credits to reduce the project-related increase in runoff volume to pre-project levels.

The discharger has the option of using the spreadsheet (**Appendix 2.1**) or a more sophisticated, watershed process-based model (e.g. Storm Water Management Model, Hydrological Simulation Program Fortran) to determine the project-related increase in runoff volume.

***In Appendix 4.1, you must complete the worksheet for each land use/soil type combination for each project sub-watershed.***

### **Steps 1 through 9 pertain specifically to the Runoff Volume Calculator:**

Step 1: Enter the county where the project is located in cell H3.

Step 2: Enter the soil type in cell H6.

Step 3: Enter the existing pervious (dominant) land use type in cell H7.

Step 4: Enter the proposed pervious (dominant) land use type in cell H8.

Step 5: Enter the total project site area in cell H11 or J11.

Step 6: Enter the sub-watershed area in cell H12 or J12.

- Step 7: Enter the existing rooftop area in cell H17 or J17, the existing non-rooftop impervious area in cell H18 or J18, the proposed rooftop area in cell H19 or J19, and the proposed non-rooftop impervious area in cell H20 or J20
- Step 8: Work through each of the impervious area reduction credits and claim credits where applicable. Volume that cannot be addressed using non-structural practices must be captured in structural practices and approved by the Regional Water Board.
- Step 9: Work through each of the impervious volume reduction credits and claim credits where applicable. Volume that cannot be addressed using non-structural practices must be captured in structural practices and approved by the Regional Water Board.

### **Non-structural Practices Available for Crediting**

- ***Porous Pavement***
- ***Tree Planting***
- ***Downspout Disconnection***
- ***Impervious Area Disconnection***
- ***Green Roof***
- ***Stream Buffer***
- ***Vegetated Swales***
- ***Rain Barrels and Cisterns***
- ***Landscaping Soil Quality***

## APPENDIX 3

### Bioassessment Monitoring Guidelines

Bioassessment monitoring is required for projects that meet all of the following criteria:

1. The project is rated Risk Level 3 or LUP Type 3
2. The project directly discharges runoff to a freshwater wadeable stream (or streams) that is either: (a) listed by the State Water Board or USEPA as impaired due to sediment, and/or (b) tributary to any downstream water body that is listed for sediment; and/or have the beneficial use SPAWN & COLD & MIGRATORY
3. Total project-related ground disturbance exceeds 30 acres.

For all such projects, the discharger shall conduct bioassessment monitoring, as described in this section, to assess the effect of the project on the biological integrity of receiving waters.

Bioassessment shall include:

1. The collection and reporting of specified instream biological data
2. The collection and reporting of specified instream physical habitat data

#### Bioassessment Exception

If a site qualifies for bioassessment, but construction commences out of an index period for the site location, the discharger shall:

1. Receive Regional Water Board approval for the sampling exception
2. Make a check payable to: Cal State Chico Foundation (SWAMP Bank Account) or San Jose State Foundation (SWAMP Bank Account) and include the WDID# on the check for the amount calculated for the exempted project.
3. Send a copy of the check to the Regional Water Board office for the site's region
4. Invest **7,500.00 X The number of samples required** into the SWAMP program as compensation (upon Regional Water Board approval).
5. Conduct bioassessment monitoring, as described in Appendix 4
6. Include the collection and reporting of specified instream biological data and physical habitat
7. Use the bioassessment sample collection and Quality Assurance & Quality Control (QA/QC) protocols developed by the State of California's Surface Water Ambient Monitoring Program (SWAMP)

#### Site Locations and Frequency

Macroinvertebrate samples shall be collected both before ground disturbance is initiated and after the project is completed. The "after" sample(s) shall be collected after at least one winter season resulting in surface runoff has transpired after project-related ground disturbance has ceased. "Before" and "after" samples shall be collected both upstream and downstream of the project's

discharge. Upstream samples should be taken immediately before the sites outfall and downstream samples should be taken immediately after the outfall (when safe to collect the samples). Samples should be collected for each freshwater wadeable stream that is listed as impaired due to sediment, or tributary to a water body that is listed for sediment. Habitat assessment data shall be collected concurrently with all required macroinvertebrate samples.

#### Index Period (Timing of Sample Collection)

Macroinvertebrate sampling shall be conducted during the time of year (i.e., the “index period”) most appropriate for bioassessment sampling, depending on ecoregion. This map is posted on the State Water Board’s Website:

[http://www.waterboards.ca.gov/water\\_issues/programs/stormwater/construction.shtml](http://www.waterboards.ca.gov/water_issues/programs/stormwater/construction.shtml)

#### Field Methods for Macroinvertebrate Collections

In collecting macroinvertebrate samples, the discharger shall use the “Reachwide Benthos (Multi-habitat) Procedure” specified in *Standard Operating Procedures for Collecting Benthic Macroinvertebrate Samples and Associated Physical and Chemical Data for Ambient Bioassessments in California* (Ode 2007).<sup>1</sup>

#### Physical - Habitat Assessment Methods

The discharger shall conduct, concurrently with all required macroinvertebrate collections, the “Full” suite of physical habitat characterization measurements as specified in *Standard Operating Procedures for Collecting Benthic Macroinvertebrate Samples and Associated Physical and Chemical Data for Ambient Bioassessments in California* (Ode 2007), and as summarized in the Surface Water Ambient Monitoring Program’s *Stream Habitat Characterization Form — Full Version*.

#### Laboratory Methods

Macroinvertebrates shall be identified and classified according to the Standard Taxonomic Effort (STE) Level I of the Southwestern Association of Freshwater Invertebrate Taxonomists (SAFIT),<sup>2</sup> and using a fixed-count of 600 organisms per sample.

#### Quality Assurance

The discharger or its consultant(s) shall have and follow a quality assurance (QA) plan that covers the required bioassessment monitoring. The QA plan shall include, or be supplemented to include, a specific requirement for external QA checks (i.e., verification of taxonomic identifications and correction of data where errors are identified). External QA checks shall be performed on one of the

<sup>1</sup> This document is available on the Internet at: [http://www.swrcb.ca.gov/swamp/docs/phab\\_sopr6.pdf](http://www.swrcb.ca.gov/swamp/docs/phab_sopr6.pdf).

<sup>2</sup> The current SAFIT STEs (28 November 2006) list requirements for both the Level I and Level II taxonomic effort, and are located at: [http://www.swrcb.ca.gov/swamp/docs/safit/ste\\_list.pdf](http://www.swrcb.ca.gov/swamp/docs/safit/ste_list.pdf). When new editions are published by SAFIT, they will supersede all previous editions. All editions will be posted at the State Water Board’s SWAMP website.

discharger's macroinvertebrate samples collected per calendar year, or ten percent of the samples per year (whichever is greater). QA samples shall be randomly selected. The external QA checks shall be paid for by the discharger, and performed by the California Department of Fish and Game's Aquatic Bioassessment Laboratory. An alternate laboratory with equivalent or better expertise and performance may be used if approved in writing by State Water Board staff.

#### Sample Preservation and Archiving

The original sample material shall be stored in 70 percent ethanol and retained by the discharger until: 1) all QA analyses specified herein and in the relevant QA plan are completed; and 2) any data corrections and/or re-analyses recommended by the external QA laboratory have been implemented. The remaining subsampled material shall be stored in 70 percent ethanol and retained until completeness checks have been performed according to the relevant QA plan. The identified organisms shall be stored in 70 percent ethanol, in separate glass vials for each final ID taxon. (For example, a sample with 45 identified taxa would be archived in a minimum of 45 vials, each containing all individuals of the identified taxon.) Each of the vials containing identified organisms shall be labeled with taxonomic information (i.e., taxon name, organism count) and collection information (i.e., site name/site code, waterbody name, date collected, method of collection). The identified organisms shall be archived (i.e., retained) by the discharger for a period of not less than three years from the date that all QA steps are completed, and shall be checked at least once per year and "topped off" with ethanol to prevent desiccation. The identified organisms shall be relinquished to the State Water Board upon request by any State Water Board staff.

#### Data Submittal

The macroinvertebrate results (i.e., taxonomic identifications consistent with the specified SAFIT STEs, and number of organisms within each taxa) shall be submitted to the State Water Board in electronic format. The State Water Board's Surface Water Ambient Monitoring Program (SWAMP) is currently developing standardized formats for reporting bioassessment data. All bioassessment data collected after those formats become available shall be submitted using the SWAMP formats. Until those formats are available, the biological data shall be submitted in MS-Excel (or equivalent) format.<sup>3</sup>

The physical/habitat data shall be reported using the standard format titled *SWAMP Stream Habitat Characterization Form — Full Version*.<sup>4</sup>

---

<sup>3</sup> Any version of Excel, 2000 or later, may be used.

<sup>4</sup> Available at:

[http://www.waterboards.ca.gov/water\\_issues/programs/swamp/docs/reports/fieldforms\\_fullversion052908.pdf](http://www.waterboards.ca.gov/water_issues/programs/swamp/docs/reports/fieldforms_fullversion052908.pdf)

Invasive Species Prevention

In conducting the required bioassessment monitoring, the discharger and its consultants shall take precautions to prevent the introduction or spread of aquatic invasive species. At minimum, the discharger and its consultants shall follow the recommendations of the California Department of Fish and Game to minimize the introduction or spread of the New Zealand mudsnail.<sup>5</sup>

---

<sup>5</sup> Instructions for controlling the spread of NZ mudsnails, including decontamination methods, can be found at: <http://www.dfg.ca.gov/invasives/mudsnail/>  
More information on AIS More information on AIS  
[http://www.waterboards.ca.gov/water\\_issues/programs/swamp/ais/](http://www.waterboards.ca.gov/water_issues/programs/swamp/ais/)

## Appendix 4 Sediment TMDLs

Implemented Sediment TMDLs in California. Construction was listed as a source in all fo these TMDLs in relation to road construction. Although construction was mentioned as a source, it was not given a specific allocation amount. The closest allocation amount would be for the road activity management WLA. **Implementation Phase** – Adoption process by the Regional Board, the State Water Resources Control Board, the Office of Administrative Law, and the US Environmental Protection Agency completed and TMDL being implemented.

A. Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres	WLA tons mi <sup>2</sup> yr
1 R1.epa.albionfinalt mdl	R	Albion River	Sedimentation	Road Construction	2001	43 acres	See A (table 6)

B Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres	WLA tons mi <sup>2</sup> yr
1 R1.epa.EelR- middle.mainSed.te mp	R	Middle Main Eel River and Tributaries (from Dos Rios to the South Fork)	Sedimentation Road	Construction	2005-2006 521	mi <sup>2</sup>	100

C Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres	WLA tons mi <sup>2</sup> yr
1 R1.epa.EelRsouth. sed.temp	R	South Fork Eel River	Sedimentation	Road Construction	12 1999	See chart	473

D Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres	WLA tons mi <sup>2</sup> yr
1 R1.epa.bigfinaltmd l	R Big	River	Sedimentation	Road Construction	12 2001	181 mi <sup>2</sup> watershed drainage	TMDL = loading capacity = nonpoint sources + background =

393 t mi<sup>2</sup> yr

<b>E Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres</b>	<b>WLA tons mi<sup>2</sup> yr</b>
1 R1.epa.EelR-lower.Sed.temp-121807-signed	R	Lower Eel River	Sedimentation	Road Construction	12 2007	300 square-mile watershed	898

<b>F Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres</b>	<b>WLA tons mi<sup>2</sup> yr</b>
1 R1.epa.EelR-middle.Sed.temp-	R	Middle Fork Eel River	Sedimentation	Road Construction	12 2003	753 mi <sup>2</sup> (approx. 482,000 acres)	82

<b>G Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres Mi<sup>2</sup></b>	<b>WLA tons mi<sup>2</sup> yr</b>
1 R1.epa.EelRnorth-Sed.temp.final-121807-signed	R	North Fork Eel River	Sedimentation	Road Construction	12 30 2002	289 (180,020 acres)	20

<b>H Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres Mi<sup>2</sup></b>	<b>WLA tons mi<sup>2</sup> yr</b>
1 R1.epa.EelR-upper.mainSed.tem-	R	Upper Main Eel River and Tributaries (including Tomki Creek, Outlet Creek and Lake Pillsbury)	Sedimentation	Road Construction	12 29 2004	688 (approx. 440,384 acres)	14

I Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres	WLA tons mi <sup>2</sup> yr
1 R1.epa.gualalafina ltmdl	R	Gualala River	Sedimentation	Road Construction	Not sure	300 (191,145 acres)	7

J Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.Mad- sed.turbidity	R	Mad River	Sedimentation	Road Construction	12 21 2007	480	174

K Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.mattole.se diment	R	Mattole River	Sedimentation	Road Construction	12 30 2003	296	27 or 520+27 = 547

L Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.navarro.se d.temp	R	Navarro River	Sedimentation	Road Construction	Not sure	315 (201,600 acres).	50

M Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.noyo.sedi ment	R	Noyo River	Sedimentation	Road Construction	12 16 1999	113 (72,323 acres)	68 (three areas measured) Table 16 in the TMDL

<b>N Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres mi<sup>2</sup></b>	<b>WLA tons mi<sup>2</sup> yr</b>
1 R1.epa.RedwoodCk.sed	Cr	Redwood Creek	Sedimentation	Road Construction	12 30 1998	278	1900 Total allocation

<b>O Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres mi<sup>2</sup></b>	<b>WLA – Roads tons mi<sup>2</sup> yr</b>
1 R1.epa.tenmile.sed	R	Ten Mile River	Sedimentation	Road Construction	2000	120	9

<b>P Region</b>	<b>Type</b>	<b>Name</b>	<b>Pollutant Stressor</b>	<b>Potential Sources</b>	<b>TMDL Completion Date</b>	<b>Watershed Acres mi<sup>2</sup></b>	<b>WLA management tons mi<sup>2</sup> yr</b>
1 R1.epa.trinity.sed	R	Trinity River	Sedimentation	Road Construction	12 20 2001	2000 of 3000 covered in this TMDL	See rows below
1	Cr	Horse Linto Creek	Sedimentation	Road Construction	12 20 2001	64	528
1	Cr	Mill creek and Tish Tang	Sedimentation	Road Construction	12 20 2001	39	210
1	Cr	Willow Creek	Sedimentation	Road Construction	12 20 2001	43	94
1	Cr	Campbell Creek and Supply Creek	Sedimentation	Road Construction	12 20 2001	11	1961
1	Cr	Lower Mainstem and Coon Creek	Sedimentation	Road Construction	12 20 2001	32	63
1 R		Reference Subwatershed <sup>1</sup>	Sedimentation	Road Construction	12 20 2001	434	24
1	Cr	Canyon Creek	Sedimentation	Road	12 20 2001	64	326

				Construction			
1 R		Upper Tributaries <sup>2</sup>	Sedimentation	Road Construction	12 20 2001	72	67
1 R		Middle Tributaries <sup>3</sup>	Sedimentation	Road Construction	12 20 2001	54	53
1 R		Lower Tributaries <sup>4</sup>	Sedimentation	Road Construction	12 20 2001	96	55
1	Cr	Weaver and Rush Creeks	Sedimentation	Road Construction	12 20 2001	72	169
1 Cr		Deadwood Creek Hoadley Gulch Poker Bar	Sedimentation	Road Construction	12 20 2001	47	68
1	L	Lewiston Lake	Sedimentation	Road Construction	12 20 2001	25	49
1 Cr		Grassvalley Creek	Sedimentation	Road Construction	12 20 2001	37	44
1	Cr	Indian Creek	Sedimentation	Road Construction	12 20 2001	34	81
1	Cr	Reading and Browns Creek	Sedimentation	Road Construction	12 20 2001	104	66
1 Cr		Reference Subwatersheds <sup>5</sup>	Sedimentation	Road Construction	12 20 2001	235	281
1	L, Cr	Westside tributaries <sup>6</sup>	Sedimentation	Road Construction	12 20 2001	93	105
1 R,	Cr, G	Upper trinity <sup>7</sup>	Sedimentation	Road Construction	12 20 2001	161	690
1 R,	Cr, G	East Fork Tributaries <sup>8</sup>	Sedimentation	Road Construction	12 20 2001	115	65
1	R, L	Eastside Tributaries <sup>9</sup>	Sedimentation	Road Construction	12 20 2001	89	60

1 New River, Big French, Manzanita, North Fork, East Fork, North Fork

2 Dutch, Soldier, Oregon gulch, Conner Creek

3 Big Bar, Prairie Creek, Little French Creek

4 Swede, Italian, Canadian, Cedar Flat, Mill, McDonald, Hennessy, Quimby, Hawkins, Sharber

5 Stuarts Fork, Swift Creek, Coffee Creek

6 Stuart Arm, Stoney Creek, Mule Creek, East Fork, Stuart Fork, West Side Trinity Lake, Hatchet Creek, Buckeye Creek,

7 Upper Trinity River, Tangle Blue, Sunflower, Graves, Bear Upper Trinity Mainstream, Ramshorn Creek, Ripple Creek, Minnehaha Creek, Snowslide Gulch, Scorpion Creek

8 East Fork Trinity, Cedar Creek, Squirrel Gulch

## 9 East Side Tributaries, Trinity Lake

Q Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.trinity.so.sed	R, Cr	South Fork Trinity River and Hayfork Creek	Sedimentation	Road Construction	12 1998	Not given, 19 miles long	33 (road total)

R Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
1 R1.epa.vanduzen.sed	R, Cr	Van Duzen River and Yager Creek	Sedimentation	Various	12 16 1999	429	1353 total allocation
1		Upper Basin	Sedimentation	Road Construction			7
1		Middle Basin	Sedimentation	Road Construction			22
1		Lower Basin	Sedimentation	Road Construction			20

S Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
6 R6.blackwood.sed Cr		Blackwood Creek (Placer County)	Bedded Sediment	Various	9 2007	11	17272 total

T Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Acres mi <sup>2</sup>	WLA tons mi <sup>2</sup> yr
6 R6.SquawCk.sed R		Squaw Creek (Placer County)	Sedimentation /controllable sources	Various – basin plan amendment	4 13 2006	8.2	10,900

## Adopted TMDLs for Construction Sediment Sources

Region	Type	Name	Pollutant Stressor	Potential Sources	TMDL Completion Date	Watershed Area mi <sup>2</sup>	Waste load Allocation tons mi <sup>2</sup> yr
8 R		Newport Bay San Diego Creek Watershed	Sedimentation	Construction Land Development	1999 2.24	(1432 acres)	125,000 tons per Year (no more than 13,000 tons per year from construction sites)

## Appendix 4 Non Sediment TMDLs

Region 1 Lost River-DIN and CBOD

Region 1 Source: Cal Trans Construction TMDL Completion Date: 12 30 2008 TMDL Type: River, Lake Watershed Area= 2996 mi <sup>2</sup>	Pollutant Stressors/WLA	
	Dissolved inorganic nitrogen (DIN) (metric tons/yr)	Carbonaceous biochemical oxygen demand (CBOD) (metric tons/yr)
Lost River from the Oregon border to Tule Lake	.1 .2	
Tule Lake Refuge	.1	.2
Lower Klamath Refuge	.1	.2

Region 2 San Francisco Bay-Mercury

Region 2 Source:Non-Urban Stormwater Runoff TMDL Type: Bay	Name	Pollutant Stressor/WLA	TMDL Completion Date
	San Francisco Bay	Mercury 25 kg/year	08 09 2006

**Region 4 Machado Lake Nutrients - Resolution No. 2008-006**  
**(Effective Date - March 11, 2009)**

<b>General Construction Stormwater Permit WLAs</b>	<b>Years After Effective Date</b>	<b>Total Phosphorus (mg/L)</b>	<b>Total Nitrogen (TKN + NO3-N + NO2-N) (mg/L)</b>
Interim WLAs <sup>1</sup>	At Effective Date	1.25	3.50
Interim WLAs <sup>2</sup> 5	years	1.25	2.45
Final WLAs <sup>2</sup>	9.5 years	0.10	1.00

<sup>1</sup> The compliance points for effective date interim WLAs are measured in the lake.

<sup>2</sup> No compliance points are specified for general construction stormwater permits for the year 5 interim WLAs and final WLAs

**Region 4 Ballona Creek-Metals and Selenium – Resolution No. 2007-015**  
**(Effective Date October 29, 2008)**

**Wet Weather WLAs**

Region 4 Source: NPDES General Construction TMDL Completion Date: 10 29 2008 TMDL Type: Creek								
	<b>Copper (Cu)</b>		<b>Lead (Pb)</b>		<b>Selenium (Se)</b>		<b>Zinc (Zn)</b>	
	g/day	g/day/acre	g/day	g/day/acre	g/day	g/day/acre	g/day	g/day/acre
Ballona Creek	4.94E-07 x Daily storm volume (L)	2.20E-10 x Daily storm volume (L)	1.62E-06 x Daily storm volume (L)	7.20E-10 x Daily storm volume (L)	1.37E-07 x Daily storm volume (L)	6.10E-11 x Daily storm volume (L)	3.27E-06 x Daily storm volume (L)	1.45E-09 x Daily storm volume (L)

**Wet-weather WLA Implementation**

- Within seven years of the effective date of the TMDL, the construction industry will submit the results of BMP effectiveness studies to determine BMPs that will achieve compliance with the final waste load allocations assigned to construction storm water permittees.
- Regional Board staff will bring the recommended BMPs before the Regional Board for consideration within eight years of the effective date of the TMDL.
- General construction storm water permittees will be considered in compliance with final waste load allocations if they implement these Regional Board approved BMPs. All permittees must implement the approved BMPs within nine years of the effective date of the TMDL. If no effectiveness studies are conducted and no BMPs are approved by the Regional Board within eight years of the effective date of the TMDL, each general construction storm water permit holder will be subject to site-specific BMPs and monitoring requirements to demonstrate compliance with final waste load allocations.

**Dry-weather WLAs**

A waste load allocation of zero is assigned to all general construction storm water permits during dry weather.

**Dry-weather WLA Implementation**

Non-storm water flows authorized by the General Permit for Storm Water Discharges Associated with Construction Activity (Water Quality Order No. 99-08 DWQ), or any successor order, are exempt from the dry-weather waste load allocation equal to zero as long as they comply with the provisions of sections C.3 and A.9 of the Order No. 99-08 DWQ, which state that these authorized non-storm discharges shall be:

- (1) infeasible to eliminate
- (2) comply with BMPs as described in the Storm Water Pollution Prevention Plan prepared by the permittee, and
- (3) not cause or contribute to a violation of water quality standards, or comparable provisions in any successor order.

Unauthorized non-storm water flows are already prohibited by Order No. 99-08 DWQ.

**Region 4 Los Angeles River and Tributaries-Metals- Resolution No. 2007-014**  
**(Effective Date October 29, 2008)**

**Wet Weather WLAs**

	Cadmium (Cd)		Copper (Cu)		Lead (Pb)		Zinc (Zn)	
	kg/day	g/day/acre	kg/day	g/day/acre	kg/day	g/day/acre	kg/day	g/day/acre
	5.9x10 <sup>-11</sup> x	7.6x10 <sup>-12</sup> x	3.2x10 <sup>-10</sup> x	4.2x10 <sup>-11</sup> x	1.2x10 <sup>-9</sup> x	1.5x10 <sup>-10</sup> x	3.01x10 <sup>-9</sup> x	3.9x10 <sup>-10</sup> x
Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	Daily storm volume (L)	

**Wet-weather WLA Implementation**

- Within seven years of the effective date of the TMDL, the construction industry will submit the results of BMP effectiveness studies to determine BMPs that will achieve compliance with the final waste load allocations assigned to construction storm water permittees.
- Regional Board staff will bring the recommended BMPs before the Regional Board for consideration within eight years of the effective date of the TMDL.
- General construction storm water permittees will be considered in compliance with final waste load allocations if they implement these Regional Board approved BMPs. All permittees must implement the approved BMPs within nine years of the effective date of the TMDL. If no effectiveness studies are conducted and no BMPs are approved by the Regional Board within eight years of the effective date of the TMDL, each general construction storm water permit holder will be subject to site-specific BMPs and monitoring requirements to demonstrate compliance with final waste load allocations.

**Dry-weather WLAs**

A waste load allocation of zero is assigned to all general construction storm water permits during dry weather.

**Dry-weather WLA Implementation**

Non-storm water flows authorized by the General Permit for Storm Water Discharges Associated with Construction Activity (Water Quality Order No. 99-08 DWQ), or any successor order, are exempt from the dry-weather waste load allocation equal to zero as

long as they comply with the provisions of sections C.3 and A.9 of the Order No. 99-08 DWQ, which state that these authorized non-storm discharges shall be:

- (1) infeasible to eliminate
  - (2) comply with BMPs as described in the Storm Water Pollution Prevention Plan prepared by the permittee, and
  - (3) not cause or contribute to a violation of water quality standards, or comparable provisions in any successor order.
- Unauthorized non-storm water flows are already prohibited by Order No. 99-08 DWQ.

**Region 4 Calleguas Creek Metals TMDL – Resolution No. 2006-012**  
**(Effective Date - March 26, 2007)**

**Interim Limits and Final WLAs for Total Recoverable Copper, Nickel, and Selenium**

Interim limits and waste load allocations are applied to receiving water.

**A. Interim Limits**

Constituents	Calleguas and Conejo Creek			Revolon Slough		
	Dry CMC (ug/L)	Dry CCC (ug/L)	Wet CMC (ug/L)	Dry CMC (ug/L)	Dry CCC (ug/L)	Wet CMC (ug/L)
<b>Copper*</b>	23	19	204	23	19	204
<b>Nickel</b>	15	13	(a)	15	13	(a)
<b>Selenium</b>	(b)	(b)	(b)	14	13	(a)

(a) The current loads do not exceed the TMDL under wet conditions; interim limits are not required.

(b) Selenium allocations have not been developed for this reach as it is not on the 303(d) list.

(c) Attainment of interim limits will be evaluated in consideration of background loading data, if available.

**B. Final WLAs for Total Recoverable Copper, Nickel, and Selenium**

**Dry-Weather WLAs in Water Column**

Flow Range	Calleguas and Conejo Creek			Revolon Slough		
	Low Flow	Average Flow	Elevated Flow	Low Flow	Average Flow	Elevated Flow
Copper <sup>1</sup> (lbs/day)	0.04*WER 0.02	0.12*WER 0.02	0.18*WER 0.03	0.03*WER - 0.01	0.06*WER - 0.03	0.13*WER 0.02
Nickel (lbs/day)	0.100	0.120	0.440	0.050	0.069	0.116
Selenium (lbs/day)	(a)	(a)	(a)	0.004	0.003	0.004

<sup>1</sup> If site-specific WERs are approved by the Regional Board, TMDL waste load allocations shall be implemented in accordance with the approved WERs using the equations set forth above. Regardless of the final WERs, total copper loading shall not exceed current loading.

(a) Selenium allocations have not been developed for this reach as it is not on the 303(d) list.

**Wet-Weather WLAs in Water Column**

Constituent	Calleguas Creek	Revolon Slough
Copper <sup>1</sup> (lbs/day)	$(0.00054*Q^2 + 0.032*Q - 0.17)*WER - 0.06$	$(0.0002*Q^2 + 0.0005*Q)*WER$
Nickel <sup>2</sup> (lbs/day)	$0.014*Q^2 + 0.82*Q$	$0.027*Q^2 + 0.47*Q$
Selenium <sup>2</sup> (lbs/day)	(a)	$0.027*Q^2 + 0.47*Q$

<sup>1</sup> If site-specific WERs are approved by the Regional Board, TMDL waste load allocations shall be implemented in accordance with the approved WERs using the equations set forth above. Regardless of the final WERs, total copper loading shall not exceed current loading.

<sup>2</sup> Current loads do not exceed loading capacity during wet weather. Sum of all loads cannot exceed loads presented in the table

(a) Selenium allocations have not been developed for this reach as it is not on the 303(d) list.

Q: Daily storm volume.

**Interim Limits and Final WLAs for Mercury in Suspended Sediment**

Flow Range	Calleguas Creek		Revolon Slough	
	Interim (lbs/yr)	Final (lbs/yr)	Interim (lbs/yr)	Final (lbs/yr)
0-15,000 MGY	3.3	0.4	1.7	0.1
15,000-25,000 MGY	10.5	1.6	4	0.7
Above 25,000 MGY	64.6	9.3	10.2	1.8

MGY: million gallons per year.

In accordance with current practice, a group concentration-based WLA has been developed for all permitted stormwater discharges, including municipal separate storm sewer systems (MS4s), Caltrans, general industrial and construction stormwater permits, and Naval Air Weapons Station Point Mugu. Dischargers will have a required 25%, 50% and 100% reduction in the difference between the current loadings and the load allocations at 5, 10 and 15 years after the effective date, respectively. Achievement of required reductions will be evaluated based on progress towards BMP implementation as outlined in the urban water quality management plans (UWQMPs). If the interim reductions are not met, the dischargers will submit a report to the Executive Officer detailing why the reductions were not met and the steps that will be taken to meet the required reductions.

**Region 4 Calleguas Creek-OC Pesticides, PCBs, and Siltation (Resolution 2005-010)**  
**Effective Date - March 24, 2006**

**Interim Requirements**

<b>Region 4 Calleguas Creek</b> Source: Minor NPDES point sources/WDRs TMDL Completion Date: 3 24 2006 TMDL Type:Creek	<b>Pollutant Stressor</b>	<b>WLA Daily Max (µg/L)</b>	<b>WLA Monthly Ave (µg/L)</b>
	Chlordane 1.2		0.59
	4,4-DDD 1.7		0.84
	4,4-DDE 1.2		0.59
	4,4-DDT 1.2		0.59
	Dieldrin 0.28		0.14
	PCB's 0.34		0.17
	Toxaphene 0.33		0.16

**Region 4 Calleguas Creek-Calleguas Creek Toxicity (Resolution 2005-009)**  
**Effective Date - March 24, 2006**

Minor sources include NPDES permittees other than POTWs and MS4s, discharging to the Calleguas Creek Watershed. A wasteload of 1.0 TUC is allocated to the minor point sources discharging to the Calleguas Creek Watershed. Additionally, the following wasteloads for chlorpyrifos and diazinon are established. Final WLAs apply as of March 24, 2006.

**Chlorpyrifos WLAs, ug/L**

Final WLA  
 (4 day)  
 0.014

**Diazinon WLAs, ug/L**

Final WLA  
 Acute and Chronic  
 0.10

**Region 4 Calleguas Creek-Salts (Resolution 2007-016)**  
**Effective Date – December 2, 2008**

Final Dry Weather Pollutant WLA (mg/L)					
Region 4 Calleguas Creek Source Permitted Stormwater Dischargers TMDL Completion Date: 12 2 2008 TMDL Type:Creek	Critical Condition Flow Rate (mgd)	Chloride (lb/day)	TDS (lb/day)	Sulfate (lb/day)	Boron (lb/day)
Simi	1.39	1738 9849 2897	12		
Las Posas	0.13	157 887 261	N/A		
Conejo	1.26	1576 8931 2627	N/A		
Camarillo	0.06	72	406 119	N/A	
Pleasant Valley (Calleguas)	0.12	150 850 250	N/A		
Pleasant Valley (Revolon)	0.25	314	1778	523	2
Dry Weather Interim Pollutant WLA (mg/L)					
	Chloride (mg/L)	TDS (mg/L)	Sulfate (mg/L)	Boron (mg/L)	

Simi 230.0		1720.0	1289.0	1.3
Las Posas	230	1720	1289	1.3
Conejo 230		1720	1289	1.3
Camarillo 230		1720	1289	1.3
Pleasant Valley (Calleguas)	230	1720	1289	1.3
Pleasant Valley (Revolon)	230	1720	1289	1.3

- Dry- weather waste load allocations apply in the receiving water at the base of each subwatershed. Dry weather allocations apply when instream flow rates are below the 86th percentile flow and there has been no measurable precipitation in the previous 24 hours.
- Because wet weather flows transport a large mass of salts at low concentrations, these dischargers meet water quality objectives during wet weather. No wet weather allocations are assigned.

**Ballona Creek Toxic Pollutants (Resolution No. 2005-008)**  
**Effective Date - January 11, 2006**

Each storm water permittee enrolled under the general construction or industrial storm water permits will receive an individual waste load allocation on a per acre basis, based on the acreage of their facility.

**Metals per Acre WLAs for Individual General**

<b><u>Construction or Industrial Storm Water Permittees (g/yr/ac)</u></b>				
Cadmium	Copper	Lead	Silver	Zinc
0.1	3.4	0.1		13

**Organics per Acre WLAs for Individual General**

<b><u>Construction or Industrial Storm Water Permittees (mg/yr/ac)</u></b>			
Chlordane	DDTs	Total PCBs	Total PAHs
0.04	0.14	2	350

Waste load allocations will be incorporated into the State Board general permit upon renewal or into a watershed specific general construction storm water permit developed by the Regional Board.

Within seven years of the effective date of the TMDL, the construction industry will submit the results of BMP effectiveness studies to determine BMPs that will achieve compliance with the waste load allocations assigned to construction storm water permittees. Regional Board staff will bring the recommended BMPs before the Regional Board for consideration within eight years of the

effective date of the TMDL. General construction storm water permittees will be considered in compliance with waste load allocations if they implement these Regional Board approved BMPs.

All general construction permittees must implement the approved BMPs within nine years of the effective date of the TMDL. If no effectiveness studies are conducted and no BMPs are approved by the Regional Board within eight years of the effective date of the TMDL, each general construction storm water permit holder will be subject to site-specific BMPs and monitoring requirements to demonstrate compliance with waste load allocations.

**Region 4 Marina Del Rey Harbor Toxic Pollutants TMDL (Resolution No. 2005-012)**  
**Effective Date March 22, 2006**

Each storm water permittee enrolled under the general construction or industrial storm water permits will receive an individual waste load allocation on a per acre basis, based on the acreage of their facility.

**Metals per Acre WLAs for Individual General Construction or Industrial Storm Water Permittees (g/yr/ac)**

Copper	Lead	Zinc
2.3	3.1	10

**Organics per acre WLAs for Individual General Construction or Industrial Storm Water Permittees (mg/yr/ac)**

Chlordane	Total PCBs
0.03	1.5

Waste load allocations will be incorporated into the State Board general permit upon renewal or into a watershed specific general construction storm water permit developed by the Regional Board.

Within seven years of the effective date of the TMDL, the construction industry will submit the results of BMP effectiveness studies to determine BMPs that will achieve compliance with the waste load allocations assigned to construction storm water permittees. Regional Board staff will bring the recommended BMPs before the Regional Board for consideration within eight years of the effective date of the TMDL. General construction storm water permittees will be considered in compliance with waste load allocations if they implement these Regional Board approved BMPs.

All general construction permittees must implement the approved BMPs within nine years of the effective date of the TMDL. If no effectiveness studies are conducted and no BMPs are approved by the Regional Board within eight years of the effective date of

the TMDL, each general construction storm water permit holder will be subject to site-specific BMPs and monitoring requirements to demonstrate compliance with waste load allocations.

**Region 4 San Gabriel River and Tributaries-Metals and Selenium (EPA-established TMDL – Effective date: 3/26/07)**

**Wet-weather allocations**

Waterbody	Copper	Lead	Zinc
San Gabriel River Reach 2*		0.8 kg/d	
Coyote Creek**	0.513 kg/d	2.07 kg/d	3.0 kg/d

\*Mass-based allocations are based on a flow of 260 cfs (daily storm volume =  $6.4 \times 10^8$  liters)

\*\*Mass-based allocations are based on a flow of 156 cfs (daily storm volume =  $3.8 \times 10^8$  liters)

**Dry-weather allocations**

The dry-weather copper waste load allocation for general construction storm water permittees that discharge to San Gabriel Reach 1, Coyote Creek, and the Estuary is zero.

The dry-weather selenium allocation for general construction storm water permittees that discharge to San Jose Creek Reach 1 and Reach 2 is 5 µg/L (total recoverable metals).

**Region 4 Upper Santa Clara River Chloride TMDL Adopted by Resolution No 2006-016**  
**Effective Date June 12, 2008**

“Other NPDES dischargers” have a chloride WLA equal to 100 mg/L.

This TMDL was revised by Resolution No 2008-012, which, when it becomes effective, includes the following conditional WLAs for “Other minor NPDES discharges”:

Reach	Concentration-based Conditional WLA for Chloride (mg/L)*
6	150 (12-month Average), 230 (Daily Maximum)
5	150 (12-month Average), 230 (Daily Maximum)
4B	117 (3-month Average), 230 (Daily Maximum)

\*The conditional WLAs for chloride for all point sources shall apply only when chloride load reductions and/or chloride export projects are in operation by the Santa Clarita Valley Sanitation District according to the implementation plan for the TMDL. If these conditions are not met, WLAs shall be based on existing water quality objectives for chloride of 100 mg/L.

**Region 4 The Harbor Beaches of Ventura County-Bacteria (Adopted by Resolution No. 2007-017)**  
**Effective Date – December 18, 2008**

Current and future enrollees in the Statewide Construction Activity Storm Water General Permit in the Channel Islands Harbor subwatershed are assigned WLAs of zero (0) days of allowable exceedances of the single sample limits and the rolling 30-day geometric mean limits.

Single Sample Limits are:

- Total coliform density shall not exceed 10,000/100 ml.
- Fecal coliform density shall not exceed 400/100 ml.
- Enterococcus density shall not exceed 104/100 ml.
- Total coliform density shall not exceed 1,000/100 ml, if the ratio of fecal-to-total coliform exceeds 0.1.

Rolling 30-day Geometric Mean Limits are:

- Total coliform density shall not exceed 1,000/100 ml.
- Fecal coliform density shall not exceed 200/100 ml.
- Enterococcus density shall not exceed 35/100 ml.

**Los Angeles Harbor Bacteria TMDL (Adopted by Resolution No. 2004-001)**  
**Effective Date – March 10, 2005**

Current and future enrollees in the Statewide Construction Activity Storm Water General Permit in the watershed are assigned WLAs of zero (0) days of allowable exceedances of the single sample limits and the rolling 30-day geometric mean.

Single Sample Limits are:

- a. Total coliform density shall not exceed 10,000/100 ml.
- b. Fecal coliform density shall not exceed 400/100 ml.
- c. Enterococcus density shall not exceed 104/100 ml.
- d. Total coliform density shall not exceed 1,000/100 ml, if the ratio of fecal-to-total coliform exceeds 0.1.

Rolling 30-day Geometric Mean Limits are:

- a. Total coliform density shall not exceed 1,000/100 ml.
- b. Fecal coliform density shall not exceed 200/100 ml.
- c. Enterococcus density shall not exceed 35/100 ml.

**Ballona Creek Bacteria TMDL (Adopted by Resolution No. 2006-011)**  
**Effective Date – April 27, 2007**

Current and future enrollees in the Statewide Construction Activity Storm Water General Permit in the watershed are assigned WLAs of zero (0) days of allowable exceedances of the single sample limits and the rolling 30-day geometric mean.

Single Sample Limits are:

- a. Total coliform density shall not exceed 10,000/100 ml.
- b. Fecal coliform density shall not exceed 400/100 ml.
- c. Enterococcus density shall not exceed 104/100 ml.
- d. Total coliform density shall not exceed 1,000/100 ml, if the ratio of fecal-to-total coliform exceeds 0.1.

Rolling 30-day Geometric Mean Limits are:

- a. Total coliform density shall not exceed 1,000/100 ml.
- b. Fecal coliform density shall not exceed 200/100 ml.
- c. Enterococcus density shall not exceed 35/100 ml.

**Region 4 Resolution No. 03-009 Los Angeles River and Tributaries-Nutrients**

Minor Point Sources

Waste loads are allocated to minor point sources enrolled under NPDES or WDR permits including but not limited to Tapia WRP, Whittier Narrows WRP, Los Angeles Zoo WRP, industrial and construction stormwater, and municipal storm water and urban runoff from municipal separate storm sewer systems (MS4s)

Region 4 Minor Point Sources for NPDES/WDR Permits TMDL Effective Date: 3 23 2004  TMDL Type: River	Pollutant Stressor/WLA				
	Total Ammonia (NH <sub>3</sub> )		Nitrate-nitrogen (NO <sub>3</sub> -N)	Nitrite-nitrogen (NO <sub>2</sub> -N)	NO <sub>3</sub> -N + NO <sub>3</sub> -N
	1 Hr Ave mg/l	30 Day Ave mg/l	30 Day Ave mg/l		30 Day Ave mg/l
LA River Above Los Angeles-Glendale WRP (LAG)	4.7 1.6 8.0			1.0	8.0
LA River Below LAG	8.7	2.4	8.0	1.0	8.0
Los Angeles Tributaries 10.1		2.3	8.0	1.0	8.0

**Malibu Creek Attachment A to Resolution No. 2004-019R-Bacteria**

Effective date: 1 24 2006. The WLAs for permittees under the NPDES General Stormwater Construction Permit are zero (0) days of allowable exceedances for the single sample limits and the rolling 30-day geometric mean.

Single Sample Limits are:

- a. Total coliform density shall not exceed 10,000/100 ml.
- b. Fecal coliform density shall not exceed 400/100 ml.
- c. Enterococcus density shall not exceed 104/100 ml.
- d. Total coliform density shall not exceed 1,000/100 ml, if the ratio of fecal-to-total coliform exceeds 0.1.

Rolling 30-day Geometric Mean Limits are:

- a. Total coliform density shall not exceed 1,000/100 ml.
- b. Fecal coliform density shall not exceed 200/100 ml.
- c. Enterococcus density shall not exceed 35/100 ml.

**Region 4 Marina del Rey Harbor, Mothers' Beach and Back Basins**  
**Attachment A to Resolution No. 2003-012-Bacteria**

Effective date: 3 18 2004. Discharges from general construction storm water permits are not expected to be a significant source of bacteria. Therefore, the WLAs for these discharges are zero (0) days of allowable exceedances for the single sample limits and the rolling 30-day geometric mean. Any future enrollees under a general NPDES permit, general industrial storm water permit or general construction storm water permit within the Mdr Watershed will also be subject to a WLA of zero days of allowable exceedances.

Single Sample Limits are:

- a. Total coliform density shall not exceed 10,000/100 ml.
- b. Fecal coliform density shall not exceed 400/100 ml.
- c. Enterococcus density shall not exceed 104/100 ml.
- d. Total coliform density shall not exceed 1,000/100 ml, if the ratio of fecal-to-total coliform exceeds 0.1.

Rolling 30-day Geometric Mean Limits are:

- a. Total coliform density shall not exceed 1,000/100 ml.
- b. Fecal coliform density shall not exceed 200/100 ml.
- c. Enterococcus density shall not exceed 35/100 ml.

**Santa Clara River Nutrients TMDL (Adopted by Resolution No. 2003-011**  
**Effective Date - March 23, 2004**

Concentration-based wasteloads are allocated to municipal, industrial and construction stormwater sources regulated under NPDES permits. For stormwater permittees discharging into Reach 7, the thirty-day WLA for ammonia as nitrogen is 1.75 mg/L and the one-hour WLA for ammonia as nitrogen is 5.2 mg/L; the thirty-day average WLA for nitrate plus nitrite as nitrogen is 6.8 mg/L. For stormwater permittees discharging into Reach 3, the thirty-day WLA for ammonia as nitrogen is 2.0 mg/L and the one-hour WLA for ammonia as nitrogen is 4.2 mg/L; the thirty-day average WLA for nitrate plus nitrite nitrogen is 8.1 mg/L.

**Region 8 RESOLUTION NO. R8-2007- 0024**

Total Maximum Daily Loads (TMDLs) for San Diego Creek,  
Upper and Lower Newport Bay, Orange County, California

Region 8 NPDES Construction Permit TMDL Completion Date: 1 24 1995  TMDL Type: River. Cr, Bay	Organochlorine Compounds							
	Total DDT		Chlordane		Total PCBs		Toxaphene	
	g/day	g/yr	g/day	g/yr	g/day	g/yr	g/day	g/yr
San Diego Creek	.27	99.8	.18*	64.3*	.09*	31.5*	.004	1.5
Upper Newport Bay	.11	40.3	.06	23.4	.06	23.2	X	X
Lower Newport Bay	.04	14.9	.02	8.6	.17	60.7	X	X

\*Red= Informational WLA only, not for enforcement purposes

**Organochlorine Compounds TMDLs Implementation Tasks and Schedule**

Regional Board staff shall develop a SWPPP Improvement Program that identifies the Regional Board’s expectations with respect to the content of SWPPPs, including documentation regarding the selection and implementation of BMPs, and a sampling and analysis plan. The Improvement Program shall include specific guidance regarding the development and implementation of monitoring plans, including the constituents to be monitored, sampling frequency and analytical protocols. The SWPPP Improvement Program shall be completed by *(the date of OAL approval of this BPA)*. **No later than two months** from completion of the Improvement Program, Board staff shall assure that the requirements of the Program are communicated to interested parties, including dischargers with existing authorizations under the General Construction Permit. Existing, authorized dischargers shall revise their project SWPPPs as needed to address the Program requirements as soon as possible but **no later than (three months of completion of the SWPPP Improvement Program)**. Applicable SWPPPs that do not adequately address the Program requirements shall be considered inadequate and enforcement by the Regional Board shall proceed accordingly. The Caltrans and Orange County MS4 permits shall be revised as needed to assure that the permittees communicate the Regional Board’s SWPPP expectations, based on the SWPPP Improvement Program, with the Standard Conditions of Approval.

## APPENDIX 5: Glossary

### **Active Areas of Construction**

All areas subject to land surface disturbance activities related to the project including, but not limited to, project staging areas, immediate access areas and storage areas. All previously active areas are still considered active areas until final stabilization is complete. [The construction activity Phases used in this General Permit are the Preliminary Phase, Grading and Land Development Phase, Streets and Utilities Phase, and the Vertical Construction Phase.]

### **Active Treatment System (ATS)**

A treatment system that employs chemical coagulation, chemical flocculation, or electrocoagulation to aid in the reduction of turbidity caused by fine suspended sediment.

### **Acute Toxicity Test**

A chemical stimulus severe enough to rapidly induce a negative effect; in aquatic toxicity tests, an effect observed within 96 hours or less is considered acute.

### **Air Deposition**

Airborne particulates from construction activities. .

### **Approved Signatory**

A person who has legal authority to sign, certify, and electronically submit Permit Registration Documents and Notices of Termination on behalf of the Legally Responsible Person.

### **Beneficial Uses**

As defined in the California Water Code, beneficial uses of the waters of the state that may be protected against quality degradation include, but are not limited to, domestic, municipal, agricultural and industrial supply; power generation; recreation; aesthetic enjoyment; navigation; and preservation and enhancement of fish, wildlife, and other aquatic resources or preserves.

### **Best Available Technology Economically Achievable (BAT)**

As defined by USEPA, BAT is a technology-based standard established by the Clean Water Act (CWA) as the most appropriate means available on a national basis for controlling the direct discharge of toxic and nonconventional pollutants to navigable waters. The BAT effluent limitations guidelines, in general, represent the best existing performance of treatment technologies that are economically achievable within an industrial point source category or subcategory.

### **Best Conventional Pollutant Control Technology (BCT)**

As defined by USEPA, BCT is a technology-based standard for the discharge from existing industrial point sources of conventional pollutants including biochemical oxygen demand (BOD), total suspended sediment (TSS), fecal coliform, pH, oil and grease.

#### **Best Professional Judgment (BPJ)**

The method used by permit writers to develop technology-based NPDES permit conditions on a case-by-case basis using all reasonably available and relevant data.

#### **Best Management Practices (BMPs)**

BMPs are scheduling of activities, prohibitions of practices, maintenance procedures, and other management practices to prevent or reduce the discharge of pollutants. BMPs also include treatment requirements, operating procedures, and practices to control site runoff, spillage or leaks, sludge or waste disposal, or drainage from raw material storage.

#### **Chain of Custody (COC)**

Form used to track sample handling as samples progress from sample collection to the analytical laboratory. The COC is then used to track the resulting analytical data from the laboratory to the client. COC forms can be obtained from an analytical laboratory upon request.

#### **Coagulation**

The clumping of particles in a discharge to settle out impurities, often induced by chemicals such as lime, alum, and iron salts.

#### **Common Plan of Development**

Generally a contiguous area where multiple, distinct construction activities may be taking place at different times under one plan. A plan is generally defined as any piece of documentation or physical demarcation that indicates that construction activities may occur on a common plot. Such documentation could consist of a tract map, parcel map, demolition plans, grading plans or contract documents. Any of these documents could delineate the boundaries of a common plan area. However, broad planning documents, such as land use master plans, conceptual master plans, or broad-based CEQA or NEPA documents that identify potential projects for an agency or facility are not considered common plans of development.

#### **Daily Average Discharge**

The discharge of a pollutant measured during any 24-hour period that reasonably represents a calendar day for purposes of sampling. For pollutants with limitations expressed in units of mass, the daily discharge is calculated as the total mass of the pollutant discharged during the day. For pollutants with limitations expressed in other units of measurement (e.g., concentration) the daily discharge is calculated as the average measurement of the pollutant

throughout the day (40 CFR 122.2). In the case of pH, the pH must first be converted from a log scale.

**Debris**

Litter, rubble, discarded refuse, and remains of destroyed inorganic anthropogenic waste.

**Direct Discharge**

A discharge that is routed directly to waters of the United States by means of a pipe, channel, or ditch (including a municipal storm sewer system), or through surface runoff.

**Discharger**

The Legally Responsible Person (see definition) or entity subject to this General Permit.

**Dose Rate (for ATS)**

In exposure assessment, dose (e.g. of a chemical) per time unit (e.g. mg/day), sometimes also called dosage.

**Drainage Area**

The area of land that drains water, sediment, pollutants, and dissolved materials to a common outlet.

**Effluent**

Any discharge of water by a discharger either to the receiving water or beyond the property boundary controlled by the discharger.

**Effluent Limitation**

Any numeric or narrative restriction imposed on quantities, discharge rates, and concentrations of pollutants which are discharged from point sources into waters of the United States, the waters of the contiguous zone, or the ocean.

**Erosion**

The process, by which soil particles are detached and transported by the actions of wind, water, or gravity.

**Erosion Control BMPs**

Vegetation, such as grasses and wildflowers, and other materials, such as straw, fiber, stabilizing emulsion, protective blankets, etc., placed to stabilize areas of disturbed soils, reduce loss of soil due to the action of water or wind, and prevent water pollution.

**Field Measurements**

Testing procedures performed in the field with portable field-testing kits or meters.

**Final Stabilization**

All soil disturbing activities at each individual parcel within the site have been completed in a manner consistent with the requirements in this General Permit.

**First Order Stream**

Stream with no tributaries.

**Flocculants**

Substances that interact with suspended particles and bind them together to form flocs.

**Good Housekeeping BMPs**

BMPs designed to reduce or eliminate the addition of pollutants to construction site runoff through analysis of pollutant sources, implementation of proper handling/disposal practices, employee education, and other actions.

**Grading Phase (part of the Grading and Land Development Phase)**

Includes reconfiguring the topography and slope including; alluvium removals; canyon cleanouts; rock undercuts; keyway excavations; land form grading; and stockpiling of select material for capping operations.

**Hydromodification**

Hydromodification is the alteration of the hydrologic characteristics of coastal and non-coastal waters, which in turn could cause degradation of water resources. Hydromodification can cause excessive erosion and/or sedimentation rates, causing excessive turbidity, channel aggradation and/or degradation.

**Identified Organisms**

Organisms within a sub-sample that is specifically identified and counted.

**Inactive Areas of Construction**

Areas of construction activity that are not active and those that have been active and are not scheduled to be re-disturbed for at least 14 days.

**Index Period**

The period of time during which bioassessment samples must be collected to produce results suitable for assessing the biological integrity of streams and rivers. Instream communities naturally vary over the course of a year, and sampling during the index period ensures that samples are collected during a time frame when communities are stable so that year-to-year consistency is obtained. The index period approach provides a cost-effective alternative to year-round sampling. Furthermore, sampling within the appropriate index period will yield results that are comparable to the assessment thresholds or criteria for a given region, which are established for the same index period. Because index

periods differ for different parts of the state, it is essential to know the index period for your area.

**K Factor**

The soil erodibility factor used in the Revised Universal Soil Loss Equation (RUSLE). It represents the combination of detachability of the soil, runoff potential of the soil, and the transportability of the sediment eroded from the soil.

**Legally Responsible Person**

The person who possesses the title of the land or the leasehold interest of a mineral estate upon which the construction activities will occur for the regulated site. For linear underground/overhead projects, it is in the person in charge of the utility company, municipality, or other public or private company or agency that owns or operates the LUP.

**Likely Precipitation Event**

Any weather pattern that is forecasted to have a 50% or greater chance of producing precipitation in the project area. The discharger shall obtain likely precipitation forecast information from the National Weather Service Forecast Office (e.g., by entering the zip code of the project's location at <http://www.srh.noaa.gov/forecast>).

**Maximum Allowable Threshold Concentration (MATC)**

The allowable concentration of residual, or dissolved, coagulant/flocculant in effluent. The MATC shall be coagulant/flocculant-specific, and based on toxicity testing conducted by an independent, third-party laboratory. A typical MATC would be:

The MATC is equal to the geometric mean of the NOEC (No Observed Effect Concentration) and LOEC (Lowest Observed Effect Concentration) Acute and Chronic toxicity results for most sensitive species determined for the specific coagulant. The most sensitive species test shall be used to determine the MATC.

**Natural Channel Evolution**

The physical trend in channel adjustments following a disturbance that causes the river to have more energy and degrade or aggrade more sediment. Channels have been observed to pass through 5 to 9 evolution types. Once they pass through the suite of evolution stages, they will rest in a new state of equilibrium.

**Non-Storm Water Discharges**

Discharges are discharges that do not originate from precipitation events. They can include, but are not limited to, discharges of process water, air conditioner condensate, non-contact cooling water, vehicle wash water, sanitary wastes, concrete washout water, paint wash water, irrigation water, or pipe testing water.

**Non-Visible Pollutants**

Pollutants associated with a specific site or activity that can have a negative impact on water quality, but cannot be seen through observation (ex: chlorine). Such pollutants being discharged are not authorized.

**Numeric Action Level (NAL)**

Level is used as a warning to evaluate if best management practices are effective and take necessary corrective actions. Not an effluent limit.

**Original Sample Material**

The material (i.e., macroinvertebrates, organic material, gravel, etc.) remaining after the subsample has been removed for identification.

**pH**

Unit universally used to express the intensity of the acid or alkaline condition of a water sample. The pH of natural waters tends to range between 6 and 9, with neutral being 7. Extremes of pH can have deleterious effects on aquatic systems.

**Post-Construction BMPs**

Structural and non-structural controls which detain, retain, or filter the release of pollutants to receiving waters after final stabilization is attained.

**Preliminary Phase (Pre-Construction Phase - Part of the Grading and Land Development Phase)**

Construction stage including rough grading and/or disking, clearing and grubbing operations, or any soil disturbance prior to mass grading.

**Project****Qualified SWPPP Developer**

Individual who is authorized to develop and revise SWPPPs.

**Qualified SWPPP Practitioner**

Individual assigned responsibility for non-storm water and storm water visual observations, sampling and analysis, and responsibility to ensure full compliance with the permit and implementation of all elements of the SWPPP, including the preparation of the annual compliance evaluation and the elimination of all unauthorized discharges.

**Qualifying Rain Event**

Any event that produces 0.5 inches or more precipitation with a 48 hour or greater period between rain events.

**R Factor**

Erosivity factor used in the Revised Universal Soil Loss Equation (RUSLE). The R factor represents the erosivity of the climate at a particular location. An

average annual value of R is determined from historical weather records using erosivity values determined for individual storms. The erosivity of an individual storm is computed as the product of the storm's total energy, which is closely related to storm amount, and the storm's maximum 30-minute intensity.

**Rain Event Action Plan (REAP)**

Written document, specific for each rain event, that when implemented is designed to protect all exposed portions of the site within 48 hours of any likely precipitation event.

**Remaining Sub sampled Material**

The material (e.g., organic material, gravel, etc.) that remains after the organisms to be identified have been removed from the subsample for identification. (Generally, no macroinvertebrates are present in the remaining subsampled material, but the sample needs to be checked and verified using a complete Quality Assurance (QA) plan)

**Routine Maintenance**

Activities intended to maintain the original line and grade, hydraulic capacity, or original purpose of a facility.

**Runoff Control BMPs**

Measures used to divert runoff from offsite and runoff within the site.

**Run-on**

Discharges that originate offsite and flow onto the property of a separate project site.

**Revised Universal Soil Loss Equation (RUSLE)**

Empirical model that calculates average annual soil loss as a function of rainfall and runoff erosivity, soil erodibility, topography, erosion controls, and sediment controls.

**Sampling and Analysis Plan**

Document that describes how the samples will be collected, under what conditions, where and when the samples will be collected, what the sample will be tested for, what test methods and detection limits will be used, and what methods/procedures will be maintained to ensure the integrity of the sample during collection, storage, shipping and testing (i.e., quality assurance/quality control protocols).

**Sediment**

Solid particulate matter, both mineral and organic, that is in suspension, is being transported, or has been moved from its site of origin by air, water, gravity, or ice and has come to rest on the earth's surface either above or below sea level.

**Sedimentation**

Process of deposition of suspended matter carried by water, wastewater, or other liquids, by gravity. It is usually accomplished by reducing the velocity of the liquid below the point at which it can transport the suspended material.

**Sediment Control BMPs**

Practices that trap soil particles after they have been eroded by rain, flowing water, or wind. They include those practices that intercept and slow or detain the flow of storm water to allow sediment to settle and be trapped (e.g., silt fence, sediment basin, fiber rolls, etc.).

**Settleable Solids (SS)**

Solid material that can be settled within a water column during a specified time frame. It is typically tested by placing a water sample into an Imhoff settling cone and then allowing the solids to settle by gravity for a given length of time. Results are reported either as a volume (mL/L) or a mass (mg/L) concentration.

**Sheet Flow**

Flow of water that occurs overland in areas where there are no defined channels where the water spreads out over a large area at a uniform depth.

**Site****Soil Amendment**

Any material that is added to the soil to change its chemical properties, engineering properties, or erosion resistance that could become mobilized by storm water.

**Streets and Utilities Phase**

Construction stage including excavation and street paving, lot grading, curbs, gutters and sidewalks, public utilities, public water facilities including fire hydrants, public sanitary sewer systems, storm sewer system and/or other drainage improvements.

**Structural Controls**

Any structural facility designed and constructed to mitigate the adverse impacts of storm water and urban runoff pollution

**Suspended Sediment Concentration (SSC)**

The measure of the concentration of suspended solid material in a water sample by measuring the dry weight of all of the solid material from a known volume of a collected water sample. Results are reported in mg/L.

**Total Suspended Solids (TSS)**

The measure of the suspended solids in a water sample includes inorganic substances, such as soil particles and organic substances, such as algae,

aquatic plant/animal waste, particles related to industrial/sewage waste, etc. The TSS test measures the concentration of suspended solids in water by measuring the dry weight of a solid material contained in a known volume of a sub-sample of a collected water sample. Results are reported in mg/L.

**Toxicity**

The adverse response(s) of organisms to chemicals or physical agents ranging from mortality to physiological responses such as impaired reproduction or growth anomalies.

**Turbidity**

The cloudiness of water quantified by the degree to which light traveling through a water column is scattered by the suspended organic and inorganic particles it contains. The turbidity test is reported in Nephelometric Turbidity Units (NTU) or Jackson Turbidity Units (JTU).

**Vertical Construction Phase**

The Build out of structures from foundations to roofing, including rough landscaping.

**Waters of the United States**

Generally refers to surface waters, as defined by the federal Environmental Protection Agency in 40 C.F.R. § 122.2.<sup>1</sup>

**Water Quality Objectives (WQO)**

Water quality objectives are defined in the California Water Code as limits or levels of water quality constituents or characteristics, which are established for the reasonable protection of beneficial uses of water or the prevention of nuisance within a specific area.

---

<sup>1</sup> The application of the definition of "waters of the United States" may be difficult to determine; there are currently several judicial decisions that create some confusion. If a landowner is unsure whether the discharge must be covered by this General Permit, the landowner may wish to seek legal advice.

## APPENDIX 6: Acronym List

ASBS		Areas of Special Biological Significance
ASTM		American Society of Testing and Materials; Standard Test Method for Particle-Size Analysis of Soils
ATS		Active Treatment System
BASMAA		Bay Area Storm water Management Agencies Association
BAT		Best Available Technology Economically Achievable
BCT	Best	Conventional Pollutant Control Technology
BMP		Best Management Practices
BOD	Biochem	ical Oxygen Demand
BPJ		Best Professional Judgment
CAFO		Confined Animal Feeding Operation
CCR		California Code of Regulations
CEQA		California Environmental Quality Act
CFR		Code of Federal Regulations
CGP		NPDES General Permit for Storm Water Discharges Associated with Construction Activities
CIWQS		California Integrated Water Quality System
CKD		Cement Kiln Dust
COC	Chain	of Custody
CPESC		Certified Professional in Erosion and Sediment Control
CPSWQ		Certified Professional in Storm Water Quality
CSMP		Construction Site Monitoring Program
CTB		Cement Treated Base
CTR		California Toxics Rule
CWA		Clean Water Act
CWC	California	Water Code
CWP		Center for Watershed Protection
DADMAC		Diallyldimethyl-ammonium chloride
DDNR		Delaware Department of Natural Resources
DFG		Department of Fish and Game
DHS		Department of Health Services
DWQ		Division of Water Quality
EC	Electrical	Conductivity
ELAP	Environmental	Laboratory Accreditation Program
EPA	Environmental	Protection Agency
ESA	Environmentally	Sensitive Area
ESC		Erosion and Sediment Control
HSPF		Hydrologic Simulation Program Fortran
JTU	Jackson	Turbidity Units
LID		Low Impact Development
LOEC		Lowest Observed Effect Concentration
LRP	Legally	Responsible Person
LUP		Linear Underground/Overhead Projects

MATC	Maximum	Allowable Threshold Concentration
MDL	Method	Detection Limits
MRR		Monitoring and Reporting Requirements
MS4		Municipal Separate Storm Sewer System
MUSLE		Modified Universal Soil Loss Equation
NAL		Numeric Action Level
NEL		Numeric Effluent Limitation
NICET		National Institute for Certification in Engineering Technologies
NOAA		National Oceanic and Atmospheric Administration
NOEC		No Observed Effect Concentration
NOI		Notice of Intent
NOT		Notice of Termination
NPDES		National Pollutant Discharge Elimination System
NRCS		Natural Resources Conservation Service
NTR		National Toxics Rule
NTU		Nephelometric Turbidity Units
O&M	Operation	and Maintenance
PAC	Polya	luminum chloride
PAM	Polyacryla	mide
PASS	Polya	luminum chloride Silica/sulfate
POC	Pollutants	of Concern
PoP	Probability	of Precipitation
POTW		Publicly Owned Treatment Works
PRDs		Permit Registration Documents
PWS	Planning	Watershed
QAMP		Quality Assurance Management Plan
QA/QC		Quality Assurance/Quality Control
REAP		Rain Event Action Plan
Regional Board		Regional Water Quality Control Board
ROWD		Report of Waste Discharge
RUSLE		Revised Universal Soil Loss Equation
RW	Receiv	ing Water
SMARTS System		Storm water Multi Application Reporting and Tracking
SS	Settleable	Solids
SSC		Suspended Sediment Concentration
SUSMP		Standard Urban Storm Water Mitigation Plan
SW	Storm	Water
SWARM		Storm Water Annual Report Module
SWAMP		Surface Water Ambient Monitoring Program
SWMM		Storm Water Management Model
SWMP		Storm Water Management Program
SWPPP		Storm Water Pollution Prevention Plan
TC	Treatment	Control
TDS	Total	Dissolved Solids

TMDL	Total Maximum Daily Load
TSS Total	Suspended Solids
USACOE	U.S. Army Corps of Engineers
USC United	States Code
USEPA	United States Environmental Protection Agency
USGS	United States Geological Survey
WDID Waste	Discharge Identification Number
WDR Waste	Discharge Requirements
WLA Waste	Load Allocation
WET Whole	Effluent Toxicity
WRCC	Western Regional Climate Center
WQBEL	Water Quality Based Effluent Limitation
WQO Water	Quality Objective
WQS Water	Quality Standard

## APPENDIX 7: State and Regional Water Resources Control Board Contacts

**NORTH COAST REGION (1)**  
5550 Skylane Blvd, Ste. A  
Santa Rose, CA 95403  
(707) 576-2220 FAX: (707)523-0135

**SAN FRANCISCO BAY REGION (2)**  
1515 Clay Street, Ste. 1400  
Oakland, CA 94612  
(510) 622-2300 FAX: (510) 622-2640

**CENTRAL COAST REGION (3)**  
895 Aerovista Place, Ste 101  
San Luis Obispo, CA 93401  
(805) 549-3147 FAX: (805) 543-0397

**LOS ANGELES REGION (4)**  
320 W. 4<sup>th</sup> Street, Ste. 200  
Los Angeles, CA 90013  
(213) 576-6600 FAX: (213) 576-6640

**LAHONTAN REGION (6 SLT)**  
2501 Lake Tahoe Blvd.  
South Lake Tahoe, CA 96150  
(530) 542-5400 FAX: (530) 544-2271

**VICTORVILLE OFFICE (6V)**  
14440 Civic Drive, Ste. 200  
Victorville, CA 92392-2383  
(760) 241-6583 FAX: (760) 241-7308

**CENTRAL VALLEY REGION (5S)**  
11020 Sun Center Dr., #200  
Rancho Cordova, CA 95670-6114  
(916) 464-3291 FAX: (916) 464-4645

**FRESNO BRANCH OFFICE (5F)**  
1685 E St.  
Fresno, CA 93706  
(559) 445-5116 FAX: (559) 445-5910


**REDDING BRANCH OFFICE (5R)**  
415 Knollcrest Drive, Ste. 100  
Redding, CA 96002  
(530) 224-4845 FAX: (530) 224-4857

**COLORADO RIVER BASIN REGION (7)**  
73-720 Fred Waring Dr., Ste. 100  
Palm Desert, CA 92260  
(760) 346-7491 FAX: (760) 341-6820

**SANTA ANA REGION (8)**  
3737 Main Street, Ste. 500  
Riverside, CA 92501-3339  
Phone (951) 782-4130 FAX: (951) 781-6288

**SAN DIEGO REGION (9)**  
9174 Sky Park Court, Ste. 100  
San Diego, CA 92123-4340  
(858) 467-2952 FAX: (858) 571-6972


**STATE WATER BOARD**  
PO Box 1977  
Sacramento, CA 95812-1977  
stormwater@waterboards.ca.gov

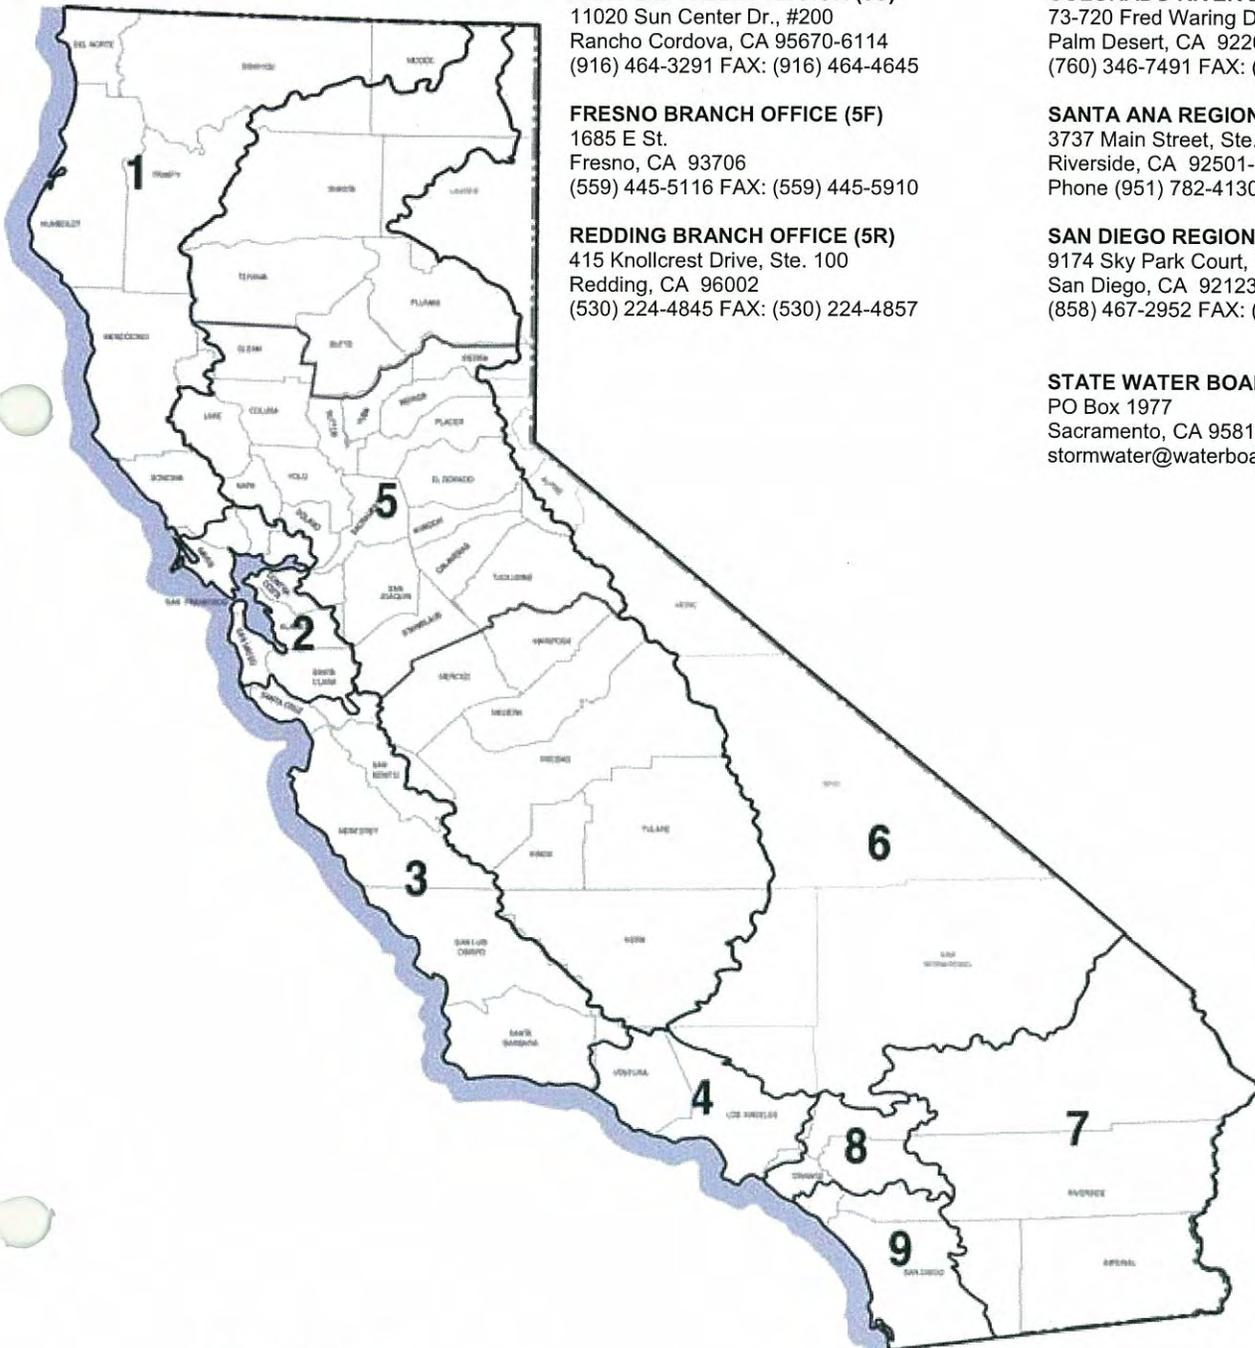

# Appendix III

## Site Map

# VICINITY MAP

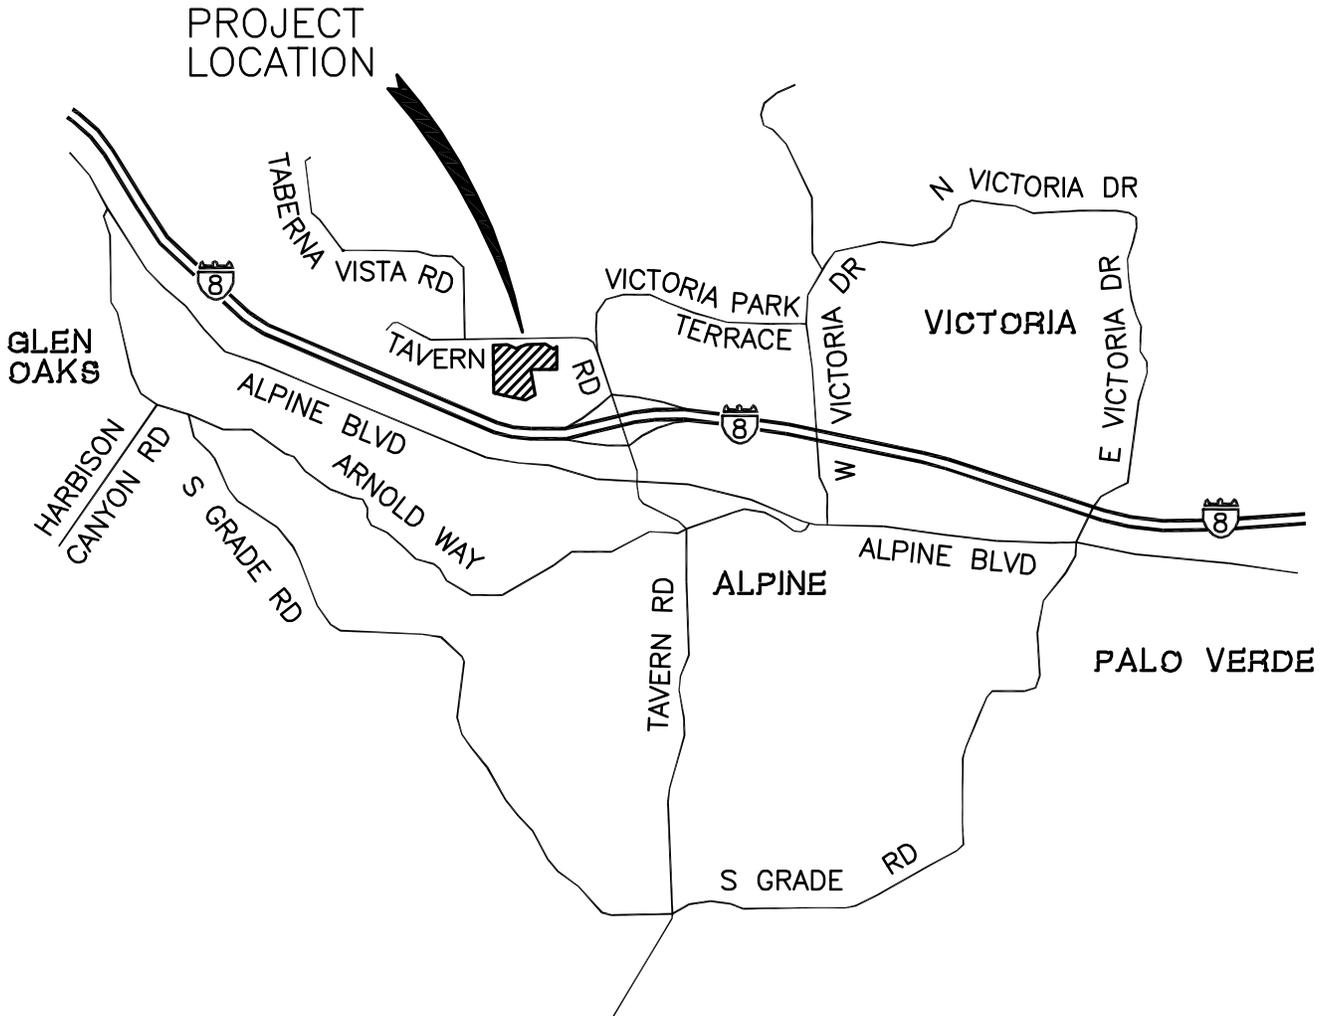

**BUREAU  
VERITAS**

**Bureau Veritas North America, Inc.**

11590 West Bernardo Court Suite 100  
San Diego, CA 92127-1624  
Tel: (858) 451-6100 Fax: (858) 451-2846  
[www.us.bureauveritas.com](http://www.us.bureauveritas.com)

**ALPINE CONSTRUCTION MANAGEMENT  
FACILITY PROJECT  
ALPINE, CA**

SCALE: NTS


DRAWN BY: JL

DATE: 1/26/10

SHEET 1 OF 1

Retain in this Appendix the current  
and all historic Site Maps

P:\16920\_SDGE\_SVPPPs\CADD\EROSION\_CONTROL\_V1-Alpine\_Regional\_HQ\_Facility\Plans\C-7-AlpineFieldOffice-Erosion.dwg [Map - 30-2011] 16.24

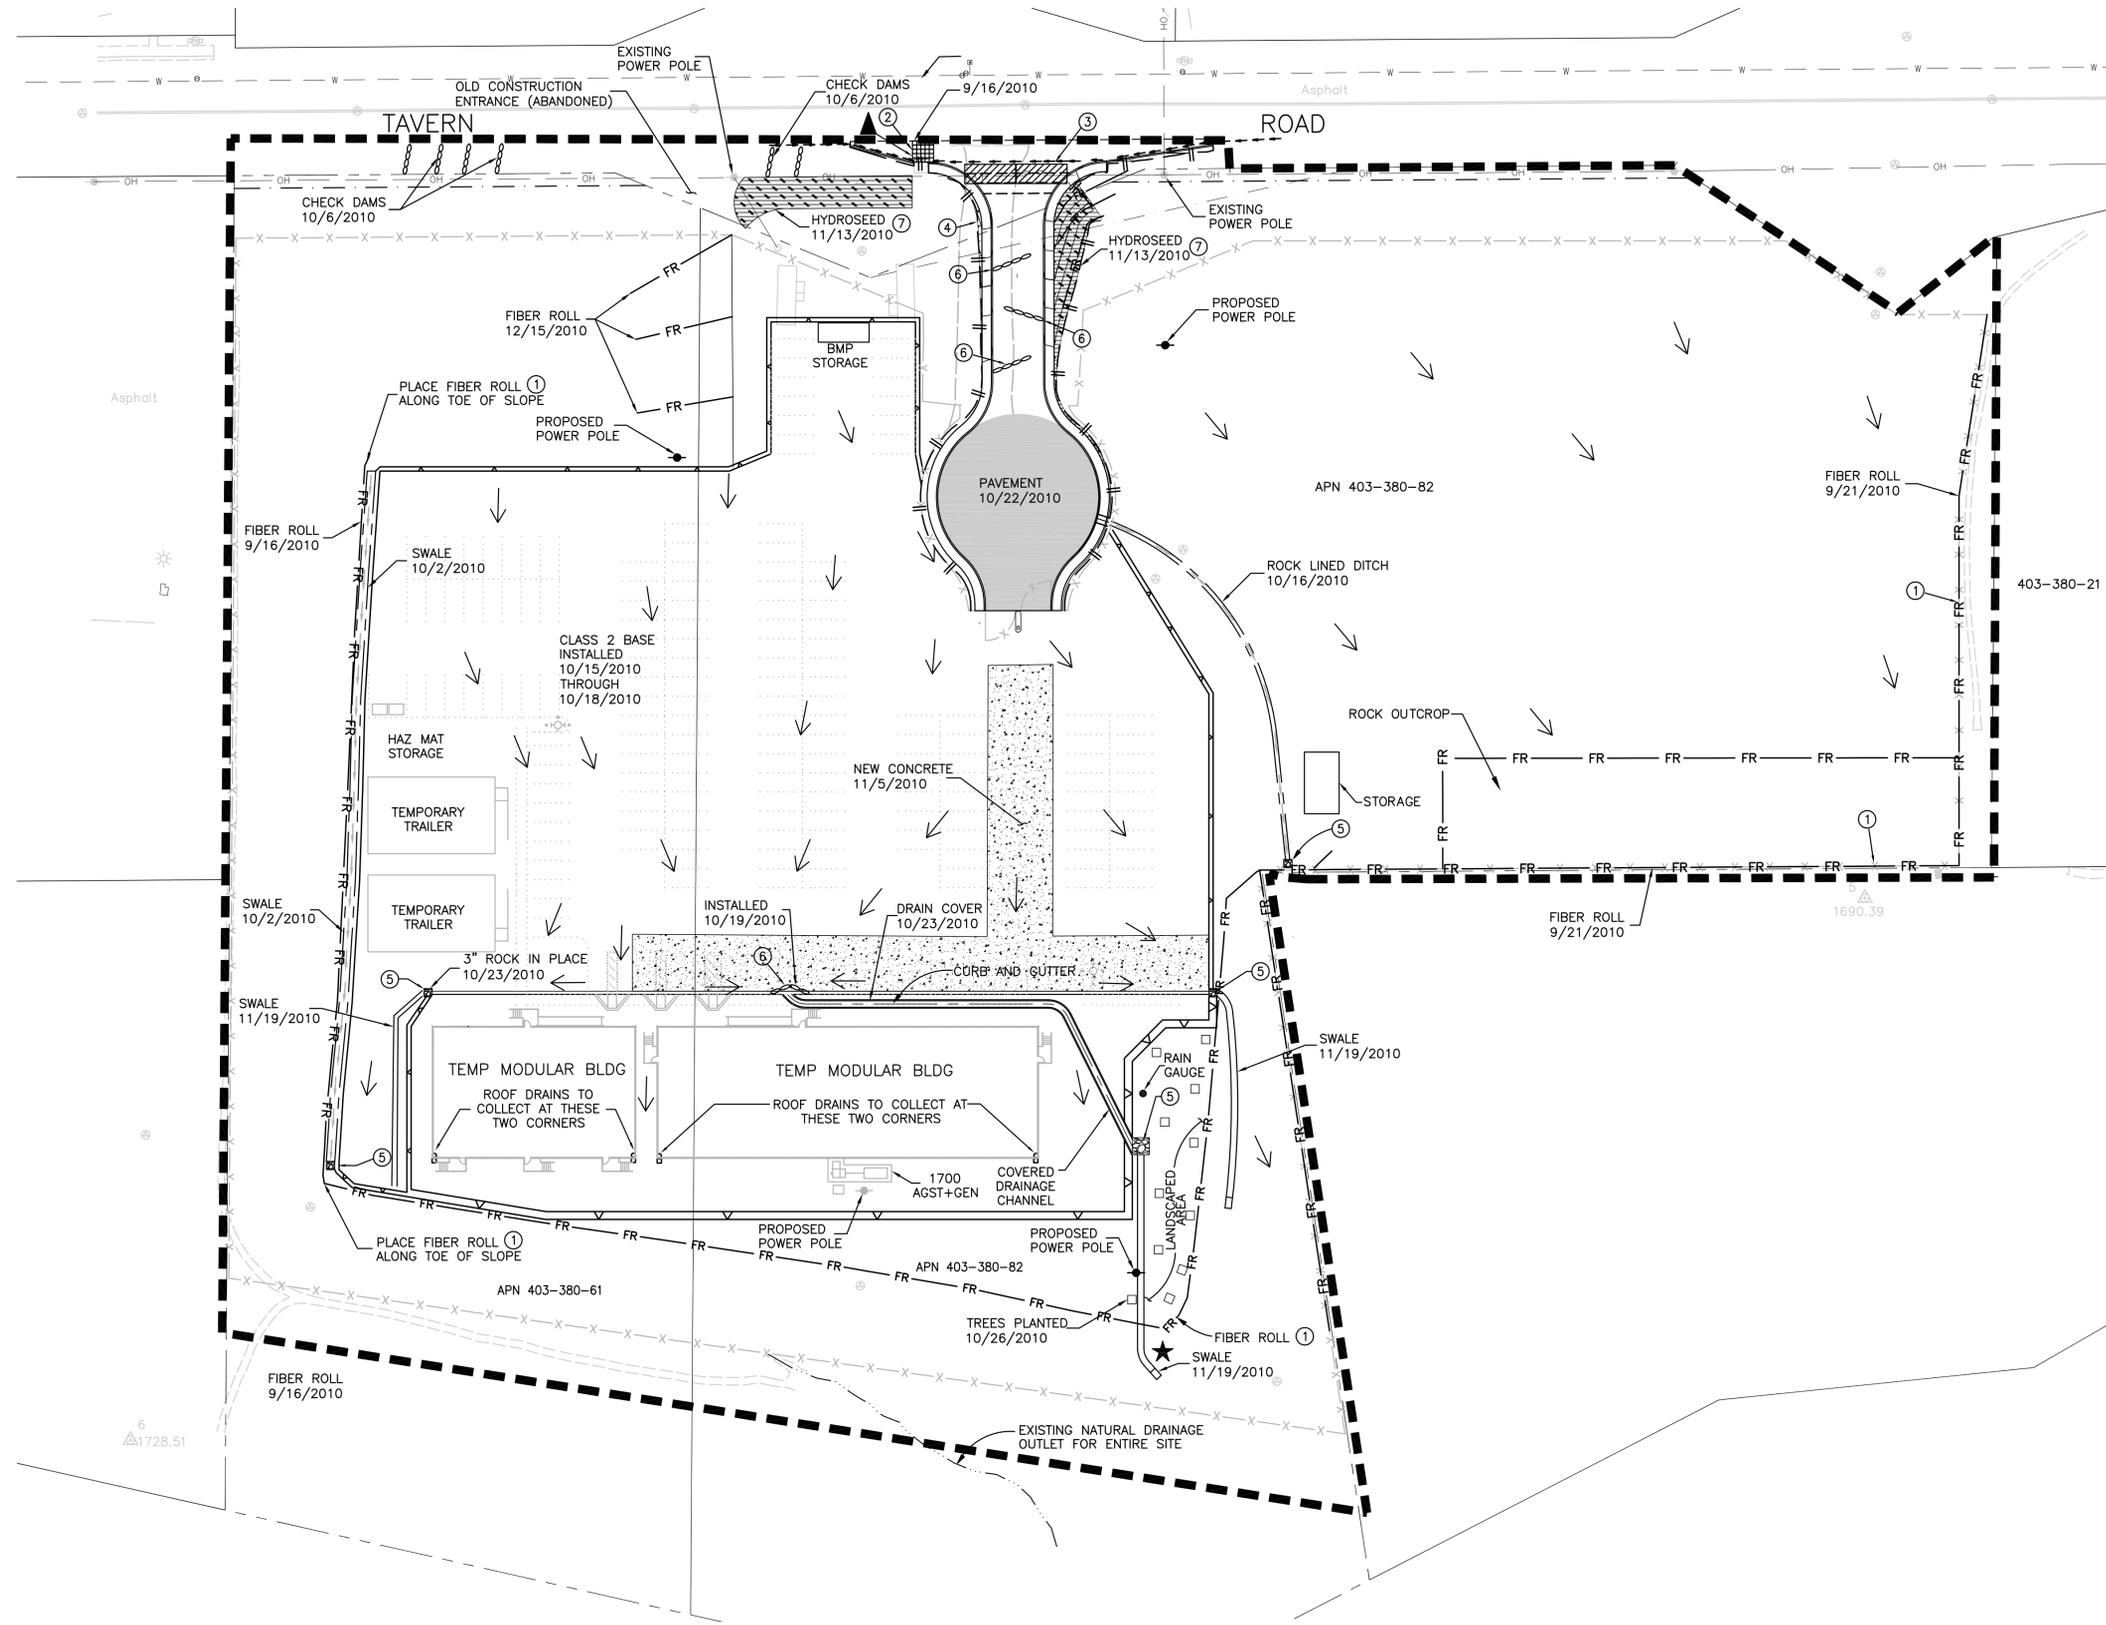

DESCRIPTION	SEE CON. NOTE #	CALTRANS/SDG&E WATER QUALITY CONSTRUCTION BMP MANUAL STD. DWG.	SYMBOL
GRADED SWALE			---
FIBER ROLLS	①	SC-5/BMP-1-03	FR
STORM DRAIN INLET PROTECTION	②	SC-10/BMP-1-06	[Symbol]
STABILIZED CONSTRUCTION ENTRANCE	③	TC-1/BMP-1-07	[Symbol]
DOUBLE NET STRAW BLANKET	④	SS-7/BMP-4-07	[Symbol]
DOWNSPOUT EXIT PROTECTION		SEE DETAIL HEREON	[Symbol]
DOWNSPOUT FILTER		SEE DETAIL HEREON	[Symbol]
RUN ON/RUN OFF WATER SAMPLING LOCATION			▲/★
PROJECT BOUNDARY			---
DIRECTION OF LOT DRAINAGE			→
ENERGY DISSIPATOR	⑤		[Symbol]
GRAVEL BAGS	⑥	SC-4/BMP 1-04	[Symbol]
HYDROSEEDING	⑦		[Symbol]

SCALE: 1"=40'

- CONSTRUCTION NOTES:**
- INSTALL FIBER ROLLS. SEE BMP SHEETS SC-5 AND BMP-1-03 FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - INSTALL STORM DRAIN INLET PROTECTION AT ALL INLETS AND CATCH BASINS. SEE BMP SHEETS SC-10 AND BMP-1-06 FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - INSTALL STABILIZED CONSTRUCTION ENTRANCE/TRACKING CONTROLS. SEE BMP SHEETS TC-1 AND BMP-1-07 FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - INSTALL STRAW BLANKET ON ALL NEWLY GRADED SLOPES. SEE BMP SHEETS SS-7 AND BMP-4-07 FOR APPLICATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - INSTALL ENERGY DISSIPATOR. SEE BMP SHEET SHEET SS-10 FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - INSTALL GRAVEL BAG, TWO BAGS HIGH. SEE BMP SHEETS NS-3/BMP 1-04 FOR INSTALLATION, MAINTENANCE, AND INSPECTION INSTRUCTIONS AND PROCEDURES.
  - PERFORM HYDROSEEDING ON ALL NEWLY GRADED SLOPES. SEE BMP SHEETS SS-4 AND BMP-4-04 FOR APPLICATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.

- EROSION & SEDIMENT CONTROL NOTES:**
- FOR BMP SHEETS REFER TO CALTRANS AND SDG&E WATER QUALITY CONSTRUCTION BEST MANAGEMENT PRACTICES MANUAL (DECEMBER 2002) AND PROJECT'S FINAL APPROVED SWPPP.
  - CONTRACTOR TO DETERMINE THE LOCATION OF CONCRETE WASHOUT AREA. SEE BMP SHEETS WM-8 AND BMP-3-05 FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - CONTRACTOR TO DETERMINE THE LOCATION OF MATERIAL DELIVERY AND STORAGE, STOCKPILE MANAGEMENT, SOLID WASTE MANAGEMENT, HAZARDOUS WASTE MANAGEMENT, SANITARY/SEPTIC WASTE MANAGEMENT, AND LIQUID WASTE MANAGEMENT. SEE BMP SHEETS WM-1/BMP-2-01, BMP-1-08, WM-5/BMP-2-04, WM-6/BMP-2-05, WM-9/BMP-2-07, AND BMP-2-08 RESPECTIVELY, FOR INSTALLATION, INSPECTION, AND MAINTENANCE INSTRUCTIONS AND PROCEDURES.
  - CONTRACTOR TO IMPLEMENT STREET SWEEPING AND VACUUMING (PER BMP SHEETS SC-7/BMP-1-07), PAVING OPERATIONS (PER BMP SHEET BMP-3-02) AND CONCRETE/CORING/SAWCUTTING/CURING/ FINISHING (PER BMP SHEET BMP-3-05) AS NECESSARY.
  - CONTRACTOR TO DETERMINE THE LOCATION FOR VEHICLE AND EQUIPMENT CLEANING, FUELING, AND/OR MAINTENANCE PER BMP SHEETS BMP-3-03 AND BMP-3-04 RESPECTIVELY.
  - CONTRACTOR TO IMPLEMENT THE FOLLOWING CONSTRUCTION BMPs, AS NECESSARY:
    - SCHEDULING, PER BMP SHEET BMP-1-01
    - DUST/WIND EROSION CONTROL, PER BMP SHEET BMP-4-08
    - SPILL CONTROL, PER BMP SHEET BMP-2-03
    - GEOTEXTILES, PLASTIC COVERS AND EROSION CONTROL BLANKETS/MATS PER BMP SHEET BMP-4-07
  - NO WORK HAVING THE POTENTIAL TO CAUSE WATER POLLUTION, AS DETERMINED BY THE ENGINEER, SHALL BE PERFORMED UNTIL THE SWPPP HAS BEEN SUBMITTED TO THE ENGINEER BY THE CONTRACTOR, AND APPROVED.
  - THE CONTRACTOR SHALL CONSIDER OTHER CONTROL MEASURES, AS NECESSARY, TO SUPPLEMENT THE CRITICAL TEMPORARY CONTROL MEASURES SHOWN ON THESE PLANS, IN ORDER TO MEET THE POLLUTION CONTROL OBJECTIVES OF THE SWPPP.
  - THE APPROXIMATE AREA OF SOIL DISTURBANCE FOR THIS PROJECT IS 10.5 ACRES.



**Bureau Veritas North America**  
 11590 West Bernardo Court Suite 100  
 San Diego, CA 92127-1624  
 Tel: (858) 451-6100 Fax: (858) 451-2846  
 www.us.bureauveritas.com

PROPERTY OWNER INFORMATION	
NAME:	TOM C. DYKE
ADDRESS:	1115 TAVERN ROAD ALPINE, CA 91901
TELEPHONE NUMBER:	(619) 992-4380 (24 HOUR CONTACT NUMBER)
SITE A.P.N. NUMBER:	403-380-61&82
SITE ADDRESS:	1010 TAVERN RD ALPINE, CA

REVISIONS			
NO.	DESCRIPTION	APPROVED BY	DATE
1	REVISED EROSION PLANS PER BMP FIELD NOTES		3/30/11

PLAN CHECK/PERMITS	
BUILDING PERMIT PLAN CHECK NUMBER:	1017-20100021
PARCEL MAP NUMBER:	403-380-61&82
ENGINEER OF WORK	
I HEREBY DECLARE THAT I AM THE ENGINEER OF WORK FOR THIS PROJECT AND THAT I HAVE EXERCISED RESPONSIBLE CHARGE OVER THE DESIGN OF THE PROJECT.	
NAME:	DATE:
RCE NO:	EXPIRES:

PRIVATE CONTRACT	
COUNTY OF SAN DIEGO DEPARTMENT OF PUBLIC WORKS	
EROSION CONTROL PLAN FOR: <b>SDG&amp;E ALPINE FIELD OFFICE</b>	
SHEET: C-7	OF SHEETS: 7
APPROVED DIRECTOR OF PUBLIC WORKS	
BY:	DATE:

# **Appendix IV**

## **Calculations / Analysis**



U.S. ENVIRONMENTAL PROTECTION AGENCY

# National Pollutant Discharge Elimination System (NPDES)

[Recent Additions](#) | [Contact Us](#) | [Print Version](#) Search NPDES:

**GO**

[EPA Home](#) > [OW Home](#) > [OWM Home](#) > [NPDES Home](#) >

Basic Information

NPDES Topics

Alphabetical Index

Glossary

About NPDES

eNOI

Municipal MS4s

Construction Activities

Industrial Activities

Road-Related MS4s

Menu of BMPs

Green Infrastructure

Urban BMP Tool

Stormwater Home



## Rainfall Erosivity Factor Calculator for Small Construction Sites

### Facility Information

Facility Name: Alpine Regional Field Offices  
 Start Date: 09/17/2010  
 End Date: 06/15/2013  
 Latitude: 32.8411  
 Longitude: -116.7841

### Erosivity Index Calculator Results

AN EROSIVITY INDEX VALUE OF **91.35** HAS BEEN DETERMINED FOR THE CONSTRUCTION PERIOD OF **09/17/2010 - 06/15/2013**.

A rainfall erosivity factor of 5.0 or greater has been calculated for your site and period of construction. **You do not qualify for a waiver from NPDES permitting requirements.**

Start Over

Stormwater Information
<a href="#">Recent Additions</a>
<a href="#">FAQs</a>
<a href="#">Publications</a>
<a href="#">Regulations</a>
<a href="#">Training &amp; Meetings</a>
<a href="#">Links</a>
<a href="#">Contacts</a>



The documents on this site are best viewed with Acrobat 8.0

[Office of Water](#) | [Office of Wastewater Management](#) | [Disclaimer](#) | [Search EPA](#)

[EPA Home](#) | [Privacy and Security Notice](#) | [Contact Us](#)

Last updated on August 07, 2009 3:37 PM

URL: [http://cfpub.epa.gov/npdes/stormwater/lew/erosivity\\_index\\_result.cfm](http://cfpub.epa.gov/npdes/stormwater/lew/erosivity_index_result.cfm)

	A	B	C
1	<b>Sediment Risk Factor Worksheet</b>		<b>Entry</b>
2	<b>A) R Factor</b>		
3	Analyses of data indicated that when factors other than rainfall are held constant, soil loss is directly proportional to a rainfall factor composed of total storm kinetic energy (E) times the maximum 30-min intensity (I30) (Wischmeier and Smith, 1958). The numerical value of R is the average annual sum of EI30 for storm events during a rainfall record of at least 22 years. "Isoerodent" maps were developed based on R values calculated for more than 1000 locations in the Western U.S. Refer to the link below to determine the R factor for the project site.		
4	<a href="http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm">http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm</a>		
5	<b>R Factor Value</b>		91.35
6	<b>B) K Factor (weighted average, by area, for all site soils)</b>		
7	The soil-erodibility factor K represents: (1) susceptibility of soil or surface material to erosion, (2) transportability of the sediment, and (3) the amount and rate of runoff given a particular rainfall input, as measured under a standard condition. Fine-textured soils that are high in clay have low K values (about 0.05 to 0.15) because the particles are resistant to detachment. Coarse-textured soils, such as sandy soils, also have low K values (about 0.05 to 0.2) because of high infiltration resulting in low runoff even though these particles are easily detached. Medium-textured soils, such as a silt loam, have moderate K values (about 0.25 to 0.45) because they are moderately susceptible to particle detachment and they produce runoff at moderate rates. Soils having a high silt content are especially susceptible to erosion and have high K values, which can exceed 0.45 and can be as large as 0.65. Silt-size particles are easily detached and tend to crust, producing high rates and large volumes of runoff. Use Site-specific data must be submitted.		
8	<a href="#">Site-specific K factor guidance</a>		
9	<b>K Factor Value</b>		0.2
10	<b>C) LS Factor (weighted average, by area, for all slopes)</b>		
11	The effect of topography on erosion is accounted for by the LS factor, which combines the effects of a hillslope-length factor, L, and a hillslope-gradient factor, S. Generally speaking, as hillslope length and/or hillslope gradient increase, soil loss increases. As hillslope length increases, total soil loss and soil loss per unit area increase due to the progressive accumulation of runoff in the downslope direction. As the hillslope gradient increases, the velocity and erosivity of runoff increases. Use the LS table located in separate tab of this spreadsheet to determine LS factors. Estimate the weighted LS for the site prior to construction.		
12	<a href="#">LS Table</a>		
13	<b>LS Factor Value</b>		3.19
14			
15	<b>Watershed Erosion Estimate (=R<sub>x</sub>K<sub>x</sub>LS) in tons/acre</b>		58.2813
16	<b>Site Sediment Risk Factor</b>		<b>Medium</b>
17	Low Sediment Risk: < 15 tons/acre		
18	Medium Sediment Risk: >=15 and <75 tons/acre		
19	High Sediment Risk: >= 75 tons/acre		
20			

Receiving Water (RW) Risk Factor Worksheet	Entry	Score
<b>A. Watershed Characteristics</b>	yes/no	
A.1. Does the disturbed area discharge (either directly or indirectly) to a <b>303(d)-listed waterbody impaired by sediment</b> (For help with impaired waterbodies please visit the link below) or has a <b>USEPA approved TMDL implementation plan for sediment</b> ?:	<b>no</b>	<b>Low</b>
<a href="http://www.waterboards.ca.gov/water_issues/programs/tmdl/integrated2010.shtml">http://www.waterboards.ca.gov/water_issues/programs/tmdl/integrated2010.shtml</a>		
<b>OR</b>		
A.2. Does the disturbed area discharge to a waterbody with designated beneficial uses of SPAWN & COLD & MIGRATORY? (For help please review the appropriate Regional Board Basin Plan)		
<a href="http://www.waterboards.ca.gov/waterboards_map.shtml">http://www.waterboards.ca.gov/waterboards_map.shtml</a>		
<a href="#">Region 1 Basin Plan</a> <a href="#">Region 2 Basin Plan</a> <a href="#">Region 3 Basin Plan</a> <a href="#">Region 4 Basin Plan</a> <a href="#">Region 5 Basin Plan</a> <a href="#">Region 6 Basin Plan</a> <a href="#">Region 7 Basin Plan</a> <a href="#">Region 8 Basin Plan</a> <a href="#">Region 9 Basin Plan</a>		

		Combined Risk Level Matrix		
		<u>Sediment Risk</u>		
<u>Receiving Water Risk</u>	Low	Low	Medium	High
	Low	Level 1	Level 2	
High	Level 2		Level 3	

Project Sediment Risk: **Medium**

Project RW Risk: **Low**

Project Combined Risk: **Level 2**

**Table 3-1  
RUNOFF COEFFICIENTS FOR URBAN AREAS**

Land Use		Runoff Coefficient "C"				
NRCS Elements	County Elements	% IMPER.	Soil Type			
			A	B	C	D
Undisturbed Natural Terrain (Natural)	Permanent Open Space	0*	0.20	0.25	0.30	0.35
Low Density Residential (LDR)	Residential, 1.0 DU/A or less	10	0.27	0.32	0.36	0.41
Low Density Residential (LDR)	Residential, 2.0 DU/A or less	20	0.34	0.38	0.42	0.46
Low Density Residential (LDR)	Residential, 2.9 DU/A or less	25	0.38	0.41	0.45	0.49
Medium Density Residential (MDR)	Residential, 4.3 DU/A or less	30	0.41	0.45	0.48	0.52
Medium Density Residential (MDR)	Residential, 7.3 DU/A or less	40	0.48	0.51	0.54	0.57
Medium Density Residential (MDR)	Residential, 10.9 DU/A or less	45	0.52	0.54	0.57	0.60
Medium Density Residential (MDR)	Residential, 14.5 DU/A or less	50	0.55	0.58	0.60	0.63
High Density Residential (HDR)	Residential, 24.0 DU/A or less	65	0.66	0.67	0.69	0.71
High Density Residential (HDR)	Residential, 43.0 DU/A or less	80	0.76	0.77	0.78	0.79
Commercial/Industrial (N. Com)	Neighborhood Commercial	80	0.76	0.77	0.78	0.79
Commercial/Industrial (G. Com)	General Commercial	85	0.80	0.80	0.81	0.82
Commercial/Industrial (O.P. Com)	Office Professional/Commercial	90	0.83	0.84	0.84	0.85
Commercial/Industrial (Limited I.)	Limited Industrial	90	0.83	0.84	0.84	0.85
Commercial/Industrial (General I.)	General Industrial	95	0.87	0.87	0.87	0.87

\*The values associated with 0% impervious may be used for direct calculation of the runoff coefficient as described in Section 3.1.2 (representing the pervious runoff coefficient, Cp, for the soil type), or for areas that will remain undisturbed in perpetuity. Justification must be given that the area will remain natural forever (e.g., the area is located in Cleveland National Forest).

DU/A = dwelling units per acre

NRCS = National Resources Conservation Service

**Table 819.2B**

**Runoff Coefficients for  
 Developed Areas**

Type of Drainage Area	Runoff Coefficient
<b>Business:</b>	
Downtown areas	0.70 - 0.95
Neighborhood areas	0.50 - 0.70
<b>Residential:</b>	
Single-family areas	0.30 - 0.50
Multi-units, detached	0.40 - 0.60
Multi-units, attached	0.60 - 0.75
Suburban	0.25 - 0.40
Apartment dwelling areas	0.50 - 0.70
<b>Industrial:</b>	
Light areas	0.50 - 0.80 ⇒ 0.60 FOR AREAS 4, 5, 6, 9, & 10
Heavy areas	0.60 - 0.90
Parks, cemeteries:	0.10 - 0.25
Playgrounds:	0.20 - 0.40
Railroad yard areas:	0.20 - 0.40
Unimproved areas:	0.10 - 0.30
<b>Lawns:</b>	
Sandy soil, flat, 2%	0.05 - 0.10
Sandy soil, average, 2-7%	0.10 - 0.15
Sandy soil, steep, 7%	0.15 - 0.20
Heavy soil, flat, 2%	0.13 - 0.17
Heavy soil, average, 2-7%	0.18 - 0.25
Heavy soil, steep, 7%	0.25 - 0.35
<b>Streets:</b>	
Asphaltic	0.70 - 0.95
Concrete	0.80 - 0.95
Brick	0.70 - 0.85
Drives and walks	0.75 - 0.85
<b>Roofs:</b>	0.75 - 0.95



*Existing Site Conditions for Area 1*

Area 1 Runoff Coefficient	=	<u>0.30</u>	(A1)
Area 1 Rainfall Intensity	=	<u>7.3 in/hr</u>	(B1)
Drainage Area 1	=	<u>0.9 Acres</u>	(C1)
Site Area 1 Run-on Discharge (A1) x (B1) x (C1)	=	<u>2.0 ft<sup>3</sup>/sec*</u>	(D1)

*Existing Site Conditions for Area 2*

Area 2 Runoff Coefficient	=	<u>0.30</u>	(A2)
Area 2 Rainfall Intensity	=	<u>8.7 in/hr</u>	(B2)
Drainage Area 2	=	<u>0.6 Acres</u>	(C2)
Site Area 2 Run-on Discharge (A2) x (B2) x (C2)	=	<u>1.6 ft<sup>3</sup>/sec*</u>	(D2)

*Total Site Area Run-on Discharge*

Total Site Area Run-on Discharge (D1) + (D2)	=	<u>3.6 ft<sup>3</sup>/sec*</u>	(D)
--	---	--------------------------------	-----

# Alternative Risk Analysis

Not Applicable

# Sediment Basin Sizing

Not Applicable

# 2006 CWA SECTION 303(d) LIST OF WATER QUALITY LIMITED SEGMENTS REQUIRING TMDLS

SAN DIEGO REGIONAL WATER QUALITY CONTROL BOARD

USEPA APPROVAL DATE: JUNE 28, 2007

REGION TYPE	NAME	CALWATER WATERSHED	POLLUTANT/STRESSOR	POTENTIAL SOURCES	ESTIMATED SIZE AFFECTED	PROPOSED TMDL COMPLETION
9 B	Dana Point Harbor	90114000	Phosphorus	Source Unknown	1.9 Miles	2019
			Sediment Toxicity	Source Unknown	1.9 Miles	2019
9 B		90114000	Indicator bacteria <i>Impairment located at Baby Beach.</i>	Urban Runoff/Storm Sewers Marinas and Recreational Boating Unknown Nonpoint Source Unknown point source	119 Acres	2006
9 R	De Luz Creek	90221000	Iron	Source Unknown	14 Miles	2019
			Manganese	Source Unknown	14 Miles	2019
9 L	El Capitan Lake	90731000	Color	Source Unknown	1454 Acres	2019
			Manganese	Source Unknown	1454 Acres	2019
			pH	Source Unknown	1454 Acres	2019
9 R	Encinitas Creek	90451000	Phosphorus	Source Unknown	3 Miles	2019
				Source Unknown		

# 2006 CWA SECTION 303(d) LIST OF WATER QUALITY LIMITED SEGMENTS REQUIRING TMDLS

## SAN DIEGO REGIONAL WATER QUALITY CONTROL BOARD

USEPA APPROVAL DATE: JUNE 28, 2007

REGION TYPE	NAME	CALWATER WATERSHED	POLLUTANT/STRESSOR	POTENTIAL SOURCES	ESTIMATED SIZE AFFECTED	PROPOSED TMDL COMPLETION
9 C	Pacific Ocean Shoreline, San Clemente HA	90130000	Indicator bacteria	Impairment located at Poche Beach (large outlet), Ole Hanson Beach Club Beach at Pico Drain, San Clemente City Beach at El Portal St. Stairs, San Clemente City Beach at Mariposa St., San Clemente City Beach at Linda Lane, San Clemente City Beach at South Linda Lane, San Clemente City Beach at Lifeguard Headquarters, Under San Clemente Municipal Pier, San Clemente City Beach at Trafalgar Canyon (Trafalgar Ln.), San Clemente State Beach at Riviera Beach, San Clemente State Beach at Cypress Shores.	3.7 Miles	2005
Nonpoint/Point Source						
9 C	Pacific Ocean Shoreline, San Diego HU	90711000	Indicator bacteria	Impairment located at San Diego River Mouth (aka Dog Beach).	0.37 Miles	2005
Nonpoint/Point Source						
9 C	Pacific Ocean Shoreline, San Diequito HU	90511000	Indicator bacteria	Impairment located at San Diequito Lagoon Mouth, Solana Beach.	0.86 Miles	2005
Nonpoint/Point Source						
9 C	Pacific Ocean Shoreline, San Joaquin Hills HSA	90111000	Indicator bacteria	Impairment located at Cameo Cove at Irvine Cove Dr./Riviera Way, Heisler Park-North Urban Runoff/Storm Sewers	0.63 Miles	2005
Unknown Nonpoint Source						
Unknown point source						
9 C	Pacific Ocean Shoreline, San Luis Rey HU	90311000	Indicator bacteria	Impairment located at San Luis Rey River Mouth.	0.49 Miles	2005
Nonpoint/Point Source						
9 C	Pacific Ocean Shoreline, San Marcos HA	90451000	Indicator bacteria	Impairment located at Moonlight State Beach.	0.5 Miles	2005
Nonpoint/Point Source						
9 C	Pacific Ocean Shoreline, Scripps HA	90630000	Indicator bacteria	This listing for indicator bacteria only applies to the Childrens Pool Beach area of this ocean shoreline segment.	3.9 Miles	2019
Nonpoint/Point Source						

project clean water

clean water through local commitment and action

San Diego River Watershed

Plan

Projects

Stewards



- Home
- Overview
- Planning Efforts
- Watersheds
  - San Juan
  - Santa Margarita
  - San Luis Rey
  - Carlsbad
  - San Dieguito
  - Penasquitos
  - San Diego
  - Pueblo
  - Sweetwater
  - Otay
  - Tijuana
- For Kids
- Report Dumping
- Search



**Hydrologic Unit 907.11 - 907.43**

<b>Hydrologic Areas:</b>	Lower San Diego 907.1 San Vicente 907.2 El Capitan 907.3 Boulder Creek 907.4
<b>Major Water Bodies:</b>	San Diego River, El Capitan Reservoir, San Vicente Reservoir, Lake Murray, Boulder Creek, Santee Lakes
<b>CWA 303(d) List:</b>	El Capitan Lake: color, manganese, pH; Famosa Slough and Channel: eutrophic; Forester Creek: fecal coliform (lower 1 mile), dissolved oxygen, pH (upper 3 miles), phosphorus, TDS (lower 1 mile); Murray Reservoir: pH; Pacific Ocean Shoreline (San Diego HU): indicator bacteria; San Diego River (lower): fecal coliform (lower 6 miles), low dissolved oxygen, phosphorus, TDS; San Vicente Reservoir: chloride, color, manganese, pH (high), sulfates
<b>Major Impacts:</b>	Surface water quality degradation, habitat degradation and loss, sediment, invasive species, eutrophication, and flooding
<b>Constituents of Concern:</b>	Coliform bacteria, TDS, nutrients, petroleum chemicals, toxics, and trash
<b>Sources / Activities:</b>	Urban runoff, agricultural runoff, mining

operations, sewage spills, and sand mining

With a land area of approximately 440 square miles, the San Diego River watershed is the second largest hydrologic unit (HU) in San Diego County. It also has the highest population (~475,000) of the County's watersheds and contains portions of the cities of San Diego, El Cajon, La Mesa, Poway, and Santee and several unincorporated jurisdictions. Important hydrologic resources in the watershed include five water storage reservoirs, a large groundwater aquifer, extensive riparian habitat, coastal wetlands, and tidepools. Approximately 58.4% of the San Diego River watershed is currently undeveloped. The majority of this undeveloped land is in the upper, eastern portion of the watershed, while the lower reaches are more highly urbanized with residential (14.9%), freeways and roads (5.5%), and commercial/industrial (4.2%) land uses predominating.

The five reservoirs in the San Diego River watershed supply water to as many as 760,000 residents in the region. Other areas including the [Cleveland National Forest](#), [Mission Trails Regional Park](#), and the river flood plain near Lakeside represent three important undeveloped areas that host a wide variety of intact habitats and endangered species like the arroyo toad, least bell's vireo, and the southwestern pond turtle. In addition, Famosa Slough, near the mouth of the San Diego River contains extremely productive wetlands habitat.

The mouth of the river discharges into the Pacific Ocean at the community of Ocean Beach. Beach postings and closures from elevated levels of coliform bacteria more than doubled between 1996 and 1999 due to urban runoff and sewage spills. Discharge from the San Diego River outlet may also influence water quality in other nearby coastal areas including Sunset Cliffs, Pacific Beach, and Mission Beach. The extensive groundwater resources beneath the San Diego River provide a cost effective and reliable water supply to four local water districts and the City of San Diego. Excessive extraction, increasing total dissolved solids, and MTBE contamination now threatens this resource.

There are many [beneficial water uses within the San Diego River Watershed](#) as designated in the State Water Resources Control Board's [San Diego Region Basin Plan](#).

[Satellite photo of the mouth of the San Diego River.](#)



project clean water

**Leadership, cooperation, and education are the most important tools we have for compelling change.**

[PCW Webmaster](#)

project clean water

clean water through local commitment and action



San Diego River Watershed

Beneficial Water Uses

Plan

Projects

Stewards

**[Return to San Diego River Watershed page](#)**

Beneficial water uses within the San Diego River Watershed as designated in the State Water Resources Control Board's [San Diego Region Basin Plan](#).

- Home
- Overview
- Planning Efforts
- Watersheds
  - San Juan
  - Santa Margarita
  - San Luis Rey
  - Carlsbad
  - San Dieguito
  - Penasquitos
  - San Diego
  - Pueblo
  - Sweetwater
  - Otay
  - Tijuana
- For Kids
- Report Dumping
- Search

Beneficial Uses	Inland Surface Water	Coastal Waters	Reservoirs and Lakes	Ground Water
Municipal and Domestic Supply	X		X	X
Agricultural Supply	X			X
Industrial Service Supply	X	X	X	X
Industrial Process Supply	X		X	X
Navigation		X		
Contact Water Recreation	X	X	X	
Non-Contact Water Recreation	X	X	X	
Commercial and Sport Fishing		X		
Warm Freshwater Habitat	X		X	
Cold Freshwater Habitat	X		X	
Estuarine Habitat		X		
Wildlife Habitat	X	X	X	
Biological Habitats		X		
Rare, Threatened, or End.		X	X	
Marine Habitat		X		
Migration of Aquatic Organisms		X		
Aquaculture		X		
Shellfish Harvesting		X		
Spawning, Reprod. and/ or Early Develop.		X		

Hydropower Generation				<b>x</b>	
--------------------------	--	--	--	----------	--

[Summary of beneficial use designations.](#)

Plan

Projects

Stewards



project clean water

**Leadership, cooperation, and education are the most important tools we have for compelling change.**

[PCW Webmaster](#)

# Post-Construction Water Balance Calculator

Not Applicable

**Appendix V**  
**Construction Materials**

**Inventory of Potential Pollutant Sources Planned to be Used or Stored at the Project Site  
(Store Completed Forms in Appendix V)**

The QSP shall conduct an inventory of the products used and/or expected to be used and the end products that are produced and/or expected to be produced at the site.

A list of possible products that are typically found at construction sites are listed in Appendix V.

Typical Materials Handled, Produced, Stored, Recycled, or Disposed of at the Site	Quantity (e.g., gal, lbs, oz)	Physical Characteristics (e.g., liquid, powder, solid)	Location of Each Material	Proximity to Storm Drain Inlet/Receiving Waters

Based on the table above, describe the degree to which pollutants associated with those materials may be exposed to and mobilized by contact with storm water (i.e., proximity to storm drain inlets or receiving waters).

---

---

---

---

---

---

---

---

Describe BMPs implemented to address these pollutant sources:

---

---

---

---

---

---

---

---

Consider the direct and indirect pathways that pollutants may be exposed to storm water or authorized non-storm water discharges. This shall include an assessment of past spills or leaks, non-storm water discharges, and discharges from adjoining areas

---

---

---

---

---

---

---

---

Based on the inventory and evaluation above, describe the anticipated pollutants for the project below and include these analytes in the CSMP in Appendix X of the SWPPP.

## Appendix V List of Potential Pollutant Sources

Activity	Typical Materials
Asphalt Work	Asphalt (conventional and rubberized) Cold mix Asphalt emulsion Asphalt releases – Monocyclic Terpet Liquid asphalt Aluminate Aluminum sulfate Chip seal, seal coat, tack coat, slurry seal or fog seal
Concrete Work	Concrete curing compound – resin based “Monkey blood” (a retardant compound used for concrete curing) Arbitolor Arabitol (1,2,3,4,5-pentane pentol) pH from concrete sawing or freshly placed or washed off Portland cement products Cement Diesel fuel (sprayed on wooden forms as a non-sticking compound between concrete and wood) Concrete mix Concrete slurry
Cleaning	Various citrus based cleaners Solvents Thinners De-greasers Acids Bases Detergents Trisodium phosphate Sodium Hypochlorite
Vehicle and Equipment	Oil, Grease, Fuel Grease Coolant/antifreeze Diesel Gasoline Lubricants Hydraulic and/or brake fluid Adhesives (glues, caulk, sealants)
Pipe Work	Pipe joint compound ABS and PVC primers Chlorine – water line flushing disinfection

## Appendix V List of Potential Pollutant Sources

Activity	Typical Materials
Painting	Paints Thinners Mineral spirits Latex paint (propylene glycol) Epoxy Silicone
Electrical Work (Materials and Equipment)	Wooden electrical utility poles Electrical transformers and other electrical equipment Pole anchors Guy wires Conductor cable Stub supports Electrical distribution wire
Gas Work (Material and Equipment)	Poly pipe Steel pipe Pipe wrap primer Pipe wrap Pipe pillows Pipe skids or blocks Welding rods Miscellaneous steel fittings Metal and plastic pipelines Valves, pressure regulators Cable and conduit
Landscaping	Herbicides Pesticides Fertilizers Mulch Compost
Brick Work	Etching compounds Acid wash of brick work

## Appendix V List of Potential Pollutant Sources

Activity	Typical Materials
Soil Stabilization	Wood fiber mulch Compost Wood and bark chips Straw mulch Emulsified asphalt Lime Plant gums Bonded fiber matrix Coconut fiber Paper mulch Grass Various proprietary products
Dust Palliatives	EnviroKleen Soil Sement PX-300
Woodwork	Lumber treatment/ preservative Water sealants Stains Sawdust
Structural finishing	Plaster Fire retardants Epoxies Paints (see painting) Tar Urethane

# **Appendix VI**

## **Construction BMP Manual**

# MANUAL



## WATER QUALITY CONSTRUCTION BEST MANAGEMENT PRACTICES MANUAL

*Prepared for:*

Sempra Energy Utilities  
101 Ash Street  
San Diego, CA 92101-3017

URS Project No. 27644947.03B00

December 2002

This page intentionally left blank.

# Table of Contents

---

BMP Program Overview.....	1
BMP Selection and Implementation .....	3
BMP Details.....	9
Sediment Controls.....	11
Waste Management and Material Controls.....	29
Non-Storm Water Discharge Controls.....	39
Erosion Control and Soil Stabilization .....	51

## Tables

Table 1	Best Management Practice Selection and Sequencing Guide.....	5
Table 2	Best Management Practice Selection Worksheet for Utility Activities .....	6

## Appendices

Appendix A	Definitions and Acronyms
------------	--------------------------

This page intentionally left blank.

# BMP PROGRAM OVERVIEW

---

## *Water Quality Construction BMP Manual*

The purpose of this Manual is to provide standardized best management practices (BMPs) to reduce or eliminate pollutants in runoff from Sempra Energy Utilities<sup>1</sup> (SEU) construction projects for water quality protection. This Manual applies to projects conducted by San Diego Gas and Electric Company (SDG&E), Southern California Gas Company (SCG) (hereon known as Utilities or Utility), and their contractors. The utilities service area encompasses 23,000 square miles of diverse terrain throughout most of Central and Southern California, from Visalia to the Mexican border. Utility projects within the service area are conducted in more than 530 communities and in over 200 municipal jurisdictions. Many of these projects throughout the service area are subject to a variety of National Pollutant Discharge Elimination System (NPDES) permits.

Because of the breadth of jurisdictions and applicable permits that apply to utility projects, this Manual has been developed to provide a consistent approach to water quality management to be applied by the utilities and their contractors throughout their service areas. Most construction projects performed by the utilities and their contractors are linear pipeline or electric installations, which are usually short term, fast moving, and are low impact on narrow corridor sections of land. Many of the BMPs presented in this Manual have used the best and most practical pollution prevention features from several sources such as State of California and Caltrans BMPs that integrate well into our unique utility construction activities.

This Manual is organized into three main sections: BMP Program Overview; BMP Selection and Implementation; and BMP Details. The BMP Details section is divided into four functional BMP categories, 1-Sediment Controls, 2-Waste and Materials Management Controls, 3-Non-Storm Water Discharge Controls and 4-Erosion Control and Soil Stabilization. Within each of these categories, specific information, including “When” and “How” to implement the BMP, plus Maintenance and Inspection information are provided for each BMP. Pictures and diagrams are also provided on several BMPs for easy reference.<sup>2</sup>

The Manual is a tool designed to assist with the identification of BMPs appropriate for use on a specific site or project. The Manual provides guidance to SEU in their support for water quality goals and meeting regulatory requirements. The BMP selection process provides users with guidance for typical BMPs that may apply to standard SEU construction projects. During BMP selection, the users of this Manual should take into account the benefits and limitations of each of the BMPs considered in the context of the site conditions. Finally, BMP success is contingent not only on appropriate design and implementation, but on the coordination and communication between the designers, engineers, and the field construction teams.

## *Utility Type Projects*

Most Utility projects are very different from commercial or residential developments, building sites, and Caltrans projects. Utility projects are smaller, short term, long and thin, impacting narrow corridors of land. Utility projects are constantly moving or progressing along the route

---

<sup>1</sup> Sempra Energy Utilities is composed of San Diego Gas & Electric Company and Southern California Gas Company.

<sup>2</sup> Photographs provided in this Manual have been obtained from URS Corp., Great Circle Int'l, LLC, and Caltrans.

# BMP PROGRAM OVERVIEW

---

and thus have minimal exposure of soil or transportable materials to storm water at any one time. Often, utility projects are in the Right-of-Ways of streets or along utility corridors that must be maintained to ensure safe access to electric and gas lines. BMPs usually are only in place for a few days or even hours. Therefore, BMPs will typically be implemented just prior to a forecasted storm event.

## *BMP Field Guide*

The BMP Field Guide is a separate document developed from the Water Quality BMP Manual that contains the condensed BMPs and supporting information. The Field Guide was designed to be a “pocket sized” reference to the BMP Manual. The primary audience for the Field Guide is the SEU Construction and Maintenance crews who perform operations and activities within the utility service territory.

## *Training Program*

The importance of training and of integrating the elements of employee and contractor training for pollution prevention controls into a comprehensive training program is part of the Utilities overall Water Quality Pollution Prevention Program. All applicable company employees and contractors hired by the company have the responsibility to comply with environmental laws, rules, and regulations. Training for the prevention of environmental related incidents is conducted for applicable employees who perform any operation or activity that has the potential to cause a pollutant to be released into the environment. Records are maintained as to when employees have received this training and instruction. Verification of contractor training should also be obtained.

Applicable employees should know and contact their local Environmental Representatives for support and guidance on any aspects of the Training Program.

# BMP SELECTION AND IMPLEMENTATION

---

## *General Protocol*

To select BMPs that are appropriate for a given project, the following steps should be followed:

Step 1 – Identify Activities, Pollutants and Issues of Concern

Step 2 – Evaluate Site Conditions and Select BMPs

Step 3 – Implement, Monitor, and Maintain the BMPs

### ***Step 1 – Identify Activities, Pollutants, and Issues of Concern***

The first step in BMP selection is to identify the project activities, the potential pollutants of concern and the local issues of concern. Project activities may include saw cutting, trenching, excavation, stockpiling of soil, grading and grubbing, access road maintenance, paving, or other activities with the potential to impact storm water and non-storm water discharges. Pollutants of concern may include sediment; petroleum products such as fuel, oil, and grease from vehicle and equipment operation; paving materials such as concrete and asphalt components; other materials used or stored on site, such as pesticides, herbicides, fertilizer, detergents, paint, adhesives, and solvents; and project wastes such as litter, debris, hazardous wastes, and liquid wastes. The local issues of concern may include:

- Proximity to sensitive receiving waters (environmentally sensitive areas or Clean Water Act Section 303(d) listed water bodies, examples: Santa Monica Bay, San Diego Bay).
- Local regulatory requirements influencing BMP selection, or timing of BMP implementation.

### ***Step 2 – Evaluate Site Conditions and Select BMPs***

To assist in BMP selection, this Water Quality Construction BMP Manual presents BMPs that are anticipated to be most applicable to utility construction projects. Utility projects are unique in that they are typically very short-term and fast moving, have minimal exposure of soil or transportable materials at any one time to storm water. The selector should consider any project-specific requirements or factors such as BMP effectiveness, cost, availability, feasibility, and suitability for the site. For example, important site conditions to consider include the amount of soil disturbance, anticipated weather conditions, soil type and erodibility, flow path length, and slope of exposed soil. Selected BMPs can and should be modified to suit the scope of the project and site conditions. Table 1 presents guidelines for BMP selection and implementation at a construction site. Table 2 presents a BMP selection worksheet for utility activities. These implementation guidelines and selection worksheet can be used to select BMPs for a specific project. Finally, a selector may discover a better BMP for their situation not listed in Tables 1 or 2. Environmental Services encourages creative and practical pollution prevention techniques. These new techniques can be shared with others to support the water quality goals of the region.

### ***Step 3 – Implement, Monitor, and Maintain the BMP System***

It is important that selected BMPs be implemented in a sequence that maximizes protection of water quality, be monitored regularly for effectiveness and be maintained as necessary throughout the project. Most BMPs will only be implemented when needed, and/or when a storm

# **BMP SELECTION AND IMPLEMENTATION**

---

event is forecasted or occurs. Table 1 presents a suggested schedule for BMP implementation and sequencing. Steps in this schedule should be reviewed for each project as applicable. All BMPs should be monitored and inspected regularly and particularly before, and after rain events. BMPs should be maintained during a project in accordance with the procedures outlined in the BMP Details Section.

## ***BMP Installation Contractors***

This Water Quality Construction BMP Manual identifies some utility activities and operations that may require outside contractors to install the applicable BMPs. However, the utility crews will implement most BMPs. Most types of BMP materials are readily available from local suppliers.

# BMP SELECTION AND IMPLEMENTATION

Table 1  
BMP SELECTION AND SEQUENCING GUIDE

Step No.	Description	What to Do	BMP Options
1.	Before Construction	Before construction, evaluate, mark, and protect important trees and associated rooting zones, unique areas (e.g., wetlands), and other areas to be preserved, especially in perimeter areas.	4-01, other user-defined BMPs
2.	Site Access Areas (construction entrances, roadways equipment parking areas)	Stabilize site entrances and access roads if applicable prior to earthwork.	1-07, other user-defined BMPs
3.	Storm Drain Inlet Protection	Install inlet protection at down-gradient inlets that project runoff/tracking might impact.	1-06, other user-defined BMPs
4.	Perimeter Sediment Control	Install perimeter sediment controls (silt fence, fiber rolls, etc.) as applicable prior to land disturbing activities. Install additional runoff control measures during construction as needed.	1-02, 1-03, 1-04, 1-05, other user-defined BMPs
5.	Material and Waste Storage Areas	Prepare staging areas, material storage and disposal areas as applicable. Grade to reduce run-on and runoff, install perimeter controls, obtain clean-up materials, plastic covers for stockpiles, etc. prior to storing materials on site.	2-01 through 2-08, 1-08, other user-defined BMPs
6.	Earthwork (trenching, excavation, grading, surface roughening, grubbing)	Begin excavation, trenching, or grading after installing applicable sediment and runoff control measures. Install additional control measures as work progresses as needed.	1-01 through 1-08, other user-defined BMPs
7.	Surface Stabilization (temporary and permanent seeding, mulching)	Apply temporary or permanent soil stabilization measures as applicable on all disturbed areas where work is delayed or completed.	4-01 through 4-08, other user-defined BMPs
8.	Construction and Paving (install utilities, buildings, paving)	Implement applicable control practices as work takes place.	3-01 through 3-9, other user-defined BMPs
9.	Final Stabilization and Landscaping	Stabilize open areas as applicable. Remove temporary control measures and install final stabilization controls appropriately (topsoil, trees and shrubs, permanent seeding, mulching, sodding, riprap)	3-07, 4-03, 4-04, other user-defined BMPs

# BMP SELECTION AND IMPLEMENTATION

Table 2  
BMP SELECTION WORKSHEET FOR UTILITY ACTIVITIES

Sempra Energy Utility BMP No.	BMP Options	Construction				Maint. And Repair			
		Potholing	Overhead Electric	Underground Electric	Underground Gas	Gen. Maint. and Repair	Inspect and Repair	Tree Trimming	Veg. Control
<b>Section 1 Sediment Controls</b>									
Choose from one or more of the following BMP options when applicable:									
BMP-1-01	Scheduling								
BMP-1-02	Silt Fence								
BMP-1-03	Fiber Rolls								
BMP-1-04	Gravel Bag Berm								
BMP-1-05	Sand bag Barrier								
BMP-1-06	Storm Drain Inlet Protection								
BMP-1-07	Tracking Controls								
BMP-1-08	Stockpile Management								
Other-User Defined	BMP Description:								
<b>Section 2 Waste Management and Material Controls</b>									
Choose from one or more of the following BMP options when applicable:									
BMP-2-01	Material Delivery and Storage								
BMP-2-02	Material Use								
BMP-2-03	Spill Control								
BMP-2-04	Solid Waste Management								
BMP-2-05	Hazardous Materials/Waste Management								
BMP-2-06	Contaminated Soil Management								
BMP-2-07	Sanitary/Septic Waste Management								
BMP-2-08	Liquid Waste Management								
Other-User Defined	BMP Description:								
<b>Section 3 Non-Storm Water Discharge Controls</b>									
Choose from one or more of the following BMP options when applicable:									
BMP-3-01	Dewatering Operations								
BMP-3-02	Paving Operations								

# BMP SELECTION AND IMPLEMENTATION

Table 2 (continued)  
BMP SELECTION WORKSHEET FOR UTILITY ACTIVITIES

Sempra Energy Utility BMP No.	BMP Options	Construction				Maint. And Repair			
		Potholing	Overhead Electric	Underground Electric	Underground Gas	Gen. Maint. and Repair	Inspect and Repair	Tree Trimming	Veg. Control
<b>Section 3 Non-Storm Water Discharge Controls (Continued)</b>									
BMP-3-03	Vehicle and Equipment Washing								
BMP-3-04	Vehicle and Equipment Fueling								
BMP-3-05	Concrete/Coring/Sawcutting and Drilling Waste Management								
BMP-3-06	Dewatering Utility Substructures and Vaults								
BMP-3-07	Vegetation Management including Mechanical and Chemical Weed Control								
BMP-3-08	Over-Water Protection								
BMP-3-09	Removal of Utility Location/Mark-Out Paint								
Other-User Defined	BMP Description:								
<b>Section 4 Erosion Control and Soil Stabilization</b>									
<b>Choose from one or more of the following BMP options when applicable:</b>									
BMP-4-01	Preservation of Existing Vegetation								
BMP-4-02	Temporary Soil Stabilization								
BMP-4-03	Hydraulic Mulch								
BMP-4-04	Hydroseeding								
BMP-4-05	Soil Binders								
BMP-4-06	Straw Mulch								
BMP-4-07	Geotextiles, Plastic Covers and Erosion Control Blankets/Mats								
BMP-4-08	Dust (Wind Erosion) Control								
Other-User Defined	BMP Description:								

# BMP SELECTION AND IMPLEMENTATION

---

This page intentionally left blank.

# BMP DETAILS

---

This Section provides details for the selection and implementation of BMPs for the most common utility construction activities. Once the BMP objectives are defined, it is necessary to identify the category or categories of BMPs that are best suited to meet each objective. A category is a grouping of BMPs related in how they prevent pollution. The four categories are:

- Section 1 – Sediment Controls
- Section 2 – Waste Management and Material Controls
- Section 3 – Non-Storm Water Discharge Controls
- Section 4 – Erosion Control and Soil Stabilization


# BMP DETAILS

---

This page intentionally left blank.

# BMP DETAILS

---



## Section 1 – Sediment Controls

Sediment particles (soil/dust) from utility activities can be transported to a different location by wind or water flow. Once these particles have become detached, they are considered a pollutant. Sediment Controls include any method that traps the soil particles after they have been detached and moved by wind or water. Sediment Controls are usually passive systems that rely on filtering or settling the particles out of the water or wind that is transporting them. The sediment that has accumulated by the BMPs can be disposed of as excess soil on the construction site. Sediment Controls presented in this Manual include the following:

- BMP 1-01 Scheduling
- BMP 1-02 Silt Fence
- BMP 1 03 Fiber Rolls
- BMP 1-04 Gravel Bag Berm
- BMP 1-05 Sand bag Barrier
- BMP 1-06 Storm Drain Inlet Protection
- BMP 1-07 Tracking Controls
- BMP 1-08 Stockpile Management

# BMP DETAILS

---

This page intentionally left blank.

# SEDIMENT CONTROLS

## Scheduling

BMP 1-01



**When** Scheduling must be considered for applicable projects year-round.

**How** Use the following measures as applicable:


- Consider scheduling major soil disturbing activities or activities near environmentally sensitive areas (e.g., adjacent to water bodies) during the non-rainy season.
- Monitor the weather forecast for seasonable and unseasonable rain events. Weather information is available from the following sources:
  - San Diego: [www.wrh.noaa.gov/sandiego/index.shtml](http://www.wrh.noaa.gov/sandiego/index.shtml) or (619) 289-1212
  - Los Angeles/Oxnard: [www.nwsla.noaa.gov](http://www.nwsla.noaa.gov) or (805) 988-6610
  - AccuWeather: [www.accuweather.com](http://www.accuweather.com)
- Always be prepared to deploy erosion and sediment control and soil stabilization BMPs. Off site sediment discharges can occur during the non-rainy season because of unseasonable rainfall, wind, non-storm water discharges, and vehicle tracking and must be prevented.

**PLUS, DURING THE RAINY SEASON (October 1–May 1, Desert regions differ August 1- May 30)**

- Sequence work to minimize soil-disturbing activities during forecasted rain events.
- Limit disturbed soil area to the amount of acreage that can be protected prior to a forecasted rain event.
- Stabilize disturbed soil areas as soon as practical, and, at a minimum, prior to a forecasted rain event.
- Protect environmentally sensitive areas, such as drainage channels, streams, and natural watercourses.
- When rainfall is forecast, adjust the construction schedule to implement soil stabilization and sediment controls on all disturbed areas prior to the onset of rain.
- Review applicable scheduling and sequencing of construction activities throughout the project to minimize the amount or time that soil is exposed and the total area of exposed soil.
- Inspect erosion and sediment controls prior and after each storm event, and routinely throughout the rainy season (to be consistent with all the other BMPs).

### Maintenance and Inspection

### Pictures

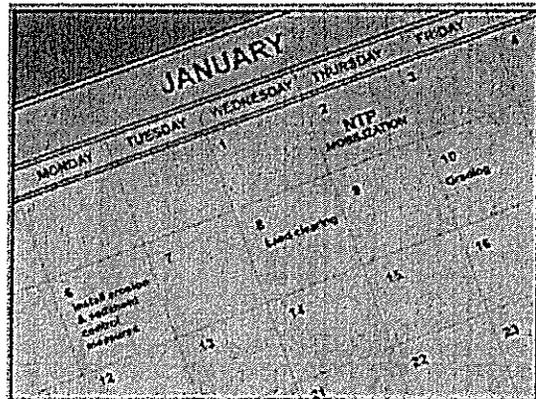

**When**

Silt fences are temporary linear sediment barriers made of permeable fabric designed to intercept and slow the flow of sediment-laden sheet flow runoff. Silt fences allow sediment to settle from runoff before water leaves the construction site.

Silt fences are placed:

- Below the toe of exposed and erodible slopes.
- Down-slope of exposed soil areas.
- Around temporary stockpiles.
- Along streams and channels.
- Along the perimeter of a project.


**How**

- Construct silt fences with a setback of at least 3 feet from the toe of a slope in areas suitable for temporary ponding or deposition of sediment. Where a 3-foot setback is not practicable, construct as far from the toe of the slope as practicable.
- Generally, silt fences shall be used in conjunction with soil stabilization source controls up slope to provide effective control, particularly for slopes adjacent to water bodies or Environmentally Sensitive Areas.
- Construct the length of each reach (length of fence) so that the change in base elevation along the reach does not exceed 1/3 the height of the barrier; each reach should not exceed 500 feet. The last 6 feet of the reach should be turned upslope.
- The maximum length of slope draining to the silt fence should be 200 ft or less.
- Excavate a trench to place the bottom of the silt fence into that is not wider or deeper than necessary.
- Key-in, or bury the bottom of silt fence fabric in trench and tamp into place. If it is not feasible to trench along the slope contour, use sand bags or backfilling to key in the bottom of the fabric.
- Install fence post at least 12 inches below grade on down slope side of trench.
- Silt fences should not be considered for installation below slopes steeper than 1:1 (vertical : horizontal) or that contain a high number of rocks or loose dirt clods.

**Maintenance and Inspection**

- Repair or replace split, torn, slumping, undercut or weathered fabric.
- Inspect silt fences prior and after each storm event, and routinely throughout the rainy season.
- Remove accumulated sediment when it reaches one third (1/3) of the barrier height. Removed sediment shall be incorporated in the project at appropriate locations or disposed of at an SCG/SDG&E-approved site
- Silt fences that are damaged and become unsuitable for the intended purpose shall be removed and disposed of and replaced with new silt fence barriers.
- Remove silt fence when no longer needed. Fill and compact post-holes and anchorage trench, remove sediment accumulation, and grade fence alignment to blend with adjacent ground.

Pictures

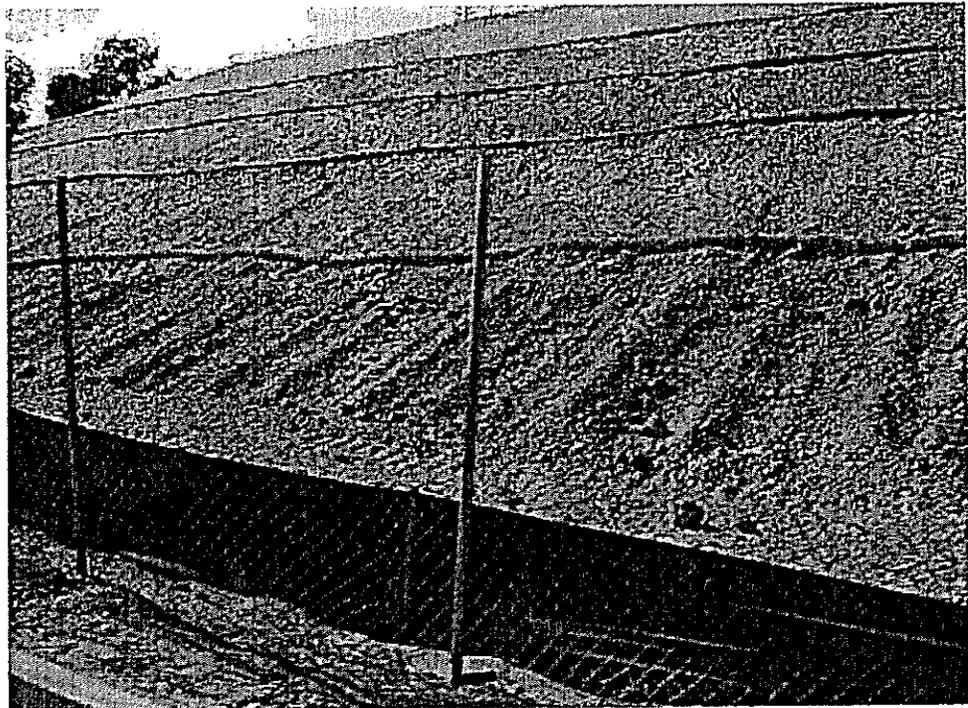


Silt fence installed at the toe of an erodible slope. Note use is combined with fiber rolls and serves as perimeter control.

# SEDIMENT CONTROLS

## Fiber Rolls

BMP 1-03



### When

A fiber roll consists of straw, flax or other similar materials that are rolled and bound into a tight roll that is generally placed on the face of slopes at regular intervals to intercept runoff, reduce flow velocity, release the runoff as sheet flow and provide the removal of sediment.

- May be used along the top, face and at grade breaks of exposed and erodible slopes to shorten slope length and spread runoff as sheet flow.
- Fiber rolls may be used as check dams.
- Fiber Rolls can also be used where flows are moderately concentrated, such as ditches, swales, and storm drain inlets (Storm Drain Inlet Protection to divert and/or detain flows.).
- Fiber rolls are appropriate for perimeter site control or along streams, channels, storm drain inlets, or around stockpiles to intercept sediment laden storm water and non-storm water runoff.

### How

#### Installation

- Locate fiber rolls on level contours spaced 8 to 20 feet apart along the face of the slope.
- Its best to stake fiber rolls into a 2 to 4 inch deep trench.
- Drive stakes into fiber rolls at a minimum of 4-foot intervals
- If more then one fiber roll is placed in a row, fiber rolls should be butted together and not overlapped.

#### Removal

- If used on slopes, fiber rolls are typically left in place.
- If used as Storm Drain Inlet Protection, stockpile control, or other temporary control measures, the fiber rolls should be removed at the completion of the construction project.
- If fiber rolls are removed, collect and dispose of fiber roll and sediment accumulation as appropriate. Fill and compact holes, trenches, depressions, or any other ground disturbance to blend with adjacent ground.

### Maintenance and Inspection

- Repair or replace spilt, torn, unraveling, or slumping fiber rolls.
- Inspect fiber rolls if rain is forecasted, perform maintenance as needed.
- Inspect fiber rolls prior and after each storm event, and routinely throughout the rainy season.

Pictures



Fiber rolls as perimeter control



Fiber roll installation on the face of a slope.



**When**

A gravel bag berm consists of a single row of gravel bags that are installed end-to-end to form a barrier across a slope to intercept runoff, reduce its flow velocity, release the runoff as sheet flow and provide some sediment removal. Gravel bags can also be used where flows are moderately concentrated, such as ditches, swales, and storm drain inlets (Storm Drain Inlet Protection to divert and/or detain flows). Gravel bag berms are appropriate for perimeter site control or along streams, channels, storm drain inlets, or around stockpiles to intercept sediment laden storm water and non-storm water runoff. Use gravel bag berms:

- Where it is desirable to filter sediment in runoff. Note that gravel bag berms are generally more permeable than sand bags. Sand bag barriers should be used in cases where it is desirable to block and pond flows (e.g., for containment of non-storm water flows).
- Along the face and at grade breaks of exposed and erodible slopes to shorten slope length and spread runoff as sheet flow.
- On a project-by-project basis to maximize effectiveness.
- Gravel bags may be implemented with other BMPs to maximize sediment containment.


**How**

- When used as a linear control for sediment removal:
  - Install along a level contour.
  - Turn ends of gravel bag row up slope to prevent flow around the ends.
  - Generally, gravel bag barriers are used in conjunction with temporary soil stabilization controls up slope to provide effective control.
- When used for concentrated flows:
  - Stack gravel bags to required height. When the height requires 3 rows or more, use a pyramid approach.
  - Upper rows of gravel bags shall overlap joints in lower rows.
- Construct gravel bag barriers with a setback of at least 3 feet from the toe of a slope. Where a 3-foot setback is not practicable, construct as far from the toe of the slope as practicable.

**Maintenance and Inspection**

- Inspect gravel bag berms prior and after each storm event, and routinely throughout the rainy season.
- Reshape or replace gravel bags as needed.
- Repair washouts or other damages as needed.
- Inspect gravel bag berms for sediment accumulations and remove sediments when accumulation reaches one-third of the berm height. Removed sediment shall be incorporated in the project at appropriate locations or disposed of at an SCG/SDG&E-approved site.
- Remove gravel bag berms when no longer needed. Remove sediment accumulation, and clean, re-grade, and stabilize the area. Removed sediment shall be incorporated in the project at appropriate locations or disposed of at an SCG/SDG&E-approved site.

Pictures

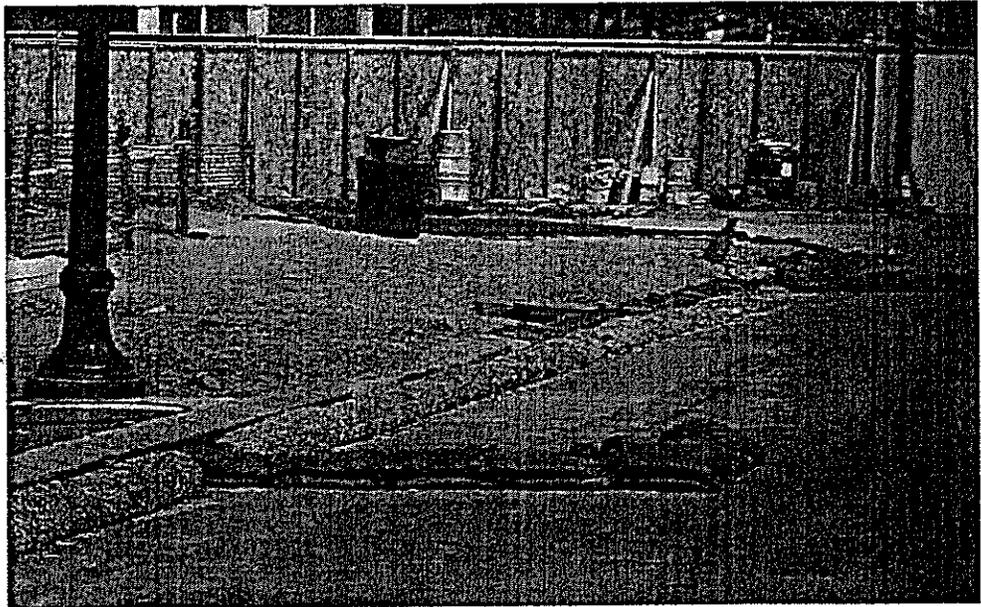

Gravel bags and fiber rolls used as a perimeter sediment control system.



Gravel bags used as perimeter control.

# SEDIMENT CONTROLS

## Sand Bag Barrier

BMP 1-05



### When

A sand bag barrier is a temporary linear sediment barrier consisting of stacked sand bags, designed to intercept and slow sediment-laden storm water and non-storm water runoff. Sand bag barriers allow sediment to settle from runoff before water leaves the construction site.

- Sand bags can be used where flows are moderately concentrated, such as ditches, swales, and storm drain inlets to divert and/or detain flows. See BMP on Storm Drain Inlet Protection.
- To divert or direct flow away from disturbed slopes or create a temporary sediment basin.
- During construction activities in streambeds when the contributing drainage area is 1 to 5 acres.
- To capture and detain non-storm water flows until proper cleaning operations occur.
- When site conditions or construction sequencing require adjustments or relocation of the barrier to meet changing field conditions and needs during construction.
- To temporarily close or continue broken, damaged or incomplete curbs.

### Sand bag barriers are used:

- Where it is desirable to block and pond flow (e.g., for containment of non-storm water flows). Use caution when using sand bag barriers in traffic areas or other areas where potential flooding is not desirable.
- Along the perimeter of a site, vehicle and equipment fueling and maintenance areas, chemical storage areas, or stockpiles.
- Below the toe or down slope of exposed and erodible slopes.
- Parallel to streams, channels, and roadways.
- Across channels to serve as a barrier for utility trenches or provide a temporary channel crossing for construction equipment, or to reduce stream impacts.

### How

- When used as a linear control for sediment removal:
  - Install along a level contour.
  - Turn ends of sand bag row up slope to prevent flow around the ends.
  - Generally, sand bag barriers shall be used in conjunction with temporary soil stabilization controls up slope to provide effective control.
- When used for concentrated flows:
  - Stack sand bags to required height. When the required height is three rows or more, use a pyramid approach. Upper rows of sand bags shall overlap joints in lower rows.
  - Construct sand bag barriers with a setback of at least 3 feet from the toe of a slope. Where a 3-foot setback is not practicable, construct as far from the toe of the slope as practicable.

# SEDIMENT CONTROLS

## Sand Bag Barrier

BMP 1-05



### Maintenance and Inspection

- Inspect sand bag barriers prior and after each storm event, and routinely throughout the rainy season.
- Repair washouts or other damages as needed, or as directed by the projects Environmental Representative.
- Inspect sand bag barriers for sediment accumulations and remove sediments when accumulation reaches one-third the barrier height.
- Remove sand bags when no longer needed. Remove sediment accumulation, and clean, re-grade, and stabilized the area. Incorporate removed sediment at appropriate project locations or dispose of at an SCG/SDG&E-approved site.

### Pictures



Sand bags used as perimeter control.

# SEDIMENT CONTROLS

## Storm Drain Inlet Protection

BMP 1-06



**When** A device used at storm drain inlets to protect against the discharge of sediment-laden storm water and non-storm water runoff from construction activities. The device develops a pond behind it giving the sediment time to settle out before discharge to the storm drain. Do not construct such that runoff will result in:

- Ponding into road traffic or onto erodible surfaces or slopes, or
- Overflowing onto the sidewalk

This BMP is required on all construction projects where sediment laden surface runoff may enter a storm drain inlet and watercourses.


**How**

- Identify downstream storm drain inlets that have the potential to runoff from construction activities.
- Where a storm drain inlet is on or at the bottom of a slope, a series of small check dams (i.e., gravel bags) constructed at intervals along the slope may be required to slow the runoff.
- Select appropriate protection and construct inlet protection based on the configuration of inlets at the site.


### Maintenance and Inspection

- Inspect inlet protection devices prior and after storm event, and routinely throughout the rainy season.
- Remove inlet protection devices at the end of the construction period, or when the inlet can no longer be impacted by the project.
- During inspections:
  - Inspect bags, silt fence, or filter fabric for holes, gashes, and snags.
  - Check gravel bags for proper arrangement and displacement; and
  - Remove the sediment behind the barrier when it reaches one-third the height of the barrier. Removed sediment should be incorporated in the project or disposed of at an approved Utility disposal site.

Pictures

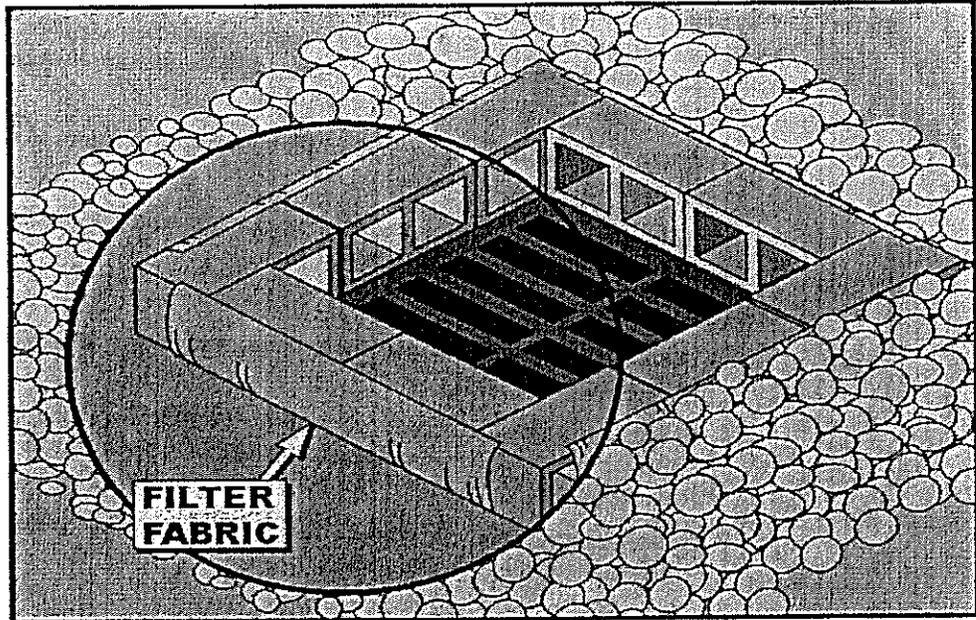

Block and gravel-type inlet protection.

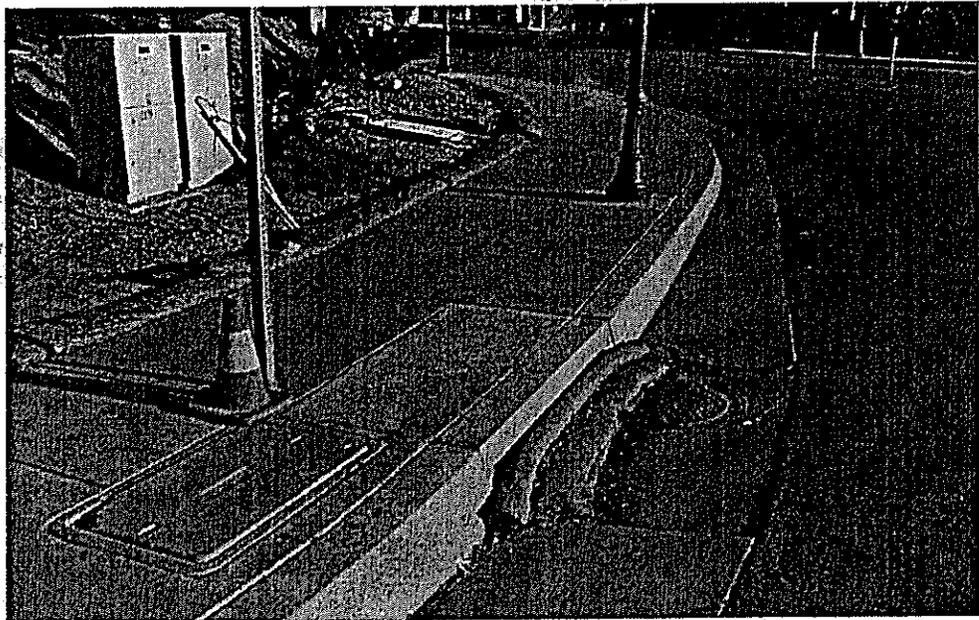


Inlet protection that blocks flow is good for preventing non-storm water discharges from entering the drain.


Pictures  
(continued)



Gravel bag inlet protection.

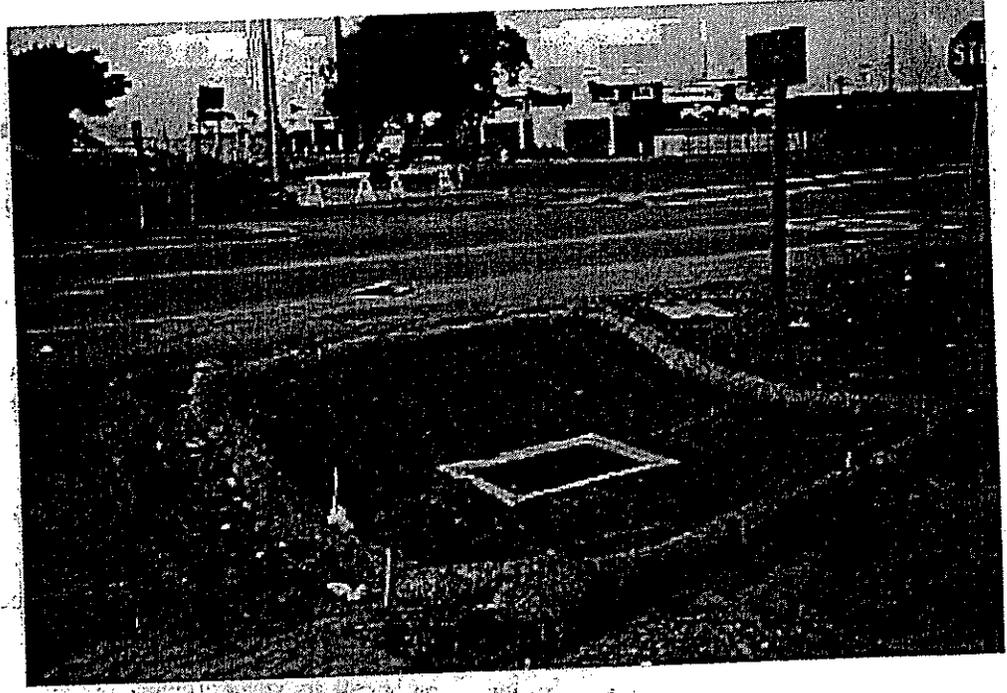

Inlet protection using fiber rolls and filter fabric.



**When** Tracking controls reduce offsite tracking of sediment and other pollutants by providing a stabilized entrance at defined construction site entrances and exits and/or providing methods to clean-up sediment or other materials to prevent them from entering a storm drain by sweeping or vacuuming.

- Stabilize entrances should be implemented on a project-by-project basis in addition to other BMPs.
- Sweeping or vacuuming should be implemented when sediment is tracked from the project site onto public or private paved roads, typically at points of site exit.
- Use stabilized entrances and/or sweeping at construction sites:
  - where dirt or mud is tracked onto public roads
  - adjacent to water bodies
  - where poor soils are encountered, such as soils containing clay.
  - where dust is a problem during dry weather conditions.

**How** Stabilized Construction Entrances

- Limit the points of entrance/exit to the construction site by designating combination or single purpose entrances and exits. Require all employees, subcontractors and others to use them. Limit speed of vehicles to control dust.
- Grade each construction entrance/exit to prevent runoff from leaving the construction site.
- Route runoff from stabilized entrances/exits through a sediment-trapping device before discharge.
- Design stabilized entrance/exit to support heaviest vehicles and equipment that will use it.
- Select construction access stabilization (aggregate, asphaltic concrete, concrete) based on longevity, required performance, and site conditions.
- Use of constructed or constructed/manufactured steel plates with ribs for entrance/exit access is allowed.
- If aggregate is selected, place crushed aggregate over geotextile fabric to at least 12 inches deep, or place aggregate to a depth recommended by a geotechnical engineer. A crushed aggregate greater than 3 inches but smaller than 6 inches shall be used.

Street Sweeping and Vacuuming

- Inspect potential sediment tracking locations routinely.
- Visible sediment tracking should be swept or vacuumed as needed. Manual sweeping is appropriate for small jobs.
- Manual sweeping is appropriate for small projects. For larger projects, it is preferred to use sweeping methods that collect removed sediment and material.

If not mixed with debris or trash, incorporate the removed sediment back into the project or dispose of it at an approved disposal site.



### Maintenance and Inspection

#### Stabilized Construction Entrance

- Inspect routinely for damage and assess effectiveness. Repair if access is clogged with sediment.
- Where tracking has occurred on roadways sweeping should be conducted the same day. Preferably water should not be used to wash sediment off the streets. If water is used, it should be captured preventing sediment-laden water from running off the site.
- Keep all temporary roadway ditches clear.

#### Street Sweeping and Vacuuming

Inspect inlet and outlet access points routinely and sweep tracked sediment as needed.

Be careful not to sweep up any unknown substance or any object that may be potentially hazardous.

- After sweeping is finished, properly dispose of sweeper wastes.


### Pictures



Manufactured metal plates knock dirt off vehicles before exiting a site.

# SEDIMENT CONTROLS

## Stockpile Management




**When** Use this BMP when projects require stockpiled soil and paving materials. The stockpile management practices used differ based on forecasted weather or terrain.

- Protection of stockpiles must be implemented whenever there is a potential for transport of materials by a water source (forecast precipitation or any non-storm water runoff).

**How** • One or more of the following options may be used to manage stockpiles and prevent stockpile erosion and sediment discharges for stormwater and non-storm water runoff/run-on.


- Stockpile may be returned to the excavation if precipitation is forecast.
- Protect stockpiles from stormwater run-on using a temporary perimeter sediment barrier such as berms, silt fences, fiber rolls, covers, sand/gravel bags, or straw bale barriers, as appropriate.
- Stockpiles may be hauled off or temporarily stored in a protected location off site.
- Keep stockpiles organized and surrounding areas clean.
- Protect storm drain inlets, watercourses, and waterbodies from stockpiles, as appropriate.
- Implement dust control practices as appropriate on all stockpiled material.
- Stockpiles should be covered, stabilized, or protected with a perimeter sediment barrier prior to the onset of precipitation.



### Maintenance and Inspection

Repair and/or replace covers, and perimeter containment structures as needed.

Pictures

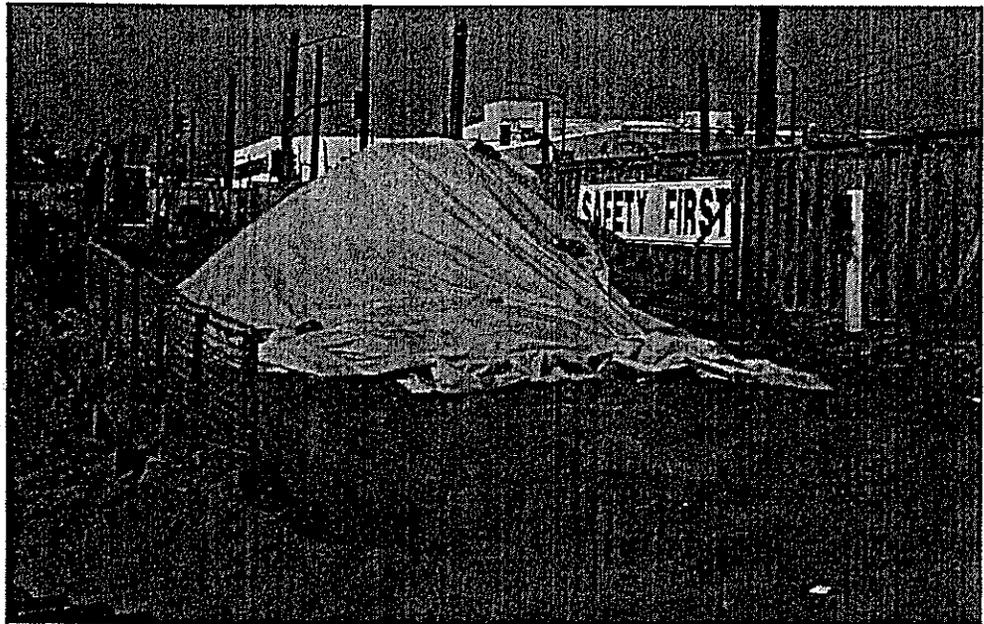

Stockpile covered with plastic and secured with large rocks.



Silt fence used for stockpile perimeter control.

# BMP DETAILS

---



## Section 2 – Waste Management and Material Controls

Federal, state and local laws, regulations, ordinances and permits prohibit the discharge of contaminated stormwater to storm drains and surface waters. Transport of sediment, and other pollutants, such as litter, paint, solvents, fuel, lubricants and demolition wastes, can be carried away from a construction site in stormwater. Therefore, BMPs are to be used for those construction activities that could cause pollution to ensure that pollutants are properly managed and are not discharged to storm drains and surface waters.

Waste Management and Materials Controls are source control BMPs that reduce or prevent contact between wastes and/or materials and storm water. Waste Management and Materials Controls presented in this Manual include the following:

- BMP 2-01 Material Delivery and Storage
- BMP 2-02 Material Use
- BMP 2-03 Spill Control
- BMP 2-04 Solid Waste Management
- BMP 2-05 Hazardous Materials/Waste Management
- BMP 2-06 Contaminated Soil Management
- BMP 2-07 Sanitary/Septic Waste Management
- BMP 2-08 Liquid Waste Management

# BMP DETAILS

---

This page intentionally left blank.

# WASTE MANAGEMENT AND MATERIAL CONTROLS

## Material Delivery and Storage

BMP 2-01



**When** If it is necessary to store materials at a construction site. This BMP does not apply to materials and supplies stored on trucks that are driven on site and off site daily.


**How** Use the following measures as appropriate:

- Only store the minimum amount of material that is needed for the job.
- Locate storage areas away from storm drain inlets, drainage systems, and watercourses to prevent storm water run-on from reaching the materials.
- If practical, store materials in enclosed storage containers such as cargo containers.
- Store materials on impervious surfaces or use plastic groundcovers to prevent any spills or leakage from contaminating the ground.
- For known hazardous materials, keep materials covered using plastic or other waterproof materials.
- If necessary provide secondary containment systems around material storage areas to prevent contaminated run-off/run-on from leaving storage area(s).
- Keep adequate supply of spill kit materials nearby.
- Ensure that qualified personnel are available when hazardous materials are delivered to ensure proper delivery and storage in designated area.
- When storage area is no longer needed, return it to original condition.
- Bagged materials such as cold patch, concrete mix, and other materials with the potential to pollute runoff should be placed on pallets and under cover.

### Maintenance and Inspection

Repair or replace covers, containment structures, or perimeter controls as needed to ensure proper functioning. Perform routine inspections of designated delivery and storage areas.

### Pictures

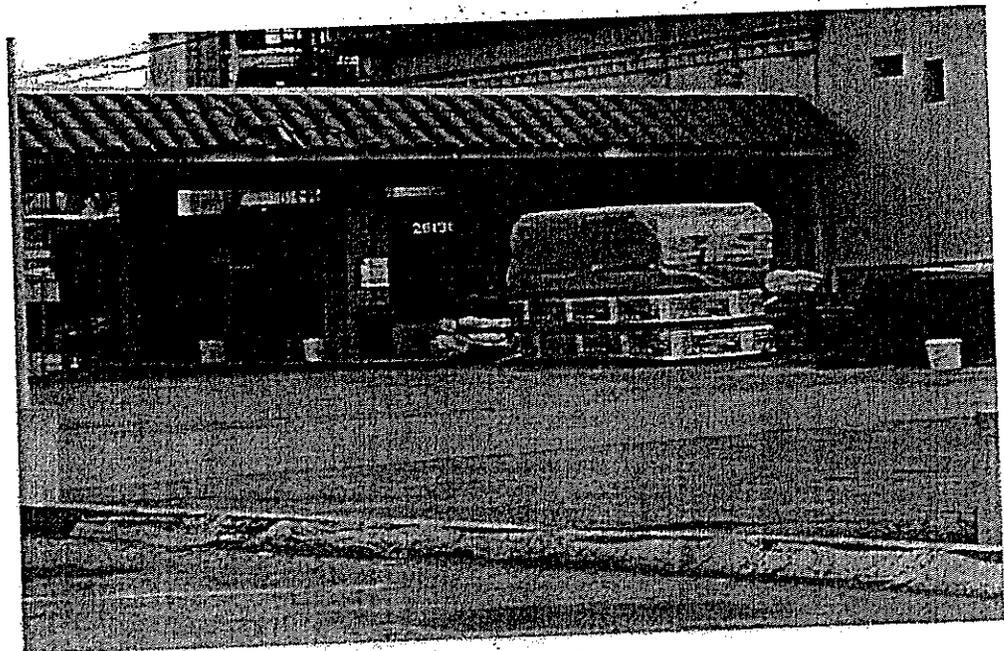

Materials are covered and neatly stored with a curbed area.

# WASTE MANAGEMENT AND MATERIAL CONTROLS

## Material Use

BMP 2-02




**When** Apply this BMP when the following materials are used or prepared on site:

- Pesticides and herbicides.
- Fertilizers and soil amendments.
- Detergents.
- Petroleum products such as fuel, oil, and grease.
- Asphalt and other concrete components.
- Hazardous chemicals such as acids, lime, glues, adhesives, paints, solvents, and curing compounds.
- Mastic, pipe wrap, primers, and paint.
- Concrete compounds.
- Welding material.
- Other materials that may be detrimental if released to the environment.

**How**

- Reduce or eliminate use of hazardous materials on site when practical. Contact your Environmental Representative for additional information.
- Empty latex paint and paint cans, used brushes, paint rags, absorbent materials, and drop cloths. When these items are thoroughly dry and are no longer hazardous, may be disposed of with other construction debris.
- Do not remove the original product label; it contains important safety and disposal information. Use the entire product before disposing of the container.
- When possible, mix paint indoors, otherwise use secondary containment structures. Do not clean paintbrushes or rinse paint containers into a street, gutter, storm drain, sanitary sewer or watercourse.
- Dispose of any paint thinners, residue and sludge(s), that cannot be recycled, as hazardous waste. For water-based paint, clean brushes to the extent practical, and rinse into a concrete washout pit or temporary sediment trap. For oil-based paints, clean brushes to the extent practical and filter and reuse thinners and solvents.
- If possible, recycle residual paints, solvents, non-treated lumber, and other materials.
- Do not over-apply fertilizers, pesticides, and soil amendments. Prepare only the amount needed. Strictly follow the recommended usage instructions.
- Keep an ample supply of spill clean up material near use areas. Instruct employees in spill clean up procedures.
- Avoid exposing applied materials to rainfall unless sufficient time has been allowed for them to dry or cure.
- Hazardous materials use shall also be managed in accordance with the BMP on "Hazardous Materials/Waste Management."



**Maintenance and Inspection**

- Spot-check employees and contractors regularly throughout the job's duration to ensure appropriate practices are being employed.



**When** This best management practice (BMP) applies to all construction sites at all times. Spill control procedures are implemented anytime chemicals and/or hazardous substances are stored. Substances may include, but are not limited to fuels, lubricants, solvents, fertilizers, pesticides, herbicides, soil binders, coolants, paints, and sewage.

To the extent that work can be accomplished safely, spills of materials or chemicals shall be contained and cleaned up immediately.

**How** Stop the spillage of material if it can be done safely. Clean the contaminated area, and properly dispose of contaminated materials. For all spills notify the project foreman and/or the Environmental Representative. Use the following spill prevention and controls when applicable.

- To the extent that it doesn't compromise clean up activities, spills shall be covered and protected from storm water run-on during rainfall.
- Spills shall not be buried or diluted with wash water.
- Used clean up materials, contaminated materials, and recovered spill material shall be stored and disposed of in accordance with federal, state and local regulations Refer to BMP on "Hazardous Materials/Waste Management").
- Use absorbent materials on spills rather than using water to hose down the spill.
- When water is used for cleaning and decontamination of a spill, the water shall not be allowed to enter storm drain inlets or watercourses, and shall be collected and disposed of properly. Coordinate disposal of these wastes with the Environmental Representative.
- Keep spill cleanup kits in areas where any materials are used and stored.

**Maintenance and Inspection**

- Perform routine inspections to verify that spill control clean up materials are near material storage, unloading, and use areas.



**When** These BMPs should be used on all construction projects that generate solid waste. Solid wastes may include, but are not limited to concrete, cement, asphalt rubble, masonry brick/block, vegetation debris, steel and scrap metals, pipe and electrical cuttings, non-hazardous equipment parts, Styrofoam, general trash and other materials used to transport and package construction materials.

- How**
- Practice good housekeeping and keep site clean.
  - Use “dry” methods for site clean up such as sweeping, vacuuming and hand pick-up.
  - Designate a waste storage area on site. If a designated waste storage area is not feasible, remove wastes from the site regularly.
  - Prohibit littering by employees, contractors and visitors.
  - Trash receptacles should be available on site and/or on construction vehicles.
  - Protect wastes from being washed away by rainfall, storm water run-on, or other waters (irrigation, water line breaks, etc.).
  - To prevent storm water run-on from contacting stored solid waste (stockpiled materials) use berms, secondary containment, covered dumpsters/roll-offs or other temporary diversion structure or measures.
  - For materials with the potential for spills or leaks, stockpile on impervious surfaces or use plastic groundcovers to prevent spills or leaks from infiltrating the ground.
  - Do not hose out or clean out dumpsters or containers at the construction site.
  - Prevent solid waste and trash from entering and clogging storm drain inlets.
  - As practical, incorporate any removed clean sediment and soil back into the project.
  - Reference BMP on Stockpile Management.

**Maintenance and Inspection**

- Collect site trash regularly, especially before rainy or windy conditions.
- Perform routine inspections of site, including storage areas, dumpsters, stockpiles and other areas where trash and debris are collected.
- Close trashcan lids and dumpster covers before rainy or windy conditions.

**When** Use this BMP when projects involve the storage and use of hazardous materials, and the generation of waste byproducts, from the following:

- Petroleum products such as oils, fuels, greases, cold mix, and tars
- Glues, adhesives, and solvents
- Herbicides, pesticides, and fertilizers
- Paints, stains, and curing compounds
- Other hazardous or toxic substances

**How** Hazardous materials and wastes shall be managed in accordance with the following procedures:

- Minimize the amount of hazardous materials stored at the construction site and the production and generation of hazardous waste at the construction site.
- Cover or containerize and protect from vandalism any hazardous materials and wastes.
- Clearly mark all hazardous materials and wastes. Place hazardous waste containers in secondary containment systems if stored at the construction site.
- Stockpiled cold mix should be placed on and covered with plastic.
- Do not mix waste materials, because this complicates or inhibits disposal and recycling options and can result in dangerous chemical reactions.
- Storm water that collects within secondary containment structures must be inspected prior to being discharged to ensure no pollutants are present. Contaminated storm water must be managed per Utility Environmental Practices (EPs)
- Spills cannot be discharged from a secondary containment system. See BMP on Spill Control.
- Hazardous waste must be segregated from other solid waste and disposed of properly.
- In addition to following this BMP, employees or contractors are responsible for compliance with federal, state, and local laws regarding storage, handling, transportation, and disposal of hazardous waste.

**Maintenance and Inspection**

- Routinely inspect the covers on hazardous material storage areas for tears or flaws and repair as necessary.
- All secondary containment systems must be able to hold the volume of the largest container in the storage area, plus provide sufficient additional capacity for storm events.
- Perform routine inspections to ensure that no hazardous materials or waste are improperly left exposed to storm water.

# WASTE MANAGEMENT AND MATERIAL CONTROLS

## Contaminated Soil Management

BMP 2-06



### When

This contaminated soil management BMP should be used whenever soil contamination is suspect or contaminated soil is encountered. Construction crews should be extra vigilant on projects located in highly urbanized or industrial areas where soil contamination may have occurred because of spills, illicit discharges, and leaks from underground storage tanks.

Contaminated soils may also be encountered during digging and trenching activities on highways and roadways.

### How

Contaminated soil wastes should be managed in accordance with the following procedures:


- Identify contaminated soil; look for the following:
  - Soil that is discolored, black, gray, white; or
  - Soil that has an unusual odor, such as, petroleum, acid, alkaline, sewage, solvent, or any other chemical smell.
- If any potentially contaminated soil is detected, discontinue the activity and contact the projects Environmental Representative.
- Contaminated soils must be managed properly per Utility Environmental Practices (EPs).

### Maintenance and Inspection

- Perform routine inspections of digging and trenching operations looking for contaminated soils.
- All contaminated soils must be managed as hazardous substances, if applicable, in accordance with applicable federal, state, and local laws.

# WASTE MANAGEMENT AND MATERIAL CONTROLS

## Sanitary/Septic Waste Management



**When** Use this BMP on all construction sites that use temporary or portable sanitary/septic waste systems.


**How** Sanitary/septic wastes shall be managed in accordance with the following procedures:

- Incorporate into regular safety meetings, education of employees, contractors, and suppliers on:
  - potential dangers to humans and the environment from sanitary/septic wastes
  - approved sanitary/septic waste storage and disposal procedures.
- Temporary sanitary facilities should be located away from drainage facilities, watercourses, and from traffic circulation. When subjected to high winds or risk of high winds, temporary sanitary facilities shall be secured to prevent overturning.
- Sanitary wastewater should not be buried or discharged, except to a properly permitted sanitary sewer discharge facility. A permit may be required from the local Sanitation District.
- Use only reputable, licensed sanitary/septic waste haulers.
- Temporary sanitary facility's holding tanks shall be emptied prior to transport.

### Maintenance and Inspection

- Onsite sanitary/septic waste storage and disposal should be routinely inspected.
- Ensure that sanitary/septic facilities are maintained in good working order routinely serviced by a licensed service.

### Pictures

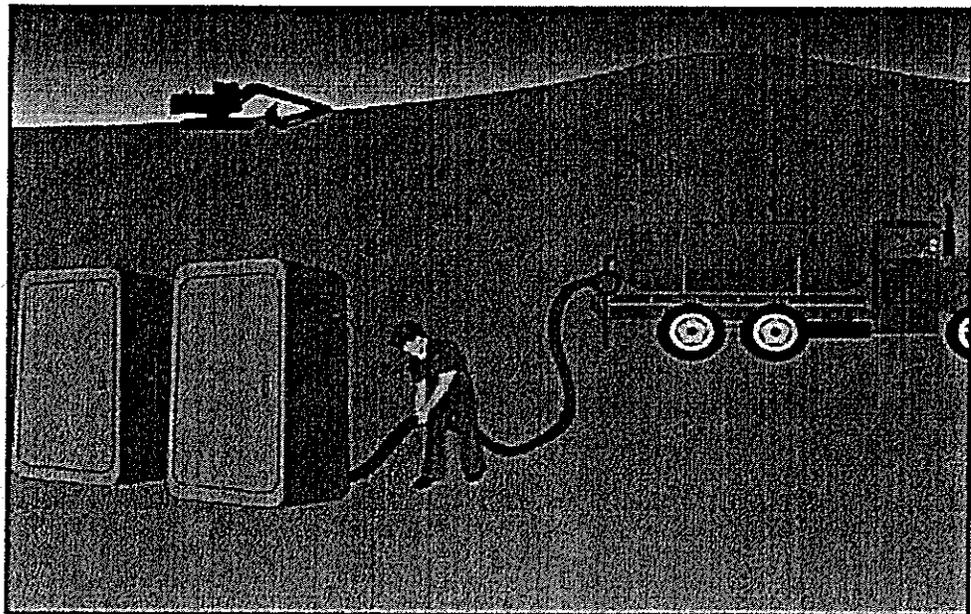

Good septic waste management.

# WASTE MANAGEMENT AND MATERIAL CONTROLS

## Liquid Waste Management

BMP 2-08



- When**
- Liquid waste management is applicable to construction projects that generate any of the following non-hazardous byproducts, residuals, or wastes, such as:
    - Drilling slurries and drilling fluids
    - Grease-free and oil-free wastewater and rinse water
    - Dredging spoils
    - Other non-storm water liquid discharges not permitted by separate permits.
  - Separate BMPs should also be referenced for the following onsite liquid wastes:
    - Dewatering operations
    - Liquid hazardous wastes, or
    - Concrete slurry residue

- How**
- Vehicle and equipment cleaning using water is discouraged on site.
  - Drilling residue and drilling fluids should be disposed of in accordance with Sempra Energy Utilities procedures at an approved disposal site. Coordinate the disposal of these wastes with your Environmental Representative.
  - Wastes generated as part of an operational procedure, such as waterladen dredged material and drilling mud, should be contained and not allowed to flow into drainage channels or receiving waters.
  - Contain non-hazardous liquid wastes in a controlled area, such as a lined holding pit, lined sediment basin, roll-off bin, or portable tank.
  - Containment devices must be of sufficient quantity or volume to completely contain the liquid wastes generated and any addition volume based on anticipated rainfall.
  - **Do not locate containment areas or devices where accidental release of the contained liquid can threaten health or safety, or discharge to watercourses, storm drain system, or to a receiving water.**
  - Capture all liquid wastes running off a surface that has the potential to affect the storm drainage system. Examples are: wash water and rinse water from cleaning walls or pavement.
  - If the liquid waste is sediment laden, use a sediment trap or capture in a containment device and allow sediment to settle.
  - Disposal of liquid wastes are subject to specific laws and regulations, or to requirements of other permits secured for the construction project. Contact your Environmental Representative for further information.



- Maintenance and Inspection**
- Remove deposited solids from containment areas and containment systems as needed, and at the completion of the project.
  - Inspect containment areas and containment systems routinely for damage, and repair as needed.

# BMP DETAILS

---



## Section 3 – Non-Storm Water Discharge Controls


Non-Storm Water Discharge Controls include general site and operations BMP measures that minimize pollution of water. Non-Storm Water Discharge Controls presented in this Manual include the following:

- BMP 3-01 Dewatering Operations
- BMP 3-02 Paving Operations
- BMP 3-03 Vehicle and Equipment Washing
- BMP 3-04 Vehicle and Equipment Fueling
- BMP 3-05 Concrete/Coring/Sawcutting and Drilling Waste Management
- BMP 3-06 Dewatering Utility Substructures and Vaults
- BMP 3-07 Vegetation Management including Mechanical and Chemical Weed Control
- BMP 3-08 Over-Water Protection
- BMP 3-09 Removal of Underground Utility Location/Mark-Out Paint

# BMP DETAILS

---

This page intentionally left blank.



- When**
- This BMP is applicable to trench or excavation dewatering.
  - Discharges of non-storm water from a trench or excavation that contain sediments or other pollutants to the sanitary sewer, storm drain systems, creek bed (even if dry), or receiving waters is prohibited. Water from dewatering activities is generally allowed to be discharged if the water does not contain any sediment or other pollutants. Verify with your local jurisdiction.
  - Generally, non-contaminated discharges of non-storm water to lands (such as infiltration) are allowed. Some areas may require a permit or other regulatory approval. Verify with your local jurisdiction.
  - **This BMP is not applicable to utility vault or sub-structure dewatering. For these applications, refer to the BMP on Dewatering Utility Substructures and Vaults.**
  - **This BMP is not applicable if the water is known, or suspected to be, contaminated. Under these conditions, contact your Environmental Representative.**

**How** Water generated by dewatering activities may be managed in accordance with the following procedures:

- Use water where possible for construction activities such as compaction and dust control. If used for these applications, ensure that the water will infiltrate and not run-off from the land to storm drain systems, to creek beds (even if dry) or to receiving waters.
- If allowed, infiltrate to an appropriate landscaped, vegetated or soil area. Note: Infiltration may be prohibited in accordance with local requirements. See “When” above.
- If water is to be discharged to land for infiltration:
  - The water may contain sediments, but must not be contaminated with other pollutants.
  - The water must not run-off from the land to storm drain systems, to creek beds (even if dry) or other surface waters.
  - Permission may be needed from the property owner on which the infiltration will occur.
- Water from dewatering, that contains only sediment, may be discharged if the sediment is allowed to settle out or the sediment is filtered out first. Alternatively, a vacuum truck may be used to remove the water and haul it to an authorized discharge location.
- If a permit is required, provide temporary onsite storage (Baker tanks, etc.) of water removed from trenches, excavations, etc., until a permit to discharge is obtained.
- If a permit is obtained for discharge to a storm water or sanitary sewer system, conduct all dewatering discharge activities in accordance with permit requirements.

**Maintenance and Inspection**

- Inspect pumps, hoses and all equipment before use. Monitor dewatering operations to ensure it does not cause offsite discharge or erosion.
- Inspect routinely, when applicable activities are under way.

# NON-STORM WATER DISCHARGE CONTROLS

## Paving Operations

BMP 3-02



**When** Use this BMP for projects that involve pavement surfacing, resurfacing, removal, or patching applications of the following:

- Cold mix
- Asphalt
- Chip seal, seal coat, tack coat, slurry seal, or fog seal
- Portland cement concrete

For pavement grinding, sawcutting, coring or drilling, refer to BMP Concrete/Coring/Sawcutting and Drilling Waste Management.

**How** Use the following methods as applicable:

- Protect storm drain inlets near work and downgradient of the area to be paved.
- If onsite mixing is planned then an area must be designed for conducting the mixing. This area should be paved or made impervious (e.g., plastic or wood sheeting) and be located away from storm drain inlets or watercourses.
- Minimize overspray of tackifying emulsions or placement of other paving materials beyond the limits of the area to be paved.
- Use dry methods to clean equipment and conduct cleaning in accordance with the BMP on Vehicle and Equipment Washing.
- Material use and stockpiles to be managed in accordance with BMPs on material Use and Stockpile Management.
- Collect and remove all broken asphalt and concrete, recycle when feasible and dispose of materials in accordance with local, state, and federal requirements.
- **Do not apply asphalt, concrete paving, seal coat, tack coat, slurry seal or fog seal if rain is expected during the application or curing period.**
- Avoid if possible, transferring, loading, or unloading paving materials near storm drain inlets or watercourses. If not possible, use BMP on Storm Drain Inlet Protection.



### Maintenance and Inspection

- Inspect and maintain equipment and machinery routinely to minimize leaks and drips.
- Inspect inlet protection measures routinely.

# NON-STORM WATER DISCHARGE CONTROLS

## Vehicle and Equipment Washing

BMP 3-03



<b>When</b>	Use these procedures on all construction sites where vehicle and equipment cleaning is performed. Note that onsite vehicle and equipment washing is not typically performed on utility type construction projects and requires specific approval of a Utility Environmental Representative.
<b>How</b>	<p>Use the following methods as applicable:</p> <ul style="list-style-type: none"><li>• Use “dry” cleaning methods such as wiping down, rather than water washing vehicles or equipment.</li><li>• Whenever possible washing should not be conducted at the construction site</li><li>• If onsite vehicle washing is authorized by the Environmental Representative, use the following general methods:<ul style="list-style-type: none"><li>– Vehicle and equipment washing must be located away from storm drain inlets, drainage systems, or watercourses.</li><li>– Place sand bags or another type of berm around storm drain inlets and drainage systems to prevent wash water from entering a storm inlet, drainage system or watercourse.</li><li>– Never discharge wash water to the storm drain system.</li><li>– Use as little water as possible. High-pressure sprayers may use less water than a hose.</li><li>– Use a positive shutoff valve to minimize water usage.</li></ul></li></ul>
<b>Maintenance and Inspection</b>	Monitor employees and contractors through the duration of the construction project to ensure appropriate practices are being implemented.

# NON-STORM WATER DISCHARGE CONTROLS

## Vehicle and Equipment Fueling

BMP 3-04



**When** Use this BMP for projects where onsite fueling of vehicles and equipment, including handheld equipment, is planned.

Vehicle and equipment fueling, except for handheld equipment, is typically not done on the construction site. Onsite fueling of vehicles and equipment may be planned if it is impractical to send vehicles and equipment off site for fueling.

Handheld equipment is treated separately from other equipment. Handheld equipment includes those smaller, manually operated pieces of equipment such as trenchers, mowers, chainsaws, generators, and other equipment that need fueling during regular daily operation.

**How** Use the following measures as applicable:

### Fueling Vehicles and Handheld Equipment

- If practical, fuel vehicles and equipment off site.
- Mobile fueling equipment is the preferred equipment used for onsite fueling.
- Fuel storage and fueling areas should be located away from storm drain inlets, drainage systems, and watercourses.
- All fueling will be conducted with the fueling operator in attendance at all times regardless if fuel nozzles are equipped with automatic shutoff features.
- Fuel tanks should not be "topped off."
- All fueling operators should have readily available spill containment and cleanup equipment and materials.
- Clean up any spills immediately and properly dispose of contaminated materials.
- Properly store and dispose of rags and absorbent material used to clean up any spilled fuel.
- Mobile fueling trucks and operators must have all necessary permits, licenses and training.

### **Maintenance and Inspection**

- Check to ensure adequate supply of spill cleanup materials are available.
- Perform routine inspections of designated fueling areas.
- Report all spills immediately to the project Supervisor or the Environmental Representative

# NON-STORM WATER DISCHARGE CONTROLS

## Concrete/Coring/Sawcutting and Drilling Waste Management

BMP 3-05



**When** Projects where concrete and asphalt are used or where slurry or pavement/concrete wastes are generated by construction activities, including:

- Sawcutting
- Coring/drilling
- Grinding, re-paving or patching
- Encasing conduit in concrete
- Tower footings

For managing any concrete curing compounds, use the BMP on Hazardous Materials/Hazardous Waste Management. For managing paving operations, use BMP Paving Operations.

**How**

- Install storm drain protection at any down-gradient inlets that may be impacted by the activity. See the BMP on Storm Drain Inlet Protection.

- Minimize the amount of water used during coring/drilling or sawcutting. During wet coring or sawcutting, use shovel or wet vacuum to lift the slurry from the pavement. Additionally, if wet vacuuming is not adequate to capture wastewater from the activity, sand bag barriers or other containment should be used.

- If concrete residue remains after drying, the area should be swept up and residue removed to avoid contact with storm water or entering a storm drain or waterbody via the wind.

- Do not wash residue or particulate matter into a storm drain inlet or watercourse.


- The following options should be used for concrete truck chute and/or pump and hose washout:

- If available, arrange to use an existing concrete washout station. Upon entering site, concrete truck drivers should be instructed about practices being used on site.

- **Concrete Washouts:** Washout stations can be a plastic lined temporary pit or bermed areas designed with sufficient volume to completely contain all liquid and waste concrete materials plus enough capacity for rainwater. The designated area must be located away from storm drain inlets, or watercourses.

- **Washout in Trench:** Manually rinsing the concrete truck chute into the trench itself.

- **Bucket Washout:** Manually rinsing the chute into a wheelbarrow, plastic bucket or pail, and then empty the bucket into the concrete truck barrel or on top of the placed concrete.



### Maintenance and Inspection

- Responsible personnel should ensure that all concrete truck drivers are instructed about project practices when the trucks arrive onsite.

- Clean out designated washout areas as needed or at a minimum when the washout is 75 percent full to maintain sufficient capacity throughout the project duration.

- Any designated onsite washout areas must be cleaned out and all debris removed upon project completion. Dispose of concrete waste according to the BMP on Solid Waste Management.

- Inspect routinely, when applicable activities are underway to ensure that concrete washout does not overflow.

# NON-STORM WATER DISCHARGE CONTROLS

## Dewatering Utility Substructures and Vaults


BMP 3-06



**When** This BMP is applicable to utility substructure (vault) dewatering. This BMP does not apply to trench, excavation or other general dewatering associated with construction activities.

**How** The discharge of water from dewatering of vaults and substructures to the storm drain is allowed under an existing NPDES permit (General Permit CAG990002, Order No. 2001-11-DWQ). General requirements for discharge under this permit are listed below:

- All dewatering discharges conducted by utility crews, including contractors, shall follow the latest versions of SCG/SDG&E Environmental Practice (EP) on Vault and Substructure Dewatering.
- Discharges to land require prior approval from the landowner.
- If the water to be discharged conforms to the practices within the EP, the discharge is allowed.
- **During discharge, do not allow pollutants (e.g., sediment) to come in contact with the discharge. For example, if there is pre-existing soil in the path of the discharge (i.e., gutter), it must be swept up or avoided before discharging the substructure water.**




### Maintenance and Inspection

- Implement applicable provisions of the Environmental Practice.
- Inspect pumps, hoses and equipment before use and routinely when applicable activities are underway.
- Observe dewatering activities to ensure they do not cause erosion or discharge of potential pollutants.

# NON-STORM WATER DISCHARGE CONTROLS

## Vegetation Management Including Mechanical and Chemical Weed Control



**When** Use this BMP whenever vegetation control is used. Vegetation control may consist of manual or mechanical removal of vegetation and/or chemical treatment.

**How** General Vegetation Management Procedures:

- Do not allow vegetation debris to enter storm drain inlets and watercourses.
- Identify drain inlets and watercourses, both upstream and downstream of the work site(s).
- Pre-plan the work to protect stormwater drainage systems and watercourses from discharge of potential pollutants, maintain equipment in good operating condition.
- Set up the work area to minimize the tracking of material by vehicles and equipment in or out of the work area.

Practice Good Housekeeping at the Work Site(s):

- Litter and debris should be collected and disposed of properly.
- Containers of liquids should be secured with lids until needed.
- Transport collected non-hazardous materials for proper disposal. If the material is a hazardous waste, follow the BMP on Hazardous Materials & Hazardous Waste Management. Contact your Environmental Representative.
- If a leak or spill occurs, protect drainage systems and watercourses from spilled material; follow the BMP on Storm Drain Inlet Protection.

Mechanical Weed Control Procedures

Mechanical weed control is the physical removal of weeds or unwanted vegetation growing around electric utility poles and electric distribution or transmission structures for fire control.



- Do not stack or leave removed weeds or vegetation or other debris on or near drain inlets or in the storm water drainage system or watercourses.
- Do not fuel equipment next to drain inlets or place fuel or oil cans near or in watercourses, the storm drainage system or next to a drain inlet.
- Because of fire control requirements, do not leave cut vegetation around structures.

Chemical Weed Control Procedures

This method of weed and vegetation control uses herbicides to eliminate and prevent weed growth. The purpose is to control vegetation growth year-round as needed for effective fire control.

To achieve effective vegetation control through chemical means and protect the environment, application personnel should:



- Use the correct herbicide for the application.
- Consider the seasonal timing of the application as applicable.
- Do not use chemical vegetation control prior to a forecasted rain event.

The applicators shall follow the following procedures:

- Only use those herbicides approved by SDG&E/SCG.
- Application of herbicides must conform to the SDG&E/SCG herbicide application protocol in addition to any Contractor owned protocols and label instructions. Contact your Environmental Representative for additional information.

# NON-STORM WATER DISCHARGE CONTROLS

## Vegetation Management Including Mechanical and Chemical Weed Control

---

BMP 3-07




### How (continued)

- Apply pesticides only as specified on the "Pesticide Use Recommendation" on the label. The pesticide label is considered the law, and use of an herbicide inconsistent with the label is considered a violation. Follow safety and application methods as specified in the Annual Pesticide Safety Training.
- Follow the herbicide/pesticide application protocol when near storm water drainage system or watercourses.
- Calibrate the spray rig as needed, to ensure accurate application of herbicides.
- Record the use of all herbicides.
- Avoid using overhead irrigation for as long as recommended by the chemical manufacturer after applying pesticides or post-emergents.
- Avoid applying post-emergents prior to a predicted rain event.

### Maintenance and Inspection

- Ensure that spraying equipment is maintained to prevent malfunctions.
- Inspect to confirm that mechanical and chemical weed control procedures have not created an erosion problem.



<b>When</b>	<p>Prior to conducting over water activities, confirm the need for permits with appropriate local and state agencies.</p> <p>This BMP applies to projects where:</p> <ul style="list-style-type: none"><li>• Construction, maintenance or repair activities will be conducted above surface waters. These activities include, but are not limited to, chipping, grinding, scraping, welding/burning, painting, wrapping and coating of pipes and conduits.</li><li>• Surface waters (dry or running) include creeks, streams, rivers, lakes and wetlands, bays, estuaries and oceans.</li></ul>
<b>How</b>	<p>Use the following measures as applicable:</p> <ul style="list-style-type: none"><li>• Containment systems must be properly designed and installed prior to the beginning of any operation that may impact a water body to prevent discharge of pollutants to surface waters.</li><li>• The work area should be kept clean of all trash and potential pollutants.</li><li>• Containment booms should be placed around the area of work as necessary to contain the discharge of potential contaminants such as oil and hydraulic fluid.</li><li>• Special attention should be given to existing and forecasted wind and weather conditions to prevent pollutant discharges to surface waters.</li><li>• Shrouds should be used to prevent paint overspray, welding slag, and other pollutants from entering surface waters and being dispersed into the air. Shrouding may not be effective during periods of high wind.</li><li>• Shrouds should be large enough to adequately enclose or segregate the working area from surface waters. This may include a plywood barrier, visqueen, and scaffolding to help prevent fugitive material from entering surface waters.</li><li>• Support structures such as scaffolding shall be used in conjunction with shrouding to withstand potential wind stress.</li><li>• Contaminated shrouding material and equipment shall be thoroughly cleaned or disposed of properly.</li></ul>
<b>Maintenance and Inspection</b>	<ul style="list-style-type: none"><li>• Inspect the containment systems and shrouds routinely during work activities to ensure their integrity.</li></ul>

# NON-STORM WATER DISCHARGE CONTROLS

## Removal of Underground Utility Location/Mark-Out Paint

BMP 3-09



**When** Use this BMP when utility projects involve mark-out by painting surfaces where underground utilities are located and where paint is required to be removed by local jurisdictions or another authority.

**How** Use the following methods and options to remove Utility Mark-Out Paint:

- Use non-toxic, light degradable mark-out paint when possible
- Hydro Pressure wash
- Dry abrasive blast/grinding
- Wet abrasive blast/grinding
- Wet/Dry Vacuum
- Dry Sweep
- Install storm drain inlet protection at adjacent down gradient inlets during wet hydro pressure washing and wet abrasive blasting and grinding.
- Minimize the amount of water used during hydro washing.
- Use shovel or wet vacuum to lift the paint slurry from the pavement or surface.
- If wet vacuuming is not adequate to capture all wastewater from these activities, use additional containment (sand bags, booms, or other containment devices) methods near the work area to prevent the discharge to a storm drain inlet or watercourse.
- If paint residue remains after drying, the area should be swept up and residue removed to avoid contact with storm water.
- If paint residue remains after sweeping, the area can be water washed, as long as the water containing the paint residue is not allowed to enter storm drain inlets or watercourses.
- All waste should be disposed of using the BMPs for Liquid Waste Disposal.

### Maintenance and Inspection

- Inspect all containment systems to ensure proper placement prior to starting utility paint removal operations
- Inspect and adjust equipment frequently; and maximize efficiency of the paint removal operations.

# BMP DETAILS

---



## Section 4 – Erosion Control and Soil Stabilization

Erosion is the detachment of soil by water or wind. Erosion is a natural process that can be accelerated by construction activities such as grading and trenching. For example, when a site is cleared and grubbed, protective vegetation is removed and the disturbed soil is directly exposed to wind and water. Erosion Controls protect the soil surface and prevent the soil particles from being detached by rainfall or wind. Preservation of Existing Vegetation is an example of an Erosion Control BMP.

Soil Stabilization is a form of erosion control. It protects the exposed soil surface from rain and wind thereby preventing erosion. Hydroseeding is an example of a Soil Stabilization BMP. Erosion Control and Soil Stabilization BMPs in this Manual include:

- BMP 4-01 Preservation of Existing Vegetation
- BMP 4-02 Temporary Soil Stabilization (General)
- BMP 4-03 Hydraulic Mulch
- BMP 4-04 Hydroseeding
- BMP 4-05 Soil Binders
- BMP 4-06 Straw Mulch
- BMP 4-07 Geotextiles, Plastic Covers and Erosion Control Blankets/Mats
- BMP 4-08 Dust (Wind Erosion) Control

# BMP DETAILS

---

This page intentionally left blank.

**When** This BMP is applicable to projects when:

- There are areas on site where no construction activity is planned or will occur later.
- Identify areas to be preserved in the immediate vicinity of the construction site, and mark as appropriate before clearing and grubbing or other soil disturbance activities begin.
- Areas with vegetation that can be preserved to protect against soil erosion, such as on steep slopes, watercourses, and building sites in wooded areas.
- Areas designated as Environmentally Sensitive Areas (ESAs), or where federal, state, or local government regulations require preservation, such as wetlands, vernal pools, marshes, etc. These areas are typically flagged by a qualified biologist.


**How** Use the following measures as applicable:

- Preserve existing vegetation whenever possible.
- If necessary, contact the project Environmental Representative for any clarification regarding areas to be preserved.
- Whenever possible minimize disturbed areas by locating temporary roadways to avoid stands of trees and shrubs and follow existing contours to reduce cutting and filling.
- Construction materials, equipment storage and parking areas should be located outside the drip line of any tree to be retained.
- Consider the impact of grade changes to existing vegetation and the root zone.
- Remove any markings, barriers, or fencing after project is completed.

**Maintenance and Inspection**

- Maintain the clearly marked limits of disturbance during construction as appropriate to preserve vegetation.
- Inspect barriers regularly during construction.

**Pictures**



Vegetation to be preserved is marked and outside the work area.

# EROSION CONTROL AND SOIL STABILIZATION


## Temporary Soil Stabilization (General)

BMP 4-02



- When** This BMP is applicable to major projects when steep slopes are disturbed.
- For surface protection methods to prepare or protect the soil surface from the combined erosive effects of wind, rain, and storm water runoff.
  - On slopes where the soil has been exposed because of construction activities, one or more Soil Stabilization BMPs may be required to be implemented.
- How**
- Use one or more of the below temporary soil stabilization practices when applicable as described above:
    - Hydraulic Mulch.
    - Hydro seeding.
    - Soil Binders.
    - Straw Mulch.
    - Geotextiles, Plastic Covers and Erosion Control Blankets/Mats.
  - Implement prior to the onset of precipitation.
  - Implement BMPs such as fiber rolls or gravel bag berms to break up the slope lengths as follows:
    - On steep slopes, BMPs should be placed on slopes 100 feet and greater at intervals no greater than 50 feet.
    - On very steep slopes, BMPs should be placed on slopes 50 feet and greater at intervals no greater than 25 feet.
  - Permanent erosion control shall be applied to areas deemed substantially complete during the project's defined seeding window.
  - Refer to individual Soil Stabilization BMPs for specific instructions for use.
- Maintenance and Inspection**
- Refer to individual temporary soil stabilization BMPs for maintenance and inspection requirements.

Pictures

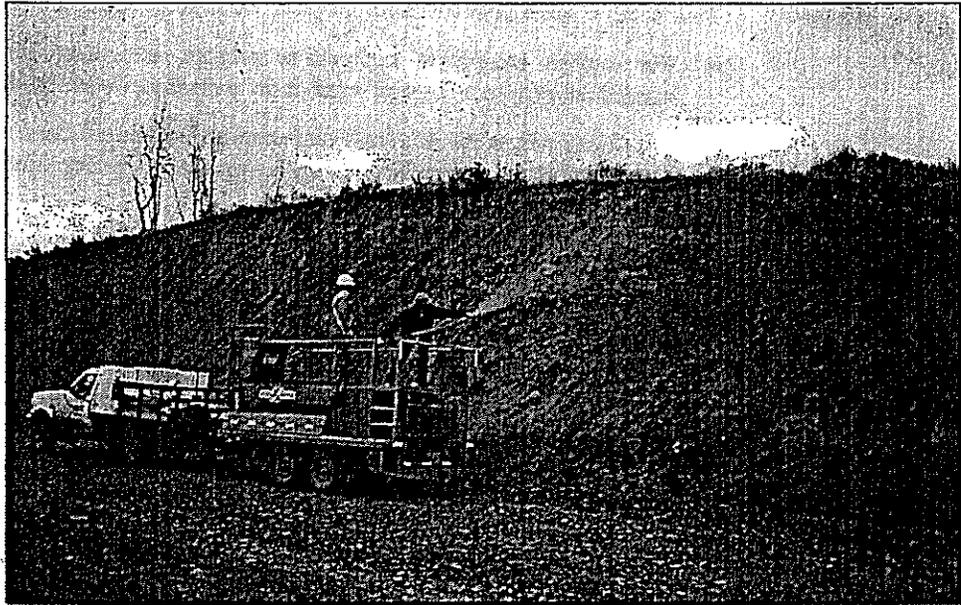

Applying a tackifier using a trailer mounted pump and hose.



Applying soil stabilization manually in harder to reach areas.

# EROSION CONTROL AND SOIL STABILIZATION

## Hydraulic Mulch


BMP 4-03




- When**
- Hydraulic mulch is typically applied to disturbed areas requiring temporary protection until permanent vegetation is established or disturbed areas that must be re-disturbed following an extended period of inactivity.
  - Avoid use in areas where the mulch would be incompatible with immediate earthwork activities and would have to be removed.
- How**
- Prior to application, roughen embankment and fill areas by rolling with a crimping or punching type roller or by track walking. Track walking shall only be used where other methods are impractical.
  - Avoid mulch over-spray onto the traveled way, sidewalks, lined drainage channels, and existing vegetation.
  - Hydraulic Mulches:
    - Apply as a liquid slurry using a hydraulic application machine (i.e., hydroseeder) at rates of mulch and stabilizing emulsion recommended by the manufacturer. Wood fiber hydraulic mulches are generally short-lived (only last a part of a growing season) and must be applied 24 hrs before rainfall to dry and become effective.
  - Hydraulic Matrices:
    - Apply a combination of wood fiber and/or paper fiber mixed with acrylic polymers as binders. Apply as a liquid slurry using a hydraulic application machine (i.e., hydroseeder) at rates recommended by the manufacturer. Hydraulic matrices must be applied 24 hours before rainfall to dry and become effective.
  - Bonded Fiber Matrix (BFM)
    - Apply BFM using a hydraulic application machine (mulch and tackifier are pre-mixed in a single bag) in accordance with manufacturers instructions. Do not apply immediately before, during, or after a rainfall.
- Maintenance and Inspection**
- Maintain an unbroken, temporary mulched ground cover throughout the period of construction when the soils are not being reworked. Inspect before expected rainstorms and repair any damaged ground cover and re-mulch exposed areas of bare soil.
  - After any rainfall event, maintain all slopes to prevent erosion.



Pictures

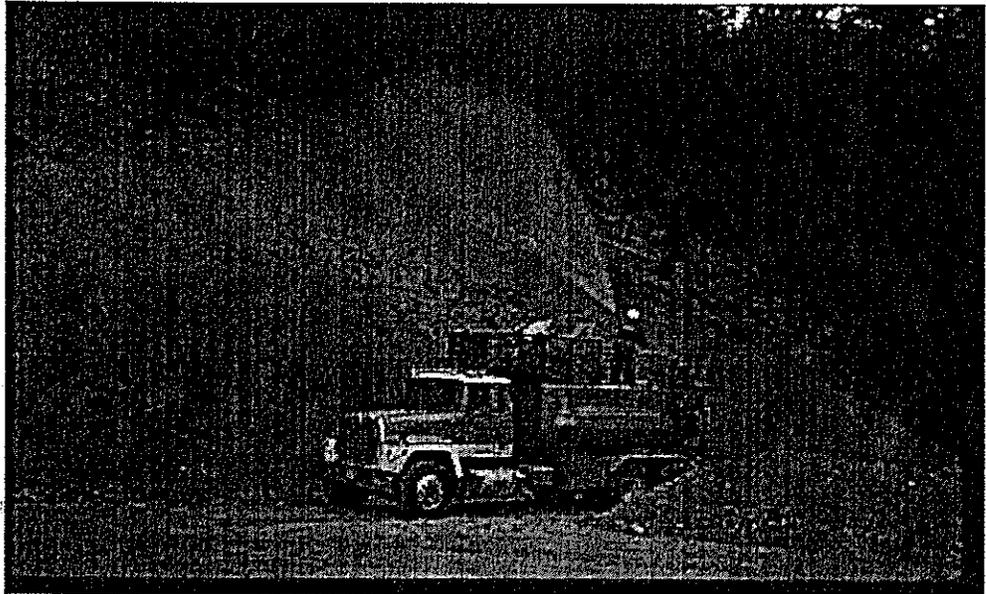

Applying hydraulic mulch.

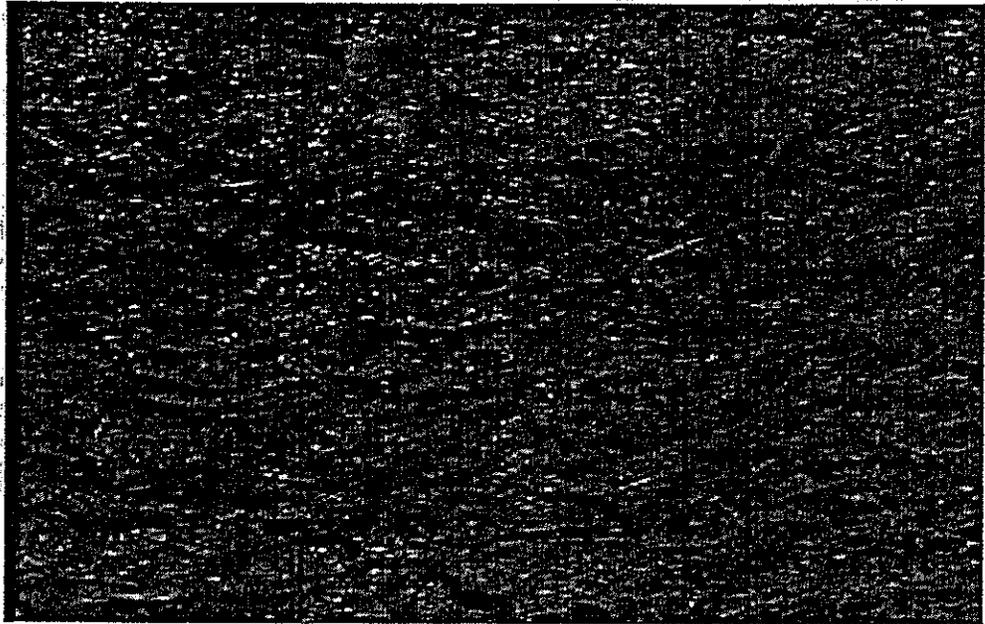

Close-up of bonded fiber matrix



## Hydroseeding

**When**

Hydroseeding typically consists of applying a mixture of fiber, seed, fertilizer, and stabilizing emulsion with hydro-mulch equipment, which temporarily protects disturbed soil areas from erosion. It is applied on:

- Disturbed Soil Areas (DSAs) requiring temporary protection until permanent vegetation is established, or
- DSAs that must be redisturbed following an extended period of inactivity.


**How**

- Avoid use of hydroseeding in areas where the best management practice (BMP) would be incompatible with future earthwork activities and would have to be removed such as:
  - Steep slopes are difficult to protect with temporary seeding.
  - Temporary seeding may not be appropriate in dry periods without supplemental irrigation.
  - Temporary vegetation may have to be removed before permanent vegetation is applied.
  - Temporary vegetation is not appropriate for short-term inactivity.
- Hydroseeding can be accomplished using a multiple-step (with straw mulch) or a one-step process (mixed with hydraulic mulch, hydraulic matrix, or bonded fiber matrix). When the one-step process is used to apply the mixture of fiber, seed, etc., the seed rate shall be increased to compensate for all seed not having direct contact with the soil.
- Prior to application, roughen the slope, fill area, or area to be seeded with the furrows trending along the contours.
- Apply a straw mulch as necessary to keep seeds in place and to moderate soil moisture and temperature until the seeds germinate and grow.
- Follow-up applications shall be made as needed to cover weak spots, and to maintain adequate soil protection.
- Avoid over-spray onto the travel way, sidewalks, drainage channels and existing vegetation.
- All seeded areas shall be inspected for failures and re-seeded, fertilized, and mulched within the planting season, using not less than half the original application rates. Any temporary revegetation efforts that do not provide adequate cover must be revegetated.
- After any rainfall event, maintain all slopes to prevent erosion.

**Maintenance and Inspection**



Pictures

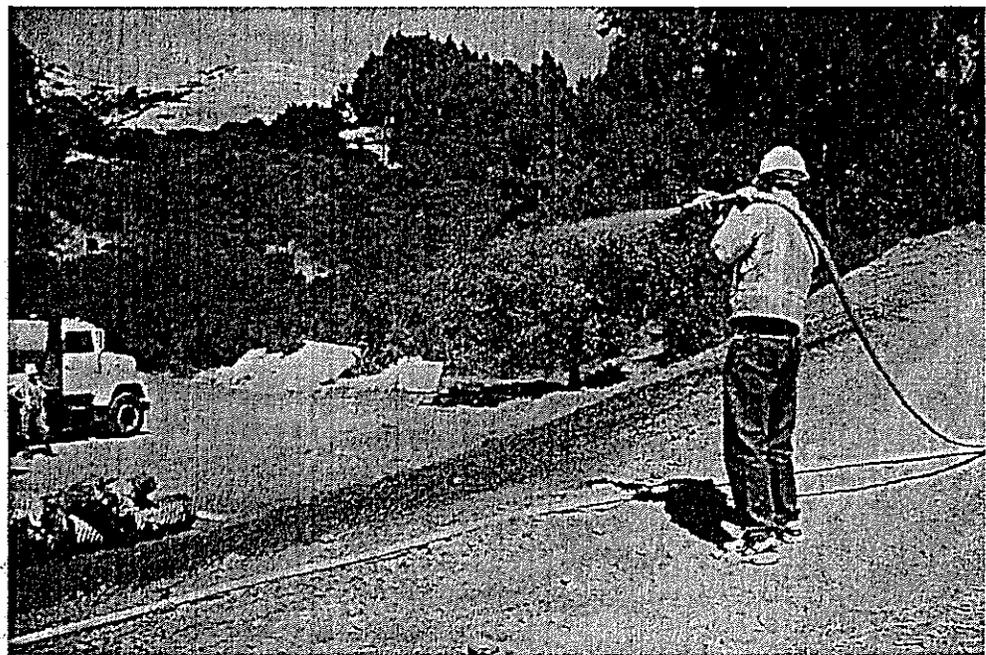

Applying hydroseed.




- When** Soil binders are typically applied to disturbed soil areas requiring short-term temporary protection. Because soil binders can often be incorporated into the work, they may be a good choice for areas where grading activities will soon resume.
- How**
- Selection of soil binders should be approved by the projects Environmental Representative after an evaluation of site-specific factors. Binders have the following limitations:
    - Soil binders generally experience spot failures during heavy rainfall and may need reapplication after a storm and do not hold up to pedestrian or vehicular traffic.
    - Soil binders may not penetrate soil surfaces made up primarily of silt and clay, particularly when compacted.
    - Some soil binders may not perform well with low relative humidity. Under rainy conditions, some agents may become slippery or leach out of the soil.
    - May not cure if low temperatures occur within 24 hours of application.
  - Follow manufacturer's recommendations for application procedures and cleaning of equipment after use. Any onsite cleaning must use appropriate BMPs for pollution prevention plans.
  - Prior to application, roughen embankment and fill areas. Track walking shall only be used where rolling is impractical.
  - Soil binders should not be applied during or immediately before rainfall, as they require a minimum curing time of 24 hours before they are fully effective.
  - Avoid over-spray onto the traveled way, sidewalks, lined drainage channels, sound walls, and existing vegetation.
  - **Do not apply soil binders to frozen soil, areas with standing water, under freezing conditions, or when the temperature is below 4°C (40°F) during the curing period.**
  - More than one treatment is often necessary, although the second treatment may be diluted or have a lower application rate.
  - For liquid agents:
    - Crown or slope ground to avoid ponding.
    - Uniformly pre-wet ground according to manufacturer's recommendations.
    - Apply solution under pressure. Overlap solution 150 to 300 mm (6 to 12 in).
    - Allow treated area to cure for the time recommended by the manufacturer; typically, at least 24 hours.
    - Apply second treatment before first treatment becomes ineffective, using 50 percent application rate.
    - In low humidities, reactivate chemicals by re-wetting according to manufacturer's recommendations.
- Maintenance and Inspection**
- Reapplying the selected soil binder may be needed for proper maintenance. Traffic areas should be inspected routinely.
  - After any rainfall event, maintain all slopes to prevent erosion.





- When** Straw mulch is used when:
- Temporary soil stabilization surface cover is needed on disturbed areas until soils can be prepared for re-vegetation and permanent vegetation is established.
  - In combination with temporary and/or permanent seeding strategies to enhance plant establishment.
  - Note, there is a potential for introduction of weed-seed and unwanted plant material with straw.
- How**
- A tackifier is the preferred method for anchoring straw mulch to the soil on slopes. Tackifiers act to glue the straw fibers together and to the soil surface, and the tackifier shall be selected based on longevity and ability to hold the fibers in place. Soil binders (tackifier) will generally experience spot failures during heavy rainfall events.
  - A tackifier is typically applied at a rate of 125 pounds per acre. In windy conditions, the rates are typically 150 pounds per acre.
  - Crimping, punch roller-type rollers, or track-walking may also be used to incorporate straw mulch into the soil on slopes. Track walking shall only be used where other methods are impractical.
  - Avoid placing straw onto the traveled way, sidewalks, lined drainage channels, sound walls, and existing vegetation.
  - Straw mulch with tackifier shall not be applied during or immediately before rainfall.
  - Apply loose straw at a minimum rate of 4,000 pounds per acre, either by machine using a straw blower or by hand distribution.
  - The straw mulch must be evenly distributed on the soil surface.
  - Anchor the mulch in place by using a tackifier or by “punching” it into the soil mechanically. “Punching” of straw does not work in sandy soils.
  - Methods for holding the straw mulch in place depend on the slope steepness, accessibility, soil conditions and longevity. If the selected method is incorporation of straw mulch into the soil, then do as follows:
    - On small areas, a spade or shovel can be used.
    - On slopes with soils, which are stable enough, and of sufficient gradient to safely support construction equipment without contributing to compaction and instability problems, straw can be “punched” into the ground using a knife-blade roller or a straight bladed coulter, known commercially as a “crimper.”
    - On small areas and/or steep slopes, straw can also be held in place using plastic netting or jute. The netting shall be held in place using 11 gauge wire staples, geotextile pins or wooden stakes (as described in BMP on “Geotextiles, Plastic Covers and Erosion Control Blankets/Mats”).
  - Remove straw as necessary prior to permanent seeding or soil stabilization.
- Maintenance and Inspection**
- The key consideration in maintenance and inspection is that the straw needs to last long enough to achieve erosion control objectives.
  - Reapplication of straw mulch and tackifier may be required to maintain effective soil stabilization over disturbed areas and slopes.
  - After any rainfall event, maintain all slopes to prevent erosion.

Pictures

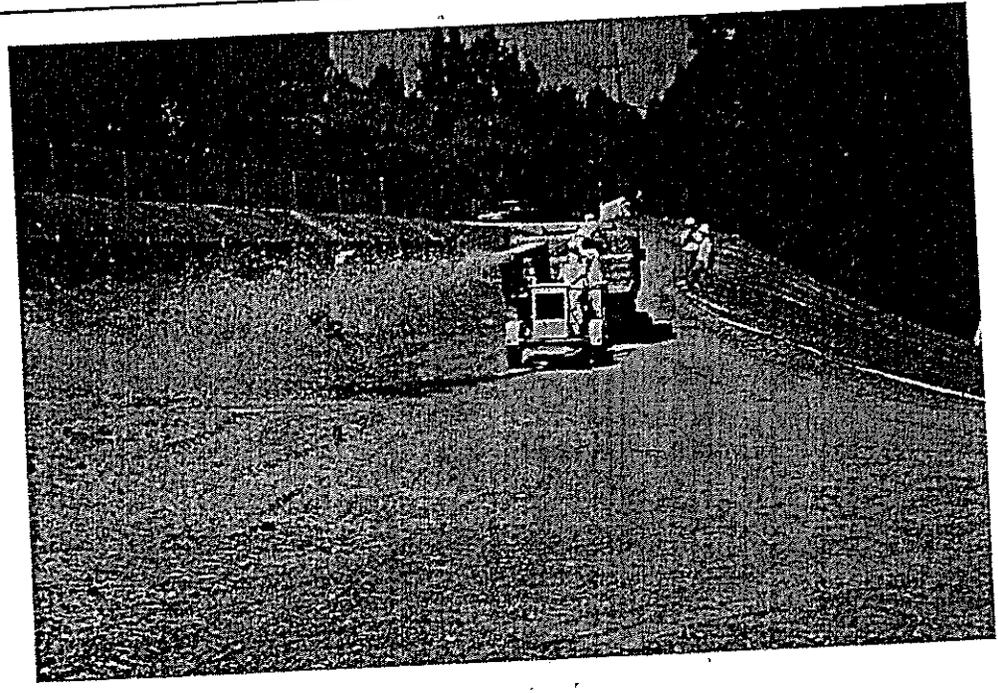

Straw mulch.




- When**
- The following methods are used when disturbed soils may be particularly difficult to stabilize or access, including the following situations:
    - Steep slopes, generally steeper than 1:3 (V:H).
    - Slopes where the erosion hazard is high.
    - Slopes and disturbed soils where mulch must be anchored.
    - Disturbed areas where plants are slow to develop adequate protective cover.
    - Channels with high flows.
    - Channels intended to be vegetated.
    - Slopes adjacent to water bodies of Environmentally Sensitive Areas (ESAs).
  - Blankets and mats are generally not suitable for excessively rocky sites, or areas where the final vegetation will be mowed (because staples and netting can catch in mowers).
  - Plastic results in 100 percent runoff, therefore, their use is limited to:
    - Covering stockpiles.
    - Covering small graded areas for short periods, such as through an imminent storm event, until alternative measures may be installed.
- How**
- Proper site preparation is essential to ensure complete contact of the blanket or matting with the soil.
  - Grade and shape the area of installation.
  - Remove all rocks, clods, vegetation or other obstructions so that the installed blankets or mats will have complete, direct contact with the soil.
  - Prepare seedbed by loosening of topsoil.
  - Seed the area before blanket installation for erosion control and revegetation. Seeding after mat installation is often specified for turf reinforcement application. When seeding prior to blanket installation, all check slots and other areas disturbed during installation must be re-seeded. Where soil filling is specified, seed the matting and the entire disturbed area after installation and prior to filling the mat with soil.
  - U-shaped wire staples, metal geotextile stake pins or triangular wooden stakes can be used to anchor mats and blankets to the ground surface.
  - Wire staples and metal stakes should be driven flush to the soil surface.
  - All anchors should be 6 in to 18 in long and have sufficient ground penetration to resist pullout. Longer anchors may be required for loose soils.
  - Installation on slopes – Consult the manufacturer's recommendations for installation. In general, these will be as follows:
    - Begin at the top of the slope and anchor the blanket in a 6 in deep by 6 in wide trench. Backfill trench and tamp earth firmly.
    - Unroll blanket downslope in the direction of water flow.
    - Overlap the edges of adjacent parallel rolls 2 in to 3 in and staple every 3 ft.
    - When blankets must be spliced, place blankets end over end (shingle style) with 6 in overlap. Staple through overlapped area, approximately 12 in apart.
    - Lay blankets loosely and maintain direct contact with the soil. Do not stretch.
    - Staple blankets sufficiently to anchor blanket and maintain contact with the soil. Staples shall be placed down the center and staggered with the staples placed along the edges.
  - Blankets and mats must be removed and disposed of prior to application of permanent soil stabilization measures.

### Maintenance and Inspection

- Areas treated with temporary soil stabilization should be inspected routinely and before and after significant forecasted storm events. Any failures should be repaired immediately. Areas treated with temporary soil stabilization should be maintained to provide adequate erosion control. Temporary soil stabilization should be reapplied or replaced on exposed soils when greater than 10 percent of the previously treated area becomes exposed or exhibits visible erosion.
- If washout or breakage occurs, re-install the material after repairing the damage to the slope or channel.

### Pictures



Several types of Erosion Control Blankets.

# EROSION CONTROL AND SOIL STABILIZATION

## Dust (Wind Erosion) Control

BMP 4-08




**When** This practice is implemented on exposed soils or materials subject to wind erosion.

**How** Use the following measures as applicable:

- Water applied for dust control should be applied evenly and in a manner that does not generate runoff.
- Appropriate methods of applying dust control (covers or water and the means to apply it) should be available for projects with the potential to create dust.
- Dust control must be implemented in accordance with local air quality requirements.
- Dust control methods should be approved by an Environmental Representative.
- Obtain prior approval to use any chemical dust suppressant from the projects Environmental Representative.
- Non-potable water should not be conveyed in tanks or drainpipes that will be used to convey potable water and there should be no connection between potable and nonpotable supplies. Non-potable tanks, pipes and other conveyances should be marked "NON-POTABLE WATER –DO NOT DRINK."
- If reclaimed wastewater is used for dust control, the sources and discharge must meet California Department of Health Services water reclamation criteria and the Regional Water Quality Control Board (RWQCB) requirements. Approval for use of reclaimed wastewater must be obtained from the projects Environmental Representative.


(dry or running)



**Maintenance and Inspection**

- Check areas protected to ensure coverage.
- Reapply water or maintain covers, as necessary to maintain their effectiveness.

**Pictures**

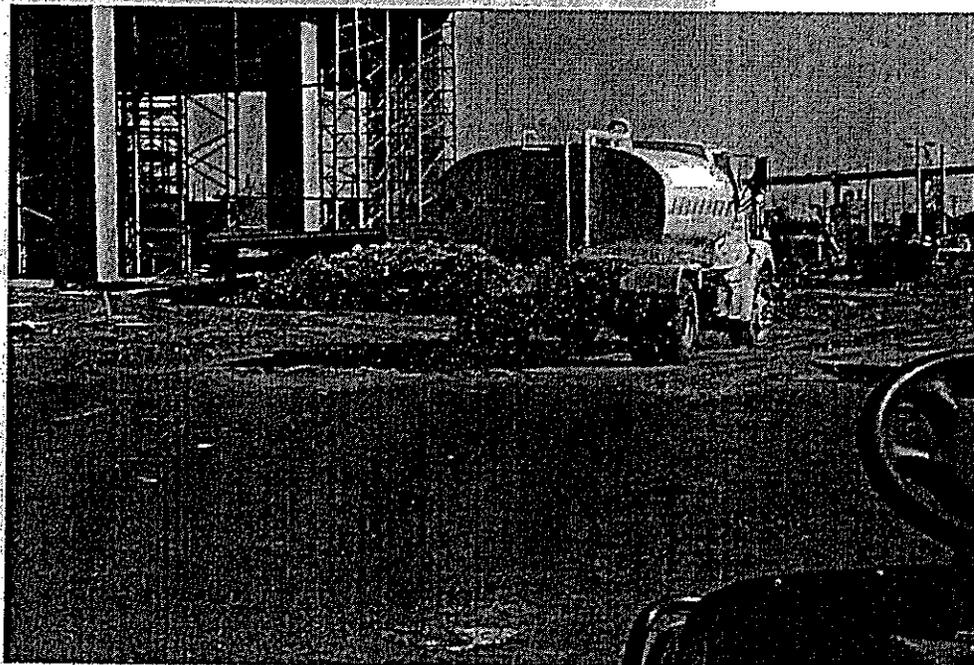


Water being applied for dust control.

# EROSION CONTROL AND SOIL STABILIZATION

## Dust (Wind Erosion) Control


---



This page intentionally left blank.

BMP	Best Management Practice
BASE	Construction and Operations Center (The Gas Company)
C&O Center	Construction and Operations Center (SDG&E)
Caltrans	California Department of Transportation
Discharger	Any person who discharges waste that could affect the quality of California waters.
DSA	Disturbed Soil Area
EP	Environmental Practice
FCD	Formal Communication Document
Non-rainy Season	May 1 to October 1, except for Southern California Desert Area where the non-rainy season ends August 1.
Rainy Season	October 1 through May 1, except for Southern California Desert Area where the rainy season starts on August 1.
RWQCB	Regional Water Quality Control Boards (RWQCB) – nine Water Boards located throughout California that are responsible for enforcing water quality standards within their boundaries.
Runoff	Rainfall or snow melt that is not absorbed by soil, evaporated, or transpired by plants, but finds its way into streams as surface flow.
ROW	Right of Way
SCG	Southern California Gas Company (The Gas Company)
SDG&E	San Diego Gas and Electric Company
SWRCB	State Water Resources Control Board (SWRCB) – The State Board responsible for protecting and preserving water quality and water rights in California.
SEU	Sempra Energy Utilities
SWPPP	Storm Water Pollution Prevention Plan
Watershed	The total land area that contributes water to a river, stream, lake, or other body of water. Synonymous with drainage area, drainage basin.

This page intentionally left blank.

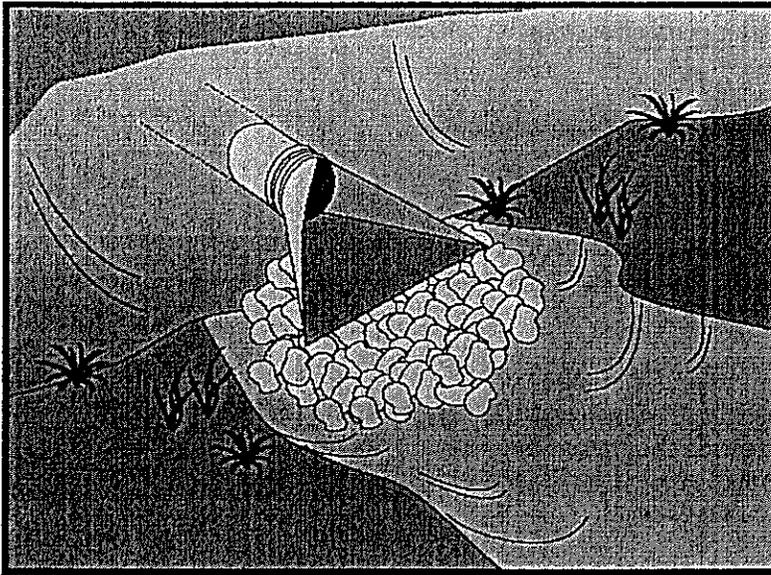

## Description and Purpose

Outlet protection is a physical device composed of rock, grouted riprap, or concrete rubble, which is placed at the outlet of a pipe or channel to prevent scour of the soil caused by concentrated, high velocity flows.

## Suitable Applications

Whenever discharge velocities and energies at the outlets of culverts, conduits, or channels are sufficient to erode the next downstream reach. This includes temporary diversion structures to divert runoff during construction.

- These devices may be used at the following locations:
  - Outlets of pipes, drains, culverts, slope drains, diversion ditches, swales, conduits, or channels.
  - Outlets located at the bottom of mild to steep slopes.
  - Discharge outlets that carry continuous flows of water.
  - Outlets subject to short, intense flows of water, such as flash floods.
  - Points where lined conveyances discharge to unlined conveyances

## Limitations

- Large storms or high flows can wash away the rock outlet protection and leave the area susceptible to erosion.

## Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	
TR	Tracking Control	
WE	Wind Erosion Control	
NS	Non-Stormwater Management Control	
WM	Waste Management and Materials Pollution Control	

## Legend:

- Primary Objective
- Secondary Objective

## Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

## Potential Alternatives

None



- Sediment captured by the rock outlet protection may be difficult to remove without removing the rock.
- Outlet protection may negatively impact the channel habitat.
- Grouted riprap may break up in areas of freeze and thaw.
- If there is not adequate drainage, and water builds up behind grouted riprap, it may cause the grouted riprap to break up due to the resulting hydrostatic pressure.

### **Implementation**

#### ***General***

Outlet protection is needed where discharge velocities and energies at the outlets of culverts, conduits or channels are sufficient to erode the immediate downstream reach. This practice protects the outlet from developing small eroded pools (plunge pools), and protects against gully erosion resulting from scouring at a culvert mouth.

#### ***Design and Layout***

As with most channel design projects, depth of flow, roughness, gradient, side slopes, discharge rate, and velocity should be considered in the outlet design. Compliance to local and state regulations should also be considered while working in environmentally sensitive streambeds. General recommendations for rock size and length of outlet protection mat are shown in the rock outlet protection figure in this BMP and should be considered minimums. The apron length and rock size gradation are determined using a combination of the discharge pipe diameter and estimate discharge rate: Select the longest apron length and largest rock size suggested by the pipe size and discharge rate. Where flows are conveyed in open channels such as ditches and swales, use the estimated discharge rate for selecting the apron length and rock size. Flows should be same as the culvert or channel design flow but never the less than the peak 5 year flow for temporary structures planned for one rainy season, or the 10 year peak flow for temporary structures planned for two or three rainy seasons.

- There are many types of energy dissipaters, with rock being the one that is represented in the attached figure.
- Best results are obtained when sound, durable, and angular rock is used.
- Install riprap, grouted riprap, or concrete apron at selected outlet. Riprap aprons are best suited for temporary use during construction. Grouted or wired tied rock riprap can minimize maintenance requirements.
- Rock outlet protection is usually less expensive and easier to install than concrete aprons or energy dissipaters. It also serves to trap sediment and reduce flow velocities.
- Carefully place riprap to avoid damaging the filter fabric.
  - Stone 4 in. to 6 in. may be carefully dumped onto filter fabric from a height not to exceed 12 in.
  - Stone 8 in. to 12 in. must be hand placed onto filter fabric, or the filter fabric may be covered with 4 in. of gravel and the 8 in. to 12 in. rock may be dumped from a height not to exceed 16 in.

- Stone greater than 12 in. shall only be dumped onto filter fabric protected with a layer of gravel with a thickness equal to one half the  $D_{50}$  rock size, and the dump height limited to twice the depth of the gravel protection layer thickness.
- For proper operation of apron: Align apron with receiving stream and keep straight throughout its length. If a curve is needed to fit site conditions, place it in upper section of apron.
- Outlets on slopes steeper than 10 percent should have additional protection.

## Costs

Costs are low if material is readily available. If material is imported, costs will be higher. Average installed cost is \$150 per device.

## Inspection and Maintenance

- Inspect BMPs prior to forecast rain, daily during extended rain events, after rain events, weekly during the rainy season, and at two-week intervals during the non-rainy season.
- Inspect BMPs subjected to non-stormwater discharges daily while non-stormwater discharges occur.
- Inspect apron for displacement of the riprap and damage to the underlying fabric. Repair fabric and replace riprap that has washed away. If riprap continues to wash away, consider using larger material.
- Inspect for scour beneath the riprap and around the outlet. Repair damage to slopes or underlying filter fabric immediately.
- Temporary devices should be completely removed as soon as the surrounding drainage area has been stabilized or at the completion of construction.

## References

County of Sacramento Improvement Standards, Sacramento County, May 1989.

Erosion and Sediment Control Handbook, S.J. Goldman, K. Jackson, T.A. Bursztynsky, P.E., McGraw Hill Book Company, 1986.

Handbook of Steel Drainage & Highway Construction, American Iron and Steel Institute, 1983.

Manual of Standards of Erosion and Sediment Control Measures, Association of Bay Area Governments, May 1995.



Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, state of California Department of Transportation (Caltrans), November 2000.

Stormwater Management of the Puget Sound Basin, Technical Manual, Publication #91-75, Washington State Department of Ecology, February 1992.

Water Quality Management Plan for the Lake Tahoe Region, Volume II, Handbook of Management Practices, Tahoe Regional Planning Agency, November 1988.

# EC-10


# Velocity Dissipation Devices

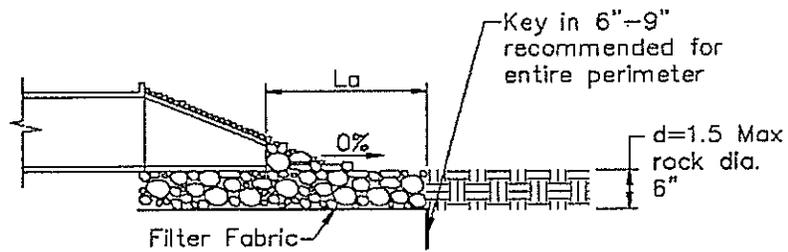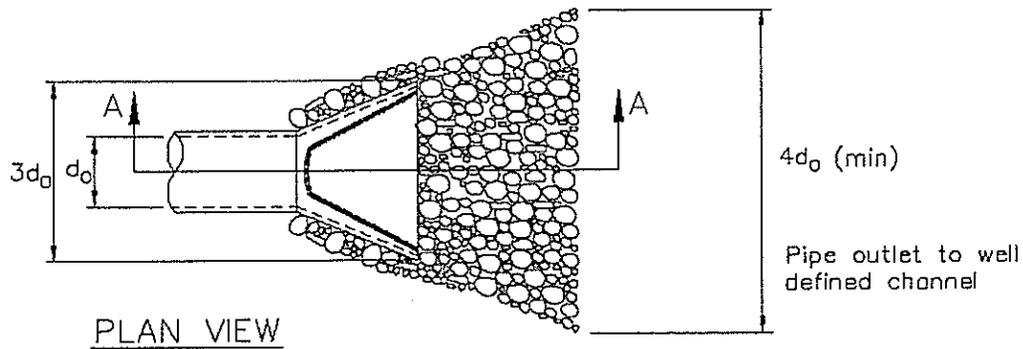

SECTION A-A

Pipe Diameter inches	Discharge ft <sup>3</sup> /s	Apron Length, L <sub>a</sub> ft	Rip Rap D <sub>50</sub> Diameter Min inches
12	5	10	4
	10	13	6
18	10	10	6
	20	16	8
	30	23	12
	40	26	16
24	30	16	8
	40	26	8
	50	26	12
	60	30	16

For larger or higher flows consult a Registered Civil Engineer  
Source: USDA - SCS

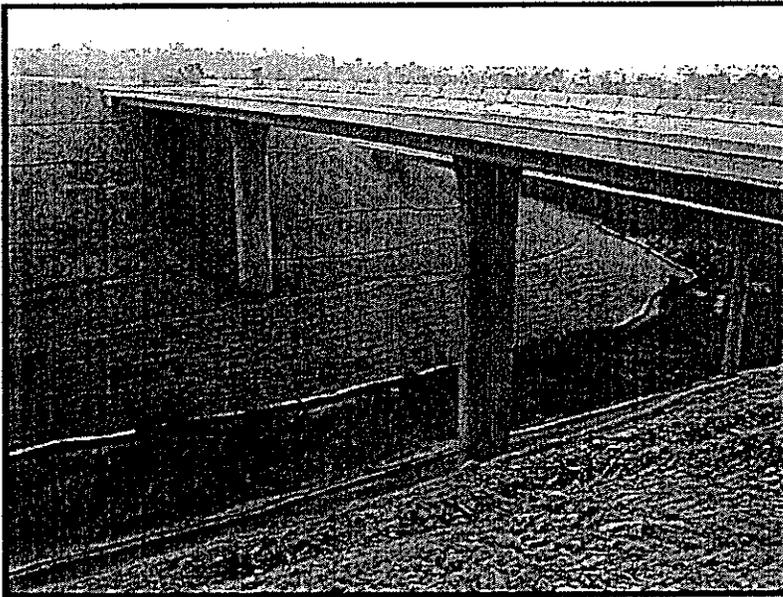

## Description and Purpose

Stream channels, streambanks, and associated riparian areas are dynamic and sensitive ecosystems that respond to changes in land use activity. Streambank and channel disturbance resulting from construction activities can increase the stream's sediment load, which can cause channel erosion or sedimentation and have adverse effects on the biotic system. BMPs can reduce the discharge of sediment and other pollutants to minimize the impact of construction activities on watercourses. Streams on the 303(d) list and listed for sediment may require numerous measures to prevent any increases in sediment load to the stream.

## Suitable Applications

These procedures typically apply to all construction projects that disturb or occur within stream channels and their associated riparian areas.

## Limitations

Specific permit requirements or mitigation measures such as Regional Water Quality Control Board (RWQCB) 401 Certification, U.S. Army Corps of Engineers 404 permit and approval by California Department of Fish and Game supercede the guidance in this BMP.

- If numerical based water quality standards are mentioned in any of these and other related permits, testing and sampling may be required. Streams listed as 303(d) impaired for sediment, silt, or turbidity, are required to conduct sampling

## Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	<input checked="" type="checkbox"/>
TR	Tracking Control	
WE	Wind Erosion Control	
NS	Non-Stormwater Management Control	<input checked="" type="checkbox"/>
WM	Waste Management and Materials Pollution Control	

### Legend:

- Primary Objective
- Secondary Objective

## Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

## Potential Alternatives

Combination of erosion and sediment controls.



to verify that there is no net increase in sediment load due to construction activities.

## Implementation

### *Planning*

- Proper planning, design, and construction techniques can minimize impacts normally associated with in stream construction activities. Poor planning can adversely affect soil, fish, wildlife resources, land uses, or land users. Planning should take into account: scheduling; avoidance of in-stream construction; minimizing disturbance area and construction time period; using pre-disturbed areas; selecting crossing location; and selecting equipment.

### *Scheduling*

- Construction activities should be scheduled according to the relative sensitivity of the environmental concerns and in accordance with EC-1, Scheduling. Scheduling considerations will be different when working near perennial streams vs. ephemeral streams and are as follows.
- When in-stream construction is conducted in a perennial stream, work should optimally be performed during the rainy season. This is because in the summer, any sediment-containing water that is discharged into the watercourse will cause a large change in both water clarity and water chemistry. During the rainy season, there is typically more and faster flowing water in the stream so discharges are diluted faster. However, should in-stream work be scheduled for summer, establishing an isolation area, or diverting the stream, will significantly decrease the amount of sediment stirred up by construction work. Construction work near perennial streams should optimally be performed during the dry season (see below).
- When working in or near ephemeral streams, work should be performed during the dry season. By their very nature, ephemeral streams are usually dry in the summer, and therefore, in-stream construction activities will not cause significant water quality problems. However, when tying up the site at the end of the project, wash any fines (see Washing Fines) that accumulated in the channel back into the bed material, to decrease pollution from the first rainstorm of the season.
- When working near ephemeral or perennial streams, erosion and sediment controls (see silt fences, straw bale barriers, etc.) should be implemented to keep sediment out of stream channel.

### *Minimize Disturbance*

- Minimize disturbance through: selection of the narrowest crossing location; limiting the number of equipment trips across a stream during construction; and, minimizing the number and size of work areas (equipment staging areas and spoil storage areas). Place work areas at least 50 ft from stream channel. Field reconnaissance should be conducted during the planning stage to identify work areas.

### *Use of Pre-Disturbed Areas*

- Locate project sites and work areas in areas disturbed by prior construction or other activity when possible.

## *Selection of Project Site*

- Avoid steep and unstable banks, highly erodible or saturated soils, or highly fractured rock.
- Select project site that minimizes disturbance to aquatic species or habitat.

## *Equipment Selection*

- Select equipment that reduces the amount of pressure exerted on the ground surface, and therefore, reduces erosion potential and/or use overhead or aerial access for transporting equipment across drainage channels. Use equipment that exerts ground pressures of less than 5 or 6 lb/in<sup>2</sup>, where possible. Low ground pressure equipment includes: wide or high flotation tires (34 to 72 in. wide); dual tires; bogie axle systems; tracked machines; lightweight equipment; and, central tire inflation systems.

## **Streambank Stabilization**

### ***Preservation of Existing Vegetation***

- Preserve existing vegetation in accordance with EC-2, Preservation of Existing Vegetation. In a streambank environment, preservation of existing vegetation provides the following benefits.

### *Water Quality Protection*

- Vegetated buffers on slopes trap sediment and promote groundwater recharge. The buffer width needed to maintain water quality ranges from 15 to 100 ft. On gradual slopes, most of the filtering occurs within the first 30 ft. Steeper slopes require a greater width of vegetative buffer to provide water quality benefits.

### *Streambank Stabilization*

- The root system of riparian vegetation stabilizes streambanks by increasing tensile strength in the soil. The presence of vegetation modifies the moisture condition of slopes (infiltration, evapo transpiration, interception) and increases bank stability.

### *Riparian Habitat*

- Buffers of diverse riparian vegetation provide food and shelter for riparian and aquatic organisms. Minimizing impacts to fisheries habitat is a major concern when working near streams and rivers. Riparian vegetation provides shade, shelter, organic matter (leaf detritus and large woody debris), and other nutrients that are necessary for fish and other aquatic organisms. Buffer widths for habitat concerns are typically wider than those recommended for water quality concerns (100 to 1500 ft).
- When working near watercourses, it is important to understand the work site's placement in the watershed. Riparian vegetation in headwater streams has a greater impact on overall water quality than vegetation in downstream reaches. Preserving existing vegetation upstream is necessary to maintain water quality, minimize bank failure, and maximize riparian habitat, downstream of the work site.

### *Limitations*

- Local county and municipal ordinances regarding width, extent and type of vegetative buffer required may exceed the specifications provided here; these ordinances should be investigated prior to construction.

*Streambank Stabilization Specific Installation*

- As a general rule, the width of a buffer strip between a road and the stream is recommended to be 50 ft plus four times the percent slope of the land, measured between the road and the top of stream bank.

**Hydraulic Mulch**

- Apply hydraulic mulch on disturbed streambanks above mean high water level in accordance with EC-3, Hydraulic Mulch to provide temporary soil stabilization.

*Limitations*

- Do not place hydraulic mulch or tackifiers below the mean high water level, as these materials could wash into the channel and impact water quality or possibly cause eutrophication (eutrophication is an algal bloom caused by excessively high nutrient levels in the water).

**Hydroseeding**

- Hydroseed disturbed streambanks in accordance with EC-4, Hydroseeding.

*Limitations*

- Do not place tackifiers or fertilizers below the mean high water level, as these materials could wash into the channel and impact water quality or possibly cause eutrophication.

**Soil Binders**

- Apply soil binders to disturbed streambanks in accordance with EC-5, Soil Binders.

*Limitations*

- Do not place soil binders below the mean high water level. Soil binder must be environmentally benign and non-toxic to aquatic organisms.

**Straw Mulch**

- Apply straw mulch to disturbed streambanks in accordance with EC-6, Straw Mulch.

*Limitations*

- Do not place straw mulch below the mean high water level, as this material could wash into the channel and impact water quality or possibly cause eutrophication.

**Geotextiles and Mats**

- Install geotextiles and mats as described in EC-7, Geotextiles and Mats, to stabilize disturbed channels and streambanks. Not all applications should be in the channel, for example, certain geotextile netting may snag fish gills and are not appropriate in fish bearing streams. Geotextile fabrics that are not biodegradable are not appropriate for in stream use. Additionally, geotextile fabric or blankets placed in channels must be adequate to sustain anticipated hydraulic forces.

**Earth Dikes, Drainage Swales, and Lined Ditches**

- Convey, intercept, or divert runoff from disturbed streambanks using EC-9, Earth Dikes and Drainage Swales.

## *Limitations*

- Do not place earth dikes in watercourses, as these structures are only suited for intercepting sheet flow, and should not be used to intercept concentrated flow.
- Appropriately sized velocity dissipation devices (EC-10) must be placed at outlets to minimize erosion and scour.

## ***Velocity Dissipation Devices***

- Place velocity dissipation devices at outlets of pipes, drains, culverts, slope drains, diversion ditches, swales, conduits or channels in accordance with EC-10, Velocity Dissipation Devices.

## ***Slope Drains***

- Use slope drains to intercept and direct surface runoff or groundwater into a stabilized watercourse, trapping device or stabilized area in accordance with EC-11, Slope Drains.

## *Limitations*

- Appropriately sized outlet protection and velocity dissipation devices (EC-10) must be placed at outlets to minimize erosion and scour.

## **Streambank Sediment Control**

### ***Silt Fences***

- Install silt fences in accordance with SE-1, Silt Fence, to control sediment. Silt fences should only be installed where sediment laden water can pond, thus allowing the sediment to settle out.

### ***Fiber Rolls***

- Install fiber rolls in accordance with SE-5, Fiber Rolls, along contour of slopes above the high water level to intercept runoff, reduce flow velocity, release the runoff as sheet flow and provide removal of sediment from the runoff. In a stream environment, fiber rolls should be used in conjunction with other sediment control methods such as SE-1, Silt Fence or SE-9 Straw Bale Barrier. Install silt fence, straw bale barrier, or other erosion control method along toe of slope above the high water level.

### ***Gravel Bag Berm***

- A gravel bag berm or barrier can be utilized to intercept and slow the flow of sediment laden sheet flow runoff in accordance with SE-6, Gravel Bag Berm. In a stream environment gravel bag barriers can allow sediment to settle from runoff before water leaves the construction site and can be used to isolate the work area from the live stream.

## *Limitations*

- Gravel bag barriers are not recommended as a perimeter sediment control practice around streams.

### ***Straw Bale Barrier***

- Install straw bale barriers in accordance with SE-9, Straw Bale Barrier, to control sediment. Straw bale barriers should only be installed where sediment laden water can pond, thus allowing the sediment to settle out. Install a silt fence in accordance with SE-1, Silt Fence,

on down slope side of straw bale barrier closest to stream channel to provide added sediment control.

***Rock Filter******Description and Purpose***

Rock filters are temporary erosion control barriers composed of rock that is anchored in place. Rock filters detain the sediment laden runoff, retain the sediment, and release the water as sheet flow at a reduced velocity. Typical rock filter installations are illustrated at the end of this BMP.

***Applications***

- Near the toe of slopes that may be subject to flow and rill erosion.

***Limitations***

- Inappropriate for contributing drainage areas greater than 5 acres.
- Requires sufficient space for ponded water.
- Ineffective for diverting runoff because filters allow water to slowly seep through.
- Rock filter berms are difficult to remove when construction is complete.
- Unsuitable in developed areas or locations where aesthetics is a concern.

***Specifications***

- Rock: open graded rock, 0.75 to 5 in. for concentrated flow applications.
- Woven wire sheathing: 1 in. diameter, hexagonal mesh, galvanized 20gauge (used with rock filters in areas of concentrated flow).
- In construction traffic areas, maximum rock berm heights should be 12 in. Berms should be constructed every 300 ft on slopes less than 5%, every 200 ft on slopes between 5% and 10%, and every 100 ft on slopes greater than 10%.

***Maintenance***

- Inspect and verify that activity-based BMPs are in place prior to the commencement of associated activities. While activities associated with the BMP are under way, inspect weekly during the rainy season and at two-week intervals in the non-rainy season to verify continued BMP implementation.
- Inspect BMPs subject to non-stormwater discharges daily while non-stormwater discharges occur.
- Reshape berms as needed and replace lost or dislodged rock, and filter fabric.
- Sediment that accumulates in the BMP must be periodically removed in order to maintain BMP effectiveness. Sediment should be removed when the sediment accumulation reaches one third of the barrier height. Sediment removed during maintenance may be incorporated into earthwork on the site or disposed at an appropriate location.

## *K-rail*

### *Description and Purpose*

This is temporary sediment control that uses K-rails to form the sediment deposition area, or to isolate the near bank construction area. Install K-rails at toe of slope in accordance with procedures described in NS-5, Clear Water Diversion.

Barriers are placed end to end in a pre-designed configuration and gravel filled bags are used at the toe of the barrier and at their abutting ends to seal and prevent movement of sediment beneath or through the barrier walls.

### *Appropriate Applications*

- This technique is useful at the toe of embankments, cuts or fills slopes.

### *Limitations*

- The K-rail method should not be used to dewater a project site, as the barrier is not watertight.

### *Implementation*

- Refer to NS-5, Clear Water Diversion, for implementation requirements.

## **Instream Construction Sediment Control**

There are three different options currently available for reducing turbidity while working in a stream or river. The stream can be isolated from the area in which work is occurring by means of a water barrier, the stream can be diverted around the work site through a pipe or temporary channel, or one can employ construction practices that minimize sediment suspension.

Whatever technique is implemented, an important thing to remember is that dilution can sometimes be the solution. A probable "worst time" to release high TSS into a stream system might be when the stream is very low; summer low flow, for example. During these times, the flow may be low while the biological activity in the stream is very high. Conversely, the addition of high TSS or sediment during a big storm discharge might have a relatively low impact, because the stream is already turbid, and the stream energy is capable of transporting both suspended solids, and large quantities of bedload through the system. The optimum time to "pull" in-stream structures may be during the rising limb of a storm hydrograph.

### ***Techniques to minimize Total Suspended Solids (TSS)***

- **Padding** - Padding laid in the stream below the work site may trap some solids that are deposited in the stream during construction. After work is done, the padding is removed from the stream, and placed on the bank to assist in re-vegetation.
- **Clean, washed gravel** - Using clean, washed gravel decreases solid suspension, as there are fewer small particles deposited in the stream.
- **Excavation using a large bucket** - Each time a bucket of soil is placed in the stream, a portion is suspended. Approximately the same amount is suspended whether a small amount of soil is placed in the stream, or a large amount. Therefore, using a large excavator bucket instead of a small one, will reduce the total amount of soil that washes downstream.

- **Use of dozer for backfilling** - Using a dozer for backfilling instead of a backhoe follows the same principles – the fewer times soil is deposited in the stream, the less soil will be suspended.
- **Partial dewatering with a pump** - Partially dewatering a stream with a pump reduces the amount of water, and thus the amount of water that can suspend sediment.

### *Washing Fines*

#### *Definition and Purpose*

- Washing fines is an “in-channel” sediment control method, which uses water, either from a water truck or hydrant, to wash stream fines that were brought to the surface of the channel bed during restoration, back into the interstitial spaces of the gravel and cobbles.
- The purpose of this technique is to reduce or eliminate the discharge of sediment from the channel bottom during the first seasonal flow. Sediment should not be allowed into stream channels; however, occasionally in-channel restoration work will involve moving or otherwise disturbing fines (sand and silt sized particles) that are already in the stream, usually below bankfull discharge elevation. Subsequent re-watering of the channel can result in a plume of turbidity and sedimentation.
- This technique washes the fines back into the channel bed. Bedload materials, including gravel cobbles, boulders and those fines, are naturally mobilized during higher storm flows. This technique is intended to delay the discharge until the fines would naturally be mobilized.

#### *Appropriate Applications*

- This technique should be used when construction BMP work is required in channels. It is especially useful in intermittent or ephemeral streams in which work is performed “in the dry”, and which subsequently become re-watered.

#### *Limitations*

- The stream must have sufficient gravel and cobble substrate composition.
- The use of this technique requires consideration of time of year and timing of expected stream flows.
- The optimum time for the use of this technique is in the fall, prior to winter flows.
- Consultation with, and approval from the Department of Fish and Game and the Regional Water Quality Control Board may be required.

#### *Implementation*

- Apply sufficient water to wash fines, but not cause further erosion or runoff.
- Apply water slowly and evenly to prevent runoff and erosion.
- Consult with Department of Fish and Game and the Regional Water Quality Control Board for specific water quality requirements of applied water (e.g. chlorine).

## *Inspection and Maintenance*

- None necessary

## **Costs**

Cost may vary according to the combination of practices implemented.

## **Inspection and Maintenance**

- Inspect and verify that activity-based BMPs are in place prior to the commencement of associated activities. While activities associated with the BMP are under way, inspect weekly during the rainy season and at two-week intervals in the non-rainy season to verify continued BMP implementation.
- Inspect BMPs subject to non-stormwater discharges daily while non-stormwater discharges occur.
- Inspect and repair equipment (for damaged hoses, fittings, and gaskets).

## **References**

Manual of Standards of Erosion and Sediment Control Measures, Association of Bay Area Governments, May 1995.



Proposed Guidance Specifying Management Measures for Sources of Nonpoint Pollution in Coastal Waters, Work Group Working Paper, USEPA, April 1992.

Sedimentation and Erosion Control Practices, An Inventory of Current Practices (Draft), USEPA, 1990.


Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

Stormwater Management for Construction Activities, Developing Pollution Prevention Plans and Best Management Practices, EPA 832-R-92005; USEPA, April 1992.

Water Quality Management Plan for the Lake Tahoe Region, Volume II, Handbook of Management Practices, Tahoe Regional Planning Agency, November 1988.

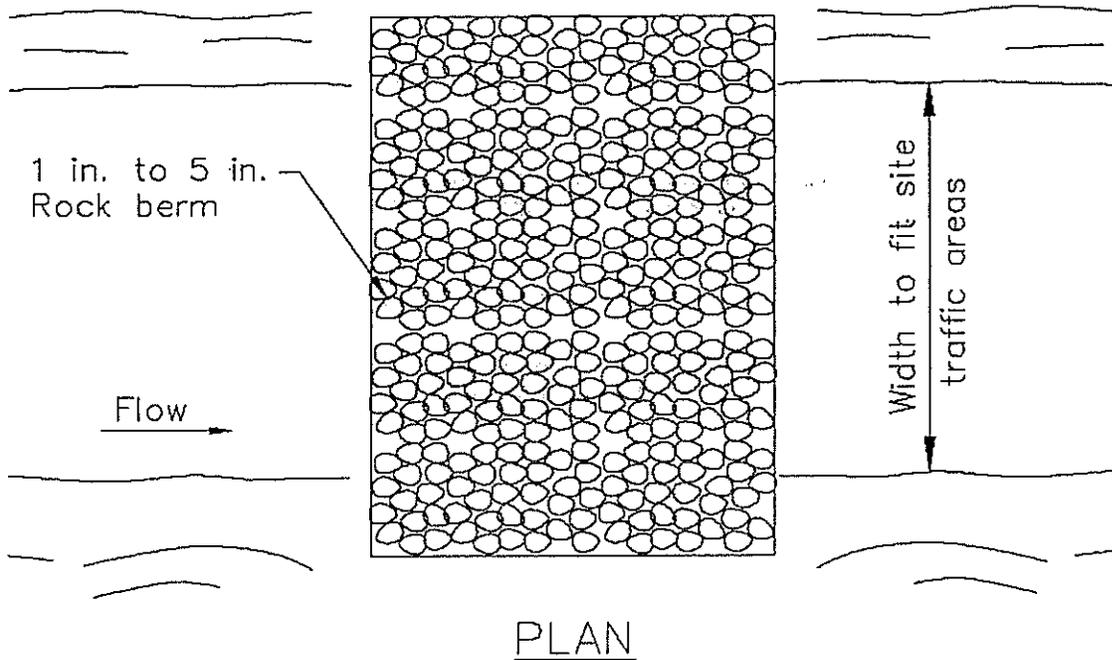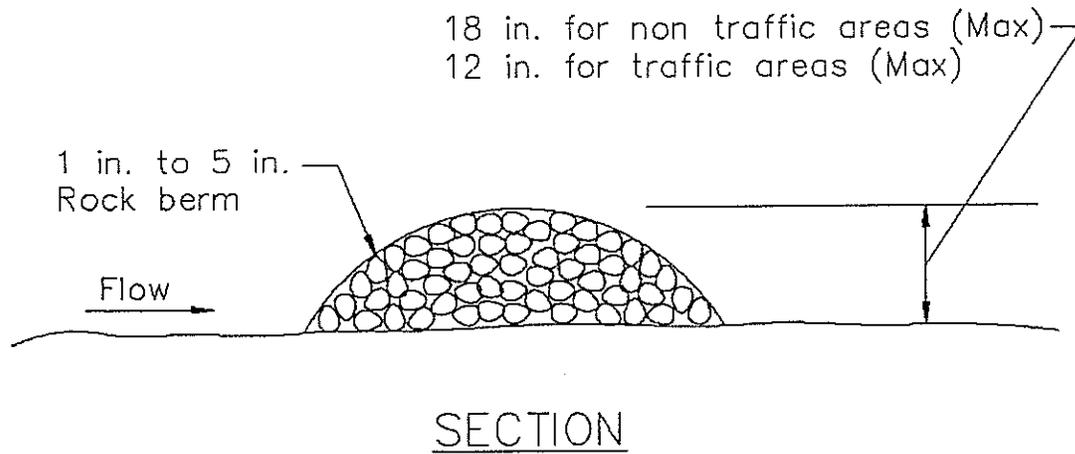

TYPICAL ROCK FILTER  
NOT TO SCALE

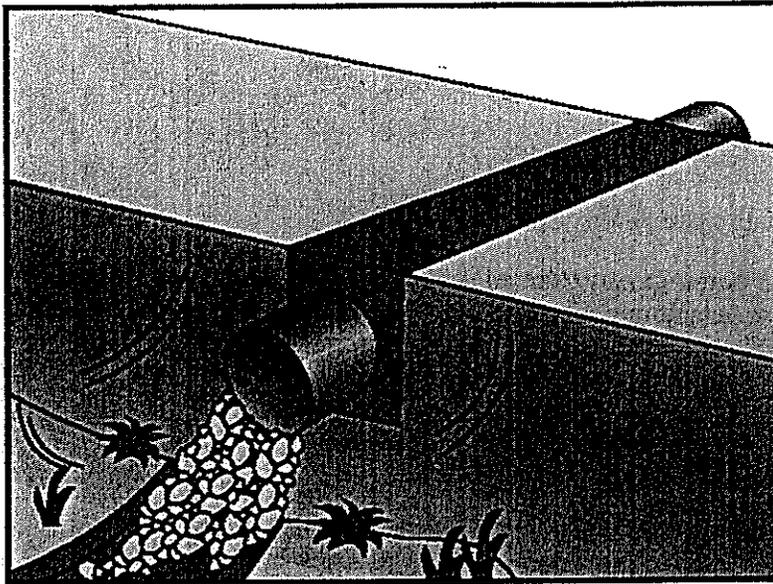

## Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	<input checked="" type="checkbox"/>
TR	Tracking Control	<input checked="" type="checkbox"/>
WE	Wind Erosion Control	
NS	Non-Stormwater Management Control	<input checked="" type="checkbox"/>
WM	Waste Management and Materials Pollution Control	

## Legend:

- Primary Objective
- Secondary Objective

## Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

## Potential Alternatives

None

## Description and Purpose


A temporary stream crossing is a temporary culvert, ford, or bridge placed across a waterway to provide access for construction purposes for a period of less than one year. Temporary access crossings are not intended to maintain traffic for the public. The temporary access will eliminate erosion and downstream sedimentation caused by vehicles.

## Suitable Applications

Temporary stream crossings should be installed at all designated crossings of perennial and intermittent streams on the construction site, as well as for dry channels that may be significantly eroded by construction traffic.

Temporary stream crossings are installed at sites:

- Where appropriate permits have been secured (404 Permits, and 401 Certifications)
- Where construction equipment or vehicles need to frequently cross a waterway
- When alternate access routes impose significant constraints
- When crossing perennial streams or waterways causes significant erosion
- Where construction activities will not last longer than one year



- Where appropriate permits have been obtained for the stream crossing

**Limitations**

The following limitations may apply:

- Installation and removal will usually disturb the waterway.
- Installation may require Regional Water Quality Control Board (RWQCB) 401 Certification, U.S. Army Corps of Engineers 404 permit and approval by California Department of Fish and Game. If numerical-based water quality standards are mentioned in any of these and other related permits, testing and sampling may be required.
- Installation may require dewatering or temporary diversion of the stream. See NS-2, Dewatering Operations and NS-5, Clear Water Diversion.
- Installation may cause a constriction in the waterway, which can obstruct flood flow and cause flow backups or washouts. If improperly designed, flow backups can increase the pollutant load through washouts and scouring.
- Use of natural or other gravel in the stream for construction of Cellular Confinement System (CCS) ford crossing will be contingent upon approval by fisheries agencies.
- Ford crossings may degrade water quality due to contact with vehicles and equipment.
- May be expensive for a temporary improvement.
- Requires other BMPs to minimize soil disturbance during installation and removal.
- Fords should only be used in dry weather.

**Implementation****General**

The purpose of this BMP is to provide a safe, erosion-free access across a stream for construction equipment. Minimum standards and specifications for the design, construction, maintenance, and removal of the structure should be established by an engineer registered in California. Temporary stream crossings may be necessary to prevent construction equipment from causing erosion of the stream and tracking sediment and other pollutants into the stream.

Temporary stream crossings are used as access points to construction sites when other detour routes may be too long or burdensome for the construction equipment. Often heavy construction equipment must cross streams or creeks, and detour routes may impose too many constraints such as being too narrow or poor soil strength for the equipment loadings. Additionally, the contractor may find a temporary stream crossing more economical for light-duty vehicles to use for frequent crossings, and may have less environmental impact than construction of a temporary access road.

Location of the temporary stream crossing should address:

- Site selection where erosion potential is low.

- Areas where the side slopes from site runoff will not spill into the side slopes of the crossing.

The following types of temporary stream crossings should be considered:

- **Culverts** – A temporary culvert is effective in controlling erosion but will cause erosion during installation and removal. A temporary culvert can be easily constructed and allows for heavy equipment loads.
- **Fords** - Appropriate during the dry season in arid areas. Used on dry washes and ephemeral streams, and low-flow perennial streams. CCS, a type of ford crossing, is also appropriate for use in streams that would benefit from an influx of gravels. A temporary ford provides little sediment and erosion control and is ineffective in controlling erosion in the stream channel. A temporary ford is the least expensive stream crossing and allows for maximum load limits. It also offers very low maintenance. Fords are more appropriate during the dry ice season and in arid areas of California.
- **Bridges** - Appropriate for streams with high flow velocities, steep gradients and where temporary restrictions in the channel are not allowed.

## *Design*

During the long summer construction season in much of California, rainfall is infrequent and many streams are dry. Under these conditions, a temporary ford may be sufficient. A ford is not appropriate if construction will continue through the winter rainy season, if summer thunderstorms are likely, or if the stream flows during most of the year. Temporary culverts and bridges should then be considered and, if used, should be sized to pass a significant design storm (i.e., at least a 10-year storm). The temporary stream crossing should be protected against erosion, both to prevent excessive sedimentation in the stream and to prevent washout of the crossing.

Design and installation requires knowledge of stream flows and soil strength. Designs should be prepared under direction of, and approved by, a registered civil engineer and for bridges, a registered structural engineer. Both hydraulic and construction loading requirements should be considered with the following:

- Comply with any special requirements for culvert and bridge crossings, particularly if the temporary stream crossing will remain through the rainy season.
- Provide stability in the crossing and adjacent areas to withstand the design flow. The design flow and safety factor should be selected based on careful evaluation of the risks due to over topping, flow backups, or washout.
- Install sediment traps immediately downstream of crossings to capture sediments. See SE-3, Sediment Trap.
- Avoid oil or other potentially hazardous materials for surface treatment.
- Culverts are relatively easy to construct and able to support heavy equipment loads.
- Fords are the least expensive of the crossings, with maximum load limits.

- CCS crossing structures consist of clean, washed gravel and cellular confinement system blocks. CCS are appropriate for streams that would benefit from an influx of gravel; for example, salmonid streams, streams or rivers below reservoirs, and urban, channelized streams. Many urban stream systems are gravel-deprived due to human influences, such as dams, gravel mines, and concrete channels.
- CCS allow designers to use either angular or naturally occurring rounded gravel, because the cells provide the necessary structure and stability. In fact, natural gravel is optimal for this technique, because of the habitat improvement it will provide after removal of the CCS.
- A gravel depth of 6 to 12 in. for a CCS structure is sufficient to support most construction equipment.
- An advantage of a CCS crossing structure is that relatively little rock or gravel is needed, because the CCS provides the stability.
- Bridges are generally more expensive to design and construct, but provide the least disturbance of the streambed and constriction of the waterway flows.

### ***Construction and Use***

- Stabilize construction roadways, adjacent work area, and stream bottom against erosion.
- Construct during dry periods to minimize stream disturbance and reduce costs.
- Construct at or near the natural elevation of the streambed to prevent potential flooding upstream of the crossing.
- Install temporary erosion control BMPs in accordance with erosion control BMP fact sheets to minimize erosion of embankment into flow lines.
- Any temporary artificial obstruction placed within flowing water should only be built from material, such as clean gravel or sandbags, that will not introduce sediment or silt into the watercourse.
- Temporary water body crossings and encroachments should be constructed to minimize scour. Cobbles used for temporary water body crossings or encroachments should be clean, rounded river cobble.
- Vehicles and equipment should not be driven, operated, fueled, cleaned, maintained, or stored in the wet or dry portions of a water body where wetland vegetation, riparian vegetation, or aquatic organisms may be destroyed.
- The exterior of vehicles and equipment that will encroach on the water body within the project should be maintained free of grease, oil, fuel, and residues.
- Drip pans should be placed under all vehicles and equipment placed on docks, barges, or other structures over water bodies when the vehicle or equipment is planned to be idle for more than one hour.

- Disturbance or removal of vegetation should not exceed the minimum necessary to complete operations. Precautions should be taken to avoid damage to vegetation by people or equipment. Disturbed vegetation should be replaced with the appropriate soil stabilization measures.
- Riparian vegetation, when removed pursuant to the provisions of the work, should be cut off no lower than ground level to promote rapid re-growth. Access roads and work areas built over riparian vegetation should be covered by a sufficient layer of clean river run cobble to prevent damage to the underlying soil and root structure. The cobble must be removed upon completion of project activities.
- Conceptual temporary stream crossings are shown in the attached figures.

## Costs

Caltrans Construction Cost index for temporary bridge crossings is \$45-\$95/ft<sup>2</sup>.


## Inspection and Maintenance

- Inspect and verify that activity-based BMPs are in place prior to the commencement of associated activities. While activities associated with the BMP are under way, inspect weekly during the rainy season and at two week intervals in the non-rainy season to verify continued BMP implementation.
- Check for blockage in the channel, sediment buildup or trapped debris in culverts, blockage behind fords or under bridges
- Check for erosion of abutments, channel scour, riprap displacement, or piping in the soil
- Check for structural weakening of the temporary crossings, such as cracks, and undermining of foundations and abutments
- Remove sediment that collects behind fords, in culverts, and under bridges periodically
- Replace lost or displaced aggregate from inlets and outlets of culverts and cellular confinement systems
- Remove temporary crossing promptly when it is no longer needed

## References


California Bank and Shore Rock Slope Protection Design – Practitioners Guide and Field Evaluations of Riprap Methods, Caltrans Study No. F90TLO3, October 2000.

Stormwater Quality Handbooks - Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

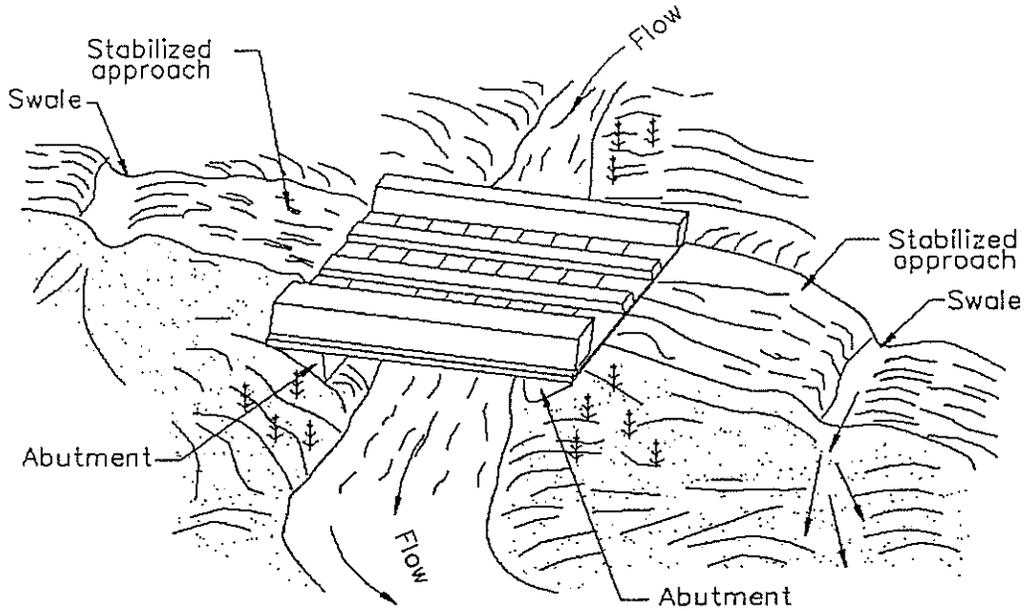


NOTE:  
Surface flow of road diverted  
by swale and/or dike.

TYPICAL BRIDGE CROSSING  
NOT TO SCALE

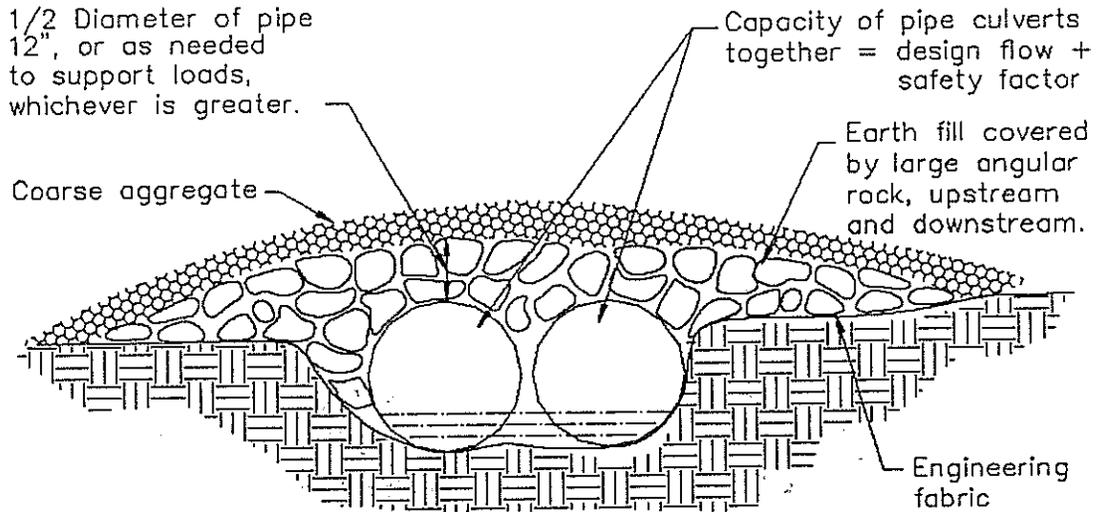


## ELEVATION

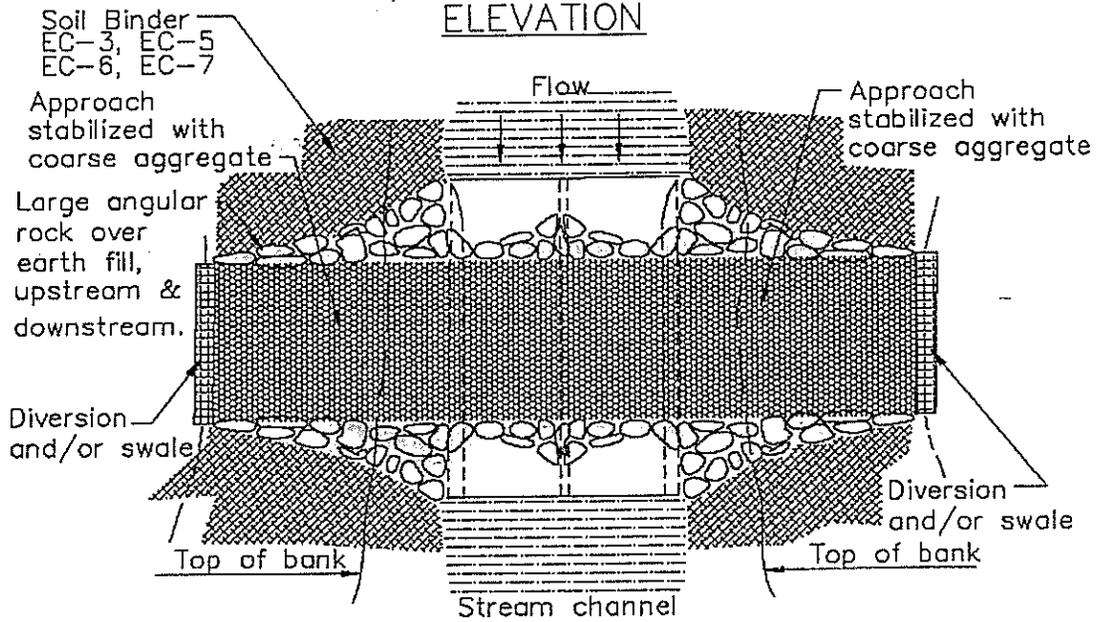


## PLAN VIEW

**TYPICAL CULVERT CROSSING**  
NOT TO SCALE

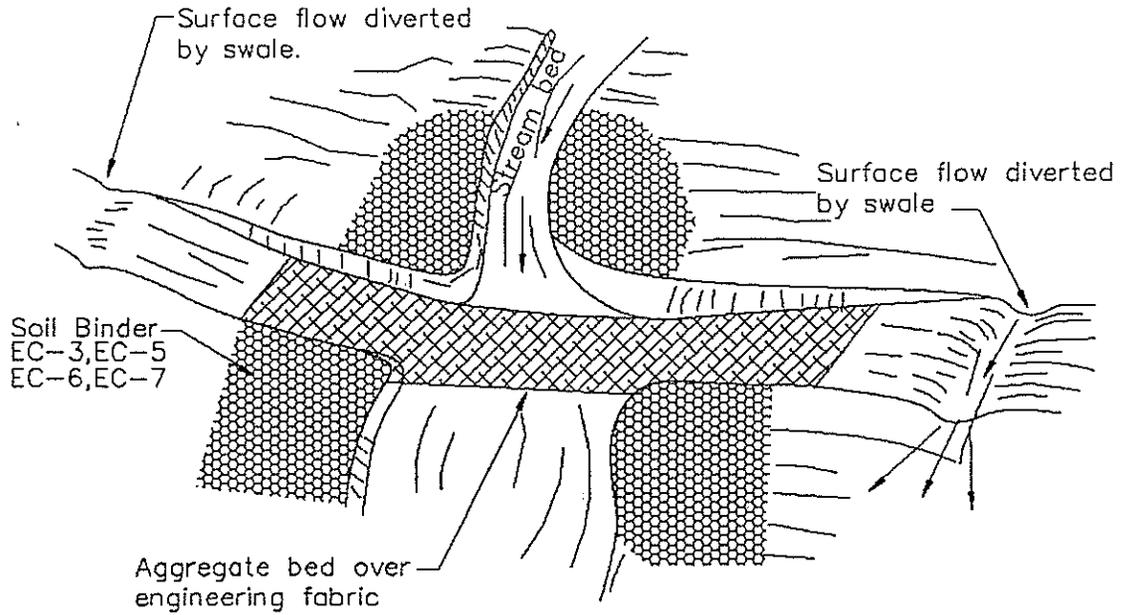

Aggregate approach  
1:5 (V:H) Maximum slope on road

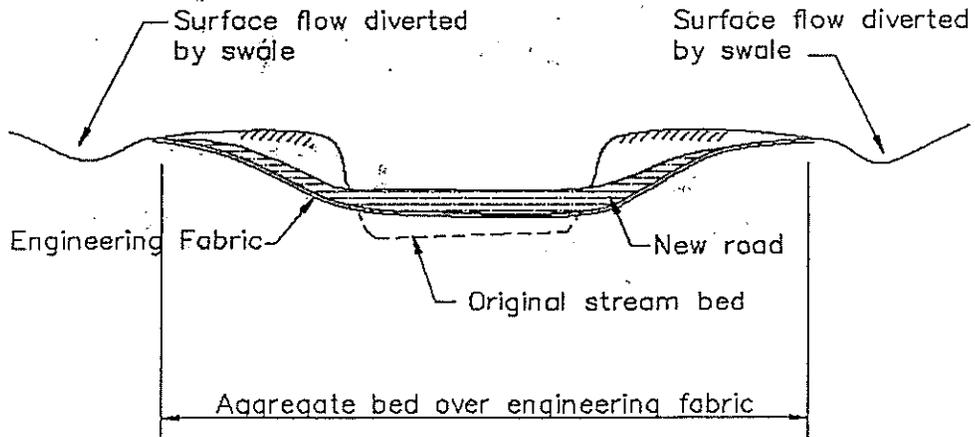

TYPICAL FORD CROSSING  
NOT TO SCALE

# **Appendix VII**

## **BMP Information**

# Post-Construction Water Balance Calculator

Not Applicable

# Appendix VIII

## REAPS

# Rain Event Action Plan (REAP)

<b>Date:</b>	<b>WDID Number:</b>	
<b>Date Rain Predicted to Occur:</b>	<b>Predicted % chance of rain:</b>	

**Site Information:**

Site Name, City and Zip Code \_\_\_\_\_ Project Risk Level:  Risk Level 2  Risk Level 3

**Site Stormwater Manager Information:**

Name, Company, Emergency Phone Number (24/7) \_\_\_\_\_

**Erosion and Sediment Control Contractor – Labor Force contracted for the site:**

Name, Company, Emergency Phone Number (24/7) \_\_\_\_\_

**Stormwater Sampling Agent:**

Name, Company, Emergency Phone Number (24/7) \_\_\_\_\_

**Current Phase of Construction**

*Check ALL the boxes below that apply to your site.*

Grading and Land Development	Vertical Construction	Inactive Site
Streets and Utilities	Final Landscaping and Site Stabilization	Other:

**Activities Associated with Current Phase(s)**

*Check ALL the boxes below that apply to your site (some apply to all Phases).*

**Grading and Land Development:**

Demolition	Vegetation Removal	Vegetation Salvage-Harvest
Rough Grade	Finish Grade	Blasting
Soil Amendment(s):	Excavation (_____ ft)	Soils Testing
Rock Crushing	Erosion and Sediment Control	Surveying
Equip. Maintenance/Fueling	Material Delivery and Storage	Other:

**Streets and Utilities:**

Finish Grade	Utility Install: water-sewer-gas	Paving Operations
Equip. Maintenance/Fueling	Storm Drain Installation	Material Delivery & Storage
Curb and Gutter/Concrete Pour	Masonry	Other:

**Vertical Construction:**

Framing	Carpentry	Concrete/Forms/Foundation
Masonry	Electrical	Painting
Drywall/Interior Walls	Plumbing	Stucco
Equip. Maintenance/Fueling	HVAC	Tile
Exterior Siding	Insulation	Landscaping & Irrigation
Flooring	Roofing	Other:

**Final Landscaping & Site Stabilization:**

Stabilization	Vegetation Establishment	E&S Control BMP Removal
Finish Grade	Storage Yard/ Material Removal	Landscape Installation
Painting and Touch-Up	Irrigation System Testing	Other:
Drainage Inlet Stencils	Inlet Filtration	Perm. Water Quality Ponds

Other:

**Inactive Construction Site:**

E & S Control Device Installation  
 E & S Control Device Maintenance\_Other:

Routine Site Inspection  
 Street Sweeping Other:

Trash Removal  
 Other:

# Rain Event Action Plan (REAP)

<b>Date:</b>		<b>WDID Number:</b>																																														
<p align="center"><b>Trades Active on Site during Current Phase(s)</b>  <i>Check ALL the boxes below that apply to your site</i></p> <table border="0"> <tr> <td>Storm Drain Improvement</td> <td>Grading Contractor</td> <td>Surveyor- Soil Technician</td> </tr> <tr> <td>Street Improvements</td> <td>Water Pipe Installation</td> <td>Sanitary Station Provider</td> </tr> <tr> <td>Material Delivery</td> <td>Sewer Pipe Installation</td> <td>Electrical</td> </tr> <tr> <td>Trenching</td> <td>Gas Pipe Installation</td> <td>Carpentry</td> </tr> <tr> <td>Concrete Pouring</td> <td>Electrical Installation</td> <td>Plumbing</td> </tr> <tr> <td>Foundation</td> <td>Communication Installation</td> <td>Masonry</td> </tr> <tr> <td>Demolition</td> <td>Erosion and Sediment Control</td> <td>Water, Sewer, Electric Utilities</td> </tr> <tr> <td>Material Delivery</td> <td>Equipment Fueling/Maintenance</td> <td>Rock Products</td> </tr> <tr> <td>Tile Work- Flooring</td> <td>Utilities, e.g., Sewer, Electric</td> <td>Painters</td> </tr> <tr> <td>Drywall</td> <td>Roofers</td> <td>Carpenters</td> </tr> <tr> <td>HVAC installers</td> <td>Stucco</td> <td>Pest Control: e.g., termite prevention</td> </tr> <tr> <td>Exterior Siding</td> <td>Masons</td> <td>Water Feature Installation</td> </tr> <tr> <td>Insulation</td> <td>Landscapers</td> <td>Utility Line Testers</td> </tr> <tr> <td>Fireproofing</td> <td>Riggers</td> <td>Irrigation System Installation</td> </tr> <tr> <td>Steel Systems</td> <td>Utility Line Testers</td> <td>Other:</td> </tr> </table>				Storm Drain Improvement	Grading Contractor	Surveyor- Soil Technician	Street Improvements	Water Pipe Installation	Sanitary Station Provider	Material Delivery	Sewer Pipe Installation	Electrical	Trenching	Gas Pipe Installation	Carpentry	Concrete Pouring	Electrical Installation	Plumbing	Foundation	Communication Installation	Masonry	Demolition	Erosion and Sediment Control	Water, Sewer, Electric Utilities	Material Delivery	Equipment Fueling/Maintenance	Rock Products	Tile Work- Flooring	Utilities, e.g., Sewer, Electric	Painters	Drywall	Roofers	Carpenters	HVAC installers	Stucco	Pest Control: e.g., termite prevention	Exterior Siding	Masons	Water Feature Installation	Insulation	Landscapers	Utility Line Testers	Fireproofing	Riggers	Irrigation System Installation	Steel Systems	Utility Line Testers	Other:
Storm Drain Improvement	Grading Contractor	Surveyor- Soil Technician																																														
Street Improvements	Water Pipe Installation	Sanitary Station Provider																																														
Material Delivery	Sewer Pipe Installation	Electrical																																														
Trenching	Gas Pipe Installation	Carpentry																																														
Concrete Pouring	Electrical Installation	Plumbing																																														
Foundation	Communication Installation	Masonry																																														
Demolition	Erosion and Sediment Control	Water, Sewer, Electric Utilities																																														
Material Delivery	Equipment Fueling/Maintenance	Rock Products																																														
Tile Work- Flooring	Utilities, e.g., Sewer, Electric	Painters																																														
Drywall	Roofers	Carpenters																																														
HVAC installers	Stucco	Pest Control: e.g., termite prevention																																														
Exterior Siding	Masons	Water Feature Installation																																														
Insulation	Landscapers	Utility Line Testers																																														
Fireproofing	Riggers	Irrigation System Installation																																														
Steel Systems	Utility Line Testers	Other:																																														
<p align="center"><b>Trade Contractor Information Provided</b>  <i>Check ALL the boxes below that apply to your site.</i></p> <table border="0"> <tr> <td><input type="checkbox"/> Educational Material Handout</td> <td>Tailgate Meetings</td> <td>Training Workshop</td> </tr> <tr> <td><input type="checkbox"/> Contractual Language</td> <td>Fines and Penalties</td> <td>Signage</td> </tr> <tr> <td><input type="checkbox"/> Other:</td> <td>Other:</td> <td>Other:</td> </tr> </table>				<input type="checkbox"/> Educational Material Handout	Tailgate Meetings	Training Workshop	<input type="checkbox"/> Contractual Language	Fines and Penalties	Signage	<input type="checkbox"/> Other:	Other:	Other:																																				
<input type="checkbox"/> Educational Material Handout	Tailgate Meetings	Training Workshop																																														
<input type="checkbox"/> Contractual Language	Fines and Penalties	Signage																																														
<input type="checkbox"/> Other:	Other:	Other:																																														
<b>Continued on next page.</b>																																																

# Rain Event Action Plan (REAP)

<b>Date of REAP</b>		<b>WDID Number:</b>	
<b>Date Rain Predicted to Occur:</b>		<b>Predicted % chance of rain:</b>	

### Predicted Rain Event Triggered Actions

Below is a list of suggested actions and items to review for this project. Each active Trade should check all material storage areas, stockpiles, waste management areas, vehicle and equipment storage and maintenance, areas of active soil disturbance, and areas of active work to ensure the proper implementation of BMPs. Project-wide BMPs should be checked and cross-referenced to the BMP progress map.

<b>Trade or Activity</b>	<b>Suggested action(s) to perform / item(s) to review prior to rain event</b>
--------------------------	---

- Information & Scheduling
  - Inform trade supervisors of predicted rain
  - Check scheduled activities and reschedule as needed
  - Alert erosion/sediment control provider
  - Alert sample collection contractor (if applicable)
  - Schedule staff for extended rain inspections (including weekends & holidays)
  - Check Erosion and Sediment Control (ESC) material stock
  - Review BMP progress map
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  - \_\_\_\_\_
  
- Material storage areas
  - Material under cover or in sheds (ex: treated woods and metals)
  - Perimeter control around stockpiles
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  
- Waste management areas
  - Dumpsters closed
  - Drain holes plugged
  - Recycling bins covered
  - Sanitary stations bermed and protected from tipping
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  
- Trade operations
  - Exterior operations shut down for event (e.g., no concrete pours or paving)
  - Soil treatments (e.g.: fertilizer) ceased within 24 hours of event
  - Materials and equipment (ex: tools) properly stored and covered
  - Waste and debris disposed in covered dumpsters or removed from site
  - Trenches and excavations protected
  - Perimeter controls around disturbed areas
  - Fueling and repair areas covered and bermed
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  
- Site ESC BMPs
  - Adequate capacity in sediment basins and traps
  - Site perimeter controls in place
  - Catch basin and drop inlet protection in place and cleaned
  - Temporary erosion controls deployed
  - Temporary perimeter controls deployed around disturbed areas and stockpiles
  - Roads swept; site ingress and egress points stabilized
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  
- Concrete rinse out area
  - Adequate capacity for rain
  - Wash-out bins covered
  - Other: \_\_\_\_\_
  - \_\_\_\_\_
  
- Spill and drips

- All incident spills and drips, including paint, stucco, fuel, and oil cleaned
- Drip pans emptied
- Other: \_\_\_\_\_
- \_\_\_\_\_

**Continued on next page.**

- Other / Discussion / Diagrams
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_

**Attach a printout of the weather forecast from the NOAA website to the REAP.**

I certify under penalty of law that this Rain Event Action Plan (REAP) will be performed in accordance with the General Permit by me or under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

\_\_\_\_\_  
 Qualified SWPPP Practitioner (Use ink please) Date: \_\_\_\_\_

# **Appendix IX**

## **Site Inspection**

# **Appendix X**

## **Construction Site Monitoring Program (CSMP)**

## **APPENDIX X CONSTRUCTION SITE MONITORING PROGRAM (CSMP)**

### **1 OVERVIEW**

A site specific CSMP is required under the Construction General Permit (CGP). The purpose of the CSMP is to include all monitoring procedures and instructions, location maps, forms, and checklists. It is the responsibility of the QSP to implement the CSMP. The QSD shall revise the CSMP as necessary to reflect project revisions and whenever there is a change of ownership for all or any portion of the construction site prior to completion or final stabilization.

This project has been determined to be a Risk Level 2 project. The CGP identifies the following types of monitoring as being applicable for a Risk Level 2 project.

#### **Risk Level 2**

- Visual monitoring of the site related to qualifying storm events;
- Visual monitoring of the site for non-stormwater discharges;
- Sampling and analysis of construction site runoff for pH and turbidity;
- Sampling and analysis of construction site runoff for non-visible pollutants when applicable; and
- Sampling and analysis of non-storm water discharges when applicable.

#### **A. Weather Tracking**

Visual monitoring, inspections, and sampling requirements of the CGP are triggered by a qualifying rain event. The CGP defines a qualifying rain event as any event that produces ½ inch of precipitation. A minimum of 48 hours of dry weather will be used to distinguish between separate qualifying storm events.

The QSP should consult the National Oceanographic and Atmospheric Administration (NOAA) for weather forecasts on a daily basis. These forecasts can be obtained at <http://www.srh.noaa.gov/>. Weather reports should be printed and maintained with the SWPPP in Appendix XI.A.

- ***Rain Gauges***

- The QSP shall install one rain gauge on the project site. Locate the gauge in an open area away from obstructions such as trees or overhangs. Mount the gauge on a post at a height of 3 to 5 feet with the gauge extending several inches beyond the post. Make sure that the top of the gauge is level. Make sure the post is not in an area where rainwater can indirectly splash from sheds, equipment, trailers, etc.

## Storm Water Pollution Prevention Plan

- The rain gauge(s) shall be read daily during normal site scheduled hours. The rain gauge should be read at approximately the same time every day and the date and time of each reading recorded. Record rain gauge readings on Visual Observation (Inspection Form) for Qualifying Rain Event. Follow the rain gauge instructions to obtain accurate measurements.
- Once the rain gauge reading has been recorded, accumulated rain shall be emptied and the gauge reset.

### **B. Monitoring Location**

Monitoring locations are shown on the Site Maps in Appendix III. Whenever changes in the construction site might affect the appropriateness of sampling locations, the sampling locations shall be revised accordingly and noted on the on-site SWPPP Map. In the event of monitoring location modifications, the QSP shall consult the QSD and owner. Direction regarding SWPPP amendments and field changes shall be coordinated with the QSD.

### **C. Monitoring Preparation**

An adequate stock of monitoring supplies and equipment for monitoring non-visible pollutants, pH, turbidity and non-storm water discharges, will be available on the project site prior to a sampling event. Monitoring supplies and equipment will be stored in a cool temperature environment that will not come into contact with rain or direct sunlight. Sampling personnel will be available to collect samples in accordance with the sampling schedule. Supplies maintained at the project site will include, but are not limited to, field meters, extra batteries; clean powder-free nitrile gloves, sample collection equipment, appropriate sample containers, paper towels, personal rain gear, and Effluent Sampling Field Log Sheets and Chain of Custody (CoC) forms provided in Appendix XI.A.

### **D. Exemptions for Visual Observation and Sample Collection**

Visual observation (inspections) are only required during daylight hours (sunrise to sunset). Visual observations (inspections) and sample collection are not required under the following conditions:

- During dangerous weather conditions such as flooding, and electrical storms.
- Outside of scheduled site business hour.
  - Scheduled Business Hours are 7:30am to 7pm Monday – Saturday
- If one or more of these conditions occur document why the sampling or observations did not occur on the applicable site inspection and maintain in the SWPPP and include the information in the Annual Report. A blank

form has been provided in Appendix XI.A. Keep a copy of the completed form in Appendix XI.B.

## 2 VISUAL MONITORING (INSPECTION) REQUIREMENTS

The visual observations (inspections) described in this Construction Site Monitoring Plan (CSMP) are specific to sampling events and are not equivalent to the Site Inspections described in Section 4.7 of this SWPPP.

### A. Visual Monitoring (Inspection) for Qualifying Rain Events (QREs).

Visual observations of the site and inspections of BMPs are required prior to a qualifying rain event; following a qualifying rain event, and every 24-hour period during a qualifying rain event. A blank Visual Observation (inspection) for a Qualifying Rain Event form is provided in Appendix I. The QSP must complete these forms during the visual observation and insert a completed copy in Appendix XI.B of this SWPPP. See Section 8.0 for record-keeping requirements.

Requirements for Risk Level 2:

- Visually observe (inspect) storm water discharges at all discharge locations within two business days (48 hours) after each qualifying rain event.
- Visually observe (inspect) the discharge of stored or contained storm water that is derived from and discharged subsequent to a QRE. Stored or contained storm water that will likely discharge after operating hours due to anticipated precipitation shall be observed prior to the discharge during operating hours.
- Observations shall be done only during business hours. Business hours are anytime work is being conducted on the site.
- Record the time, date and rain gauge reading of all QREs.
- **Before** a QRE (i.e., within 2 business days (48 hours)):
  - **Storm Water:**
    - Observe all storm water drainage areas for:
      - Spills, leaks or uncontrolled pollutant sources and implement any needed corrective actions;
      - The presence or absence of:
        - Floating and suspended materials;
        - A sheen on the surface;
        - Discolorations;
        - Turbidity;

## Storm Water Pollution Prevention Plan

- Odors; and
- Sources of any observed pollutants.
- **BMPs:**
  - Observe all BMPs for proper implementation in accordance with the SWPPP/REAP and implement appropriate corrective actions;
  - Observe any storm water storage and containment areas:
    - For leaks and to ensure maintenance of adequate freeboard;
    - The presence or absence of:
      - Floating and suspended materials;
      - A sheen on the surface;
      - Discolorations;
      - Turbidity;
      - Odors; and
      - Sources of any observed pollutants.
- **After** a QRE (Within 2 business days):
  - **BMPs:**
    - Observe whether BMPs were adequately designed, implemented, and effective; and
    - Identify additional BMPs and revise the SWPPP accordingly.
- **Follow-up and Reporting**
  - Correction of deficiencies identified by the observations or inspections, including required repairs or maintenance of BMPs, shall be initiated and completed as soon as possible.
  - If identified deficiencies require design changes, including additional BMPs, the implementation of changes will be initiated within 72 hours of identification and be completed as soon as possible. When design changes to BMPs are required, the SWPPP shall be amended to reflect the changes.
  - Deficiencies identified in site inspection reports and correction of deficiencies will be tracked on the Visual Observation Form and shall be kept in Appendix XI.B.
  - Results of visual monitoring must be summarized and reported in the Annual Report.

### **B. Visual Monitoring (Inspection) for Non-Storm Water Discharges**

Each drainage area will be inspected for the presence of or indications of prior

## Storm Water Pollution Prevention Plan

unauthorized and authorized non-storm water discharges. Blank inspection forms are provided in Appendix I The QSP must complete these forms during the visual observation and insert a completed copy in Appendix XI.B. See Section 8.0 for record-keeping requirements.

### Requirements for Risk Level 2:

Visually observe (inspect) each drainage area for:

- The presence of (or indications of prior) unauthorized and authorized non-storm water discharges; and
- Their sources.

Shall conduct one visual observation (inspection) quarterly in each of the following periods:

- January- March;
- April-June;
- July-September; and
- October-December.

Shall ensure that visual observations (inspections) document the:

- Presence or evidence of any non-stormwater discharge (authorized or unauthorized);
- Pollutant characteristics (floating and suspended material, sheen, discoloration, turbidity, odor, etc.); and
- Source of the pollutants.

Shall maintain on-site records indicating the response taken to:

- Eliminate unauthorized non-storm water discharges; and
- Reduce or prevent pollutants from contacting non-storm water discharges.

## **3 SAMPLING FOR NON-VISIBLE POLLUTANTS**

This Sampling and Analysis Plan for Non-Visible Pollutants describes the sampling and analysis strategy and schedule for monitoring non-visible pollutants in stormwater runoff discharges from the project site. Blank Sampling Event Worksheets are provided in Appendix I. The QSP must complete these forms during sampling and insert a completed copy in Appendix XI.D. See Section 6 for Sample Collection and Handling, and Section 8 for record-keeping requirements.

Risk Level 2 dischargers shall collect one or more samples during any breach, malfunction, leakage, or spill observed during a visual inspection which could result in the discharge of pollutants to surface waters that would not be visually detectable in storm water and ensure that water samples are large enough to characterize the site conditions.

## Storm Water Pollution Prevention Plan

Samples for non-visible pollutants shall be collected when a breach or malfunction of a BMP or leakage or spill is observed, and shall be collected from a discharge location where runoff, likely to contain non-visible pollutants, is produced. Site discharge locations are shown on the Site Map in Appendix III. Samples should be collected during the first two hours of discharge from rain events that occur during business hours and which generate runoff. Analyze samples for all non-visible pollutant parameters – parameters indicating the presence of pollutants identified in the pollutant source assessment located in Section 3.1 below.

Samples shall be collected and preserved in accordance with the methods identified in the “Storm Water Sample Collection and Handling”, Section 6. Only the QSP, or personnel trained in water quality sampling under the direction of the QSP shall collect samples. Following sampling collection, the QSP or his/her designee will contact the laboratory listed in Appendix XI.D.

Additionally, collect a sample of storm water that has not come in contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample) for comparison with the discharge sample. Appropriate uncontaminated sampling locations shall be selected by the QSP, and may include:

- For discharge from the substation area use the upstream side of the project site and will be taken from within the brow ditch located along the south side of the entry roadway into the substation where run on is expected.
- For discharge along the access road, use flows from the upstream side of the access road.

The QSP shall compare the runoff results with the uncontaminated sample to the samples of discharge through laboratory analysis, and keep documentation of all field or analytical data in the SWPPP document. A Sampling Event Worksheet blank form can be found in Appendix XI.A, completed forms shall be kept in Appendix XI.D.

### **1. Pollutant Source Assessment**

#### **a. Historical Pollutants**

Prior to commencement of construction at this project, the site was SDG&E’s wood to steel laydown staging yard. Material included steel reels, pallets of hardware and pole steps, wood crates, steel poles and steel pole tops and bottoms. Based on a review of SDG&E’s Alpine Yard-Summary of Biological Observations, the following existing pollutants will

be sampled:

No existing pollutants were found to be on site. Therefore, no known pollutants will be sampled for.

#### **b. Potential Pollutant Sources**

A list of construction activities and potential pollutants is located in Appendix V. The list of potential pollutants generated includes all non-visible pollutants that are known or should be known to occur on the construction site.

Based on the sources of pollutants identified above, the following indicator parameters will be analyzed to determine if pollutants are anticipated to be conveyed from the site by storm water:

- Nitrates
- Oil and Grease

#### **4 SAMPLING FOR pH AND TURBIDITY IN STORM WATER RUNOFF**

Sampling and analysis of runoff for pH and turbidity is required for this project. This Sampling and Analysis Plan describes the strategy for monitoring turbidity and pH levels of stormwater runoff discharges from the project site and run-on that may contribute to an exceedance of a Numeric Action Level (NAL). Samples for turbidity will be collected from all drainage areas with disturbed soil areas and samples for pH will be collected from all drainage areas with a high risk of pH discharge. Blank Sampling Event Worksheets are provided in Appendix I. The QSP must complete these forms during sampling and insert a completed copy in Appendix XI.D. See Section 6 for sample collection and handling, and Section 8 for record-keeping requirements.

Stormwater runoff samples shall be collected for turbidity from all qualifying rain events that result in a discharge from the project site. Turbidity samples will be collected from each of the 3 discharge locations, until the contributing area meets stabilization requirements. If less than 3 sampling locations are accessible, the QSP shall collect multiple samples from accessible discharge locations to satisfy the CGP requirement that a minimum of 3 samples from the site shall be collected per day of discharge during a qualifying event. Samples should be representative of the total discharge from the project each day of discharge during the qualifying event.

## Storm Water Pollution Prevention Plan

Stormwater runoff samples shall be collected for pH from all qualifying rain events that result in a discharge from the project site. At minimum, pH samples will be collected from each site discharge location during project phases and drainage areas with a high risk of pH discharge. A minimum of 3 samples will be collected per day of discharge during a qualifying event. Samples should be representative of the total discharge from the location each day of discharge during the qualifying event.

Stored or collected water from a qualifying storm event, when discharged, shall be tested for turbidity and pH (when applicable). Stored or collected water from a qualifying event may be sampled at the point it is released from the storage or containment area or at the site discharge location.

The monitoring locations are shown on the Site Map in Appendix III. The sample locations have been identified for the site based on the drainage conditions during construction. As site conditions change, the QSP will be responsible to identify the locations where storm water runoff exits the site, and identify the locations on the exhibit as site runoff monitoring locations. Run-on samples shall be collected whenever the QSP identifies that run-on has the potential to contribute to an exceedance of a NAL.

Turbidity and pH samples will be collected and analyzed by the QSP. Samples shall be analyzed for the constituents indicated in the table below “Sample Collection, and Analysis for Monitoring Turbidity and pH.”

<b>Sample Collection and Analysis for Monitoring Turbidity and pH</b>				
<b>Parameter</b>	<b>Test Method</b>	<b>Minimum Sample Volume<sup>(1)</sup></b>	<b>Sample Collection Container Type</b>	<b>Detection Limit (minimum)</b>
Turbidity	Field meter/probe with calibrated portable instrument	50mL	Polypropylene or Glass (Do not collect in meter sample cells)	1 NTU
pH	Field meter/probe with calibrated portable instrument or calibrated pH test kit	100 mL	Polypropylene	0.2 pH units
Notes: <sup>1</sup> Minimum sample volume recommended. Specific volume requirements will vary by instrument; check instrument manufacturer instructions. mL – Milliliter NTU – Nephelometric Turbidity Unit				

## Storm Water Pollution Prevention Plan

Samples of discharge shall be collected at the designated runoff and run-on sampling locations shown on the Site Map in Appendix III. Run-on samples shall be collected within close proximity of the point of run-on to the project. Only personnel trained in water quality sampling and field measurements working under the direction of the QSP shall collect samples. See Section 6.0 for sample collection and handling.

### Numeric Action Levels

This project is subject to Numeric Action Levels (NALs) for pH and turbidity. Compliance with the NAL for pH and turbidity is based on a weighted daily average. Upon receiving the Sampling Event Worksheet, the QSP shall immediately calculate the weighted arithmetic average of the pH and turbidity samples to determine if the NALs, shown in the table below, have been exceeded.

Numeric Action Levels		
Parameter	Unit	Daily Average
pH	pH units	Lower NAL = 6.5 Upper NAL = 8.5
Turbidity	NTU	250 NTU

The QSP shall upon completion of sample collection submit copies of the completed Sampling Event Worksheets to SDG&E.

In the event that the pH or turbidity NAL is exceeded, the QSP shall immediately notify SDG&E and investigate the cause of the exceedance and identify corrective actions. Exceedances of NALs shall be electronically reported to the State Water Board by SDG&E through the SMARTs system within 10 days of the conclusion of the storm event. If requested by the Regional Board, a NAL Exceedance report will be submitted. The NAL Exceedance Report must contain the following information:

- Analytical method(s), method reporting unit(s), and MDL(s) of each parameter;
- Date, place, time of sampling, visual observation, and/or measurements, including precipitation; and
- Description of the current BMPs associated with the sample that exceeded the NAL and the proposed corrective actions taken.

## 5 SAMPLING FOR NON-STORM WATER RUNOFF

## Storm Water Pollution Prevention Plan

This Sampling and Analysis Plan for Non-Storm Water discharges describes the sampling and analysis strategy and schedule for monitoring pollutants in authorized and unauthorized non-storm water discharges from the project site in accordance with the requirements of the CGP. Blank Sampling Event Worksheets are provided in Appendix I. The QSP must complete these forms during sampling and insert a completed copy in Appendix XI.D. See Section 6 for Sample collection and handling, and Section 8 for record-keeping requirements.

Non-stormwater discharges consist of discharges which do not originate from precipitation events. The CGP provides allowances for specified non-stormwater discharges that do not cause erosion or carry other pollutants. The CGP states “Authorized non-storm water discharges may include those from dechlorinated potable water sources such as: fire hydrant flushing, irrigation of vegetative erosion control measures, pipe flushing and testing, water to control dust, uncontaminated ground water from dewatering, and other discharges not subject to a separate general NPDES permit adopted by a Regional Water Board.”

For this project authorized non-storm water discharges include:

- Irrigation of vegetative erosion control measures
- Water to control dust
- Pipe Flushing
- Hydrant Flushing
- Uncontaminated ground water

Sampling of non-storm water discharges will be conducted when an authorized or unauthorized non-storm water discharge is observed discharging from the project site. Upstream flows that do not come in contact with disturbed areas will not require sampling, additionally attenuated stormwater released as ground water seepage will not require sampling. Samples of authorized or unauthorized non-storm water discharges shall be collected when they are observed, and tested for turbidity and pH (if applicable); if non-visible pollutants are suspected, follow “Sampling for Non-Visible Pollutants” in Section 3. Samples shall be collected from the discharge point of the construction site where the non-storm water discharge is running off the project site. Site discharge locations are shown on the Site Map in Appendix III. In the event that non-storm water discharges run-on to the project site from offsite locations, and this run-on has the potential to contribute to a violation of a NAL, the run-on will also be sampled.

## **6 STORM WATER SAMPLE COLLECTION AND HANDLING INSTRUCTIONS**

## **Field Analysis**

Turbidity and pH measurements must be conducted immediately, at each location. Do not store turbidity or pH samples for later measurement. Field meters will be calibrated, maintained, and operated by trained staff according to the manufacturer's specifications, and calibration records will be stored in Appendix XI.D. Supplies maintained at the project site will include, but are not limited to,

- Field meters
- Extra batteries
- Clean powder-free nitrile gloves
- Sample collection equipment
- Appropriate sample containers
- Paper towels
- Personal rain gear
- Sampling Event Worksheet
- Chain of custody form

## **Laboratory Analysis**

For sampling which require laboratory analysis ensure that water samples are large enough to characterize the site conditions. A sample kit should be available on site in case of a need to sample. The sample kit should include:

- Ice chest
- Ice (to be purchased when needed)
- Rubber gloves -3 to 4 pair
- Sample bottles (provided by laboratory)
- Sharpie
- Chain of custody form
- Scoop

Samples for laboratory analysis must be handled as follows. Sample bottles should be:

- Filled to top
- Do not pour between containers
- Label all bottles before collecting sample – use sharpie
- Store chilled (cooler with ice or refrigerator)

## Storm Water Pollution Prevention Plan

- Secure cap
- Keep upright

Collect samples during the first two hours of discharge from rain events that occur during business hours and which generate runoff. For non-visible pollutants, collect 3 samples per day of the qualifying rain event. Collect a sample of storm water that has not come in contact with the disturbed soil or the materials stored or used on-site (uncontaminated sample) for comparison with the discharge sample.

An analytical laboratory for sample analyses is identified in Appendix XI.D of this document.

The laboratory will provide properly cleaned and preserved (if applicable) sampling containers (bottles) for the samples, and labels on the sample bottles. The sample bottle labels will identify the analysis to be performed and any preservative contained in the bottles, and provide room for recording the sample location and time and date of collection. The laboratory will also provide chain-of-custody forms. Example Chain of Custody form is located in Appendix XI.E.

Ensure that the testing laboratories will receive samples the same day or within 48 hours of the physical sampling (unless otherwise required by the laboratory), and shall use only the sample containers provided by the laboratory to collect and store samples.

Personnel shall collect, maintain, and ship samples in accordance with the Surface Water Ambient Monitoring Program's (SWAMP) 2008 Quality Assurance Program Plan (QAPrP). See footnote 6 on page 15 of Attachment E of the CGP for additional information regarding SWAMP and QAPrP.

## Storm Water Pollution Prevention Plan

The following table provides information for constituents to be monitored for non-visible parameters.

Analyte	EPA Analytical Method Number	Minimum Sample Volume <sup>3</sup>	Sampling Container	Preservative <sup>4</sup>	Holding Time
Nitrate as Nitrogen	EPA 300	250mL	Poly	Cool <4 Deg C	48Hrs
Oil and Grease	EPA 1664	3X1Liter	Amber glass	H2SO4 pH<2,Cool	28 Days
VOCs	EPA 8260	6X40 mL	VOA Vials	HCl pH<2, Cool	14 Days
TPH	EPA 8015B	4X1Liter	Amber Glass	Unpreserved	7 Days

<sup>3</sup>Minimum sample volume recommended. Specific volume requirements will vary by laboratory and must be verified with the laboratory when bottles are ordered.

<sup>4</sup>Do not pre-rinse or overfill sample containers that contain preservative.

<sup>5</sup>All samples must be kept chilled to 4°C (keep samples on ice for delivery to analytical laboratory)

## 7 ANALYTICAL AND MONITORING METHODS

If any upgrades of BMPs occur, the SWPPP will be revised accordingly by the QSD and a record of the upgrade will be kept in Appendix XI.B.

### A. Effluent Sampling Methods:

Samples collected for field analysis, collection, analysis and equipment calibration shall be in accordance with the field instrument manufacturer's specifications. The manufacturers' instructions are included in Appendix XI.D Field Meter Information. Field sampling staff shall review the instructions prior to each sampling event and follow the instructions in completing measurement of the samples. The instrument(s) shall be maintained in accordance with manufacturer's instructions and shall be calibrated before each sampling and analysis event. Maintenance and calibration records shall be maintained with the SWPPP.

### B. Non-Visible Pollutants

The Alpine Regional Headquarter Facility project is located in the Alpine Hydrologic Subarea of Hydrologic Unit basin number 907.00. The Water Quality SWPPP Template / CSMP  
2009.00 – 122309 Traditional

## Storm Water Pollution Prevention Plan

Control Plan for the 9 Region (“Basin Plan”) provides water quality objectives for some of the analytes that will be monitored. While these do not constitute a discharge standard or limit, these water quality objectives will be used as decision making benchmark standards. Where such standards are not available through the Basin Plan, benchmark standards set forth by other agencies will be used for decision making purposes. The table below lists the benchmarks that will be used.

Benchmark Criteria for Decision Making				
Analyte		Benchmark Concentration		Reference
Nitrate		0.68 mg/L		USEPA*
Oil and Grease		15 mg/L		USEPA*
TPH		No established value		

\*United States Environmental Protection Agency Multi-Sector Industrial Permit

Benchmark provided for VOCs are from the Basin Plan groundwater and drinking water limits, and are provided for reference.

VOC	Reference Benchmark Concentration (mg/l)
Benzene	0.001
Carbon Tetrachloride	0.0005
1,2-Dichlorobenzene	0.6
1,4-Dichlorobenzene	0.005
1,1-Dichloroethane	0.005
1,2-Dichloroethane	0.0005
1,1-Dichloroethylene	0.006
cis-1,2-Dichloroethylene	0.006
trans-1,2-Dichloroethylene	0.01
Dichloromethane	0.005
1,2-Dichloropropane	0.005
1,3-Dichloropropene	0.0005
Ethylbenzene	0.3
Methyl-tert-butylether	0.013
Monochlorobenzene	0.07
Styrene	0.1
1,1,2,2-Tetrachloroethane	0.001
Tetrachloroethylene	0.005
Toluene	0.15
1,2,4-Trichlorobenzene	0.005
1,1,1-Trichloroethane	0.2
1,1,2-Trichloroethane	0.005

Trichloroethylene	0.005
Trichlorofluoromethane	0.15
1,1,2-Trichloro-1,2,2-Trifluoroethane	1.2
Vinyl Chloride	0.0005
Xylenes	1.75

## 8 RECORDS

All records of stormwater monitoring information and copies of reports (including Annual Reports) must be retained for a period of at least three years from date of submittal or longer if required by the Regional Water Board.

Results of visual monitoring, field measurements and laboratory analyses must be kept in the SWPPP along with CoCs, and other documentation related to the monitoring.

Records are to be kept onsite while construction is ongoing. Records to be retained include:

- The date, place, and time of inspections, sampling, visual observations, and/or measurements, including precipitation;
- The individual(s) who performed the inspections, sampling, visual observation, and/or field measurements;
- The date and approximate time of field measurements and laboratory analyses;
- The individual(s) who performed the laboratory analyses;
- A summary of all analytical results, the method detection limits and reporting limits, and the analytical techniques or methods used;
- Rain gauge readings from site inspections;
- QA/QC records and results;
- Calibration records;
- Visual observation and sample collection exemption records;
- The records of any corrective actions and follow-up activities that resulted from analytical results, visual observations, or inspections; and
- NAL Exceedance Reports

**APPENDIX X.D**

Samples will be analyzed by:

Laboratory Name: SDG&E Environmental Laboratory  
Contact Amethyst L. Cruspero, Compliance Specialist  
Telephone Number: (858) 654-1624

## Storm Water Pollution Prevention Plan

*The following page includes updated Sampling Event Worksheet for Appendix XI.A*





# **Appendix XI**

## **CSMP Attachments**



A Sempra Energy utility

# CHAIN OF CUSTODY/SAMPLE SUBMITTAL FORM

ENVIRONMENTAL ANALYSIS LABORATORY

6555 NANCY RIDGE DRIVE, SUITE 300, SAN DIEGO, CA 92121-3221  
(858) 503-5371 FAX: (858) 503-5398

LAB NO.

WORK ID.	CLIENT NAME	CLIENT CODE
SAMPLED BY (Print & Signature)	CLIENT'S PHONE	PROJECT CODE
CLIENT'S ADDRESS	NUMBER OF CONTAINERS	DATE DUE

SAMPLE ID	DATE	TIME	SAMPLE TYPE	SAMPLE CONTAINER	PRESERVATION	ANALYSIS NEEDED	TEST CODE(S)

COMMENTS

---



---

RELEASING	DATE	TIME	ACCEPTING	DATE	TIME
RELEASING	DATE	TIME	ACCEPTING	DATE	TIME

# **Appendix XII**

## **Permit Registration Documents**



State Water Resources Control Board  
**NOTICE OF INTENT**  
GENERAL PERMIT TO DISCHARGE STORM WATER  
ASSOCIATED WITH CONSTRUCTION ACTIVITY  
(WQ ORDER No. 2009-0009-DWQ)



WDID: 9 37C357448

Risk Level: Level1

### Property Owner Information

Type: Private Business

Name: San Diego Gas & Electric

Contact Name: Amethyst Cruspero

Address: 8315 Century Park Ct CP21G

Title:

Address 2:

Phone #: 619-778-6029

City/State/Zip: San Diego CA 92123

Email: ACruspero@SempraUtilities.com

### Contractor/Developer Information

Name: San Diego Gas & Electric

Contact Name: Amethyst Cruspero

Address: 8315 Century Park Ct CP21G

Title:

Address 2:

Phone #: 619-778-6029

City/State/Zip: San Diego CA 92123

Email: ACruspero@SempraUtilities.com

### Construction Site Information

Site Name: Sunrise Powerlink Alpine Regional Field Offices

Contact Name: Amethyst Cruspero

Address: 1010 Tavern Rd

Title:

City/State/Zip: Alpine CA 91901

Site Phone #: 619-778-6029

County: San Diego

Email: ACruspero@SempraUtilities.com

Latitude: 32.84111

Longitude: -116.784166

Total Size of Construction Area: 10.5

Construction Start: February 15, 2010

Total Area to be Disturbed: 10.5

Complete Grading:

Final Stabilization: June 15, 2013

Type of Construction: \*Utility: admin field construction offices

Receiving Water:

Qualified SWPPP Developer:

Certification #:

RWQCB Jurisdiction: Region 9 - San Diego

Phone: 858-467-2952

Email: r9\_stormwater@waterboards.ca.gov

### Certification

Name: Robert Jackson

Date: June 22, 2010

Title: General Mgr and Director

---

**PRDs Filed  
(Store Completed Forms in Appendix XII)**

PRDs were filed:

---

---

---

---

---

Copy of Submittal:

The following documents, except the Annual Fee which was mailed, were submitted electronically to the SWRCB:

- Notice of Intent (NOI) – Enclosed
- Risk Assessment – Enclosed
- Site Map – Enclosed
- Storm Water Pollution Prevention Plan – Enclosed
- Annual Fee – Enclosed
- Signed Certification Statement – Enclosed



Linda S. Adams  
Secretary for  
Environmental Protection

# State Water Resources Control Board

## Division of Water Quality

1001 I Street Sacramento, California 95814 (866) 563 3107  
Mailing Address: P.O. Box 1977 Sacramento, California 95812-1977  
FAX (916) 341-5543 Internet Address: <http://www.waterboards.ca.gov>  
Email Address: [stormwater@waterboards.ca.gov](mailto:stormwater@waterboards.ca.gov)



Arnold Schwarzenegger  
Governor

**Approved Date:** 02/26/2010

Linda Collins  
San Diego Gas & Electric  
8315 Century Park Ct CP21G  
San Diego CA 92123

### RECEIPT OF YOUR NOTICE OF INTENT (NOI)

The State Water Resources Control Board (State Water Board) has received and processed your NOI to comply with the terms of the General Permit to Discharge Storm Water Associated with Construction Activity. Accordingly, you are required to comply with the permit requirements.

The Waste Discharger Identification (WDID) number is: **9 37C357448**. Please use this number in any future communication regarding this permit.

<b>OWNER:</b>	<b>SITE DESCRIPTION</b>
<b>DEVELOPER:</b>	San Diego Gas & Electric
<b>SITE INFORMATION:</b>	San Diego Gas & Electric
	Sunrise Powerlink Alpine Regional Field Offices
	1010 Tavern Rd
	Alpine
<b>TOTAL DISTURBED ACRES:</b>	10.5
<b>START DATE:</b>	02/15/2010
<b>COMPLETION DATE:</b>	06/15/2013
<b>COUNTY:</b>	San Diego

**When the Owner changes , a new NOI, site map, and fee must be submitted by the new Owner.** As the previous owner, you are required to submit a Notice of Termination (NOT) to the local Regional Water Board stating you no longer own or operate the Site and coverage under the General Permit is not required. Unless notified, you will continue and are responsible to pay the annual fee invoiced each January.

If you have any questions regarding permit requirements, please contact your Regional Water Board at 858-467-2952 . Please visit the storm water web site at [http://www.waterboards.ca.gov/water\\_issues/programs/stormwater/](http://www.waterboards.ca.gov/water_issues/programs/stormwater/) to obtain an NOT and other storm water related information and forms.

Sincerely,

Storm Water Section  
Division of Water Quality



U.S. ENVIRONMENTAL PROTECTION AGENCY

# National Pollutant Discharge Elimination System (NPDES)

[Recent Additions](#) | [Contact Us](#) | [Print Version](#) Search NPDES:

[EPA Home](#) > [OW Home](#) > [OWM Home](#) > [NPDES Home](#) >

Basic Information

NPDES Topics

Alphabetical Index

Glossary

About NPDES

eNOI

Municipal MS4s

Construction Activities

Industrial Activities

Road-Related MS4s

Menu of BMPs

Green Infrastructure

Urban BMP Tool

Stormwater Home



## Rainfall Erosivity Factor Calculator for Small Construction Sites

### Facility Information

Facility Name: Alpine Regional Field Offices  
 Start Date: 09/17/2010  
 End Date: 06/15/2013  
 Latitude: 32.8411  
 Longitude: -116.7841

### Erosivity Index Calculator Results

AN EROSIVITY INDEX VALUE OF **91.35** HAS BEEN DETERMINED FOR THE CONSTRUCTION PERIOD OF **09/17/2010 - 06/15/2013**.

A rainfall erosivity factor of 5.0 or greater has been calculated for your site and period of construction. **You do not qualify for a waiver from NPDES permitting requirements.**

Stormwater Information
<a href="#">Recent Additions</a>
<a href="#">FAQs</a>
<a href="#">Publications</a>
<a href="#">Regulations</a>
<a href="#">Training &amp; Meetings</a>
<a href="#">Links</a>
<a href="#">Contacts</a>



The documents on this site are best viewed with Acrobat 8.0

[Office of Water](#) | [Office of Wastewater Management](#) | [Disclaimer](#) | [Search EPA](#)

[EPA Home](#) | [Privacy and Security Notice](#) | [Contact Us](#)

Last updated on August 07, 2009 3:37 PM

URL: [http://cfpub.epa.gov/npdes/stormwater/lew/erosivity\\_index\\_result.cfm](http://cfpub.epa.gov/npdes/stormwater/lew/erosivity_index_result.cfm)

	A	B	C
1	<b>Sediment Risk Factor Worksheet</b>		<b>Entry</b>
2	<b>A) R Factor</b>		
3	Analyses of data indicated that when factors other than rainfall are held constant, soil loss is directly proportional to a rainfall factor composed of total storm kinetic energy (E) times the maximum 30-min intensity (I30) (Wischmeier and Smith, 1958). The numerical value of R is the average annual sum of EI30 for storm events during a rainfall record of at least 22 years. "Isoerodent" maps were developed based on R values calculated for more than 1000 locations in the Western U.S. Refer to the link below to determine the R factor for the project site.		
4	<a href="http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm">http://cfpub.epa.gov/npdes/stormwater/LEW/lewCalculator.cfm</a>		
5	R Factor Value		91.35
6	<b>B) K Factor (weighted average, by area, for all site soils)</b>		
7	The soil-erodibility factor K represents: (1) susceptibility of soil or surface material to erosion, (2) transportability of the sediment, and (3) the amount and rate of runoff given a particular rainfall input, as measured under a standard condition. Fine-textured soils that are high in clay have low K values (about 0.05 to 0.15) because the particles are resistant to detachment. Coarse-textured soils, such as sandy soils, also have low K values (about 0.05 to 0.2) because of high infiltration resulting in low runoff even though these particles are easily detached. Medium-textured soils, such as a silt loam, have moderate K values (about 0.25 to 0.45) because they are moderately susceptible to particle detachment and they produce runoff at moderate rates. Soils having a high silt content are especially susceptible to erosion and have high K values, which can exceed 0.45 and can be as large as 0.65. Silt-size particles are easily detached and tend to crust, producing high rates and large volumes of runoff. Use Site-specific data must be submitted.		
8	<a href="#">Site-specific K factor guidance</a>		
9	K Factor Value		0.2
10	<b>C) LS Factor (weighted average, by area, for all slopes)</b>		
11	The effect of topography on erosion is accounted for by the LS factor, which combines the effects of a hillslope-length factor, L, and a hillslope-gradient factor, S. Generally speaking, as hillslope length and/or hillslope gradient increase, soil loss increases. As hillslope length increases, total soil loss and soil loss per unit area increase due to the progressive accumulation of runoff in the downslope direction. As the hillslope gradient increases, the velocity and erosivity of runoff increases. Use the LS table located in separate tab of this spreadsheet to determine LS factors. Estimate the weighted LS for the site prior to construction.		
12	<a href="#">LS Table</a>		
13	LS Factor Value		3.19
14			
15	<b>Watershed Erosion Estimate (=R<sub>x</sub>K<sub>x</sub>LS) in tons/acre</b>		58.2813
16	<b>Site Sediment Risk Factor</b>		<b>Medium</b>
17	Low Sediment Risk: < 15 tons/acre		
18	Medium Sediment Risk: >=15 and <75 tons/acre		
19	High Sediment Risk: >= 75 tons/acre		
20			

Receiving Water (RW) Risk Factor Worksheet	Entry	Score
<b>A. Watershed Characteristics</b>	yes/no	
A.1. Does the disturbed area discharge (either directly or indirectly) to a <b>303(d)-listed waterbody impaired by sediment</b> (For help with impaired waterbodies please visit the link below) or has a <b>USEPA approved TMDL implementation plan for sediment</b> ?:	<b>no</b>	<b>Low</b>
<a href="http://www.waterboards.ca.gov/water_issues/programs/tmdl/integrated2010.shtml">http://www.waterboards.ca.gov/water_issues/programs/tmdl/integrated2010.shtml</a> <p style="text-align: center;"><b>OR</b></p>		
A.2. Does the disturbed area discharge to a waterbody with designated beneficial uses of SPAWN & COLD & MIGRATORY? (For help please review the appropriate Regional Board Basin Plan)		
<a href="http://www.waterboards.ca.gov/waterboards_map.shtml">http://www.waterboards.ca.gov/waterboards_map.shtml</a>		
<a href="#">Region 1 Basin Plan</a> <a href="#">Region 2 Basin Plan</a> <a href="#">Region 3 Basin Plan</a> <a href="#">Region 4 Basin Plan</a> <a href="#">Region 5 Basin Plan</a> <a href="#">Region 6 Basin Plan</a> <a href="#">Region 7 Basin Plan</a> <a href="#">Region 8 Basin Plan</a> <a href="#">Region 9 Basin Plan</a>		

		Combined Risk Level Matrix		
		<u>Sediment Risk</u>		
<u>Receiving Water Risk</u>	Low	Low	Medium	High
	Low	Level 1	Level 2	
High	Level 2		Level 3	

Project Sediment Risk: **Medium**

Project RW Risk: **Low**

Project Combined Risk: **Level 2**

**ORIGINAL - MAKE COPIES**

**CERTIFICATION FORM  
(Store Completed Forms in Appendix XII)**

Project Name Alpine Regional Field Offices  
WDID Number 9 37C357448

This certification is for (check appropriate box):

The QSD will complete this box and, once signed by the approved signatory, insert the signed certification form in the appropriate Appendix.

- Amendment to SWPPP (Appendix XVI)
- PRDs (Appendix XII)
- NOT (Appendix XII)
- Other \_\_\_\_\_

*Any person signing documents under Section IV.1 of the CGP shall make the following certification:*

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, to the best of my knowledge and belief, the information submitted is, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

Robert C. Jackson  
Name of LRP \*

Gen Mgr + Dir. Constn Engrg  
Title

San Diego Gas + Electric  
Company

(858) 654-6451  
Telephone Number

  
Signature

6-16-2010  
Date

\*or approved signatory.



A  Sempra Energy utility®

**Patrick Lee**  
Vice President  
Sunrise Powerlink Project

**San Diego Gas & Electric**  
8330 Century Park Court, CP33A  
San Diego, CA 92123-1530

Tel: 858.650.6101  
Fax: 858.650.6106  
Patrick.lee@semprautilities.com

**TO:** Distribution

**DATE:** June 24, 2010

**FROM:** Patrick Lee

**SUBJECT: State Water Resources Control Board  
Construction Storm Water General Permit (Order 2009-0009)  
Authorized Signatories for  
San Diego Gas & Electric's Sunrise Power Link Project**

I am a Legally Responsible Person pursuant to State Water Resources Control Board Order No. 2009-0009-DWQ (NPDES General Permit No. CAS000002 – General Permit for Storm Water Discharges Associated with Construction and Land Disturbance Activities or “General Permit”). This letter is to acknowledge the persons listed below are authorized as Approved Signatories under this permit:

- ◆ Robert Jackson
- ◆ Jonathan Woldemariam

A copy of this authorization shall be retained with each Storm Water Pollution Prevention Plan prepared pursuant to this authorization.

**Distribution:** Robert Jackson; Jonathan Woldemariam, Alan Colton, Don Haines, Linda Collins, Amethyst Cruspero, Fred Jacobsen

# **Appendix XIII**

## **Responsible Parties**

## Appendix XIII List of Responsible Parties

PROJECT: Alpine Regional Field Office | **WDID NUMBER:** 9 37C357448

<input type="checkbox"/> <b>LEGALLY RESPONSIBLE PART (LRP)</b>				<input checked="" type="checkbox"/> <b>THE LRP's APPROVED SIGNATORY</b>			
<b>AREA OF RESPONSIBILITY:</b>		Construction and Engineering Sunrise Powerlink Project					
<b>NAME</b>	Robert C. Jackson				<b>TITLE:</b>	General Manager & Director	
<b>COMPANY NAME:</b>		SDG&E					
<b>ADDRESS</b>		8315 Century Park Court					
<b>CITY</b>	San Diego			<b>STATE</b>	CA	<b>ZIP</b>	92123
<b>TELEPHONE</b>	858-654-6451						
<b>EMERGENCY TELEPHONE</b>	619-778-6029						
<b>FAX</b>	858-637-3731						
<b>E-MAIL</b>	RCJackson@semprautilities.com						

<b>QUALIFIED SWPPP DEVELOPER (QSD): RESPONSIBLE FOR PREPARING THE SWPPP:</b>							
<b>NAME</b>	Sharon Humphreys, PE				<b>TITLE:</b>	Senior Project Manager	
<b>COMPANY NAME:</b>		Bureau Veritas					
<b>ADDRESS</b>		11590 West Bernardo Drive, Suite 100					
<b>CITY</b>	San Diego			<b>STATE</b>	CA	<b>ZIP</b>	92127
<b>TELEPHONE</b>	858-207-5091						
<b>EMERGENCY TELEPHONE</b>	858-776-9402						
<b>FAX</b>	858-451-2846						
<b>E-MAIL</b>	Sharon.humphreys@us.bureauveritas.com						

<b>ADDITIONAL QSD:</b>							
<b>AREA OF RESPONSIBILITY:</b>		Preparation of the SWPPP					
<b>NAME</b>	Tracy Beach, PE				<b>TITLE:</b>	Civil Engineer	
<b>COMPANY NAME:</b>		Bureau Veritas					
<b>ADDRESS</b>		11590 West Bernardo Drive, Suite 100					
<b>CITY</b>	San Diego			<b>STATE</b>	CA	<b>ZIP</b>	92127
<b>TELEPHONE</b>	858-207-5091						
<b>EMERGENCY TELEPHONE</b>	858-663-1887						
<b>FAX</b>	858-451-2846						
<b>E-MAIL</b>	Tracy.beach@us.bureauveritas.com						
<b>START DATE</b>				<b>END DATE</b>			

<b>QUALIFIED SWPPP PRACTITIONER (QSP):</b>			
<b>AREA OF RESPONSIBILITY:</b>			
<b>NAME</b>	Alex Greene	<b>TITLE:</b>	Senior Engineering Geologist
<b>COMPANY NAME:</b>		Geosyntec Consultants	
<b>ADDRESS</b>		10875 Rancho Bernardo Road, Suite 200	
<b>CITY</b>	San Diego	<b>STATE</b>	CA
		<b>ZIP</b>	92127
<b>TELEPHONE</b>	858-716-2911		
<b>EMERGENCY TELEPHONE</b>	619-997-6095		
<b>FAX</b>	858-674-6586		
<b>E-MAIL</b>	AGreene@Geosyntec.com		
<b>START DATE</b>	9/7/2010	<b>END DATE</b>	6/15/2013

<b>ADDITIONAL QSP:</b>			
<b>AREA OF RESPONSIBILITY:</b>		Daily Inspections	
<b>NAME</b>	Nick Jordan	<b>TITLE:</b>	SWPPP Coordinator
<b>COMPANY NAME:</b>		Par Electric	
<b>ADDRESS</b>		1010 Tavern Road	
<b>CITY</b>	Alpine	<b>STATE</b>	CA
		<b>ZIP</b>	91901
<b>TELEPHONE</b>	816-949-1000		
<b>EMERGENCY TELEPHONE</b>	619-772-0508		
<b>FAX</b>	619-445-4009		
<b>E-MAIL</b>	<a href="mailto:njordan@parelectric.com">njordan@parelectric.com</a>		
<b>START DATE</b>	7/25/2011	<b>END DATE</b>	6/15/2013

<b>SPILL RESPONSE PERSONNEL</b>			
<b>NAME</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	
		<b>ZIP</b>	
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>SPILL RESPONSE PERSONNEL</b>			
<b>NAME</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>SPILL RESPONSE PERSONNEL</b>			
<b>NAME</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>SPILL RESPONSE PERSONNEL</b>			
<b>NAME</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>STORM WATER SAMPLING AGENT:</b>			
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>STORM WATER SAMPLING AGENT:</b>			
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>STORM WATER SAMPLING AGENT:</b>			
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>STORM WATER SAMPLING AGENT:</b>			
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			
<b>START DATE</b>		<b>END DATE</b>	

<b>REGIONAL BOARD CONTACT INFORMATION</b>		<b>RQWQB NAME:</b>	
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			

<b>LOCAL STORM WATER MANAGEMENT AGENCY</b>		<b>AGENCY NAME:</b>	
<b>CONTACT PERSON</b>		<b>TITLE:</b>	
<b>ADDRESS</b>			
<b>CITY</b>		<b>STATE</b>	<b>ZIP</b>
<b>TELEPHONE</b>			
<b>EMERGENCY TELEPHONE</b>			
<b>FAX</b>			
<b>E-MAIL</b>			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
COMPANY NAME			
CONTACT PERSON		TITLE:	
ADDRESS			
CITY	STATE	ZIP	
TELEPHONE			
EMERGENCY TELEPHONE			
FAX			
E-MAIL			
START DATE	END DATE		

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
NAME	TITLE:		
ADDRESS			
CITY	STATE	ZIP	
TELEPHONE			
EMERGENCY TELEPHONE			
FAX			
E-MAIL			
START DATE	END DATE		

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER			
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>			
NAME	TITLE:		
ADDRESS			
CITY	STATE	ZIP	
TELEPHONE			
EMERGENCY TELEPHONE			
FAX			
E-MAIL			
START DATE	END DATE		

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

<input type="checkbox"/> CONTRACTOR <input type="checkbox"/> SUBCONTRACTOR <input type="checkbox"/> INDIVIDUAL DIRECTED BY QSP <input type="checkbox"/> OTHER				
<b>PLEASE CHECK APPROPRIATE BOX ABOVE. IF "OTHER", PLEASE INDICATE:</b>				
NAME			TITLE:	
ADDRESS				
CITY	STATE	ZIP		
TELEPHONE				
EMERGENCY TELEPHONE				
FAX				
E-MAIL				
START DATE	END DATE			

# **Appendix XIV**

## **Inspection Checklists**

# **Appendix XV**

## **Training Documentation**

## SWPPP Preparer's Training Log

Name of Person Attending Training Workshop	Date of Training Workshop	Title of Training Workshop	Location of Training Workshop
Tracy Beach	July 14-15, 2011	Low Impact Development Applications for Water Resource Management by Rod Frederick and Aaron Poresky with ASCE	San Diego, CA
Tracy Beach	February 15 – 17, 2011	QSD/QSP Training by Michael Alberson	San Diego, CA
Tracy Beach	April 8, 2010	Statewide Construction General Permit Overview Workshop by the SWRCB	Carlsbad, CA
Tracy Beach	March 3, 2010	San Diego County Model Standard Urban Stormwater Mitigation Plan (SUSMP) Seminar	San Diego, CA
Tracy Beach	February 25, 2010	Understanding the New State Water Board General Construction Permit Presented by Gerald R. Montgomery, Senior Manager, Interwest	San Diego, CA
Tracy Beach	April 22, 2008	Watershed-Friendly “Low Impact Development” Site Design & Permeable Pavements for Stormwater Management	Newport Beach, CA
Tracy Beach	March 25, 2008	Low Impact Development (LID) Seminar by Filterra Speaker Larry Coffman	Bonita, CA
Tracy Beach	February 28, 2008	National City SUSMP Workshop	National City, CA
Tracy Beach	November 19, 2007	San Diego Regional Stormwater Copermittees-Interim Hydromodification Plan/SUSMP Workshop for County of San Diego	San Diego, CA
Tracy Beach	November 6, 8 & 13, 2007	Construction Storm Water Compliance and Storm Water Pollution Prevention Plan Training Seminar by	San Diego, CA

**SWPPP Preparer's Training Log**

		the San Diego Building Industry Association (BIA)	
--	--	---	--

# CERTIFICATE OF TRAINING

CALIFORNIA CONSTRUCTION GENERAL PERMIT

## QUALIFIED SWPPP DEVELOPER (QSD) AND QUALIFIED SWPPP PRACTITIONER (QSP)

---

### Tracy Beach

Aug 30, 2011 - Aug 30, 2013

*Certificate # 20216*



California Stormwater Quality Association and  
California Construction General Permit Training Team

# **Appendix XVI**

## **Amendment Log**



**Appendix XVII**  
**Reports**

# **Appendix XVIII**


## **Secondary Containment and Spill Kit Inventory**

# **Appendix XIX**

## **Other SWPPP Exhibits**





View looking at the southwest portion of Construction Yard 19A – proposed location of the office complex. This area is currently being used to store construction materials.

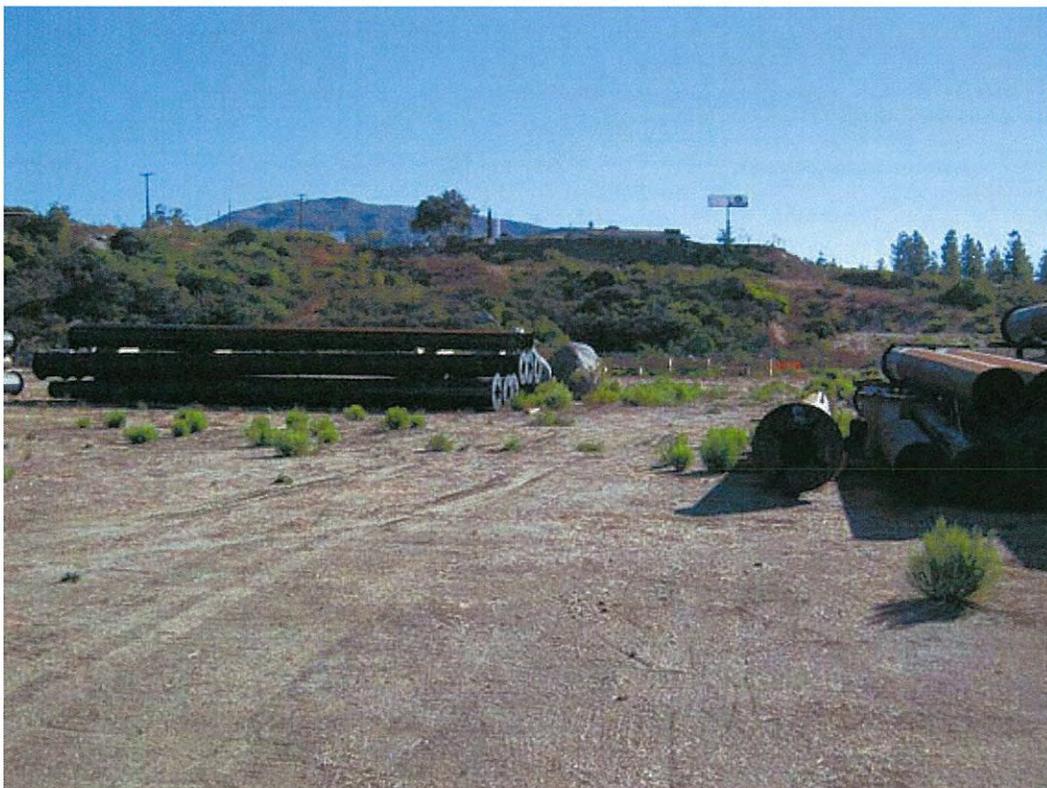

View looking at the southeast portion of Construction Yard 19A – proposed eastern portion of the Field Office area. Area is currently being used to store construction materials.



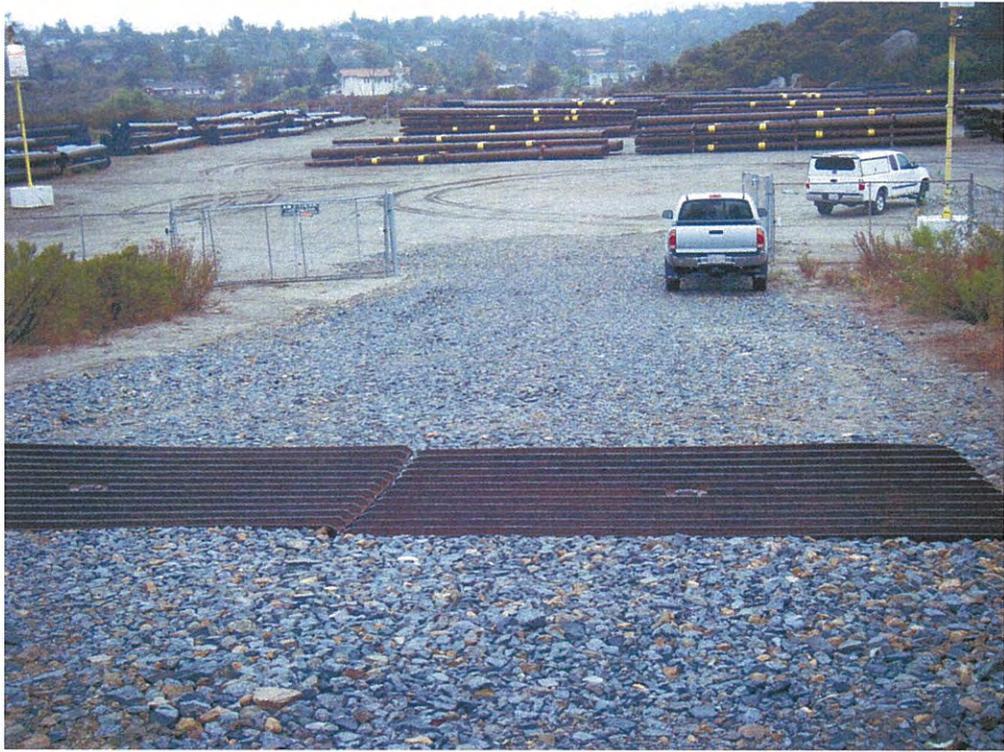

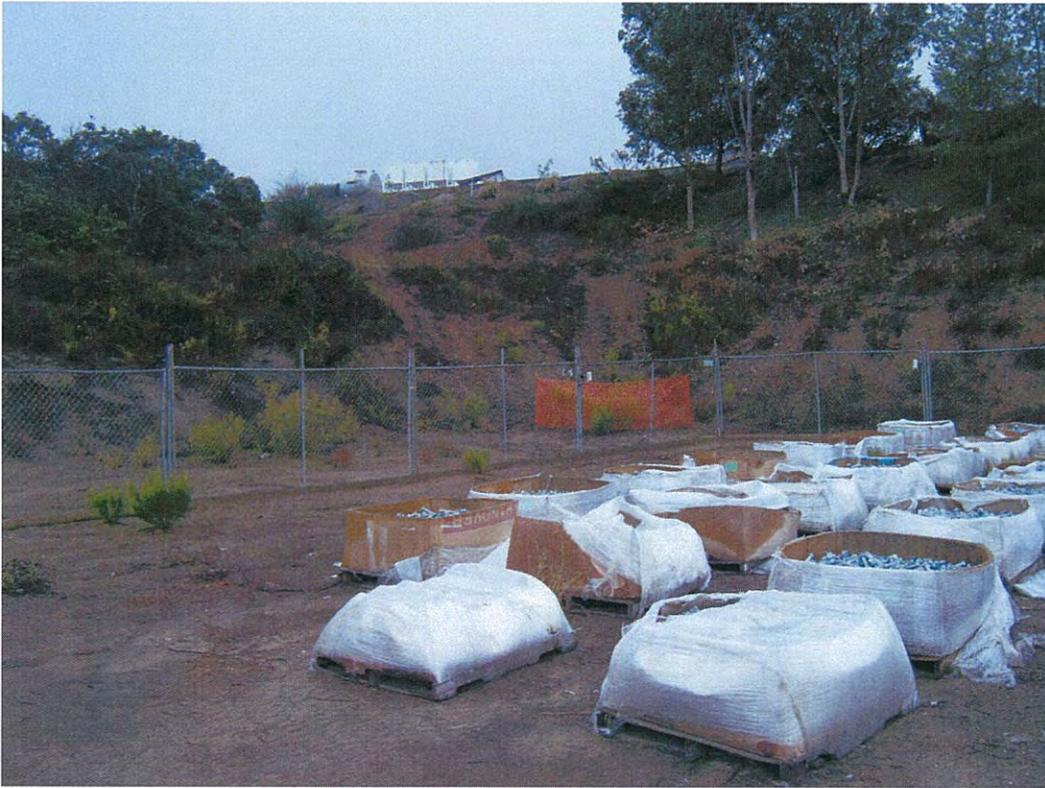



# **Appendix XX**

## **Active Treatment Systems**

# Active Treatment System (ATS)

Not Applicable

# **Appendix XXI**

## **Bioassessment**

# Bioassessment

Not Applicable

# **Appendix XXII**

## **Glossary / Acronyms**

**Glossary and Acronym List are taken from the SWRCB Order  
No.2009-0009-DWQ NPDES General Permit**

## APPENDIX 5: Glossary

### **Active Areas of Construction**

All areas subject to land surface disturbance activities related to the project including, but not limited to, project staging areas, immediate access areas and storage areas. All previously active areas are still considered active areas until final stabilization is complete. [The construction activity Phases used in this General Permit are the Preliminary Phase, Grading and Land Development Phase, Streets and Utilities Phase, and the Vertical Construction Phase.]

### **Active Treatment System (ATS)**

A treatment system that employs chemical coagulation, chemical flocculation, or electrocoagulation to aid in the reduction of turbidity caused by fine suspended sediment.

### **Acute Toxicity Test**

A chemical stimulus severe enough to rapidly induce a negative effect; in aquatic toxicity tests, an effect observed within 96 hours or less is considered acute.

### **Air Deposition**

Airborne particulates from construction activities. .

### **Approved Signatory**

A person who has legal authority to sign, certify, and electronically submit Permit Registration Documents and Notices of Termination on behalf of the Legally Responsible Person.

### **Beneficial Uses**

As defined in the California Water Code, beneficial uses of the waters of the state that may be protected against quality degradation include, but are not limited to, domestic, municipal, agricultural and industrial supply; power generation; recreation; aesthetic enjoyment; navigation; and preservation and enhancement of fish, wildlife, and other aquatic resources or preserves.

### **Best Available Technology Economically Achievable (BAT)**

As defined by USEPA, BAT is a technology-based standard established by the Clean Water Act (CWA) as the most appropriate means available on a national basis for controlling the direct discharge of toxic and nonconventional pollutants to navigable waters. The BAT effluent limitations guidelines, in general, represent the best existing performance of treatment technologies that are economically achievable within an industrial point source category or subcategory.

### **Best Conventional Pollutant Control Technology (BCT)**

As defined by USEPA, BCT is a technology-based standard for the discharge from existing industrial point sources of conventional pollutants including biochemical oxygen demand (BOD), total suspended sediment (TSS), fecal coliform, pH, oil and grease.

#### **Best Professional Judgment (BPJ)**

The method used by permit writers to develop technology-based NPDES permit conditions on a case-by-case basis using all reasonably available and relevant data.

#### **Best Management Practices (BMPs)**

BMPs are scheduling of activities, prohibitions of practices, maintenance procedures, and other management practices to prevent or reduce the discharge of pollutants. BMPs also include treatment requirements, operating procedures, and practices to control site runoff, spillage or leaks, sludge or waste disposal, or drainage from raw material storage.

#### **Chain of Custody (COC)**

Form used to track sample handling as samples progress from sample collection to the analytical laboratory. The COC is then used to track the resulting analytical data from the laboratory to the client. COC forms can be obtained from an analytical laboratory upon request.

#### **Coagulation**

The clumping of particles in a discharge to settle out impurities, often induced by chemicals such as lime, alum, and iron salts.

#### **Common Plan of Development**

Generally a contiguous area where multiple, distinct construction activities may be taking place at different times under one plan. A plan is generally defined as any piece of documentation or physical demarcation that indicates that construction activities may occur on a common plot. Such documentation could consist of a tract map, parcel map, demolition plans, grading plans or contract documents. Any of these documents could delineate the boundaries of a common plan area. However, broad planning documents, such as land use master plans, conceptual master plans, or broad-based CEQA or NEPA documents that identify potential projects for an agency or facility are not considered common plans of development.

#### **Daily Average Discharge**

The discharge of a pollutant measured during any 24-hour period that reasonably represents a calendar day for purposes of sampling. For pollutants with limitations expressed in units of mass, the daily discharge is calculated as the total mass of the pollutant discharged during the day. For pollutants with limitations expressed in other units of measurement (e.g., concentration) the daily discharge is calculated as the average measurement of the pollutant

throughout the day (40 CFR 122.2). In the case of pH, the pH must first be converted from a log scale.

**Debris**

Litter, rubble, discarded refuse, and remains of destroyed inorganic anthropogenic waste.

**Direct Discharge**

A discharge that is routed directly to waters of the United States by means of a pipe, channel, or ditch (including a municipal storm sewer system), or through surface runoff.

**Discharger**

The Legally Responsible Person (see definition) or entity subject to this General Permit.

**Dose Rate (for ATS)**

In exposure assessment, dose (e.g. of a chemical) per time unit (e.g. mg/day), sometimes also called dosage.

**Drainage Area**

The area of land that drains water, sediment, pollutants, and dissolved materials to a common outlet.

**Effluent**

Any discharge of water by a discharger either to the receiving water or beyond the property boundary controlled by the discharger.

**Effluent Limitation**

Any numeric or narrative restriction imposed on quantities, discharge rates, and concentrations of pollutants which are discharged from point sources into waters of the United States, the waters of the contiguous zone, or the ocean.

**Erosion**

The process, by which soil particles are detached and transported by the actions of wind, water, or gravity.

**Erosion Control BMPs**

Vegetation, such as grasses and wildflowers, and other materials, such as straw, fiber, stabilizing emulsion, protective blankets, etc., placed to stabilize areas of disturbed soils, reduce loss of soil due to the action of water or wind, and prevent water pollution.

**Field Measurements**

Testing procedures performed in the field with portable field-testing kits or meters.

**Final Stabilization**

All soil disturbing activities at each individual parcel within the site have been completed in a manner consistent with the requirements in this General Permit.

**First Order Stream**

Stream with no tributaries.

**Flocculants**

Substances that interact with suspended particles and bind them together to form flocs.

**Good Housekeeping BMPs**

BMPs designed to reduce or eliminate the addition of pollutants to construction site runoff through analysis of pollutant sources, implementation of proper handling/disposal practices, employee education, and other actions.

**Grading Phase (part of the Grading and Land Development Phase)**

Includes reconfiguring the topography and slope including; alluvium removals; canyon cleanouts; rock undercuts; keyway excavations; land form grading; and stockpiling of select material for capping operations.

**Hydromodification**

Hydromodification is the alteration of the hydrologic characteristics of coastal and non-coastal waters, which in turn could cause degradation of water resources. Hydromodification can cause excessive erosion and/or sedimentation rates, causing excessive turbidity, channel aggradation and/or degradation.

**Identified Organisms**

Organisms within a sub-sample that is specifically identified and counted.

**Inactive Areas of Construction**

Areas of construction activity that are not active and those that have been active and are not scheduled to be re-disturbed for at least 14 days.

**Index Period**

The period of time during which bioassessment samples must be collected to produce results suitable for assessing the biological integrity of streams and rivers. Instream communities naturally vary over the course of a year, and sampling during the index period ensures that samples are collected during a time frame when communities are stable so that year-to-year consistency is obtained. The index period approach provides a cost-effective alternative to year-round sampling. Furthermore, sampling within the appropriate index period will yield results that are comparable to the assessment thresholds or criteria for a given region, which are established for the same index period. Because index

periods differ for different parts of the state, it is essential to know the index period for your area.

**K Factor**

The soil erodibility factor used in the Revised Universal Soil Loss Equation (RUSLE). It represents the combination of detachability of the soil, runoff potential of the soil, and the transportability of the sediment eroded from the soil.

**Legally Responsible Person**

The person who possesses the title of the land or the leasehold interest of a mineral estate upon which the construction activities will occur for the regulated site. For linear underground/overhead projects, it is in the person in charge of the utility company, municipality, or other public or private company or agency that owns or operates the LUP.

**Likely Precipitation Event**

Any weather pattern that is forecasted to have a 50% or greater chance of producing precipitation in the project area. The discharger shall obtain likely precipitation forecast information from the National Weather Service Forecast Office (e.g., by entering the zip code of the project's location at <http://www.srh.noaa.gov/forecast>).

**Maximum Allowable Threshold Concentration (MATC)**

The allowable concentration of residual, or dissolved, coagulant/flocculant in effluent. The MATC shall be coagulant/flocculant-specific, and based on toxicity testing conducted by an independent, third-party laboratory. A typical MATC would be:

The MATC is equal to the geometric mean of the NOEC (No Observed Effect Concentration) and LOEC (Lowest Observed Effect Concentration) Acute and Chronic toxicity results for most sensitive species determined for the specific coagulant. The most sensitive species test shall be used to determine the MATC.

**Natural Channel Evolution**

The physical trend in channel adjustments following a disturbance that causes the river to have more energy and degrade or aggrade more sediment. Channels have been observed to pass through 5 to 9 evolution types. Once they pass through the suite of evolution stages, they will rest in a new state of equilibrium.

**Non-Storm Water Discharges**

Discharges are discharges that do not originate from precipitation events. They can include, but are not limited to, discharges of process water, air conditioner condensate, non-contact cooling water, vehicle wash water, sanitary wastes, concrete washout water, paint wash water, irrigation water, or pipe testing water.

**Non-Visible Pollutants**

Pollutants associated with a specific site or activity that can have a negative impact on water quality, but cannot be seen through observation (ex: chlorine). Such pollutants being discharged are not authorized.

**Numeric Action Level (NAL)**

Level is used as a warning to evaluate if best management practices are effective and take necessary corrective actions. Not an effluent limit.

**Original Sample Material**

The material (i.e., macroinvertebrates, organic material, gravel, etc.) remaining after the subsample has been removed for identification.

**pH**

Unit universally used to express the intensity of the acid or alkaline condition of a water sample. The pH of natural waters tends to range between 6 and 9, with neutral being 7. Extremes of pH can have deleterious effects on aquatic systems.

**Post-Construction BMPs**

Structural and non-structural controls which detain, retain, or filter the release of pollutants to receiving waters after final stabilization is attained.

**Preliminary Phase (Pre-Construction Phase - Part of the Grading and Land Development Phase)**

Construction stage including rough grading and/or disking, clearing and grubbing operations, or any soil disturbance prior to mass grading.

**Project****Qualified SWPPP Developer**

Individual who is authorized to develop and revise SWPPPs.

**Qualified SWPPP Practitioner**

Individual assigned responsibility for non-storm water and storm water visual observations, sampling and analysis, and responsibility to ensure full compliance with the permit and implementation of all elements of the SWPPP, including the preparation of the annual compliance evaluation and the elimination of all unauthorized discharges.

**Qualifying Rain Event**

Any event that produces 0.5 inches or more precipitation with a 48 hour or greater period between rain events.

**R Factor**

Erosivity factor used in the Revised Universal Soil Loss Equation (RUSLE). The R factor represents the erosivity of the climate at a particular location. An

average annual value of R is determined from historical weather records using erosivity values determined for individual storms. The erosivity of an individual storm is computed as the product of the storm's total energy, which is closely related to storm amount, and the storm's maximum 30-minute intensity.

**Rain Event Action Plan (REAP)**

Written document, specific for each rain event, that when implemented is designed to protect all exposed portions of the site within 48 hours of any likely precipitation event.

**Remaining Sub sampled Material**

The material (e.g., organic material, gravel, etc.) that remains after the organisms to be identified have been removed from the subsample for identification. (Generally, no macroinvertebrates are present in the remaining subsampled material, but the sample needs to be checked and verified using a complete Quality Assurance (QA) plan)

**Routine Maintenance**

Activities intended to maintain the original line and grade, hydraulic capacity, or original purpose of a facility.

**Runoff Control BMPs**

Measures used to divert runoff from offsite and runoff within the site.

**Run-on**

Discharges that originate offsite and flow onto the property of a separate project site.

**Revised Universal Soil Loss Equation (RUSLE)**

Empirical model that calculates average annual soil loss as a function of rainfall and runoff erosivity, soil erodibility, topography, erosion controls, and sediment controls.

**Sampling and Analysis Plan**

Document that describes how the samples will be collected, under what conditions, where and when the samples will be collected, what the sample will be tested for, what test methods and detection limits will be used, and what methods/procedures will be maintained to ensure the integrity of the sample during collection, storage, shipping and testing (i.e., quality assurance/quality control protocols).

**Sediment**

Solid particulate matter, both mineral and organic, that is in suspension, is being transported, or has been moved from its site of origin by air, water, gravity, or ice and has come to rest on the earth's surface either above or below sea level.

**Sedimentation**

Process of deposition of suspended matter carried by water, wastewater, or other liquids, by gravity. It is usually accomplished by reducing the velocity of the liquid below the point at which it can transport the suspended material.

**Sediment Control BMPs**

Practices that trap soil particles after they have been eroded by rain, flowing water, or wind. They include those practices that intercept and slow or detain the flow of storm water to allow sediment to settle and be trapped (e.g., silt fence, sediment basin, fiber rolls, etc.).

**Settleable Solids (SS)**

Solid material that can be settled within a water column during a specified time frame. It is typically tested by placing a water sample into an Imhoff settling cone and then allowing the solids to settle by gravity for a given length of time. Results are reported either as a volume (mL/L) or a mass (mg/L) concentration.

**Sheet Flow**

Flow of water that occurs overland in areas where there are no defined channels where the water spreads out over a large area at a uniform depth.

**Site****Soil Amendment**

Any material that is added to the soil to change its chemical properties, engineering properties, or erosion resistance that could become mobilized by storm water.

**Streets and Utilities Phase**

Construction stage including excavation and street paving, lot grading, curbs, gutters and sidewalks, public utilities, public water facilities including fire hydrants, public sanitary sewer systems, storm sewer system and/or other drainage improvements.

**Structural Controls**

Any structural facility designed and constructed to mitigate the adverse impacts of storm water and urban runoff pollution

**Suspended Sediment Concentration (SSC)**

The measure of the concentration of suspended solid material in a water sample by measuring the dry weight of all of the solid material from a known volume of a collected water sample. Results are reported in mg/L.

**Total Suspended Solids (TSS)**

The measure of the suspended solids in a water sample includes inorganic substances, such as soil particles and organic substances, such as algae,

aquatic plant/animal waste, particles related to industrial/sewage waste, etc. The TSS test measures the concentration of suspended solids in water by measuring the dry weight of a solid material contained in a known volume of a sub-sample of a collected water sample. Results are reported in mg/L.

**Toxicity**

The adverse response(s) of organisms to chemicals or physical agents ranging from mortality to physiological responses such as impaired reproduction or growth anomalies.

**Turbidity**

The cloudiness of water quantified by the degree to which light traveling through a water column is scattered by the suspended organic and inorganic particles it contains. The turbidity test is reported in Nephelometric Turbidity Units (NTU) or Jackson Turbidity Units (JTU).

**Vertical Construction Phase**

The Build out of structures from foundations to roofing, including rough landscaping.

**Waters of the United States**

Generally refers to surface waters, as defined by the federal Environmental Protection Agency in 40 C.F.R. § 122.2.<sup>1</sup>

**Water Quality Objectives (WQO)**

Water quality objectives are defined in the California Water Code as limits or levels of water quality constituents or characteristics, which are established for the reasonable protection of beneficial uses of water or the prevention of nuisance within a specific area.

---

<sup>1</sup> The application of the definition of "waters of the United States" may be difficult to determine; there are currently several judicial decisions that create some confusion. If a landowner is unsure whether the discharge must be covered by this General Permit, the landowner may wish to seek legal advice.

## APPENDIX 6: Acronym List

ASBS	Areas of Special Biological Significance
ASTM	American Society of Testing and Materials; Standard Test Method for Particle-Size Analysis of Soils
ATS	Active Treatment System
BASMAA	Bay Area Storm water Management Agencies Association
BAT	Best Available Technology Economically Achievable
BCT	Best Conventional Pollutant Control Technology
BMP	Best Management Practices
BOD	Biochemical Oxygen Demand
BPJ	Best Professional Judgment
CAFO	Confined Animal Feeding Operation
CCR	California Code of Regulations
CEQA	California Environmental Quality Act
CFR	Code of Federal Regulations
CGP	NPDES General Permit for Storm Water Discharges Associated with Construction Activities
CIWQS	California Integrated Water Quality System
CKD	Cement Kiln Dust
COC	Chain of Custody
CPESC	Certified Professional in Erosion and Sediment Control
CPSWQ	Certified Professional in Storm Water Quality
CSMP	Construction Site Monitoring Program
CTB	Cement Treated Base
CTR	California Toxics Rule
CWA	Clean Water Act
CWC	California Water Code
CWP	Center for Watershed Protection
DADMAC	Diallyldimethyl-ammonium chloride
DDNR	Delaware Department of Natural Resources
DFG	Department of Fish and Game
DHS	Department of Health Services
DWQ	Division of Water Quality
EC	Electrical Conductivity
ELAP	Environmental Laboratory Accreditation Program
EPA	Environmental Protection Agency
ESA	Environmentally Sensitive Area
ESC	Erosion and Sediment Control
HSPF	Hydrologic Simulation Program Fortran
JTU	Jackson Turbidity Units
LID	Low Impact Development
LOEC	Lowest Observed Effect Concentration
LRP	Legally Responsible Person
LUP	Linear Underground/Overhead Projects

MATC	Maximum Allowable Threshold Concentration
MDL	Method Detection Limits
MRR	Monitoring and Reporting Requirements
MS4	Municipal Separate Storm Sewer System
MUSLE	Modified Universal Soil Loss Equation
NAL	Numeric Action Level
NEL	Numeric Effluent Limitation
NICET	National Institute for Certification in Engineering Technologies
NOAA	National Oceanic and Atmospheric Administration
NOEC	No Observed Effect Concentration
NOI	Notice of Intent
NOT	Notice of Termination
NPDES	National Pollutant Discharge Elimination System
NRCS	Natural Resources Conservation Service
NTR	National Toxics Rule
NTU	Nephelometric Turbidity Units
O&M	Operation and Maintenance
PAC	Polyaluminum chloride
PAM	Polyacrylamide
PASS	Polyaluminum chloride Silica/sulfate
POC	Pollutants of Concern
PoP	Probability of Precipitation
POTW	Publicly Owned Treatment Works
PRDs	Permit Registration Documents
PWS	Planning Watershed
QAMP	Quality Assurance Management Plan
QA/QC	Quality Assurance/Quality Control
REAP	Rain Event Action Plan
Regional Board	Regional Water Quality Control Board
ROWD	Report of Waste Discharge
RUSLE	Revised Universal Soil Loss Equation
RW	Receiving Water
SMARTS System	Storm water Multi Application Reporting and Tracking
SS	Settleable Solids
SSC	Suspended Sediment Concentration
SUSMP	Standard Urban Storm Water Mitigation Plan
SW	Storm Water
SWARM	Storm Water Annual Report Module
SWAMP	Surface Water Ambient Monitoring Program
SWMM	Storm Water Management Model
SWMP	Storm Water Management Program
SWPPP	Storm Water Pollution Prevention Plan
TC	Treatment Control
TDS	Total Dissolved Solids

TMDL	Total Maximum Daily Load
TSS	Total Suspended Solids
USACOE	U.S. Army Corps of Engineers
USC	United States Code
USEPA	United States Environmental Protection Agency
USGS	United States Geological Survey
WDID	Waste Discharge Identification Number
WDR	Waste Discharge Requirements
WLA	Waste Load Allocation
WET	Whole Effluent Toxicity
WRCC	Western Regional Climate Center
WQBEL	Water Quality Based Effluent Limitation
WQO	Water Quality Objective
WQS	Water Quality Standard
