



5020 Chesebro Road, Suite 200, Agoura Hills, CA 91301-2285
Tel. 818-597-3407 • Fax 818-597-8001 • www.aspeneg.com

PROJECT MEMORANDUM
SCE WEST OF DEVERS UPGRADE PROJECT

To: John Forsythe, Project Manager, CPUC
From: Vida Strong, Aspen Project Manager
Date: April 16, 2020
Subject: Monitoring Report #107: April 6 to April 12, 2020

Introduction

This report provides a summary of the construction and compliance activities associated with Southern California Edison’s (SCE) West of Devers (WOD) Upgrade Project. SCE self-performed work (NTPs #2 and #3) is essentially complete with the exception of substation equipment upgrades and minor tie-ins. 220 kV work (NTPs #4 and #5) is approximately 55% complete.

CPUC Environmental Monitor (EM): CPUC EM, Rosina Goodman, was onsite April 6 through 8, and CPUC EM, Jamie Miner, was onsite April 11, 2020.

CPUC Notices to Proceed (NTPs)

Table 1 summarizes the NTPs with construction for the WOD Upgrade Project. No additional NTPs are required.

Table 1 - NTPs

| NTP # | Date Requested | Date Issued | Phase | Description |
|--------|----------------|-------------|--|--|
| NTP #1 | 04/04/17 | 06/29/17 | Material Yards | Construction or use of 10 Material Yards |
| NTP #2 | 05/18/17 | 06/29/17 | Substation Upgrades | Upgrades to 5 existing Substations |
| NTP #3 | 06/05/17 | 08/10/17 | Distribution, Subtransmission, and Telecom | Construction of the Distribution, Subtransmission, and Telecommunication portions of the Project |
| NTP #4 | 07/13/17 | 09/05/17 | Transmission | Transmission Line Construction on private lands |
| NTP #5 | 08/07/17 | 03/29/18 | Construction on BLM lands | Transmission Line construction on BLM lands |

Construction & Compliance

A summary of construction and compliance activities is provided below by NTP.

Material Yards (NTP #1)

As defined in NTP #1, Project material yards (MY) include:

- Mountain View #1 MY
- Lugonia MY (not being used)
- Grand Terrace MY
- Poultry MY

- San Timoteo MY (not being used)
- Beaumont #1 MY (not being used)
- Beaumont #2 MY
- Matich MY
- Hathaway #2 MY (not being used)
- Devers MY

To date, all material yard pre-compliance materials associated with NTP #1 that have been submitted have been approved.

Summary of Construction Activity

1. For the currently approved MYs, all activities are being performed by the contractor operating out of each respective yard.
2. The Poultry MY is being utilized by Barnard Construction and Power Grade Incorporated as their primary base of operations and material/equipment storage location. Work associated with the Poultry MY included material/equipment deliveries and general yard maintenance throughout the monitoring period. Helicopter operations occurred out of the Poultry MY during the subject monitoring period.
3. The Matich MY is being utilized by Barnard Construction primarily for tubular steel pole (TSP) storage and by Wilson as their primary base of operations and material/equipment storage location. Work associated with the Matich MY included material/equipment deliveries throughout the monitoring period. Helicopter operations occurred out of the Matich MY during the subject monitoring period.
4. The Mountain View #1 MY is being utilized by Abercrombie Services as their primary base of operations for materials/equipment storage, mobilization, and maintenance.
5. The Beaumont #2 MY is being utilized by CJ/Aldridge Drilling as their primary base of operations for material/equipment storage, mobilization, and maintenance.
6. The Grand Terrace MY is being used primarily as a show-up location for project construction crews.
7. The Devers MY is being utilized by CJ/Aldridge, Abercrombie Services, and Power Grade for construction activities on Segment 6 for material/equipment deliveries.

Environmental Compliance

1. There were no SCE self-reported and no CPUC incidents documented for construction activities associated with NTP #1 throughout the monitoring period.
2. There were no SWPPP maintenance item and no corrective actions associated with NTP #1 recorded during the monitoring period. To date, there are no open SWPPP maintenance or corrective actions associated with NTP #1.
3. There were no reportable (> 1 gallon) or non-reportable (< 1 gallon) spills associated with NTP #1 identified during the monitoring period.
4. As of the end of the monitoring period, there are no active nests at locations associated with NTP #1 during the monitoring period. If required, nest management, including establishment of buffers and the removal of inactive non-special-status bird species' nests, is being implemented per the requirements of the Project Nesting Bird Management Plan (NBMP). No nests were removed during the subject reporting period.
5. No special-status species were observed or identified at locations associated with NTP #1 during the monitoring period.

Substations (NTP #2)

Five substations are identified for improvements in NTP #2. These include:

- Etiwanda Substation
- San Bernardino Substation
- Vista Substation
- El Casco Substation
- Devers Substation

To date, all pre-compliance materials associated with NTP #2 that have been submitted have been approved.

Summary of Construction Activity

1. For the currently approved substation components, all work is being managed by Circle Wood Services with construction support from TTR Substations, Roberson Waite, Cunningham-Davis, and SCE crews. Wire stringing connections and wreck-out activities between the project alignment and locations within the substations are being performed by Abercrombie Services.
2. Construction activities at the San Bernardino Substation included applying protective grounding, removing primary grounding from disconnects to line drops, and boring new holes for foundations.
3. Construction activities at the Devers Substation included breaker installation and upgrade work at Position 8 (see Photo 1).
4. No construction activities occurred at the El Casco substation. Construction activities at the Etiwanda and Vista substations are complete.

Environmental Compliance

1. There were no SCE self-reported and no CPUC incidents documented for construction activities associated with NTP #2 throughout the monitoring period.
2. There were no SWPPP maintenance items or corrective actions associated with NTP #2 recorded during the monitoring period. To date, there are no open SWPPP maintenance or corrective actions associated with NTP #2.
3. There were no reportable (>1 gallon) or non-reportable (<1 gallon) spills associated with NTP #2 identified during the monitoring period.
4. As of the end of the monitoring period, there are five active nests located within work areas associated with NTP #2. These include red-tailed hawk, common raven, and great horned owl. If required, nest management, including establishment of buffers and the removal of inactive non-special-status bird species' nests, is being implemented per the requirements of the Project NBMP. There is one nest buffer reduction associated with NTP#2 during the subject reporting period for a common raven nest. No nests were removed during the subject reporting period.
5. No new special status species were observed or identified at locations associated with NTP #2 during the monitoring period.

Distribution, Subtransmission, and Telecommunication Work (NTP #3)

NTP #3 included distribution, subtransmission, and telecommunication improvements as presented below. These construction activities have been essentially completed, with minor follow up required in response to Project activities.

Distribution improvements included the following:

- Dental 12-kV Distribution Circuit (Dental Circuit)
- Intern 12-kV Distribution Circuit Underbuild (Intern Circuit)
- Reconductor on Juanita Street (Juanita Reconductor)

Subtransmission improvements included the following:

- Removal of San Bernardino–Redlands-Timoteo and the San Bernardino–Redlands-Tennessee 66-kV Lines (Timoteo-Tennessee Removal)
- Relocation of San Bernardino–Redlands-Timoteo 66-kV Lines (Timoteo Relocation)
- Relocation of San Bernardino–Redlands-Tennessee 66-kV Lines (Tennessee Relocation)

Telecommunication improvements included the following:

- San Bernardino Substation Connection to Redlands Inland Empire District Office (San Bernardino Connection)
- Timoteo-Redlands District Office Fiber Optic Cable Connection (Timoteo-Redlands Connection)
- El Casco Substation Connection to Vista Moreno OPGW (El Casco Connection), Segment 3
- Maraschino Substation Connection to Devers-Valley OPGW (Maraschino Connection)
- El Casco–Banning Connection to Devers-Vista Skywrap (El Casco–Banning Connection), Segment 4
- Banning Substation Connection to Devers-Valley OPGW (Banning Connection), Segment 6

Summary of Construction Activity

1. For the currently approved subtransmission and distribution components, construction activities are being performed by Abercrombie Services and SCE crews. No construction activities associated with NTP #3 occurred during the monitoring period.
2. As summarized below, construction of the NTP #3 primary components is essentially complete with the exception of minor tie-ins.
 - For distribution components, all 19 12-kV poles have been framed, all 12 12-kV underground vaults have been installed, and 7,430 feet of 7,430 feet of 12-kV duct bank (conduit) and 10,760 feet of 10,760 feet of 12-kV conductor wire has been installed.
 - For subtransmission components, 119 of 119 66-kV light weight TSPs have been erected, 19 of 19 TSPs have been erected, and 25,610 feet of 25,610 feet of 66-kV wire has been installed. Both the Timoteo and Tennessee circuits have been energized. Wreck-out of the existing subtransmission infrastructure has been completed.

Environmental Compliance

1. There were no SCE self-reported or CPUC incidents documented for construction activities associated with NTP #3 throughout the monitoring period.

2. There were no SWPPP maintenance items or corrective actions associated with NTP #3 recorded during the monitoring period. To date, there are no open SWPPP maintenance items or corrective actions associated with NTP #3.
3. There were no reportable (>1 gallon) or non-reportable (<1 gallon) spills associated with NTP #3 identified during the monitoring period.
4. As of the end of the monitoring period, there is one active nest (golden eagle) nest located within work areas associated with NTP #3 for which the required buffer has been established; however, no work is planned for the area. If required, nest management, including establishment of buffers and the removal of inactive non-special-status bird species' nests is being implemented per the requirements of the Project NBMP. No nests were removed during the subject reporting period.
5. No special-status species were observed or identified at locations associated with NTP #3 during the monitoring period.

Transmission Work (NTP #4)

NTP #4 includes six transmission line segments, identified as Segments 1 through 6, generally moving from west to east.

To date, pre-compliance materials associated with NTP #4, Segments 1 through 6, have been submitted and approved.

Summary of Construction Activity

1. For the currently approved transmission components, Power Grade Incorporated is conducting access road maintenance/stabilization, BMP installation, vegetation removal, and site grading. CJ/Aldridge Drilling is performing foundation work. Abercrombie Services is assembling and erecting new towers, and conducting wire operations with support from Summit Helicopters. Wilson Construction is conducting wire removal operations. Cunningham Davis Corporation is removing existing towers and foundations. Ancillary telecommunication work approved in NTP #4 is being performed by SCE crews.
2. Construction activities were limited during the subject monitoring period due to weather conditions.
3. Work activities associated with Segment 1 included foundation activities at Construction Areas 1X12, 1X13, and 1X15, and tower assembly at Construction Area 1X16.
4. Work activities associated with Segment 2 included storm preparation activities at Construction Area 2N32 and access road maintenance at Construction Area WS-2-PradoLn-MPR-27 (see Photo 2).
5. There were no work activities associated with Segment 3 during the subject monitoring period.
6. Work associated with Segment 4 included: Wire wreck-out activities (ground and helicopter) at Construction Areas 4X01 through 4X16, 4X23, and 4X25; installing snubs at Construction Areas 4X26 through 4X29; setting guard structures at Construction Areas 4X27, M23-T3, and 4X31; de-clipping and installing master grounds and cutting jumpers open at Construction Areas 4S56 and 4X58; setting TSP at Construction Area SF410; tower wreck-out at Construction Areas 4X01 and 4X02 (see Photo 3); and BMP maintenance at Construction Area 4X14.
7. Work associated with Segment 5 (which includes sites within Morongo lands along Segment 5 as reported by SCE) included: Wire wreck-out activities (ground and helicopter) at Construction Areas 5X52 through 5X54 and M76-T4; tower wreck-out at Construction Areas 5X23, WSS-5X31-5X32, 5X46, through 5X49, M72-T2 through M72-T3, WSS-M74-T4, M74-T3, M75-T2, M15-T2, M12-T2, M15-T3, and M15-T4; foundation wreck-out activities at Construction Areas 5X18 and 5X19; foundation activities at Construction Area 5X08; tower assembly at Construction Areas 5X07 through 5X16, 5X20, and

5X22 through 5X24; helicopter wire pull test-run at Construction Areas 5X08 through 5X11; wire pulling activities (ground and helicopter) at Construction Areas 5X14 through 5X32 and 5X36; BMP maintenance at Construction Areas 5X08 and 5X14; bird deterrent installation at Construction Areas 5X22 and 5X23; and counterpoise grounding installation at Construction Areas 5X16 through 5X20 and 5X22.

8. Work associated with Segment 6 (non-BLM lands) included: Wreck-out activities at Construction Areas 6X09-6X10, 6N18, 6X21, M61-T1, M62-T1, M62-T3, and M62-T4 (see Photo 4); site cleanup activities at Construction Area 6N32; BMP maintenance activities at Construction Areas 6N32 and 6N40; and punch-list activities at Construction Area 6N30.
9. 220 kV construction updates from SCE are being provided on a bi-weekly basis. The next update will be provided on April 28. As of April 14, construction progress associated with NTP #4 is as follows:
 - Grading for foundation installation has been completed at 458 of 469 sites.
 - Foundations are completed for 365 of 386 lattice towers and 70 of 83 TSPs.
 - Erection of 191 of 386 lattice towers and 63 of 83 TSPs have been completed.
 - Erection of 60 of 94 temporary shoofly locations has been completed.
 - Stringing of approximately 3.7 of 8.0 circuit miles of shoofly conductor, 65.1 of 184.0 circuit miles of mainline conductor, and 32.33 of 99.0 circuit miles of OPGW fiber has been completed.
 - Demolition of 165 of 602 existing structures and 124 of 415 existing foundations has been completed.
 - Wire wreck-out has been completed along 54.45 circuit miles of 184.
 - 25 of 304 sites have been restored and hydroseeded.
10. The first required outages (Project Move 1 and Project Move 2) were completed in 2018. Project Moves 3 and 4 were completed in 2019. Move 5 in Segments 1, 2, 5, and 6 began on August 5, 2019 and was completed January 15, 2020. Move 6 in Segment 2 began on October 14, 2019 and was completed on February 14, 2020. Move 7 in Segment 1 began on February 24, 2020 and was completed on March 18, 2020. Move 8, in all segments except Segment 2, began on March 9, 2020 and is expected to be completed by August 14, 2020.

Environmental Compliance

1. There were no SCE self-reported or CPUC incidents reported during the subject monitoring period. Two observations were reported for non-project related construction activities on Segment 6 during the subject monitoring period.
2. There were two SWPPP maintenance items associated with NTP #4 recorded during the monitoring period. These included sediment build-up on pro wattles on Segments 2 and 4. To date, there are no open SWPPP maintenance items or corrective actions associated with NTP #4.
3. There were no reportable (>1 gallon) or non-reportable (<1 gallon) spills associated with NTP #4 identified during the monitoring period.
4. Meetings to review helicopter flight tracks with SCE generally occur every two weeks. Flight tracks are reviewed to monitor compliance with local jurisdiction construction work hours and sensitive receptor avoidance, including residences, schools, and nesting bird avoidance areas. Flight tracks were not reviewed as scheduled on April 2 due to technical difficulties. SCE identified two helicopter nest buffer incursions during internal review of the tracks. One incursion occurred on March 25 for a red-

tailed hawk nest at Construction Area 5S43 on Segment 5. The second nest buffer incursion occurred on March 26 for a common raven nest at Construction Area M8-T4, also on Segment 5. SCE determined the incursions occurred due to a miscommunication between the pilot and SCE's environmental team. For each nest, the buffer information was not included in the GPS data the pilot had uploaded. Each nest was discovered the same day as the incursions occurred and the pilot had not yet been made aware of their presence. No impacts to the nests occurred and incubation was observed at both nests as of April 1, 2020. The next flight track review will take place on April 16, 2020.

5. As of the end of the monitoring period, there are 143 active nests associated with NTP #4 during the monitoring period. These nests include great horned owl, barn owl, burrowing owl, Anna's hummingbird, verdin, Say's phoebe, California thrasher, common raven, greater roadrunner, cactus wren, rock wren, Lawrence's goldfinch, lesser goldfinch, bushtit, house finch, California towhee, black-throated sparrow, California quail, mourning dove, killdeer, loggerhead shrike, Cooper's hawk, white-tailed kite, red-shouldered hawk, and red-tailed hawk. Buffers have been established per the Project NBMP. If required, nest management, including establishment of buffers and the removal of inactive non-special-status bird species' nests is being implemented per the requirements of the Project NBMP. There are fifty-one nest buffer reductions associated with NTP #4 during the monitoring period for red-tailed hawk, greater roadrunner, cactus wren, verdin, common raven, burrowing owl, black-throated sparrow, house finch, song sparrow, Anna's hummingbird, lesser goldfinch, and great horned owl. No nests were removed during the subject reporting period.
6. There were two special-status species observed or identified at locations associated with NTP #4 during the monitoring period. These included burrowing owl and northern harrier.
7. There was one new woodrat midden identified on Segment 5. A 10-foot Environmentally Sensitive Area (ESA) avoidance buffer was staked per the Special-status Small Mammals Avoidance and Minimization Plan. There were no woodrat midden relocations documented during the monitoring period.
8. SCE provided documentation of FAA filings for the Project on September 17 and September 26, 2018; FAA concurrence will be required prior to tower installation where applicable. Additional information was provided February 11, 2019. FAA recommended marker balls have been installed on the shoofly spans near El Casco Substation; from Construction Area 2N01 to 2N04, and 2N12 to 2N14 on Segment 2; and from Construction Area 6S27 to 6S28 on Segment 6. FAA lighting was installed at Construction Area 2N02.

Transmission Work BLM Lands (NTP #5)

NTP #5 includes the portion of one transmission line segment, identified as Segment 6, which traverses properties managed by the Bureau of Land Management (BLM). NTP #5 was approved by BLM on March 29, 2018. The preconstruction compliance package for BLM lands was deemed acceptable by BLM on February 5, 2019.

Summary of Construction Activity

1. For the currently approved transmission components, Power Grade Incorporated is conducting access road maintenance/stabilization, BMP installation, vegetation removal, and site grading. CJ/Aldridge Drilling is performing foundation work. Abercrombie Services is assembling and erecting new towers, and conducting wire operations with support from Summit Helicopters. Wilson Construction is conducting wire wreck-out activities. Cunningham Davis Corporation is removing existing towers and foundations.
2. Work activities associated with Segment 6 (BLM lands) during the monitoring period included punch-list activities at Construction Areas 6N30.

Environmental Compliance

See NTP #4 discussion above for environmental compliance activities.

Temporary Extra Workspaces (TEWS) and Minor Project Refinements (MPRs)

One TEWS and no MPRs were approved during the subject monitoring period. Table 2 summarizes the TEWS and MPRs for the WOD Upgrade Project to date.

Table 2 – TEWS & MPRs
(Updated 04/16/20)

| TEWS / MPR | Date Requested | Date Issued | Phase | Description |
|--|----------------|-------------|-----------------------------|--|
| Temporary Extra Workspaces (TEWS) | | | | |
| TEWS #1 | 10-12-17 | 10-19-17 | Maraschino Connection | Access to Beaumont Cherry Valley District water hydrant meter located near the intersection of Highland Springs Avenue and Crooked Creek, Beaumont. |
| TEWS #2 | 11-13-17 | 11-21-17 | El Casco–Banning Connection | Water source on Oak Valley Boulevard. |
| TEWS #3 | 12-15-17 | 12-15-17 | Banning Connection | Access to existing poles off of Lincoln Street. |
| TEWS #4 | 12-18-17 | 12-18-17 | Banning Connection | Access to existing poles off of Wesley Street. |
| TEWS #5 | 12-20-17 | 12-21-17 | Banning Connection | Access to existing poles at intersection of Wesley Street and Old Idyllwild Road. |
| TEWS #6 | 6-13-18 | 6-13-18 | Timoteo Relocation | Extra workspace to facilitate erection of TSP #4696058 at intersection of Redlands Boulevard and Bryn Mawr Street. |
| TEWS #7 | 7-27-18 | 7-30-18 | Timoteo Relocation | Extra workspace to facilitate wire pulling activities along Research Drive and Almond Avenue. |
| TEWS #8 | 8-27-18 | 8-28-18 | Dental/Intern Circuits | DENIED AND RESCINDED – Extra workspace to facilitate construction along Mission Road. |
| TEWS #9 | 10-18-18 | 10-19-18 | Timoteo Relocation | Extra workspace for walking path at Bryn Mawr and I-10. |
| TEWS #10 | 11-05-18 | 11-05-18 | Timoteo Relocation | Extra workspace along Barton and Mountain View Roads for cutover operations. |
| TEWS #11 | 01-30-19 | 01-31-19 | Timoteo Relocation | Extra workspace to facilitate the removal of fiber optic cable from overhead poles north along Mountain View Avenue and east along Redlands Boulevard. |
| TEWS #12 | 02-06-19 | 02-07-19 | Timoteo Relocation | Extra workspace along Mountain View Avenue for subtransmission pole removal. |
| TEWS #13 | 02-26-19 | 02-26-19 | Segment 3 | Temporary access road detour for vehicle and equipment travel to/from San Timoteo Canyon Road and Tower Site 3X41. |
| TEWS #14 | 05-13-19 | 05-14-19 | Banning Connection | Extra workspace along the east side of south Alola Street, City of Banning. |
| TEWS #15 | 05-16-19 | 05-17-19 | Segment 1 | HLZ and temporary staging area for construction vehicles, materials, and equipment. |
| TEWS #16 | 07-24-19 | 07-24-19 | Segment 2 | Concrete V-ditch south of 3012 Prado Lane, accessible from approved access roads to Construction Area 2X18. |
| TEWS #17 | 08-07-19 | 08-07-19 | Segment 6 | Access road for guard pole installation near Construction Area 6S15. |

| TEWS / MPR | Date Requested | Date Issued | Phase | Description |
|---|-----------------------|--------------------|---|---|
| TEWS #18 | 08-16-19 | 08-16-19 | Segment 6 | Helicopter landing zone and temporary staging area for construction vehicles, materials, and equipment. |
| TEWS #19 | 09-05-19 | 09-05-19 | Segment 5 | Mobile guard structure on an existing road to Construction Area SF501 for wire stringing activities. |
| TEWS #20 | 09-27-19 | 09-30-19 | Segment 6 | Mobile guard structure on existing access road to Construction Areas 6S20 and 6S21 for wire stringing activities. |
| TEWS #21 | 12-11-19 | 12-12-19 | Etiwanda Substation | Extra workspace within the existing concrete switchrack trench inside the active substation. |
| TEWS #22 | 01-31-20 | 01-31-20 | Segment 2 | Extra workspace adjacent to Construction Area 2N35 for staging and operating a wire puller. |
| TEWS #23 | 03-11-20 | 03-12-20 | Segment 6 | Access road near 6N38 for guard structure. |
| TEWS #24 | 03-17-20 | 03-17-20 | Segment 5 | Extra workspace for staging wire stringing equipment. |
| TEWS #25 | 04-08-20 | 04-08-20 | Segment 4 | Extra workspace for guard structure near Construction Area 4X25. |
| Minor Project Refinements (MPRs) | | | | |
| MPR #1 | 11-17-17 | 11-22-17 | Maraschino Connection | Revisions to the amount of new underground telecom construction. |
| MPR #2 | 12-13-17 | 12-15-17 | Maraschino Connection | Addition of two vault work areas on Highland Springs Road. |
| MPR #3 | 12-21-17 | 12-28-17 | El Casco–Banning Connection | Adjustments to alignment along Oak Valley Parkway. |
| MPR #4 | 12-27-17 | 1-3-18 | Maraschino/El Casco–Banning Connections | Continued use of two fire hydrants previously approved as TEWS #1 and TEWS #2. |
| MPR #5 | 1-16-18 | 1-22-18 | Banning Connection | Continued use of access routes described in TEWS #3, 4, and 5 and temporary access paths through private property along Coyote Trail. |
| MPR #6 | 2-8-18 | 2-12-18 | Project-wide | Use of 10 water sources to support construction activities. |
| MPR #7 | 2-23-18 | 2-28-18 | Poultry MY | Temporary water and electrical supply to yard. |
| MPR #8 | 2-27-18 | 3-2-18 | El Casco Connection/Segment 1 | New telecom splice location and single new steel pole installation. |
| MPR #9 | 3-26-18 | 3-27-18 | El Casco Connection | Telecom work areas along El Casco Substation access road. |
| MPR #10 | 4-6-18 | 4-9-18 | Mountain View #1 MY/All subtrans | Additional workspaces at Mountain View #1 MY entry and at subtransmission improvements work areas. |
| MPR #11 | 5-4-18 | 5-8-18 | Tennessee Relocation | Relocation of 5 subtransmission structures from the east side to the west side of Nevada Street. |
| MPR #12 | 5-14-18 | 5-16-18 | Timoteo Relocation | Additional workspace for TSP erection at Bryn Mawr Avenue and Interstate 10. |
| MPR #13 | 5-23-18 | 5-25-18 | Project-wide | Addition of encased fire hose to O'Grady Court water source and use of 17 water sources to support construction activities. |

| TEWS / MPR | Date Requested | Date Issued | Phase | Description |
|-------------------|-----------------------|--------------------|--|--|
| MPR #14 | 5-24-18 | 5-31-18 | Timoteo/ Tennessee Relocations | Location shift of 3 TSPs and 1 vault location. |
| MPR #15 | 5-31-18 | 6-4-18 | Poultry MY | Paving of access road and trailer complex area. |
| MPR #16 | 6-11-18 | 6-13-18 | Banning Connection | Shift of horizontal directional drilling (HDD) alignment through Smith Creek and addition of walking paths along Coyote Trail. |
| MPR #17 | 6-20-18 | 6-22-18 | Dental Circuit/ Tennessee Relocation | Additional workspace along Mission Road, Lugonia Avenue, and Nevada Street. |
| MPR #18 | 8-3-18 | 8-7-18 | Timoteo Relocation/ Beaumont #2 MY | Expansion of vault installation work area off Mountain View Avenue and new water source near Beaumont #2 MY. |
| MPR #19 | 8-13-18 | 8-20-18 | Segment 4 | Additional workspace requests at Sites 4N58, 4N59, and 4N64. |
| MPR #20 | 8-21-18 | 8-27-18 | Banning Connection | Use of unpaved access road west of Smith Creek. |
| MPR #21 | 10-4-18 | 10-10-18 | Project-wide/ Segments 3&4 | Use of 6 water sources, installation of water tank, use of access road, and expansion of WSS. |
| MPR #22 | 11-19-18 | 11-20-18 | Subtrans and Telecom | Pole replacement, switch replacement, and shift in underground telecom route. |
| MPR #23 | 12-11-18 | 12-21-18 | Transmission | Site 3N32 and Move 3 work areas. |
| MPR #24 | 01-15-19 | 01-28-19 | Transmission | Additional Wire Stringing Site in Segment 1. |
| MPR #25 | 03-11-19 | 03-14-19 | Transmission | Additional work area west of Supersite 3X55, Segment 3. |
| MPR #26 | 04-02-19 | 04-04-19 | Transmission | Use of Prado Lane access road (Segment 2) and two existing hydrants (Segment 6). |
| MPR #27 | 04-30-18 | 05-01-19 | Transmission | Use of two existing hydrants (Segment 1), water tank (Segment 2), and helicopter work area (Segment 3). |
| MPR #28 | 05-31-19 | 06-06-19 | Transmission | Extra workspace areas, including helicopter landing zones and access roads, on Segments 1, 2, and 6. |
| MPR #29 | 06-27-19 | 07-03-19 | Transmission | Extra workspace areas for equipment/material staging, wire stringing, and telecom work, on Segments 3, 4, and 6. |
| MPR #30 | 08-01-19 | 08-06-19 | Subtrans and Telecom | Additional workspaces for Maraschino and Devers Telecom Cable Removals, Segments 4 and 6. |
| MPR #31 | 10-2-19 | 10-08-19 | Transmission | Extra temporary work areas for wire stringing on Segment 2 and use of an existing access road on Segment 4. |
| MPR #32 | 11-18-19 | 12-03-19 | Transmission | Additional work areas for Segments 4 and 6 construction activities. |
| MPR #33 | 01-08-20 | 01-09-20 | Transmission | Installation of platform in existing tower to facilitate RTHA nest relocation. |
| MPR #34 | 02-19-20 | 03-02-20 | Transmission | Additional Move 8 work areas and access road to the Match MY. |
| MPR #35 | 04-14-20 | 04-15-20 | Transmission | Additional Move 8 work areas on Segments 2, 4, and 6. |

CPUC Compliance Incidents, Project Memoranda (PMs) and Non-Compliance Reports (NCRs)

No Incidents, PMs, or NCRs were issued by the CPUC EMs during the subject reporting period. Table 3 summarizes the CPUC Incidents, PMs, and NCRs issued to date.

Table 3
CPUC Incidents, Project Memoranda, and Non-Compliance Reports
 (Updated 04/16/20)

| Incident/PM/NCR | Regulatory Requirement | Date Issued | Phase | Description |
|------------------|------------------------|-------------|------------------------------|--|
| Level 1 Incident | Traffic Control Plan | 01-30-18 | Banning Connection | Traffic control was set up in such a way that diverted flow into active work area and deviated from approved Traffic Control Plan. |
| Level 1 Incident | MM WIL-1b | 04-19-18 | Timoteo/Tennessee Relocation | A portable water tank was observed uncovered for four consecutive days. |
| Level 1 Incident | MM VEG-1a | 5-24-18 | El Casco Substation | Equipment was staged outside of approved disturbance limits for at least 1-2 days. |
| Level 1 Incident | MM AQ-1a | 8-15-18 | Banning Connection | Fugitive dust observed from construction activities. |
| Level 1 Incident | MM WIL-1b | 8-15-18 | Banning Connection | Use of unapproved access road. |
| Level 1 Incident | MM WIL-1b | 8-15-18 | Banning Connection | Use of unapproved staging area. |
| Level 1 Incident | Fire Management Plan | 9-18-18 | Segment 4 | Lack of adequate fire abatement equipment at 3 locations. |
| Level 1 Incident | Fire Management Plan | 9-20-18 | Segment 4 | Lack of adequate fire abatement equipment |
| Level 1 Incident | HH-1a | 10-17-18 | Segment 4 | Lack of proper secondary containment for 4 pieces of equipment. |
| Level 1 Incident | N-1a | 10-17-18 | Segment 4 | Work outside of approved hours |
| Level 1 Incident | WIL-1b | 10-18-18 | Grand Terrace MY | Lack of proper covering for pipes between 1.5" to 4" |
| Level 1 Incident | N-1a | 10-18-18 | Segment 4 | Work outside of approved hours |
| Level 1 Incident | AQ-1a | 10-30-18 | Grand Terrace MY | Fugitive Dust Emissions Outside of Property Boundaries at the Grand Terrace Yard. |
| Level 1 Incident | WIL-1b | 01-24-19 | Segment 3 | Pipes/tubing left open at Sites 3X08 and 3X10. |
| Level 1 Incident | AQ-1a | 02-13-19 | Segment 3 | Fugitive dust along Segment 3 access road to 3X06. |
| Level 2 Incident | VEG-3a | 02-13-19 | Segment 3 | Offsite sediment discharge from access road into JD ID 3054. |
| Level 1 Incident | SWPPP | 09-25-19 | Segment 6 | The disposal of slurry at tower sites in Segment 6. |

| Incident/ PM/NCR | Regulatory Requirement | Date Issued | Phase | Description |
|-----------------------------|-----------------------------------|------------------------|-------------------------------------|---|
| Level 1 Incident | SWPPP | 10-22-19 | Devers, Match, and Poultry MY | Improper storage of treated wood poles. |
| Level 1 Incident | VEG-1c | 12-06-19 | Segment 2 | Materials staged outside of approved work limits just north of M4-T3. |
| Level 1 Incident | MMCRP | 03-16-20 | Segment 5 | Material and equipment staged outside of approved disturbance areas between Construction Areas 5X28 and 5X29. |

PROJECT PHOTOGRAPHS



Photo 1 – Breaker installation at the Devers Substation (April 6, 2020) (Photo courtesy of SCE).



Photo 2 – Access road maintenance at Construction Area WS-2-PradoLn-MPR-27, Segment 2 (April 10, 2020) (Photo courtesy of SCE).



Photo 3 – Tower wreck-out at Construction Area 4X01, Segment 4 (April 11, 2020) (Photo courtesy of SCE).

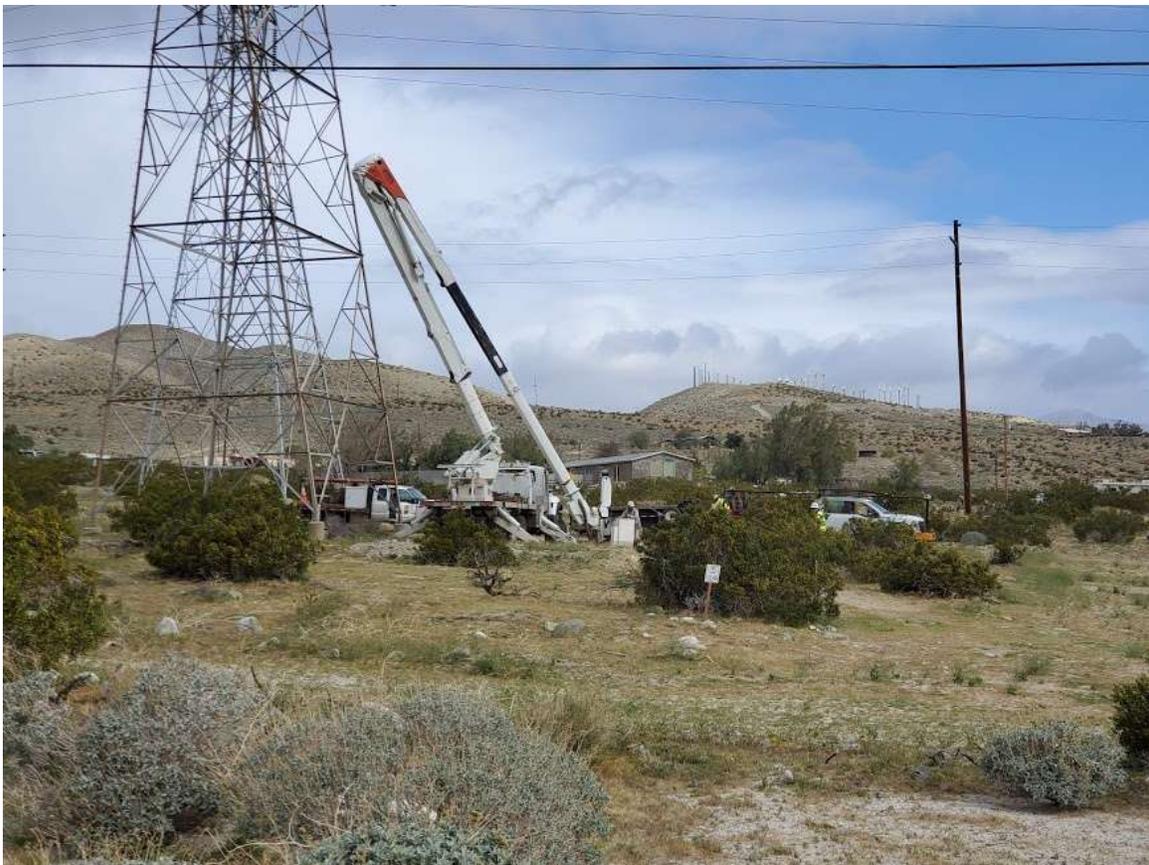


Photo 4 – Wreck-out activities at Construction Area 6N18, Segment 6 (April 6, 2020).
