



5020 Chesebro Road, Suite 200, Agoura Hills, CA 91301-4316
Tel. 818-597-3407, Fax 818-597-8001, www.aspeneg.com

**PROJECT MEMORANDUM
SDG&E'S SUNRISE POWERLINK PROJECT**

To: Billie Blanchard, Project Manager, CPUC
From: Vida Strong, Aspen Project Manager
Date: May 30, 2013
Subject: Weekly Reports 133 – 139, March 31, 2013 – May 18, 2013

INTRODUCTION

This report provides a summary of the construction, restoration and compliance activities associated with the SDG&E Sunrise Powerlink Project. This report is organized as follows:

- Transmission Line Construction
- Substation Construction and Upgrades
- Construction Yards
- Notices to Proceed
- Variances & Temporary Extra Workspace
- Non-Compliances & Incidents

CPUC/Aspen Environmental Monitors (EM): Valerie Yep.

TRANSMISSION LINE CONSTRUCTION

Summary of Activity:

The Sunrise Powerlink transmission line, including the 500 kV and 230 kV links, was energized between June 15 and 17, 2012. Since energization, restoration, including monitoring and weed control, of disturbed project areas along the transmission line right-of-way has been underway.

The habitat restoration sites for the Sunrise Powerlink right-of-way are divided into six sections: desert, mountains east, mountains west, coastal, total uplands, and total wetlands. As presented in Table 1, the site preparation, seeding, and cactus planting (if applicable) have been completed for the Sunrise habitat restoration sites. In addition, each habitat restoration site, in each section, has a rotating monitoring and maintenance schedule. According to Table 17 of the Restoration Plan for Sensitive Vegetation in Temporary Impact Areas (RPSV), during Year 1, maintenance and monitoring site visits will occur at least monthly for the first 120 days after planting and at least four additional times during the remainder of the year, respectively. Table 1 below provides a summary of this progress for the habitat restoration sites.

In addition, weed control is being conducted at all areas which were temporarily impacted and permanently impacted (PIAs) by the Sunrise Powerlink Project. Weed control efforts began in 2011, concurrent with construction activities, and will continue throughout the life of the project. The project has been divided into five parts for weed management: Coastal, Mountains West, Mountains East, Desert, and Helicopter Access PIA sites; with field crews assigned to each section. Within each section, the field crews move throughout their territory and control weeds on a prescribed schedule, but are also reassigned to treat priority weeds at certain sites as they are observed. As of May 2013, field crews have covered at least two weeding cycles within their respective regions. Future maintenance visits are scheduled to occur for at least two additional cycles before the year's end. More site visits may be scheduled based on the need of individual sites and the emergence of weeds.



TABLE 1
Sunrise Habitat Restoration Implementation, Maintenance & Monitoring
MONTHLY PROGRESS SUMMARY

(Updated: May 2, 2013)

Section	Implementation Tasks (Percent Complete)			Maintenance Visit (Percent Complete)			Monitoring (Qualitative)			Performance Monitoring (Quantitative)
	Site Prep	Seeding	Cactus Planting	1st	2nd	3rd	1st	2nd	3rd	2013
Desert	100%	100%	100%	100%	100%	63%	100%	100%	0%	100%
Mountains East	100%	100%	100%	100%	61%	12%		89%	0%	0%
Mountains West	100%	100%	100%	100%	85%	0%	100%	98%	0%	0%
Coastal	100%	100%	N/A	100%	88%	21%	99%	96%	6%	20%
Total Uplands	100%	100%	100%	100%	84%	22%	100%	95%	2%	25%
Total Wetlands	100%	100%	N/A	100%	100%	—*	—*	N/A	N/A	0%

*Pending

Environmental Compliance:

No CPUC Non-Compliance Reports or Project Memoranda were issued during the subject period for transmission line activities. Non-Compliance activities for the project to date are summarized in Table 5.

Agency Representatives during Construction (other than EMs):

None.

SUBSTATION CONSTRUCTION AND UPGRADES

Summary of Activity:

1. Suncrest Substation, Link 3 (non-federal lands): Complete and in the operation and maintenance phase.
2. Imperial Valley (IV) Substation Upgrade (BLM lands): No Sunrise related work occurred during the subject reporting period.
3. San Luis Rey Substation (non-federal lands): During Week 133 crews continued to work on the 69 kV upgrades to the distribution banks. During Week 134 equipment was removed and site cleanup was conducted. Upgrade work has been completed.
4. Encina Substation (non-federal lands): The following work was conducted at the Encina Substation during the subject period:
 - Week 133: Crews excavated piers in the 138 kV section of the substation, placed conduit inside the previously excavated trench, and backfilled with an approved slurry mix.
 - Week 134: Crews built forms, installed rebar, poured concrete, backfilled trenches, excavated additional pad sites, and drilled piers. Rebar cages were assembled for installation.
 - Week 135: Crews poured concrete, prepped rebar, and excavated trenches for the pier locations.
 - Week 136: Crews excavated conduit trenches, laid conduit, poured slurry and backfilled trenches to final grade (see Figure 1). Crews also poured a pad site within the 230 kV yard.

- Week 137: Crews installed shooting grounds, laid ground wire grids and backfilled the area. Final grade was completed at finished pad sites. Steel assembly and site cleanup began (see Figure 2).
 - Week 138: No work was conducted during this reporting period.
 - Week 139: Crews drilled a foundation for the termination point in the new 230 kV yard (see Figure 3). Rebar cages were assembled and a foundation was poured.
5. Pomerado Substation: (non-federal lands): No Sunrise related work occurred during the subject reporting period.
 6. Sycamore Substation: No Sunrise related work occurred during the subject reporting period.

Environmental Compliance:

1. All applicable Biological, Cultural, Paleontological, and Native American monitors have been present during ground disturbing activities at all substations.
2. Trash was removed from Encina Substation and crews utilized a magnetic broom to collect small metal debris from the work area.
3. A Biological Monitor began weekly site inspections and nesting bird surveys at Encina Substation beginning Week 138. Environmentally Sensitive Area (ESA) signage was installed to establish a bird nest buffer (see Figure 4).

No CPUC Non-Compliance Reports or Project Memoranda were issued during the subject period for Substation Construction and Upgrade activities. Non-Compliance activities for the project to date are summarized in Table 5.

Agency Representatives during Construction (Other than CPUC EMs):

None.

Construction YARDS

Summary of Activity:

The Sunrise Powerlink transmission line, including the 500 kV and 230 kV links, was energized between June 15 and 17, 2012. Since energization, restoration, including monitoring and weed control, of project construction yards has been underway with the exception of the Alpine and Rough Acres yards. The project yards, like the transmission line habitat restoration sites, have been divided into the six sections as presented above. Table 1 above provides a summary of restoration implementation, maintenance, and monitoring. In addition, weed control is being conducted at the construction yards as described above.

Environmental Compliance:

No Non-Compliance Reports or Project Memorandums were issued during the subject period for Construction Yards. Non-Compliance activities for the project to date are summarized in Table 5.

Agency Representatives during Construction (other than CPUC EMs)

None.

NOTICES TO PROCEED (NTPs)

No NTPs were submitted or reviewed during the subject period. Table 2 summarizes the CPUC Notice to Proceed activity for the SDG&E Sunrise Powerlink Project to date.

TABLE 2
CPUC NTPs
(Updated 05/30/13)

NTP#	Date Requested	Date Issued	Segment	Description
#1	01/04/10	04/28/10	25	San Luis Rey Substation Upgrades
#2	02/08/10	04/29/10	23	South Bay Substation Upgrades
#3	02/26/10	05/20/10	Yard	Alpine Yard 18
#4	01/26/10	05/28/10	Yard	Alpine Yard 18A
#5	02/05/10	09/28/10	Yard	Rough Acres Yard, Phase 1
#6	05/26/10	09/28/10	24	Encina Substation Upgrades
#7	05/28/10	09/28/10	Telecomm	White Star Communication Facility
#8	06/09/10	10/06/10	Substation	Pomerado Substation Upgrades
#9	06/09/10	10/06/10	Substation	Scripps Switchyard/Substation Upgrades
#10	10/13/10	11/23/10	15	Link 4, Alpine 230 kV Underground Construction
#11	10/19/10	12/15/10	13	Link 3, Suncrest Substation/Wilson Construction Yard
#12	11/30/10	12/23/10	Yard	Rough Acres Yard, Phase 2
#13	11/09/10	01/14/11	2-18, 20-22	Links 1, 2, and 5, overhead construction on non-federal lands
BLM #1	01/19/11	02/03/11	1	Imperial Valley Substation upgrades.
BLM #2	03/28/11	04/04/11	2-12, 16-17	Links 1, 2, and 5 overhead construction on BLM Lands.
Miramar	01/20/11	06/28/11	22	Overhead and substation construction.
USFS	07/29/11	08/09/11	6, 7, 10, 12,14,16	Links 1, 2, and 5 overhead construction on USFS Lands.

VARIANCE & TEMPORARY EXTRA WORKSPACE REQUESTS

No Variance or TEWS requests were submitted or reviewed during the subject period. Variance and Temporary Extra Workspace (TEWS) requests submitted to date are presented in Tables 3 and 4, respectively.

TABLE 3
VARIANCE REQUESTS
(Updated 05/30/13)

Variance Request	Date Requested	Date Issued	Segment #	Description
#1	11/04/10	11/10/10	Yard	Thomas Yard (El Centro, CA)
#2	12/22/10	03/18/11	Yard	Sycamore Estates Construction Yard. Response to inquiry received 02/23.
#3	01/06/10	01/18/11	All	Modification to tree trimming requirements.
#3 MOD	01/25/11	01/26/11	All	Modification to brush clearing requirements.
#4	01/13/11	03/01/11	Yard	Helicopter Temporary Landing Pad area at the Alpine Regional Field Offices.
#5	02/01/11	02/09/11	Yard	Site improvements at the Wilson Construction yard and along Bell Bluff Trail
#6	02/01/11	03/01/11	Link 5	Variance from Mitigation Measure H-1a (CC) to allow work outside of the dry season.

Variance Request	Date Requested	Date Issued	Segment #	Description
#7	02/11/11	02/17/11	Link 3	Additional work areas for construction trailers, parking, etc.
#8	03/02/11	03/08/11	Link 2	Alternate access route to Structure EP 27.
#9	03/29/11	04/06/11	All	Perform construction activities outside of hours allowed by local ordinances with local jurisdiction approval.
#10	04/04/11 (revised)	04/14/11	Link 4	Additional construction work space at Viejas Creek Bridge.
#11	04/06/11	04/22/11	Link 1	Additional workspace east of EP215.
#12	04/15/11	04/25/11	Link 1	Additional turnaround along the access road to EP 220-1.
#13	04/13/11	05/06/11	Links 1 & 2	Two fiber optic regeneration sites.
#13 Mod	05/08/12	05/10/12	Links 1 & 2	Alter configuration of regeneration sites to meet fire safety requirements.
#14	04/28/11	05/03/11	Yards	Change visual screening at Project construction yards from slats to fabric.
#15	05/12/11	05/19/11	Link 2	Alternate access to EP 84.
#16	05/16/11	05/21/11	Link 4	Additional parking space for use during underground construction.
#17	05/18/11	05/24/11	Encina Substation	Driveway improvement.
#18	06/27/11	07/14/11	Link 1	Gate installation between mile markers 38.5 and 39.5.
#18 Mod	10/03/11	Under Review	Link 1	Alternative for installation of Gate #4.
#19	06/27/11	06/29/11	Link 1	Installation of training tower at Rough Acres Construction Yard.
#20	06/28/11	08/05/11	Link 5	Additional disturbance for access, pull sites and topsoil stockpile at CP48-2 to CP51-2.
#21	07/07/11	07/15/11	Link 1	Guard structure from EP255 to Imperial Valley Substation.
#22	07/08/11	08/04/11	Link 1	Fromm Construction Yard. Additional information submitted 08/04.
BLM DNA #1	06/22/11	08/05/11	Link 1, 2 and 5	Minor modifications to portions of the Project on Bureau of Land Management lands.
#23	08/15/11	10/20/11	Links 1, 2, & 5	Additional landing platforms and TSAPS.
#24	08/25/11	08/29/11	Suncrest Substation	Additional vegetation clearing around construction trailers.
#25	09/01/11	09/09/11	Links 1 & 5	Extended use of approved TEWS areas for parking and staging.
#26	09/15/11	09/20/11	Link 2	Water tank installation at Barrett Canyon Yard.
#27	09/20/11	10/18/11	Link 1	Temporary Staging area near Mountain Springs Grade Road.

Variance Request	Date Requested	Date Issued	Segment #	Description
#28	10/19/11	Denied	Link 3	Allow work to continue at Suncrest Substation during a Red Flag Warning (RFW) event.
#29	10/21/11	11/01/11	Links 1, 2, & 5	Additional guard structures identified for wire pulling activities.
#29 Mod	01/04/12	01/06/12		Modification to guard structure location.
#30	11/01/11	11/15/11	Links 1, 2, & 5	Temporary parking and turnaround areas.
#30 Mod	02/09/12	02/09/12	Links 5	Modification to perform long lining activities.
#31	11/08/11	Retracted	Links 2 & 5	Request for site specific exemption of Condition 37 of NTP 13.
#32	11/15/11	12/09/11	Links 1, 2, & 5	Additional workspace for wire pulling activities.
#32 Mod	01/04/12	01/06/12		Modification to guard structure location
BLM DNA #2	10/21/11	12/14/11	Overhead	Micrositing changes
#33	11/28/11	12/16/11	Links 1, 2, & 5	Additional workspace for structure access and wire pulling activities.
#34	11/29/11	12/02/11	Links 2 & 5	Extension of allowable work window within GE buffer (MM B-7h).
#35	12/22/11	01/04/12	Link 5	Improvements to existing road & drainage, Simpson property.
#36	01/20/12	02/08/12	Links 1, 2, & 5	Variance to allow vegetation clearing between January 15 through February 14.
#37	01/20/12	02/08/12	Links 1, 2, & 5	Temporary placement of concrete blocks outside of approved work areas.
BLM DNA #3	02/08/12	02/10/12	Overhead	Anchor block micrositing
#38	02/10/12	02/22/12	Link 5	Gate installation near CP55.
#39	02/10/12	Retracted	Link 5	Additional work space at CP23 pull site.
#40	03/20/12	03/21/12	Link 5	Additional work space near GS-NF-7, San Vicente Reservoir.
#41	04/17/12	04/27/12	Link 2	Cinnamon Drive Road improvements near EP36-1.
#42	05/09/12	Retracted	Link 2	Temporary concrete anchor block placement.
#43	09/05/12	09/13/12	Yards	Post-construction landowner requests.
#44	09/06/12	10/02/12	Links 1, 2 & 5	Three permanent telecommunication facilities.
BLM DNA #4	11/09/12	01/30/13	Links 2 and 5	Permanent placement of radio communication facilities and secondary TSAPS at CP60 and EP146.

TABLE 4
TEMPORARY EXTRA WORKSPACE (TEWS) REQUESTS
(Updated 05/30/13)

TEWS Request	Date Requested	Date Approved	Segment #	Description
TEWS #1	11/01/10	11/01/10	White Star	Asphalt paved area for vehicle parking and staging
TEWS #2	03/17/11	03/18/11	Link 4	Parking on Puetz Valley and Alpine Blvd
TEWS #3	03/17/11	03/18/11	Link 4	Parking on Harbison Canyon and Alpine Blvd
TEWS #4	03/22/11	03/23/11	Link 5	Storage on One Father Junipero Sierra Trail
TEWS #5	03/24/11	03/24/11	Link 4	Parking at 3900 Willows Road West
TEWS #6	03/24/11	03/24/11	Link 4	Parking at 5840 Willows Road East
TEWS #7	04/06/11	04/07/11	Link 2	Northern access road to EP 79
TEWS #8	04/14/11	04/14/11	Link 2	Northeast spur of access road to EP 84
TEWS #9	05/17/11	05/24/11	Link 1	Use of SWPL tower sites for parking (EP331-341)
TEWS #10	05/24/11	05/24/11	Link 5	Parking and pullsite adjacent to Alliant University
TEWS #11	06/16/11	06/16/11	Link 1	Use of alternative access to EP 240, per the request of the landowner at JVR
TEWS #12	06/20/11	06/20/11	Link 1	Use of SWPL tower sites for parking (EP295-299)
TEWS #13	06/30/11	07/01/11	Link 1	Use of SWPL tower site for parking (EP324)
TEWS #14	07/01/11	07/01/11	Link 1	Use of SWPL tower sites for parking (EP300, EP302, EP306, EP307, EP312)
TEWS #15	07/06/11	07/06/11	Link 1	Use of SWPL tower sites for parking (EP294, EP303, EP304, EP305)
TEWS #16	06/30/11	07/07/11	Link 1	Additional parking along Mountain Springs Grade Road
TEWS #17	07/11/11	07/12/11	Link 5	Parking near CP20
TEWS #18	07/11/11	07/12/11	Link 5	Parking near CP24
TEWS #19	07/11/11	07/12/11	Link 5	Parking near CP29
TEWS #20	07/18/11	07/19/11	Link 1	Parking near EP314
TEWS #21	07/22/11	07/25/11	Link 1	Parking near EP315
TEWS #22	07/26/11	07/26/11	Link 1	Parking near EP291-293
TEWS #23	08/05/11	08/05/11	Link 1	Parking near EP290
TEWS #24	08/09/11	08/10/11	Link 2	Parking near EP90/EP91
TEWS #25	09/07/11	09/07/11	Link 5	Temporary use of access road near El Monte Road (12 kV)
TEWS #26	09/13/11	09/13/11	Link 2	Temporary use of access road near Barrett Substation
TEWS #27	09/29/11	09/30/11	Link 1	Parking near EP248.
TEWS #28	09/28/11	10/03/11	Link 1	Parking and Staging area adjacent to EP301.
TEWS #29	09/13/11	09/13/11	Link 2	Placement of Water Tank at Barrett Substation.
TEWS #30	10/06/11	10/06/11	Link 1	Parking and Staging at Chevron Gas Station on Carrizo Gorge Road.
TEWS #31	11/09/11	11/10/11	Link 1	Parking at EP252A-1 and EP254-3-E.
TEWS #32	11/09/11	11/15/11	Link 5	Temporary material and equipment staging area off of Willows Road.
TEWS #33	02/09/12	02/09/12	Link 5	Additional parking area between CP75 to CP88.

TEWS Request	Date Requested	Date Approved	Segment #	Description
TEWS #34	03/06/12	03/06/12	Link 5	Additional parking area along Hwy 67.
TEWS #35	03/26/12	03/27/12	Link 1	Additional parking area between EP227/EP228.
TEWS #36	04/26/12	04/26/12	Link 2	Additional workspace adjacent to Access Road EP11-3-N.
TEWS #37	05/25/12	05/25/12	Link 2	Additional workspace near EP32.
TEWS #38	05/25/12	05/29/12	Link 2	Additional workspace adjacent to EP119.
TEWS #39	06/27/12	06/27/12	Link 5	Additional parking and staging at El Monte Park.

NON-COMPLIANCES & INCIDENTS

No non-compliances or incidents were noted during subject period. CPUC and USFS Stop Work Orders, Project Memorandum (PM) and Non-Compliance Reports (NCR), and U.S. Army Corps Non-Compliances (NC) that have been issued to date are presented in Table 5.

TABLE 5
NON-COMPLIANCES (NC) AND PROJECT MEMORANDA (PM)
 (Updated 05/30/13)

Type	Date	Location	Description
PM #1	12/07/10	Thomas Yard	Failure to report unanticipated biological resources within 48 hours.
PM #2	02/11/11	EP 242, Link 1	Unauthorized ground disturbance at EP 242
NC #1	03/08/11	Suncrest Substation	Army Corp of Engineers issued Non-Compliance for not complying with Special Conditions 19, 21 and 23 of DA Permit SPL-2007-00704-SAS.
PM #3	03/15/11	CP 67-3, Link 5	Staking crews operating and delivered by helicopters within GE Buffer area.
PM #4	04/06/11	Swat Yard	Unauthorized Nest Removal from a water truck at SWAT Construction yard.
PM #5	05/16/11	EP 340, Link 1	Operation of water trucks outside of approved disturbance areas at EP 340.
PM #6	09/16/11	EP271, Link 1	Construction activities commenced at EP271 prior to the arrival of biological monitor.
Stop Work Order	09/27/11	Helicopter Operations	A pattern of helicopter incidents posed a serious concern for the safety of the general public.
PM #7	09/28/11	AER CY	Construction crew entered AER CY prior to Peninsular Bighorn Sheep monitor clearing the site.
NCR #1	09/28/11	Link 1	CPUC issued NCR for breaching a marked Environmentally Sensitive Area (ESA), construction activity without proper monitor present, and failing to communicate the event in a timely fashion.
FS NCR #1	10/27/11	Links 2 & 5	FS SUP Exhibit 4 and Traffic Control Plan violations.
NCR #2	10/27/11	Link 1	Peninsular Bighorn Sheep Construction Monitoring Plan violations.

Type	Date	Location	Description
FS NCR #2	11/03/11	Links 2 & 5	Fire Plan and Traffic Control Plan violations.
FS NCR #3	11/30/11	Links 2 & 5	Tower assembly, erection and wire stringing work is suspended for towers not associated with GE buffers on the Cleveland National Forest until resolution of all noncompliance colorization issues are agreed upon by the Forest Service
NCR #3	12/29/11	Link 1	Peninsular Bighorn Sheep Construction Monitoring Plan violations.
NCR #4	01/04/12	Link 1	Peninsular Bighorn Sheep Construction Monitoring Plan violations.
FS Stop Work Order	01/07/12	Links 2 & 5	Third non-compliance for violating the Forest Service Fire Plan.
FS NCR #4	02/01/12	Link 2	Failure to make timely notification following rope/wire drop between CP100 to CP99.
FS NCR #5	02/06/12	Links 2 & 5	Helicopter incursions into Golden Eagle Habitat Buffers.
NCR #5	02/08/12	Link 1	Construction outside of approved work spaces, intrusion into ESA, and violation of Desert Pavement Plan.
NCR#6	04/13/12	Link 1, 2, & 5	Repeated load carrying without appropriate netting.

SDG&E monitoring staff and/or crews did not identify any other compliance incidents during the subject period. Other compliance incidents identified by SDG&E monitoring staff and/or crews to date are presented in Table 6.

**TABLE 6
PROJECT INCIDENTS**
(Updated 05/30/13)

Type	Date	Location	Description
Incident	11/01/10	White Star	Delivery of a rebar cage outside of the approved disturbance area.
Incident	02/17/11	EP 244, Link 1	Nest incorrectly marked at entrance to EP 244.
Incident	02/18/11	Alpine HQ	Emergency weather landing and storage of 3 helicopters at Alpine HQ.
Incident	03/12/11	EP 252, Link 1	Bulldozer was delivered at site prior to CPUC clearance being given.
Incident	03/15/11	EP 214, Link 1	Dewatering approximately 1 gal of groundwater from an excavation hole without having submitted a dewatering plan to the CPUC.
Incident	04/06/11	JVR 12 kV, Link 1	Confusion on approved work areas due to varying maps having been distributed to workers and monitors.
Incident	04/07/11	JVR 12 kV, Link 1	A site was worked on prior to CPUC EM construction release having been received for the area, no resources were damaged.

Type	Date	Location	Description
Incident	05/05/11	Link 4	Three small fires were reported on Link 4 Underground. Fire tools were used by the on-site fire patrol to immediately respond per the Sunrise Fire Plan. Notification to Alpine Fire was made.
Incident	05/17/11	Link 1	BMP crew drove off the road between EP345 and EP346 and park within the ESA boundary.
Incident	06/07/11	Link 1	During the aerial delivery of a structure body to EP339, approximately 200 ft outside of Plaster City Yard, the piece fell from the Aircrane. No injuries have been reported.
Incident	06/10/11	Link 1	During the aerial delivery of a structure layback to EP 339, at the EP 339 construction site, 3 of the 4 hooks released and caused an emergency placement of the steel at the site. While in the process of placing on the ground, the 4 th hook released and the tower fell to the ground. No injuries have been reported.
Incident	07/07/11	Link 1	A project water tanker was stuck on the side of Evan Hughes Highway and released approximately 1,000 gallons of potable water into Coyote Wash, after pulling over to evaluate a bridge crossing. All necessary notifications were made.
Incident	07/07/11	Link 5	Construction vehicles, including project fire truck, were noted to be outside of approved disturbance areas at CP40 and CP41. Link leads were notified and immediate corrective action was taken.
Incident	07/11/11	Link 1	A skid fell off the KMax Helicopter while en route to a tower site. The skid was within the Project ROW and no injuries were reported. The item was retrieved on foot.
Incident	07/28/11	Link 1	Unapproved disturbance of approximately 50'x100' occurred during the grading operations of the AER yard. No resources were impacted.
Incident	08/04/11	Link 1	An air compressor was dropped approximately 500 ft north of EP327, from a KMax helicopter while in transit to a micropile site. Approximately 50-60 gallons of diesel was spilled in an area of approximately 75' in diameter. Site has been cleared and appropriate agencies have been contacted.
Incident	08/05/11	Link 3	Small fire resulted from excavation activities along BBTT. Burned an area approximately 50'x50' prior to it being extinguished. Notifications were made immediately.
Incident	08/13/11	Link 2	Accident along Lyons Valley Rd, where a project truck went off the embankment by 300'. No injuries reported. Assessment team was sent to the site and notifications were made.
Incident	08/15/11	Link 2	Sparks caused by loose chain from a project vehicle interacting with the roadway started a 2-acre fire. The fire was extinguished and proper notifications were made.
Incident	08/18/11	Link 2	An unsteady load caused a forklift to fall to its side at EP 91. A small spill of hydraulic fluid took place, all disturbance was contained within the established work area, and no injuries were reported.

Type	Date	Location	Description
Incident	08/22/11	Link 1	Crew member threw a rock and knocked down a rock cairn located within an ESA. Appropriate agencies were notified.
Incident	09/08/11	Link 2	CPUC EM noted a water truck entering EP91 after not having stopped at designated wash station. Corrective action was taken.
Incident	09/12/11	Link 5	Crew performed minor clearing prior to the arrival of biological monitor.
Incident	09/13/11	Link 5	Crew performed minor clearing prior to the arrival of biological monitor.
Incident	09/15/11	Link 5	Micropile platform at CP67-3 rolled 50' downhill after unstable placement. A helicopter removed from site to limit damage. Minor vegetation damage that was surveyed by onsite biologist.
Incident	09/19/11	Link 2	Small fire near EP42 started due to excavator hitting a rock during grading operations. This was immediately put out by onsite personnel using their required fire supplies.
Incident	09/19/11	Link 2	2 Micropile pipes were dropped during helicopter operations near CP107 and rolled down hill to injure a worker trying to stop them. Minor vegetation damage that was surveyed by onsite biologist.
Incident	09/20/11	Link 1	Trackout from EP252 was noted to Link Lead and was immediately remedied.
Incident	09/20/11	Link 1	Project vehicles were noted to parking outside of the approved project disturbance. Link Lead was notified and vehicles were immediately relocated.
Incident	09/21/11	Link 1	Dozer operator drove approximately 260 ft off of ROW near EP322. Area was surveyed by Cultural and Biological monitor.
Incident	09/21/11	Link 3	Approximately 800 gallons of potable water was released from Northern Sediment basin. Appropriate agencies were notified.
Incident	09/22/11	Link 3	Plywood load from helicopter dropped within substation boundaries. No injuries were reported.
Incident	09/23/11	Link 1	Improperly covered foundations holes were noted to the Link Lead. Follow up was performed with crews.
Incident	09/26/11	Link 1	Straw wattles en route via helicopter dropped into open area. No injuries were reported.
Incident	10/12/11	Link 1	A drill rig pulled to the side of the access road near EP185/EP186 and inadvertently crushed vegetation.
Incident	10/12/11	Link 4	Approximately 50 gallons of diesel fuel was released immediately off of Puetz Valley Road Site was cleaned and stained soils removed. Appropriate agencies were contacted.
Incident	10/19/11	Link 1	A door fell off a helicopter near Plaster City Yard close to EP332. No injuries were reported.
Incident	11/03/11	Link 1	Injury occurred when a tower leg fell onsite. Events surrounding the incident are still undergoing investigation. Disturbance occurred outside of approved areas. Biological/cultural monitors reviewed and found no resources to be damaged.

Type	Date	Location	Description
Incident	11/05/11	Link 5	Sediment off ROW at CP55/56 access road.
Incident	11/09/11	Link 2	Landing of project helicopter on unapproved disturbance areas.
Incident	11/15/11	Link 5	Off ROW incident along access road to CP65/66 pull site.
Incident	11/16/11	Link 1	Off ROW incident along access road to EP 226/227 pull site.
Incident	11/16/11	Link 3	Trash noted to be blown around during Air Crane activities at the Wilson Yard.
Incident	11/22/11	Link 5	Track out noted on El Monte Rd from access in/out of CP64/65 pull site. Street sweeper was dispatched.
Incident	12/03/11	Link 1	PBHS habitat violation with low elevation flights in restricted areas.
Incident	12/04/11	Link 1	PBHS habitat violation with low elevation flights in restricted areas.
Incident	12/22/11	Link 1	PBHS habitat violation with entry into Fromm Yard prior to clearance from PBHS biologists.
Incident	12/27/11	Link 1	Two PBHS habitat violation with low elevation flights in restricted areas.
Incident	01/09/12	Link 2	Road crew operating without an Arroyo Toad Monitor present at EP50, Arroyo Toad suitable habitat. Crew was retrained of the importance of a monitor being present during operations.
Incident	01/10/12	Link 2	Foundation crew damaged an oak tree during mobilization effort at EP49. Crew was retrained.
Incident	01/12/12	Link 1	Parking along McCain Valley Rd not in designated disturbance areas. Link Leads corrected immediately.
Incident	01/12/12	Link 5	A dozer failure led to disturbance outside of approved ROW by 15 feet near CP59. All personnel were safe and restoration efforts are in process.
Incident	01/13/12	Link 2	An unanticipated release of a compressor mid-flight approximately 400ft North of Kruezkamp CY. No injuries or damage to property occurred. Investigation to helicopter hook system is ongoing.
Incident	01/17/12	Link 2	Crew entered access road to EP73/74, Arroyo Toad suitable habitat, prior to the 2 hr waiting period following dawn and biological monitor clearance. Crew was spoken to and better signage is to be installed.
Incident	01/18/12	Link 1	Concrete blocks were placed outside of approved disturbance area at EP224/5 prior to the approval of Variance #37. To limit disturbance, blocks have been left, but cannot be used until approval of the variance.
Incident	01/18/12	Link 1	Assembly crew arrived at EP177 prior to an approved bird survey having been conducted and submitted. Crews were ushered out by onsite avian biologist performing said survey.
Incident	01/18/12	Link 1	Foundation crew entered PBHS habitat at EP256 outside of approved work window. They were escorted out by monitors at a nearby site upon noticing. GF for crew was released by the project and a standdown with GF and foreman was performed on 01/23/12.

Type	Date	Location	Description
Incident	01/19/12	Link 2	Bird strike occurred during helicopter operations near EP33. Monitors on board believed the bird to be a swallow, but no remains were found to confirm.
Incident	01/20/12	Link 5	Wire dropped between CP96 and CP100 during wire operations. No resources were found to be damaged, hurt or killed.
Incident	01/20/12	Link 5	Gate left open for access road to pull site between CP64/65 and released livestock that was present. Monitors were brought onsite to herd them back into the pen and ensure security of the gate.
Incident	01/24/12	Link 5	Helicopter breached the GE buffer at Bell Bluff region approximately 621 feet. No resources impacted.
Incident	01/25/12	Link 5	Helicopter was noted by CPUC EM to have landed outside of approved project workspace. Correction was made immediately and discussion was had with pilot about landing in only approved areas.
Incident	01/26/12	Link 5	Helicopter breached the GE buffer at the Bell Bluff region approximately 521 feet. No resources impacted.
Incident	01/27/12	Link 2	Helicopter breached the GE buffer at the Thing Valley region approximately 161 feet. No resources impacted.
Incident	01/31/12	Link 1	Fuel tanker was refueling a smaller fuel truck for use by project helicopters in unapproved workspace near JVR. Link Lead made immediate correction and spoke to crew.
Incident	02/01/12	Link 2	Helicopter breached the GE buffer at the Thing Valley region by an unknown amount. No resources impacted.
Incident	02/13/12	Link 2	Several contractor vehicles were parked outside of the ROW on brush adjacent to Cameron TT near EP109. Link Lead was contacted and item was corrected.
Incident	02/24/12	Link 2	Helicopter dragged a long line through vegetation outside of workspace at EP109. Minor vegetation impacts.
Incident	02/25/12	Link 5	Helicopter experienced a hard landing at the Sycamore CY and damage was incurred. No injuries or impacts were noted. Investigation is ongoing.
Incident	02/27/12	Link 3	Trash was noted to Link Lead at the Wilson CY.
Incident	02/28/12	Link 1	Project activities were noted to be occurring in PBHS areas without concurrence from Wildlife Agencies provided to CPUC monitors. Follow up discussion occurred with WA.
Incident	02/29/12	Link 1	Debris was noted to the Link Lead as being blown around JVR CY during Air Crane operations.
Incident	03/02/12	Link 2	Kmax helicopter dropped cribbing near EP5. No reports of injuries or impacts.
Incident	03/08/12	Link 1	Trash in several areas along the ROW, particularly the mylar taping utilized for bird deterrents, has been noted in various locations. Issue is currently being addressed.
Incident	03/12/12	Link 2	Vehicle was noted to be parked outside approved workspace and within the drip line of an oak tree.
Incident	03/14/12	Link 1	A helicopter noted to be operating prior to 7am at the Rough Acres Construction Yard.

Type	Date	Location	Description
Incident	03/20/12	Link 1	Crew vehicles were noted to be parked outside of approved workspaces along Old Hwy 80. Vehicles were immediately moved upon notification.
Incident	03/20/12	Link 1	Marker balls were being staged inside a noted ESA at the Jacumba Valley Ranch Yard. They were immediately moved outside of the ESA and no impacts were noted.
Incident	03/21/12	Link 1	Work equipment was placed outside of approved workspace via helicopter at EP225. Corrective action was immediately taken upon notification.
Incident	03/22/12	Link 1	Vehicle was noted to be parked outside of approved workspace near EP205-1 and project personnel was observed to be smoking in a non-designated area.
Incident	03/27/12	Link 2	Vehicle was noted to be parked within a bird buffer near EP90.
Incident	03/27/12	Link 2	Two helicopters noted to be operating prior to 7am at the SWAT Construction Yard.
Incident	03/28/12	Link 2	Breaches within the Arroyo Toad exclusionary fencing between EP65 and EP69 were noted to the Link Lead.
Incident	03/29/12	Link 1	Trash at EP190 and dust on McCain Valley Road was noted to the Link Lead.
Incident	03/31/12	Link 1	Bulldozer was noted to have parked outside of approved workspace along the access road to EP236. The equipment was moved upon notification to the crew.
Incident	04/02/12	Link 1	Parking occurred in unapproved project areas near S-2 Yard. Immediate corrective action was taken upon notification to Link Lead.
Incident	04/04/12	Link 1	Crew truck was noted to have parked outside of approved workspace along the access road to EP236. Monitors have placed additional signage along the road.
Incident	04/09/12	Link 1	Crews were noted to not being utilizing a designated path (which avoids an ESA) from TSAP to EP137-1. A warning was given and crews were addressed.
Incident	04/10/12	Link 1	Trash was observed at EP187 pull site.
Incident	04/17/12	Link 4	Cement truck was noted to be driving down Alpine Blvd with chutes open. Link Lead was contacted and contractor was informed of the activities.
Incident	04/20/12	Link 1	Bulldozer went off ROW during grading operations near EP255. No sensitive biological or cultural resources were damaged.
Incident	04/24/12	Link 1	Dust was noted to be seen at McCain Valley Construction Yard due to Air Crane operations. Coordination was to improve in future operations.
Incident	04/25/12	Link 2	Holes were noted in the Arroyo Toad fence along the access road to EP76. Crews were sent out to repair prior to rain event.
Incident	05/08/12	Link 2	Speeding was noted to Link Lead to/from Bartlett Hauser CY.
Incident	05/16/12	Link 2	Dust was noted at Kruetzkamp CY to the Link Lead during air crane operations.

Type	Date	Location	Description
Incident	05/22/12	Link 2	Speeding was noted to Link Lead to/from Bartlett Hauser CY.
Incident	05/24/12	Link 2	During the removal of flower pots and guard poles at the EP27-1 guard structure site, a small amount of vegetation was damaged. No sensitive resources or nests were noted to be damaged after assessment by biological and avian monitors.
Incident	09/28/12	Link 1	Gate remains at AER Yard and should be reviewed for removal or pursuance of variance is required.

PROJECT PHOTOGRAPHS



Figure 1: Digging trenches for conduit at Encina Substation.



Figure 2: Steel assembly at Encina Substation.

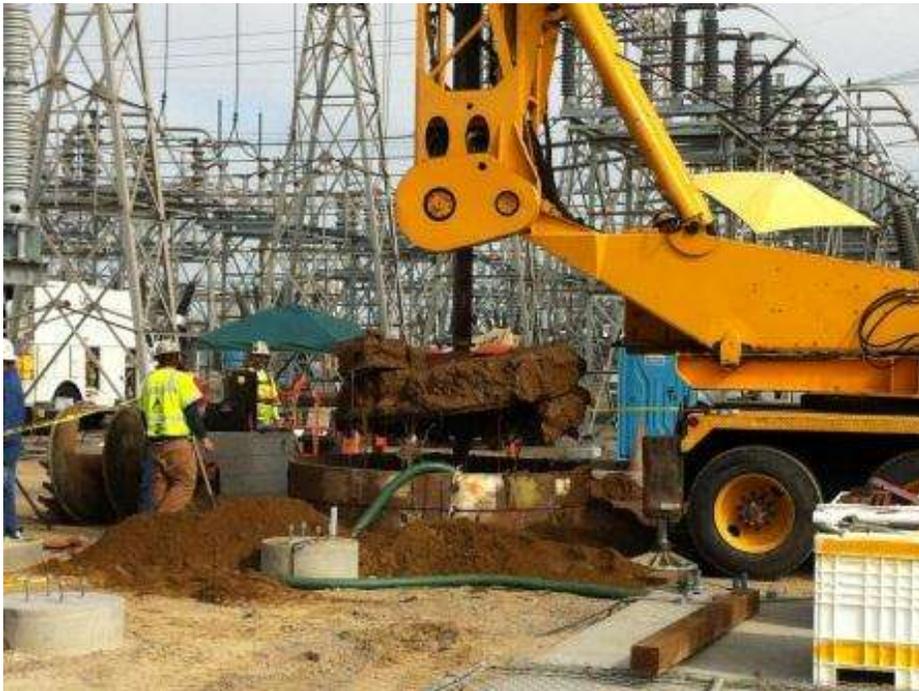


Figure 3: Foundation drilling for 230 kV termination pier at Encina Substation.



Figure 4: ESA signage at Encina Substation.
